



Remaining Level of Effort Remaining Work ◆ Milestone
Actual Work Critical Remaining Work ▶ Summary


Page 1 of 74


TASK filter: All Activities


© Oracle Corporation

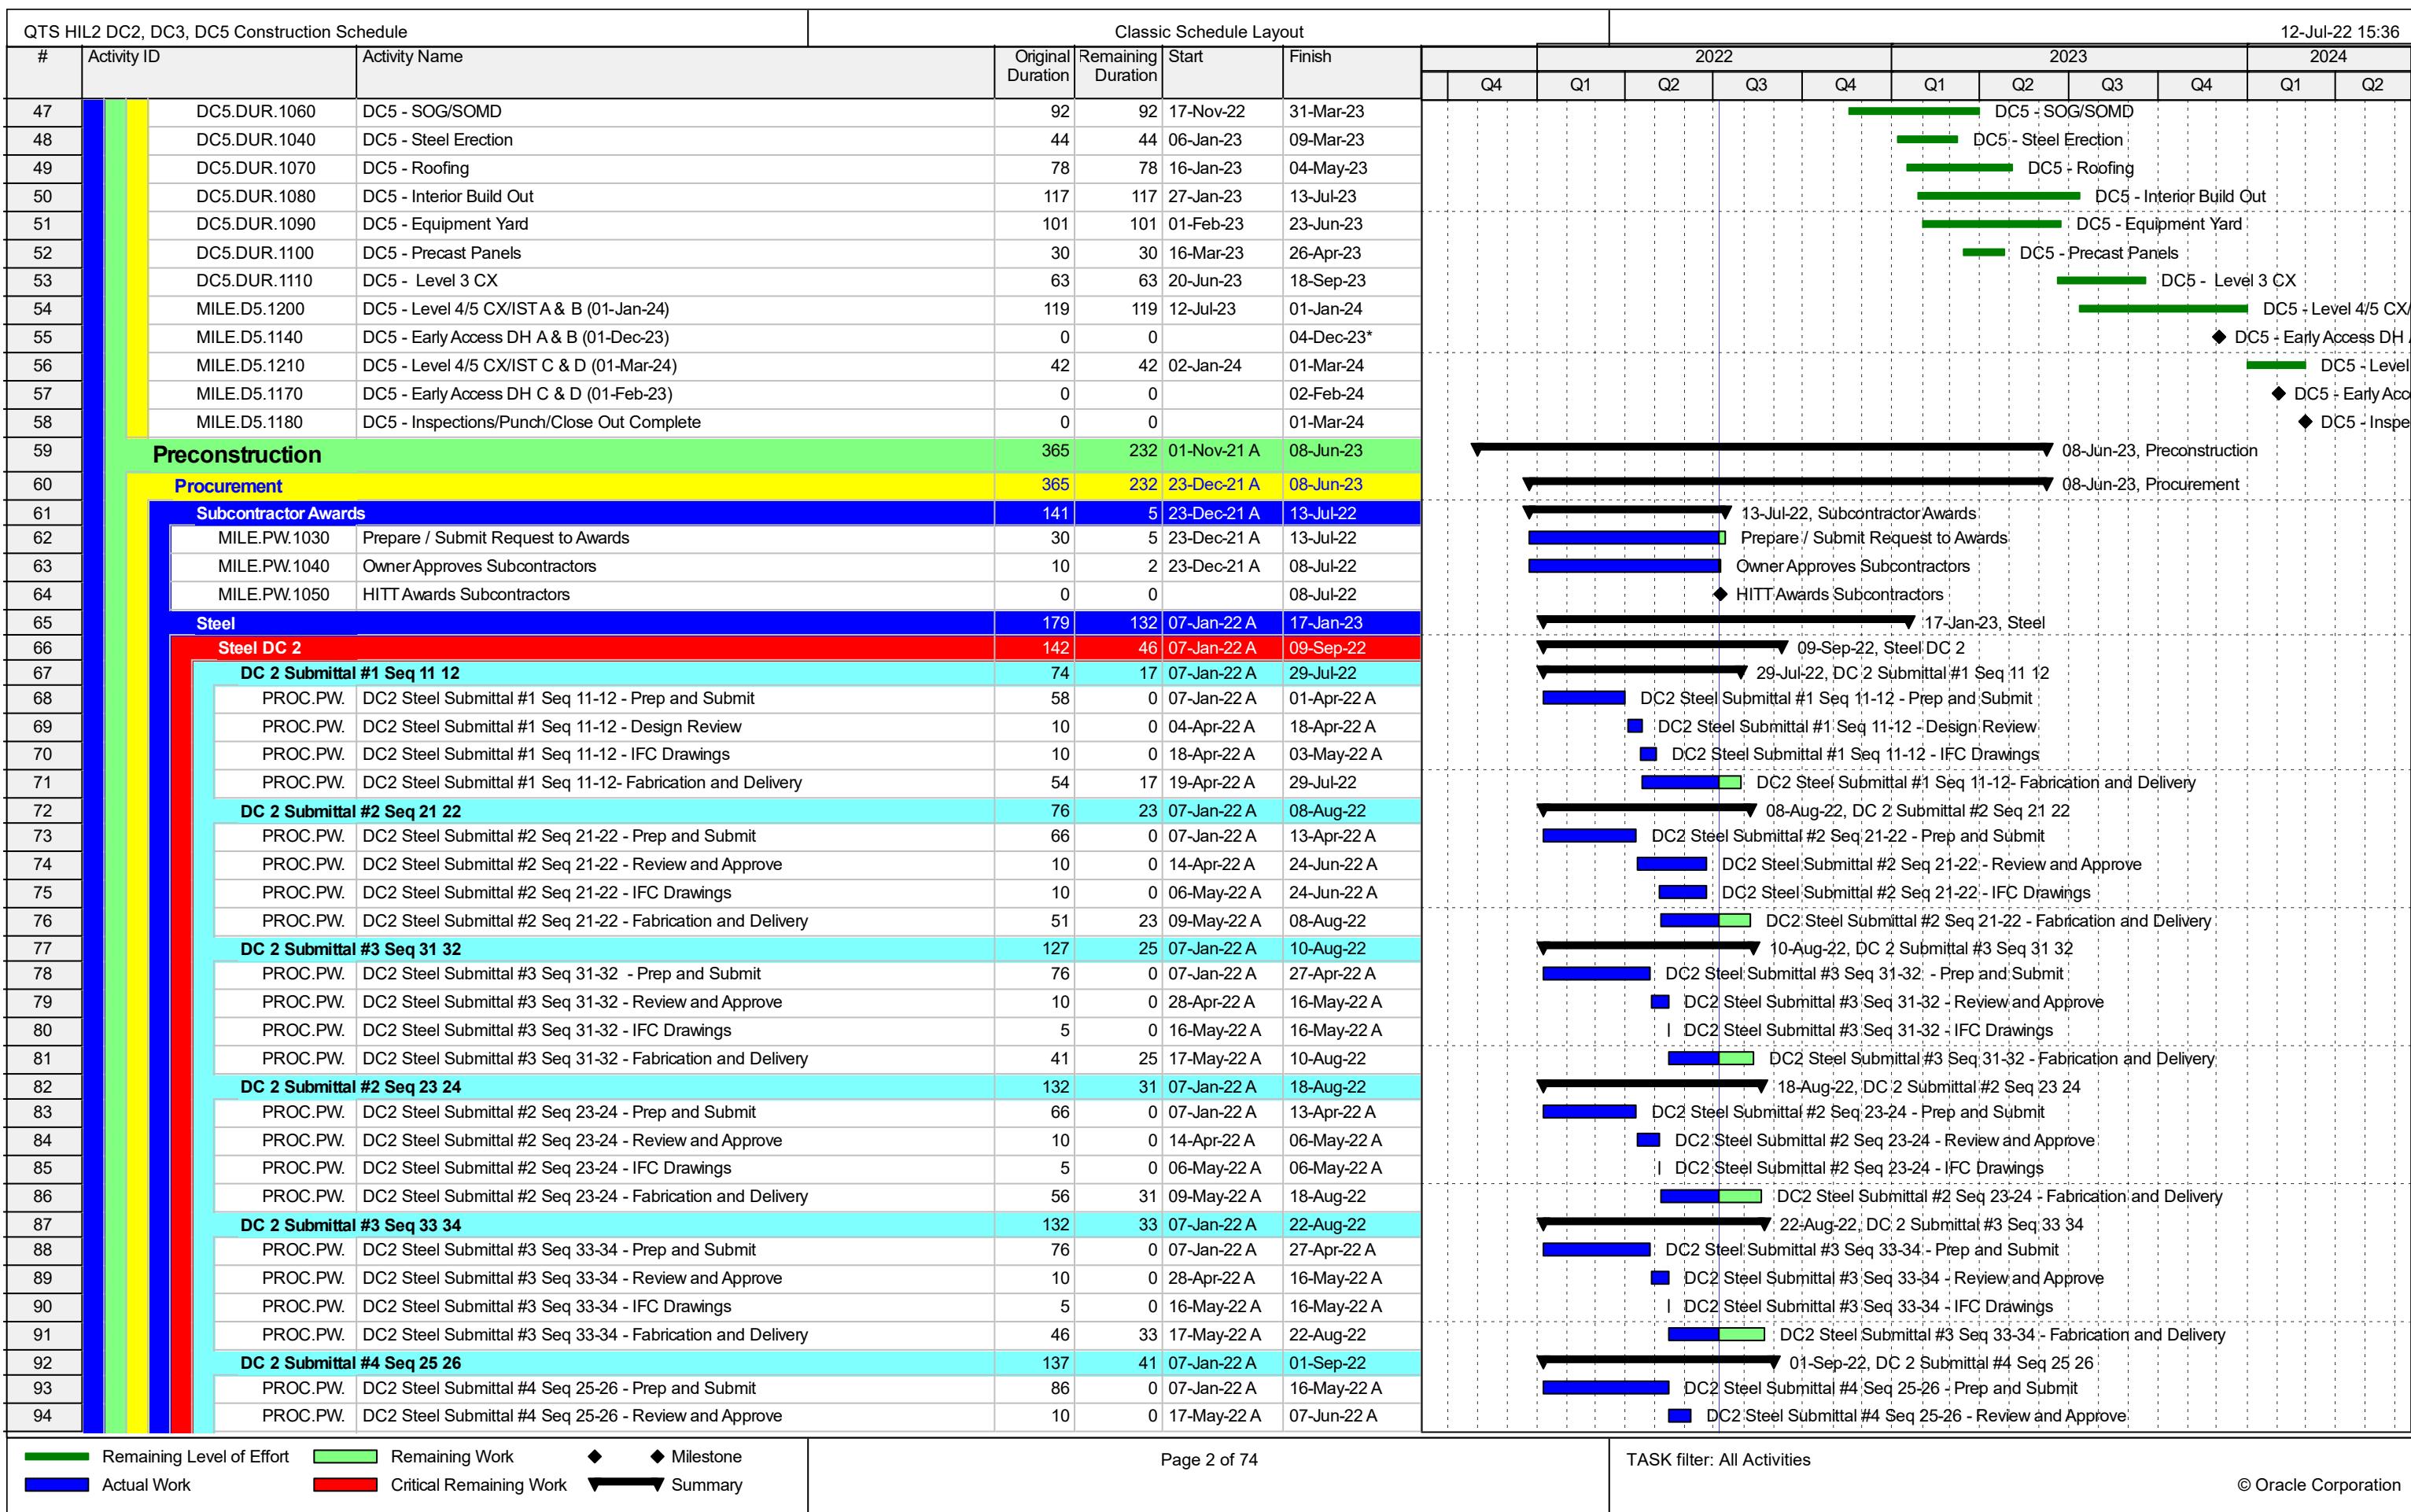


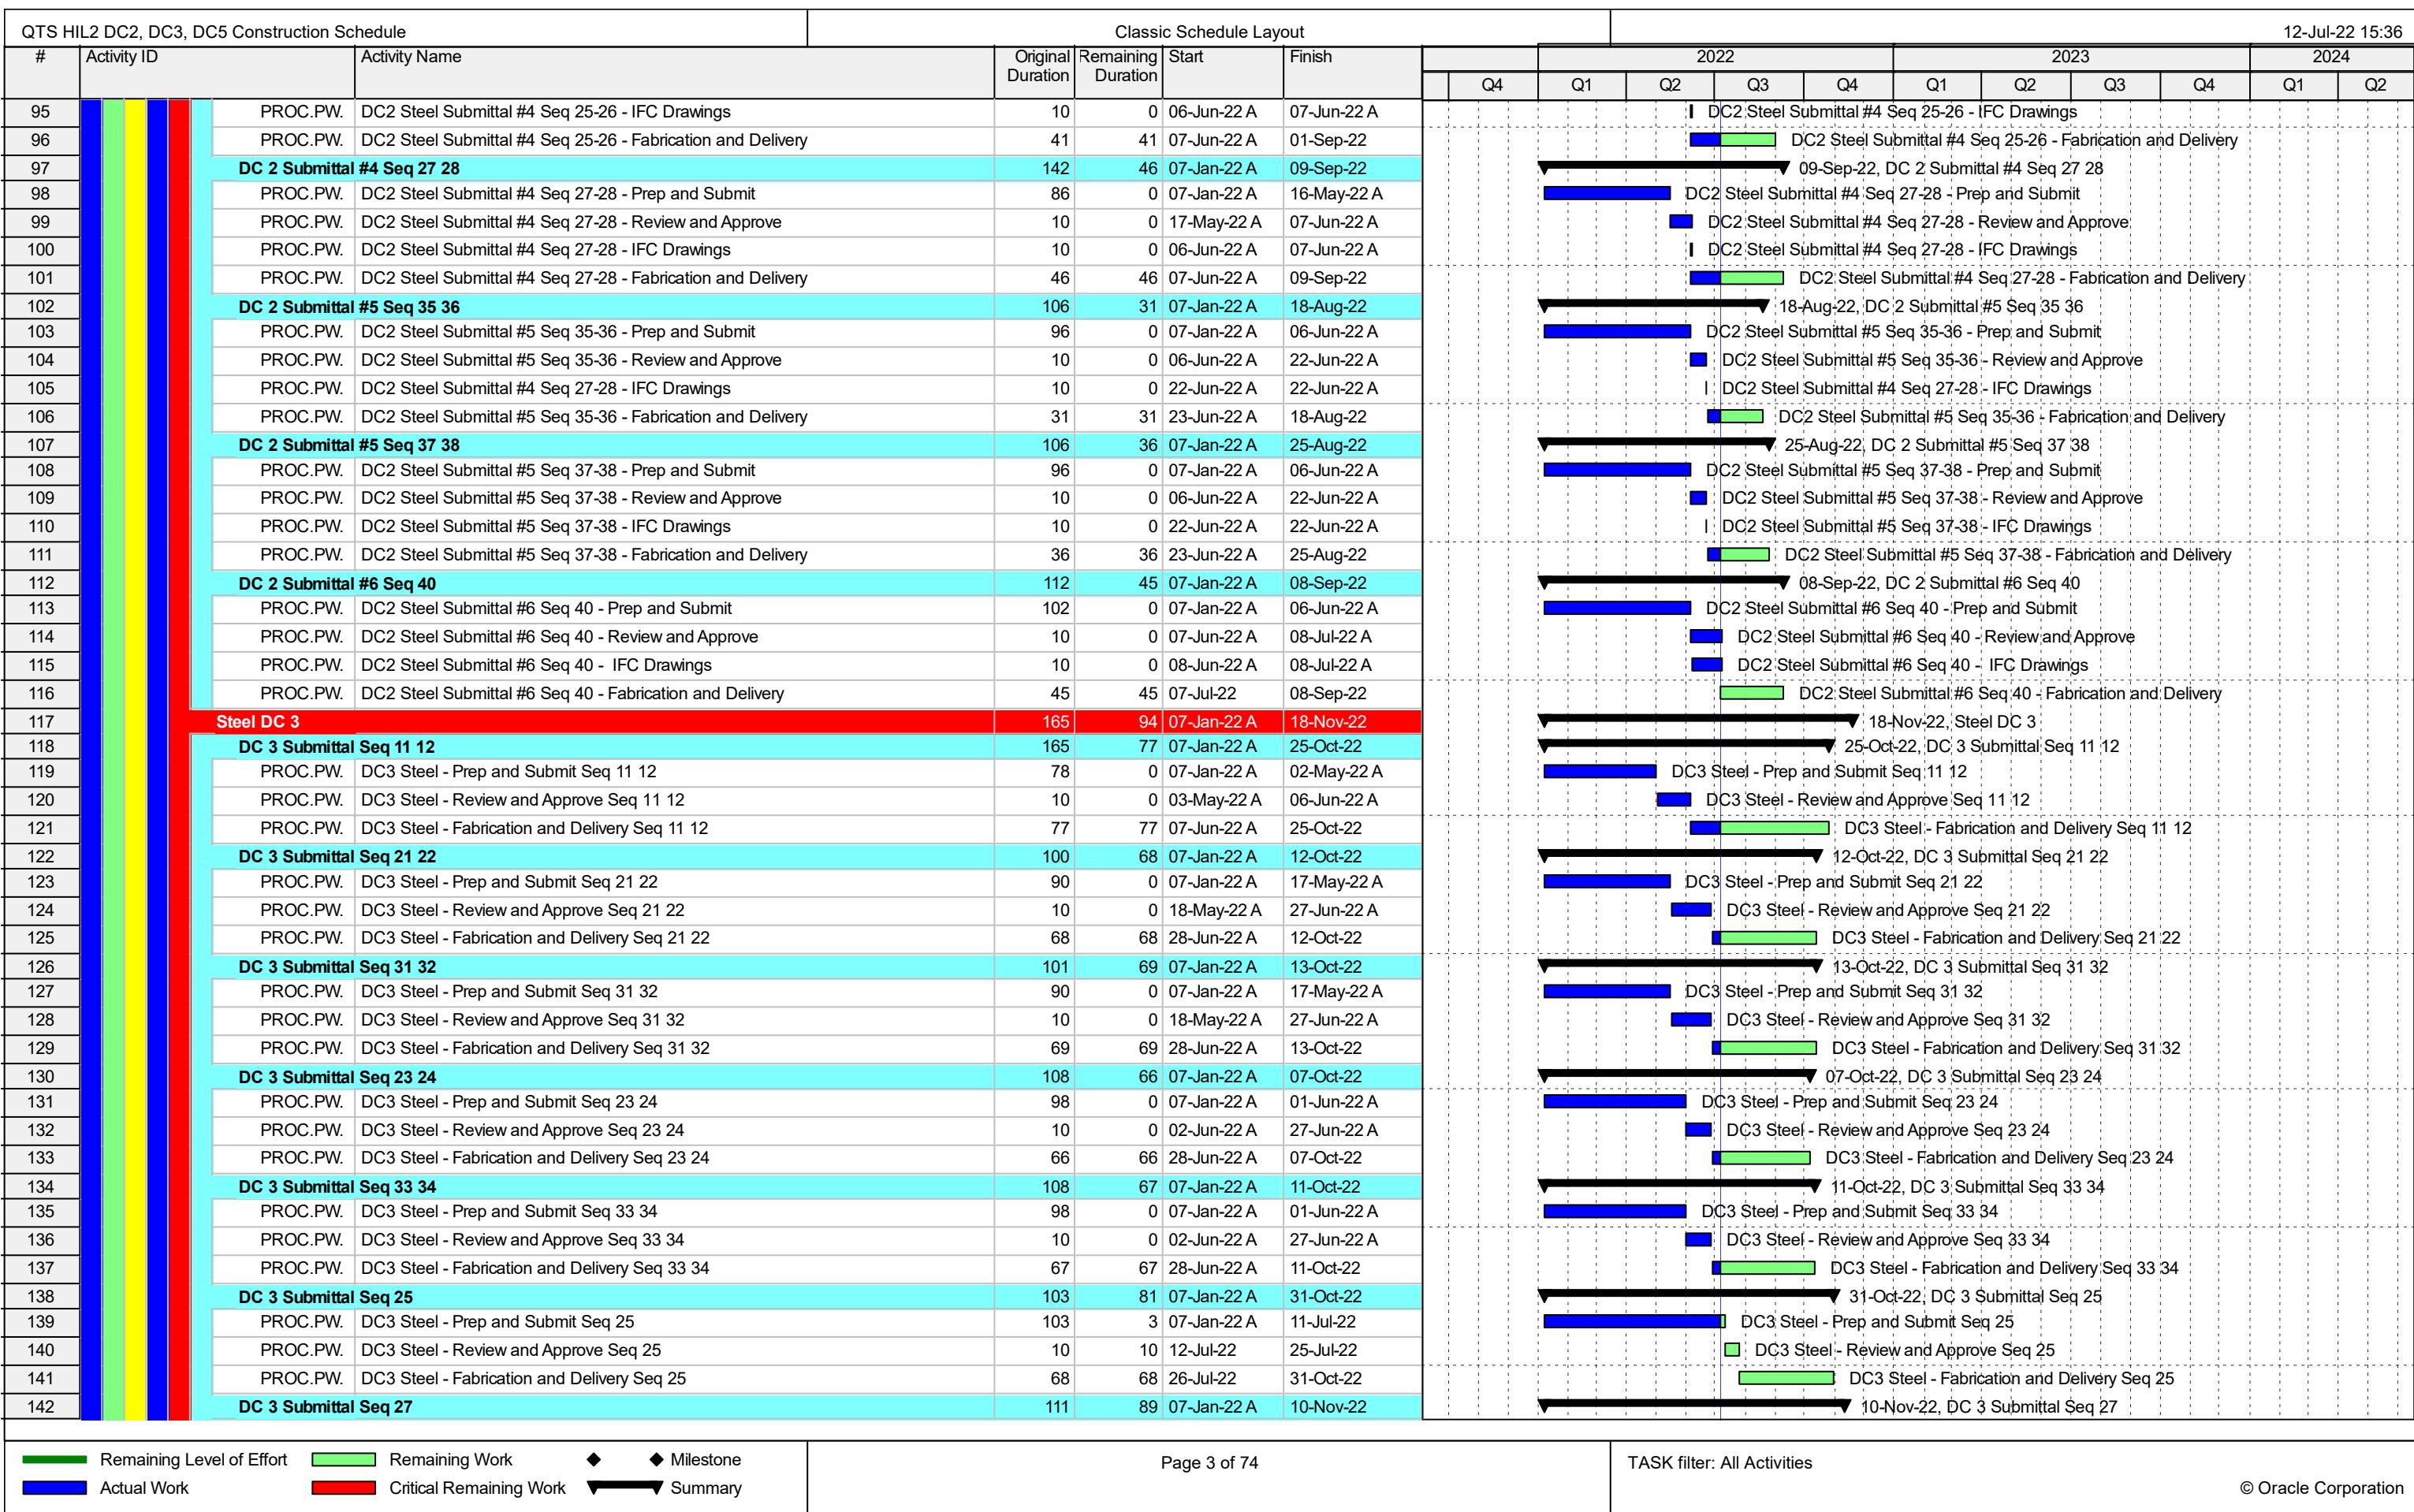

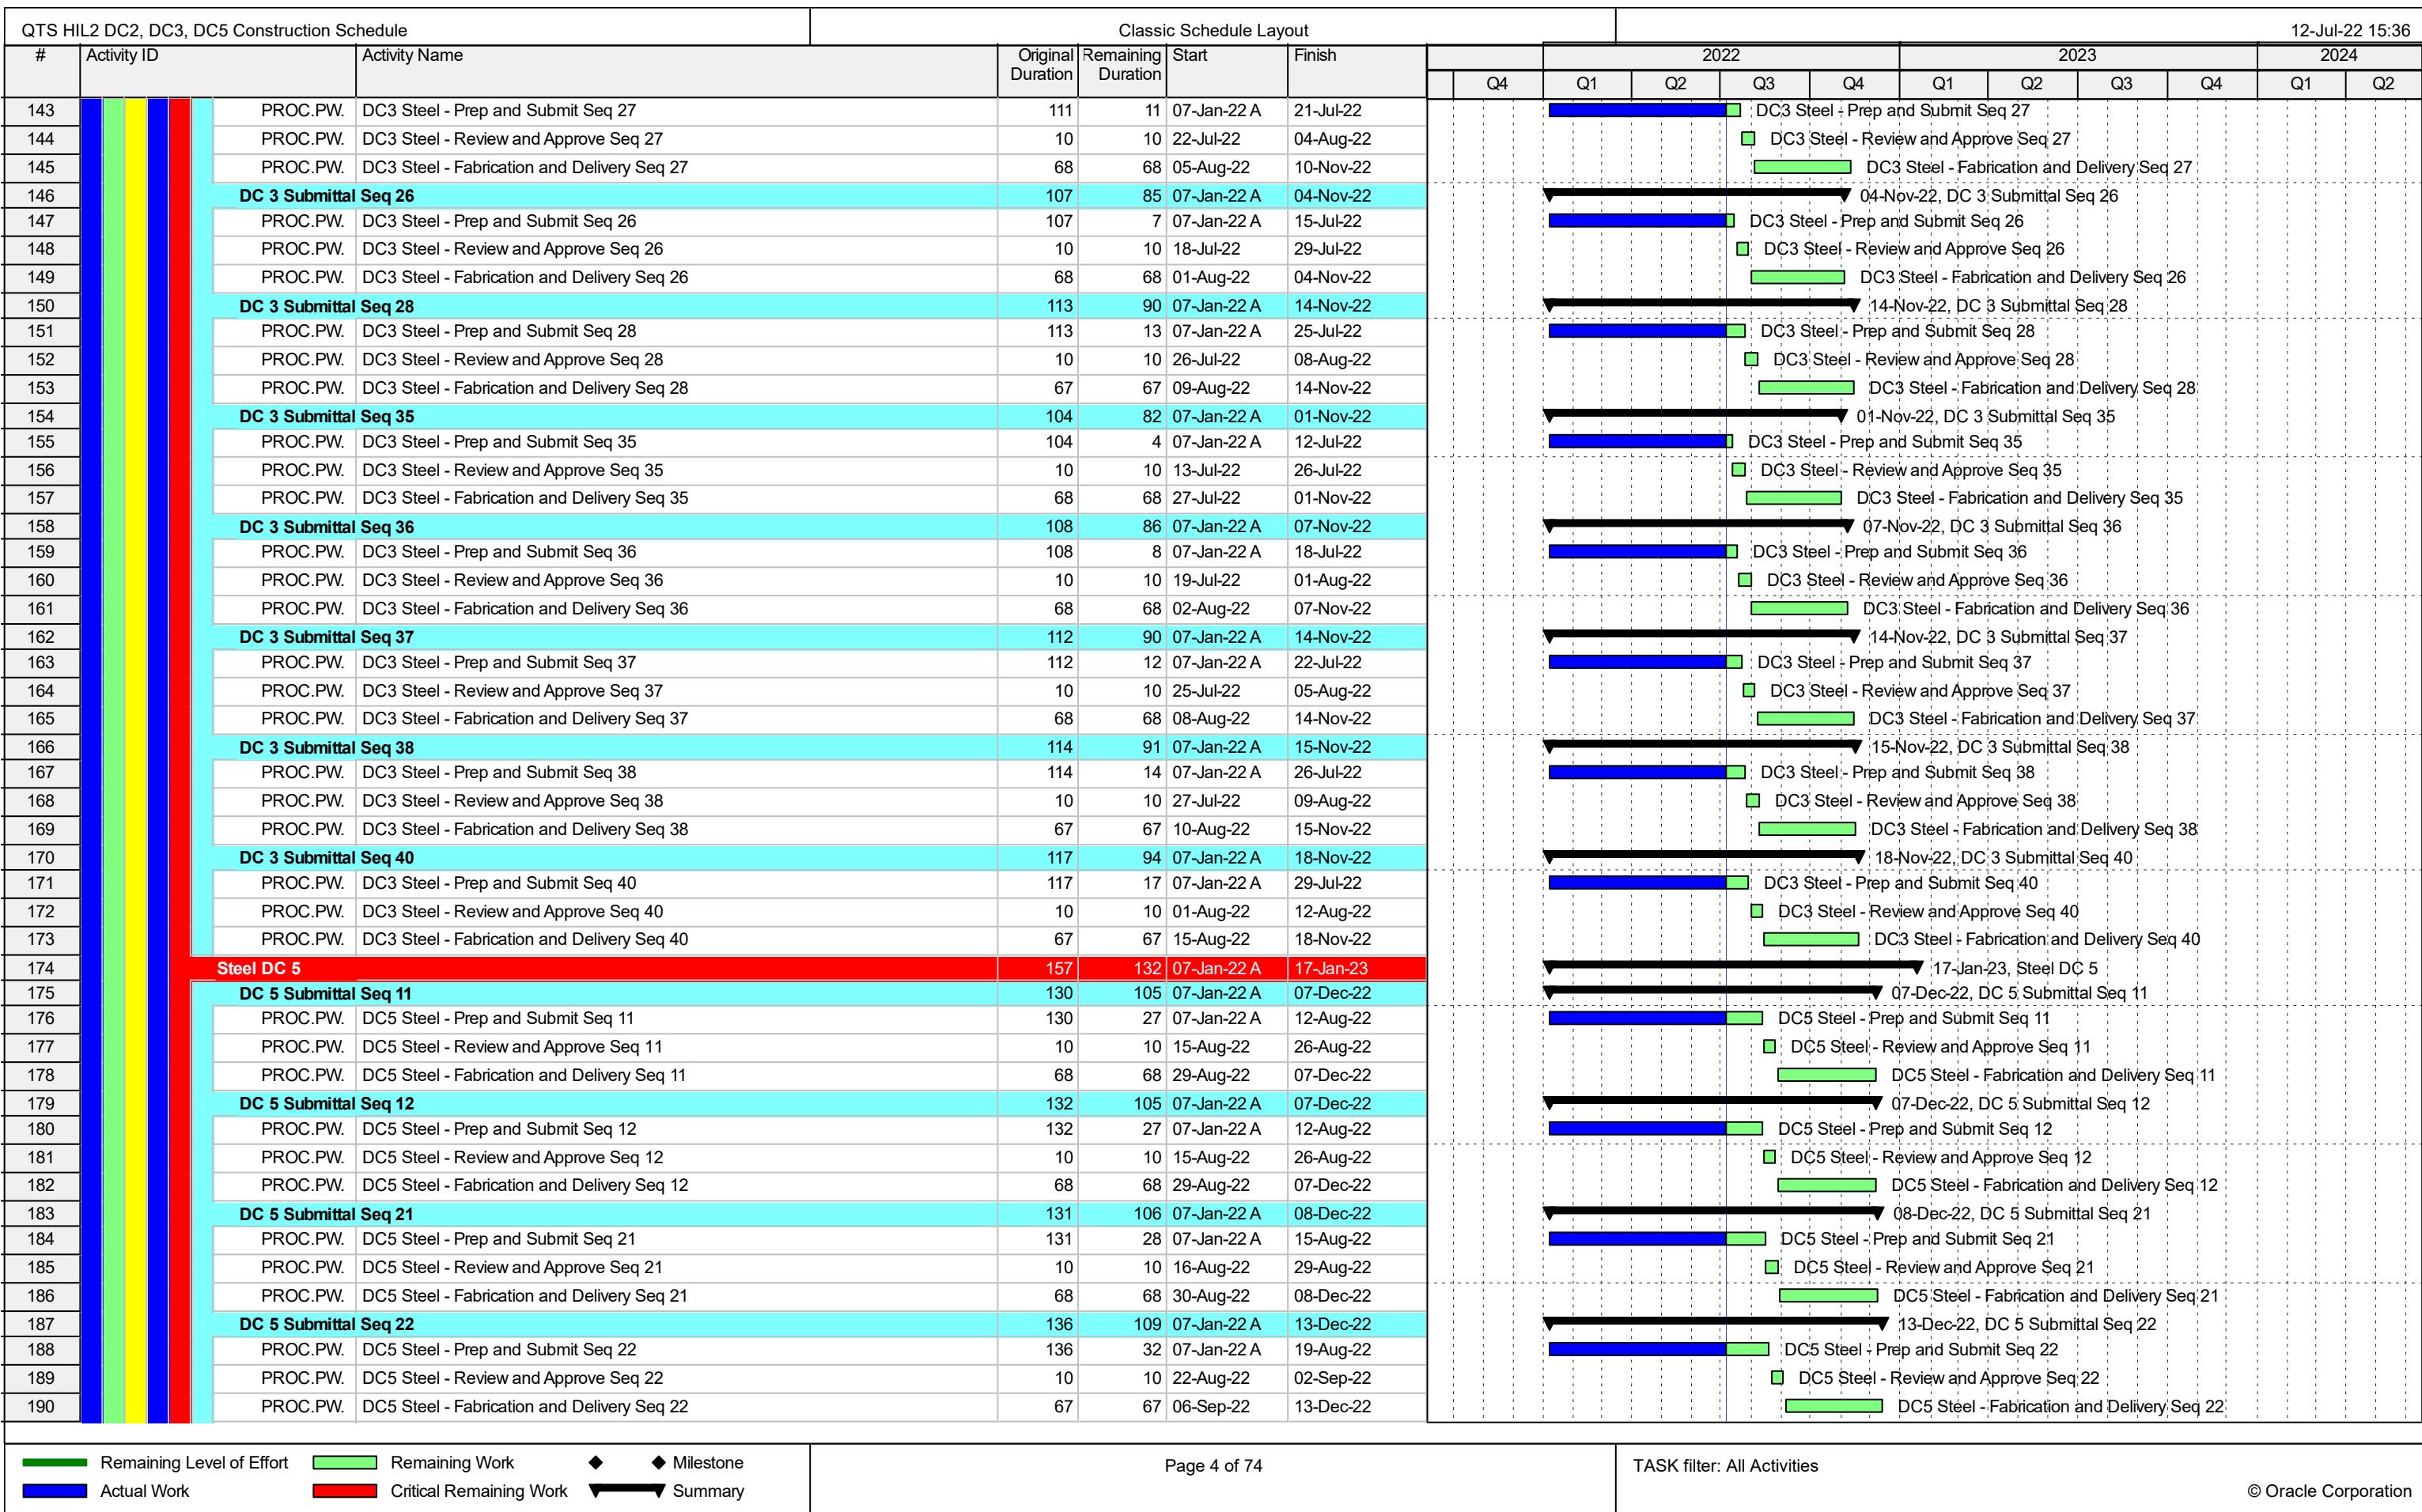

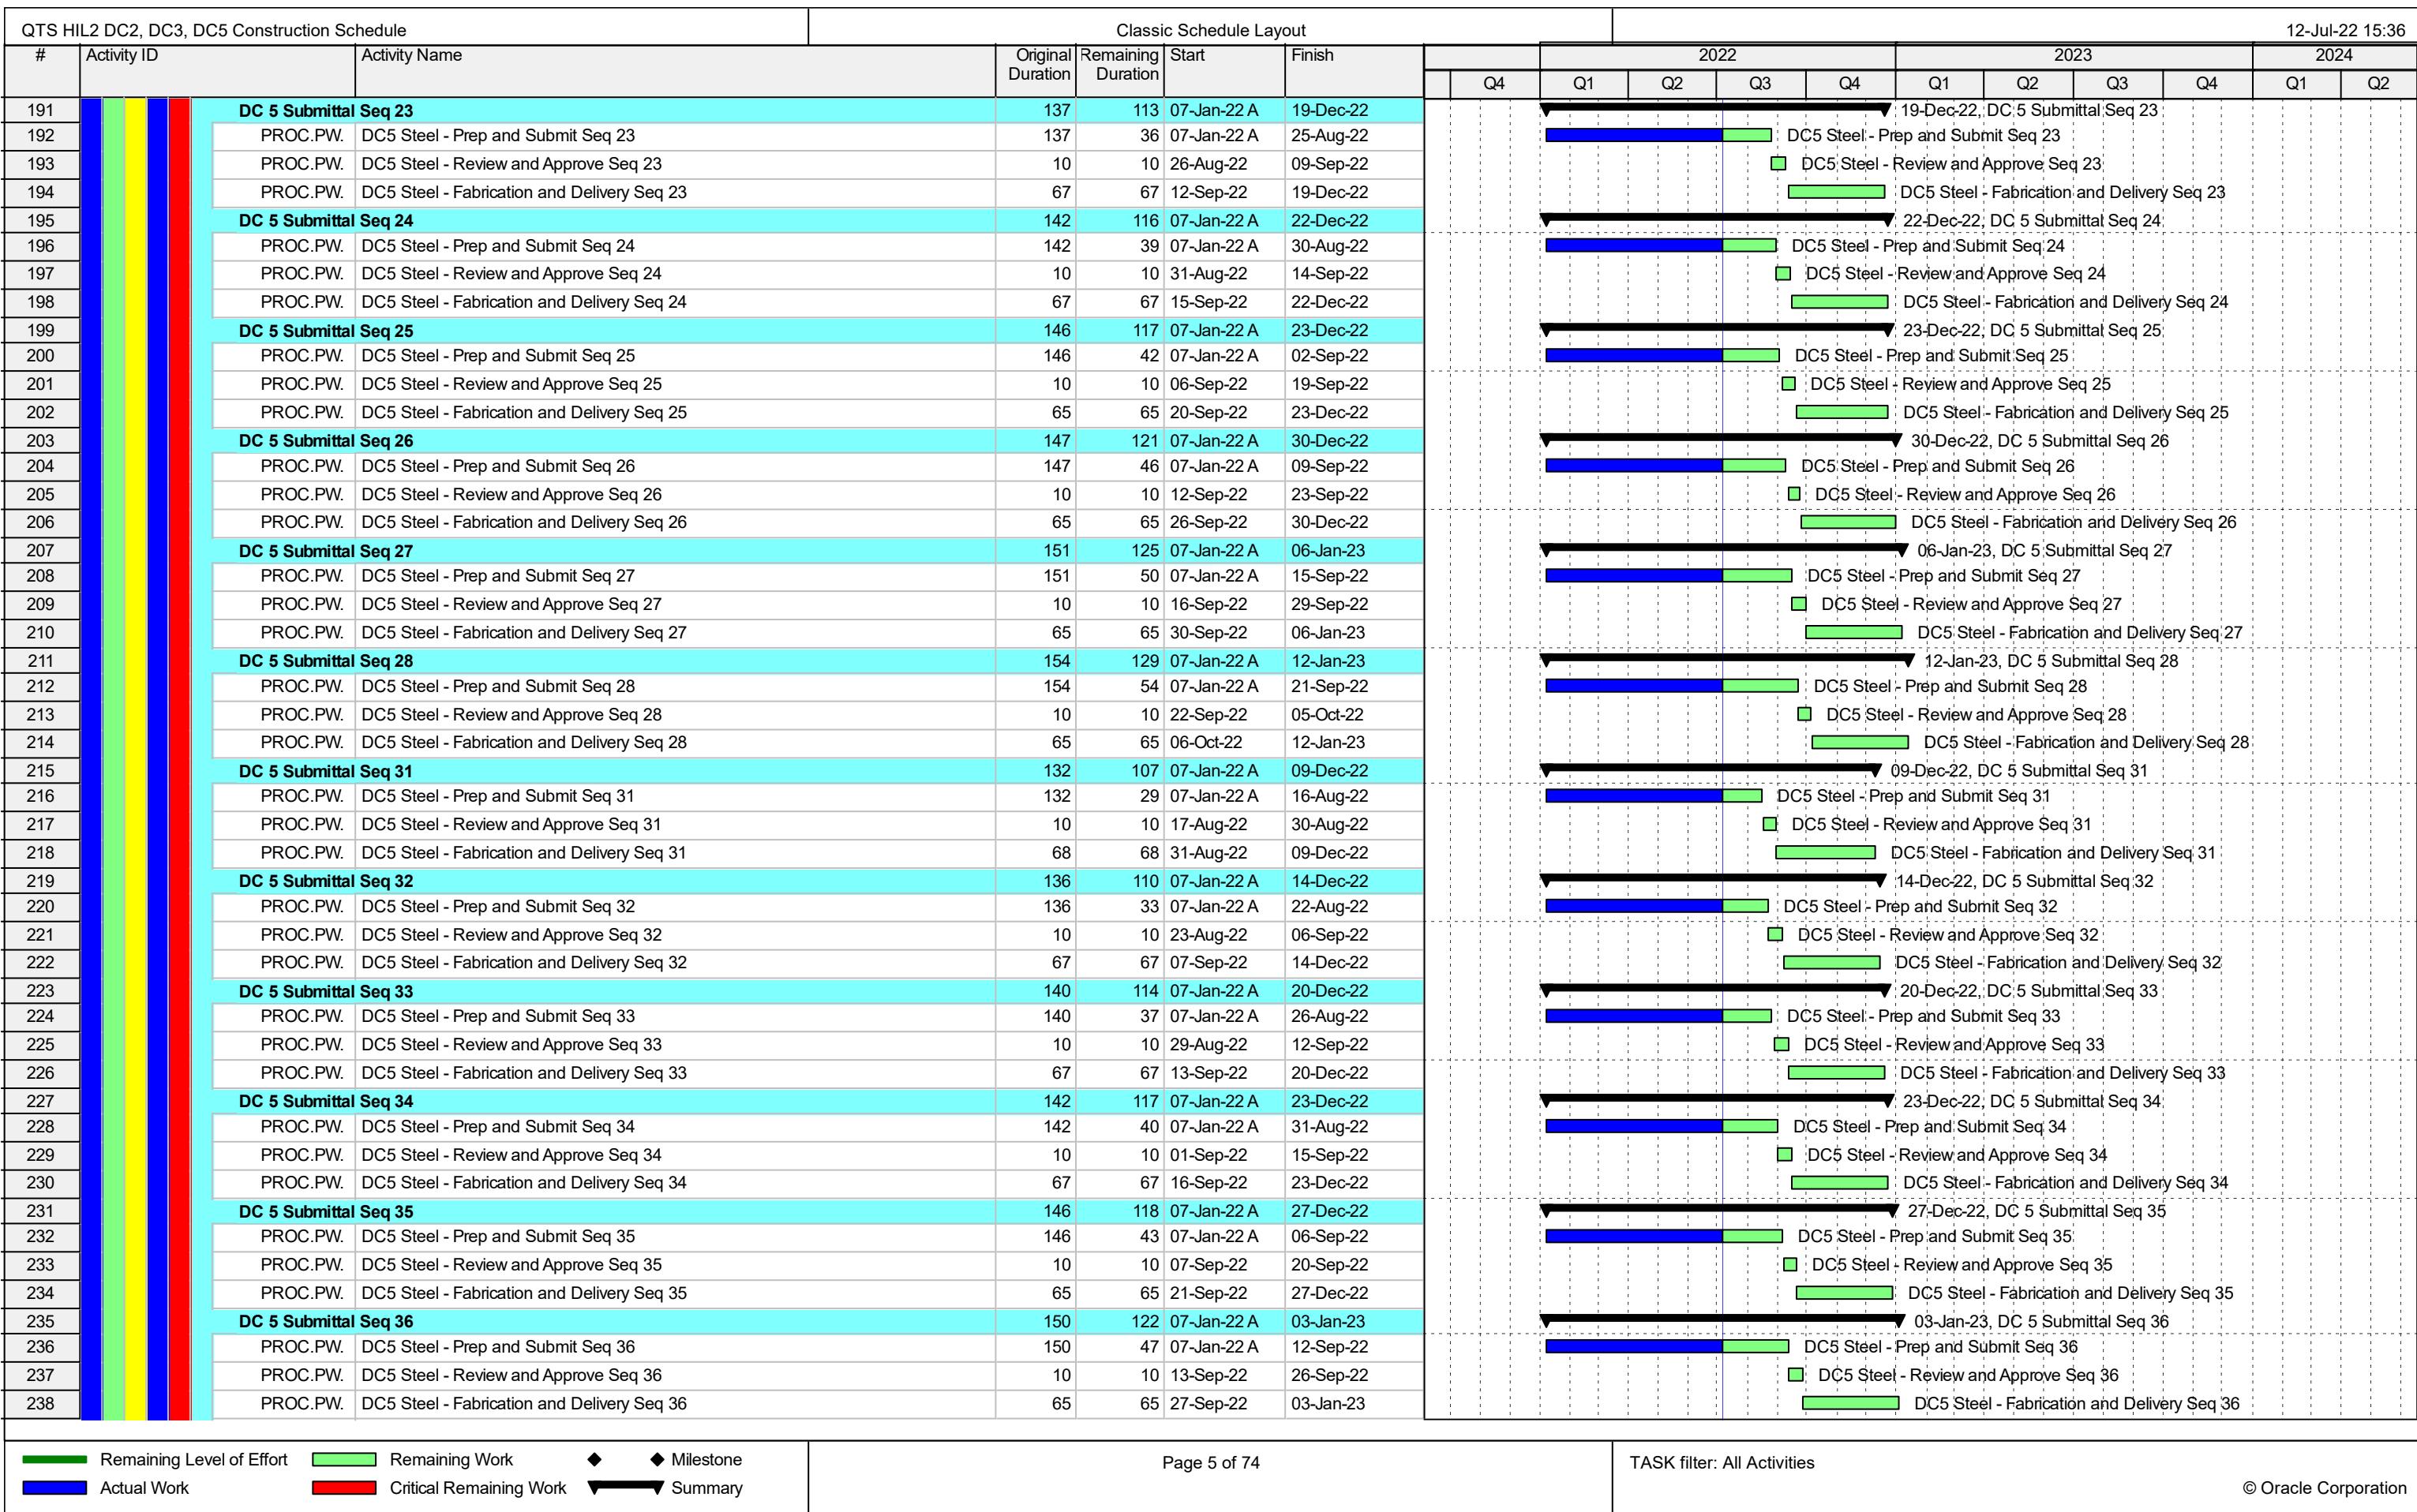


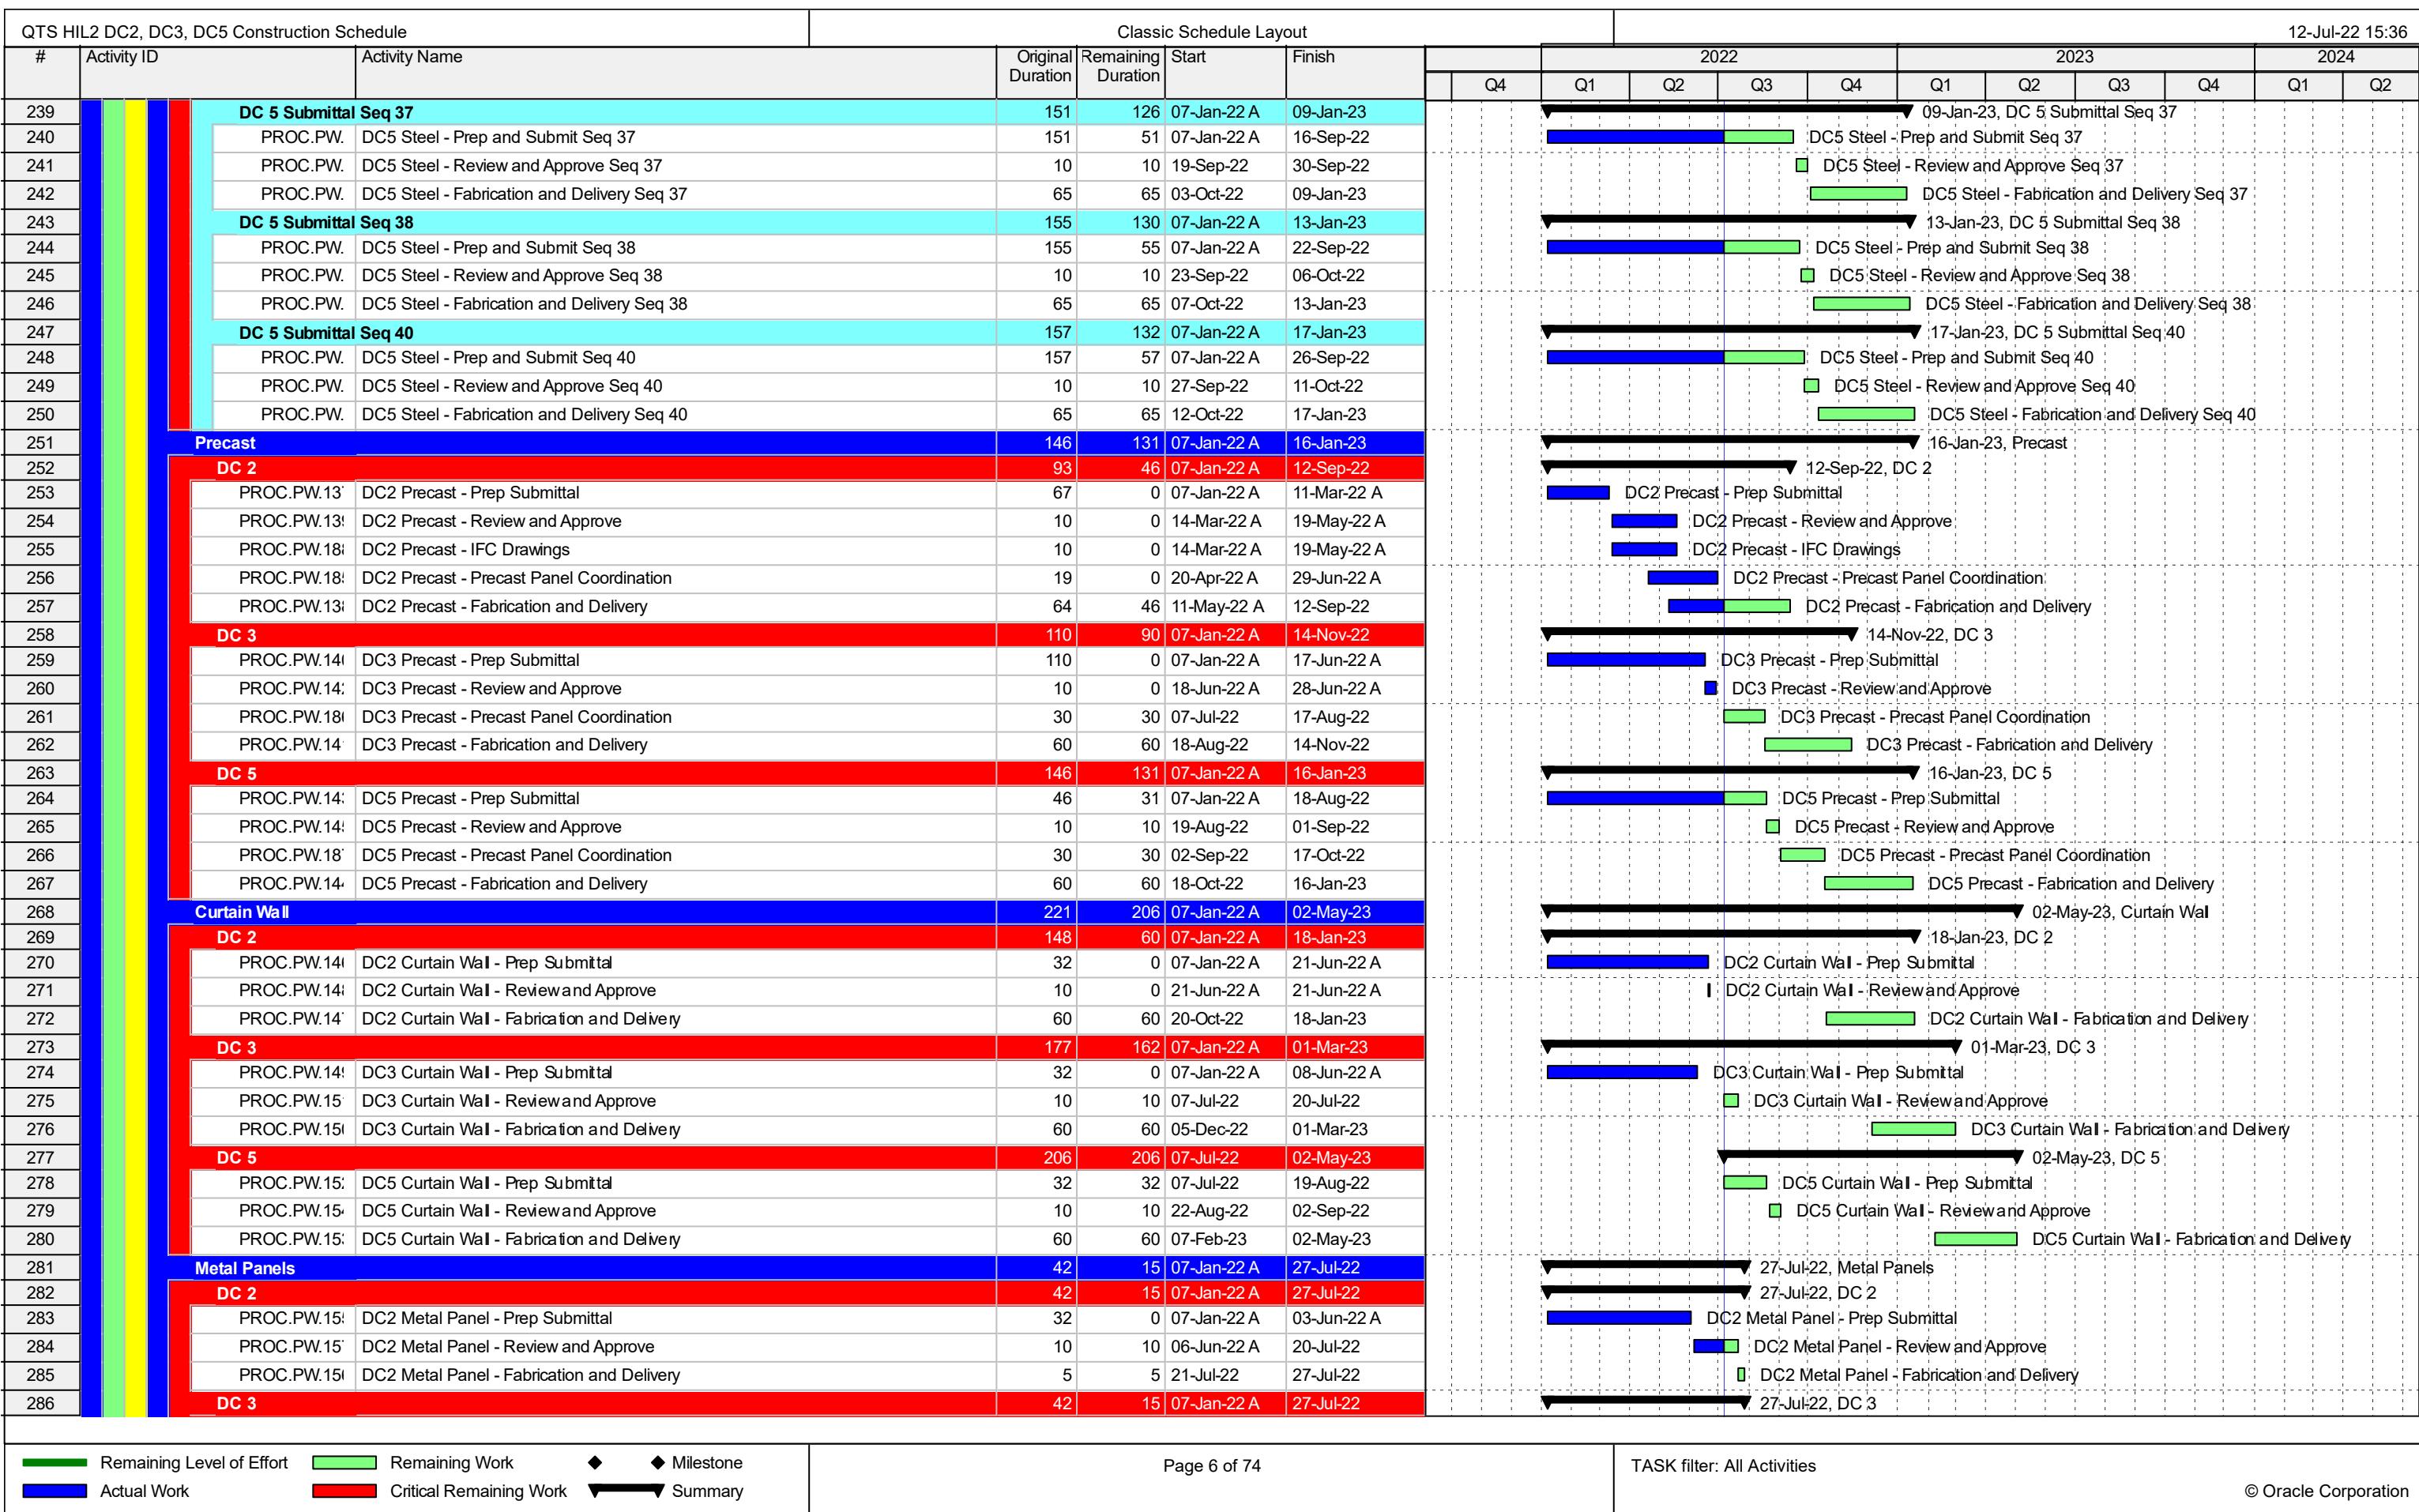


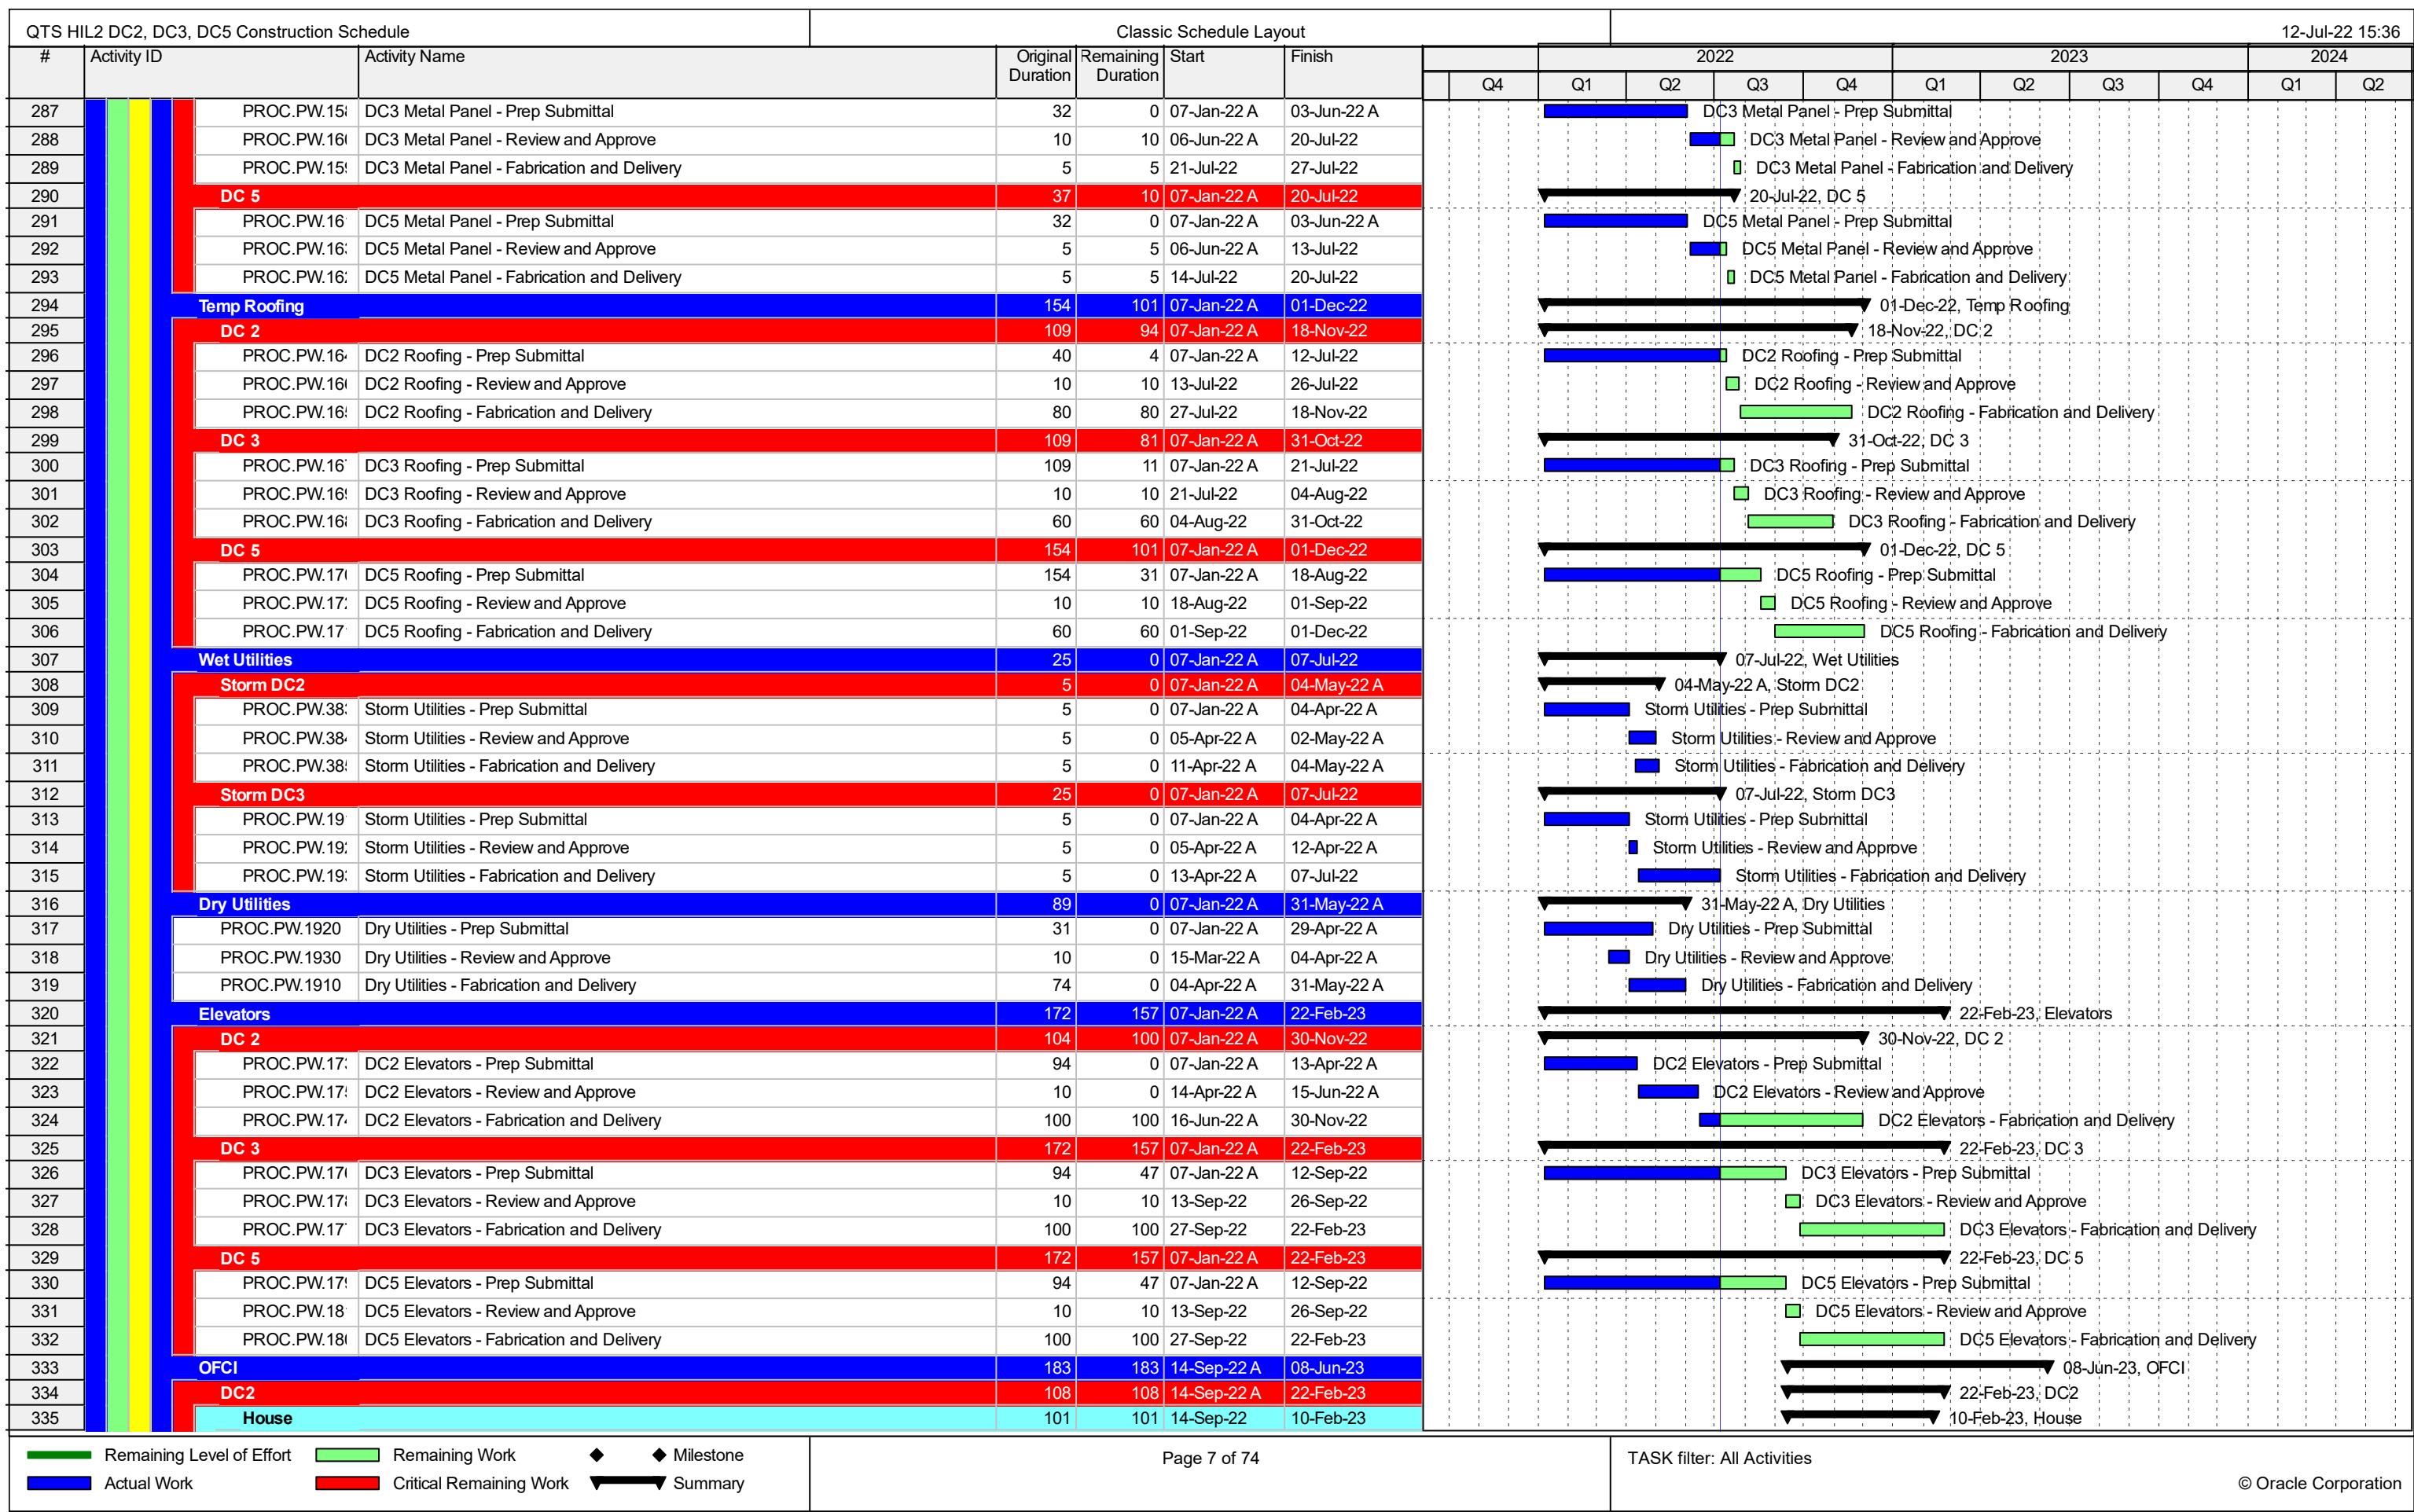


QTS HIL2 DC2, DC3, DC5 Construction Schedule				Classic Schedule Layout					12-Jul-22 15:36								
#	Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	2022					2023				2024	
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2
336		PROC.PW. OFCI Procure - RTUs House	0	0		14-Sep-22					◆ OFCI Procure - RTUs House						
337		PROC.PW. OFCI Procure - Transformer House (XFMR-H)	0	0		09-Jan-23					◆ OFCI Procure - Transformer House (XFMR-H)						
338		PROC.PW. OFCI Procure - HDP Boards House	0	0		07-Feb-23					◆ OFCI Procure - HDP Boards House						
339		PROC.PW. OFCI Procure - Medium Voltage - Service Entry Switch Gear	0	0		10-Feb-23					◆ OFCI Procure - Medium Voltage - Service Entry Switch Gear						
340		PROC.PW. OFCI Procure - Medium Voltage - Vista Switch	0	0		10-Feb-23					◆ OFCI Procure - Medium Voltage - Vista Switch						
341		MPOE/BDF		71	71	24-Oct-22 A	07-Feb-23										
342		PROC.PW. OFCI Procure - ACCU MPOE/BDF	0	0		24-Oct-22					◆ OFCI Procure - ACCU MPOE/BDF						
343		PROC.PW. OFCI Procure - UPS Pods MPOE/BDF	0	0	23-Dec-22 A						◆ OFCI Procure - UPS Pods MPOE/BDF						
344		PROC.PW. OFCI Procure - Transformers MPOE/BDF	0	0		23-Dec-22					◆ OFCI Procure - Transformers MPOE/BDF						
345		PROC.PW. OFCI Procure - Generators MPOE/BDF	0	0		30-Dec-22					◆ OFCI Procure - Generators MPOE/BDF						
346		PROC.PW. OFCI Procure - Network COD 2000AMP	0	0		09-Jan-23					◆ OFCI Procure - Network COD 2000AMP						
347		PROC.PW. OFCI Procure - COD boards MPOE/BDF	0	0		13-Jan-23					◆ OFCI Procure - COD boards MPOE/BDF						
348		PROC.PW. OFCI Procure - CRAC Units MPOE/BDF	0	0		03-Feb-23					◆ OFCI Procure - CRAC Units MPOE/BDF						
349		PROC.PW. OFCI Procure - HDP Boards MPOE/BDF	0	0		07-Feb-23					◆ OFCI Procure - HDP Boards MPOE/BDF						
350		DH A and B		82	82	29-Sep-22	31-Jan-23										
351		PROC.PW. OFCI Procure - ACCU DH A	0	0		29-Sep-22					◆ OFCI Procure - ACCU DH A						
352		PROC.PW. OFCI Procure - ACCU DH B	0	0		29-Sep-22					◆ OFCI Procure - ACCU DH B						
353		PROC.PW. OFCI Procure - Transformers DH A and B	0	0		09-Jan-23					◆ OFCI Procure - Transformers DH A and B						
354		PROC.PW. OFCI Procure - COD boards DH A	0	0		13-Jan-23					◆ OFCI Procure - COD boards DH A						
355		PROC.PW. OFCI Procure - COD boards DH B	0	0		13-Jan-23					◆ OFCI Procure - COD boards DH B						
356		PROC.PW. OFCI Procure - Generators DH A and B	0	0		17-Jan-23					◆ OFCI Procure - Generators DH A and B						
357		PROC.PW. OFCI Procure - CRAC Units DH A	0	0		23-Jan-23					◆ OFCI Procure - CRAC Units DH A						
358		PROC.PW. OFCI Procure - HDP Boards DH A & B	0	0		25-Jan-23					◆ OFCI Procure - HDP Boards DH A & B						
359		PROC.PW. OFCI Procure - CRAC Units DH B	0	0		31-Jan-23					◆ OFCI Procure - CRAC Units DH B						
360		DH C and D		71	71	07-Nov-22	22-Feb-23										
361		PROC.PW. OFCI Procure - ACCU DH C	0	0		07-Nov-22					◆ OFCI Procure - ACCU DH C						
362		PROC.PW. OFCI Procure - ACCU DH D	0	0		07-Nov-22					◆ OFCI Procure - ACCU DH D						
363		PROC.PW. OFCI Procure - Transformers DH C and D	0	0		30-Jan-23					◆ OFCI Procure - Transformers DH C and D						
364		PROC.PW. OFCI Procure - Generators DH C and D	0	0		07-Feb-23					◆ OFCI Procure - Generators DH C and D						
365		PROC.PW. OFCI Procure - COD boards DH D	0	0		07-Feb-23					◆ OFCI Procure - COD boards DH D						
366		PROC.PW. OFCI Procure - HDP Boards DH C & D	0	0		09-Feb-23					◆ OFCI Procure - HDP Boards DH C & D						
367		PROC.PW. OFCI Procure - CRAC Units DH D	0	0		17-Feb-23					◆ OFCI Procure - CRAC Units DH D						
368		PROC.PW. OFCI Procure - CRAC Units DH C	0	0		22-Feb-23					◆ OFCI Procure - CRAC Units DH C						
369		PROC.PW. OFCI Procure - COD boards DH C	0	0		22-Feb-23					◆ OFCI Procure - COD boards DH C						
370		DC3		41	41	02-Feb-23	03-Apr-23										
371		House		28	28	16-Feb-23	29-Mar-23										
372		PROC.PW. OFCI Procure - Transformer House (XFMR-H)	0	0		16-Feb-23					◆ OFCI Procure - Transformer House (XFMR-H)						
373		PROC.PW. OFCI Procure - HDP Boards House	0	0		20-Mar-23					◆ OFCI Procure - HDP Boards House						
374		PROC.PW. OFCI Procure - Medium Voltage - Service Entry Switch Gear	0	0		23-Mar-23					◆ OFCI Procure - Medium Voltage - Service Entry Switch Gear						
375		PROC.PW. OFCI Procure - Medium Voltage - Vista Switch	0	0		23-Mar-23					◆ OFCI Procure - Medium Voltage - Vista Switch						
376		PROC.PW. OFCI Procure - RTUs House	0	0		29-Mar-23					◆ OFCI Procure - RTUs House						
377		MPOE/BDF		38	38	02-Feb-23	29-Mar-23										
378		PROC.PW. OFCI Procure - UPS Pods MPOE/BDF	0	0		02-Feb-23					◆ OFCI Procure - UPS Pods MPOE/BDF						
379		PROC.PW. OFCI Procure - Transformers MPOE/BDF	0	0		03-Feb-23					◆ OFCI Procure - Transformers MPOE/BDF						
380		PROC.PW. OFCI Procure - Generators MPOE/BDF	0	0		09-Feb-23					◆ OFCI Procure - Generators MPOE/BDF						
381		PROC.PW. OFCI Procure - Network COD 2000AMP	5	5	15-Feb-23	22-Feb-23					◆ OFCI Procure - Network COD 2000AMP						
382		PROC.PW. OFCI Procure - HDP Boards MPOE/BDF	0	0		20-Mar-23					◆ OFCI Procure - HDP Boards MPOE/BDF						
383		PROC.PW. OFCI Procure - COD boards MPOE/BDF	0	0		29-Mar-23					◆ OFCI Procure - COD boards MPOE/BDF						

Remaining Level of Effort Remaining Work ◆ Milestone
 Actual Work Critical Remaining Work Summary

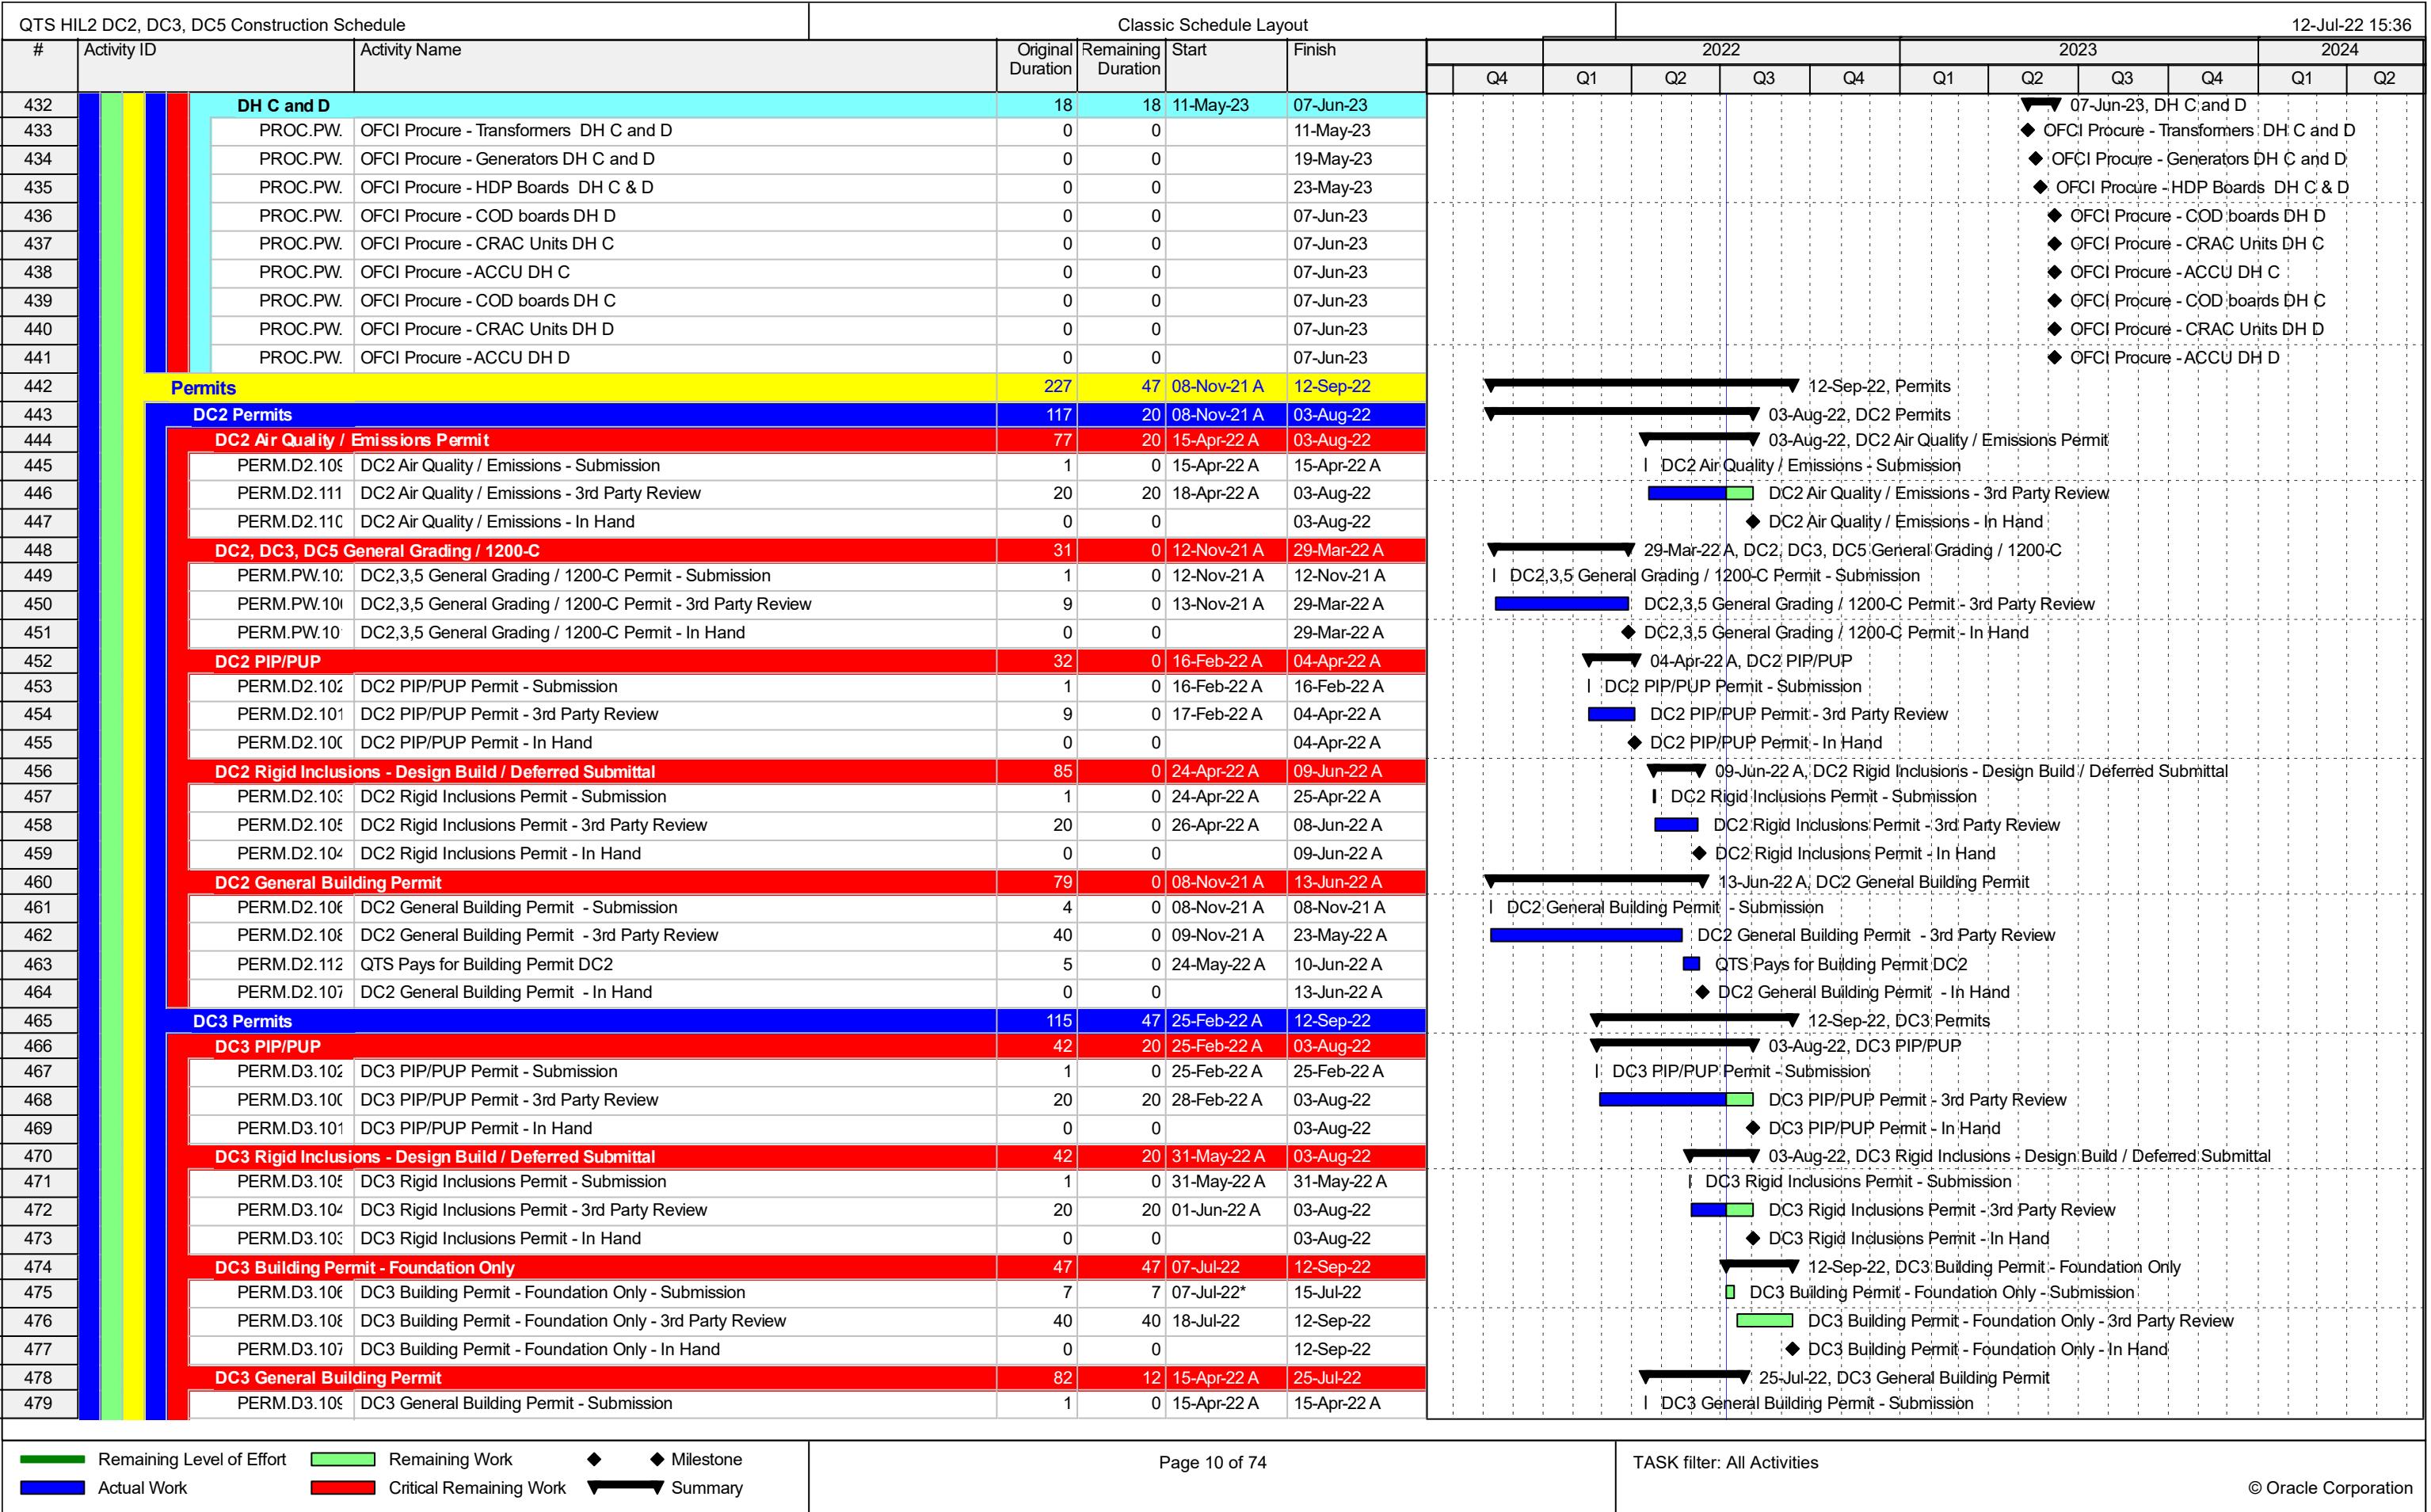

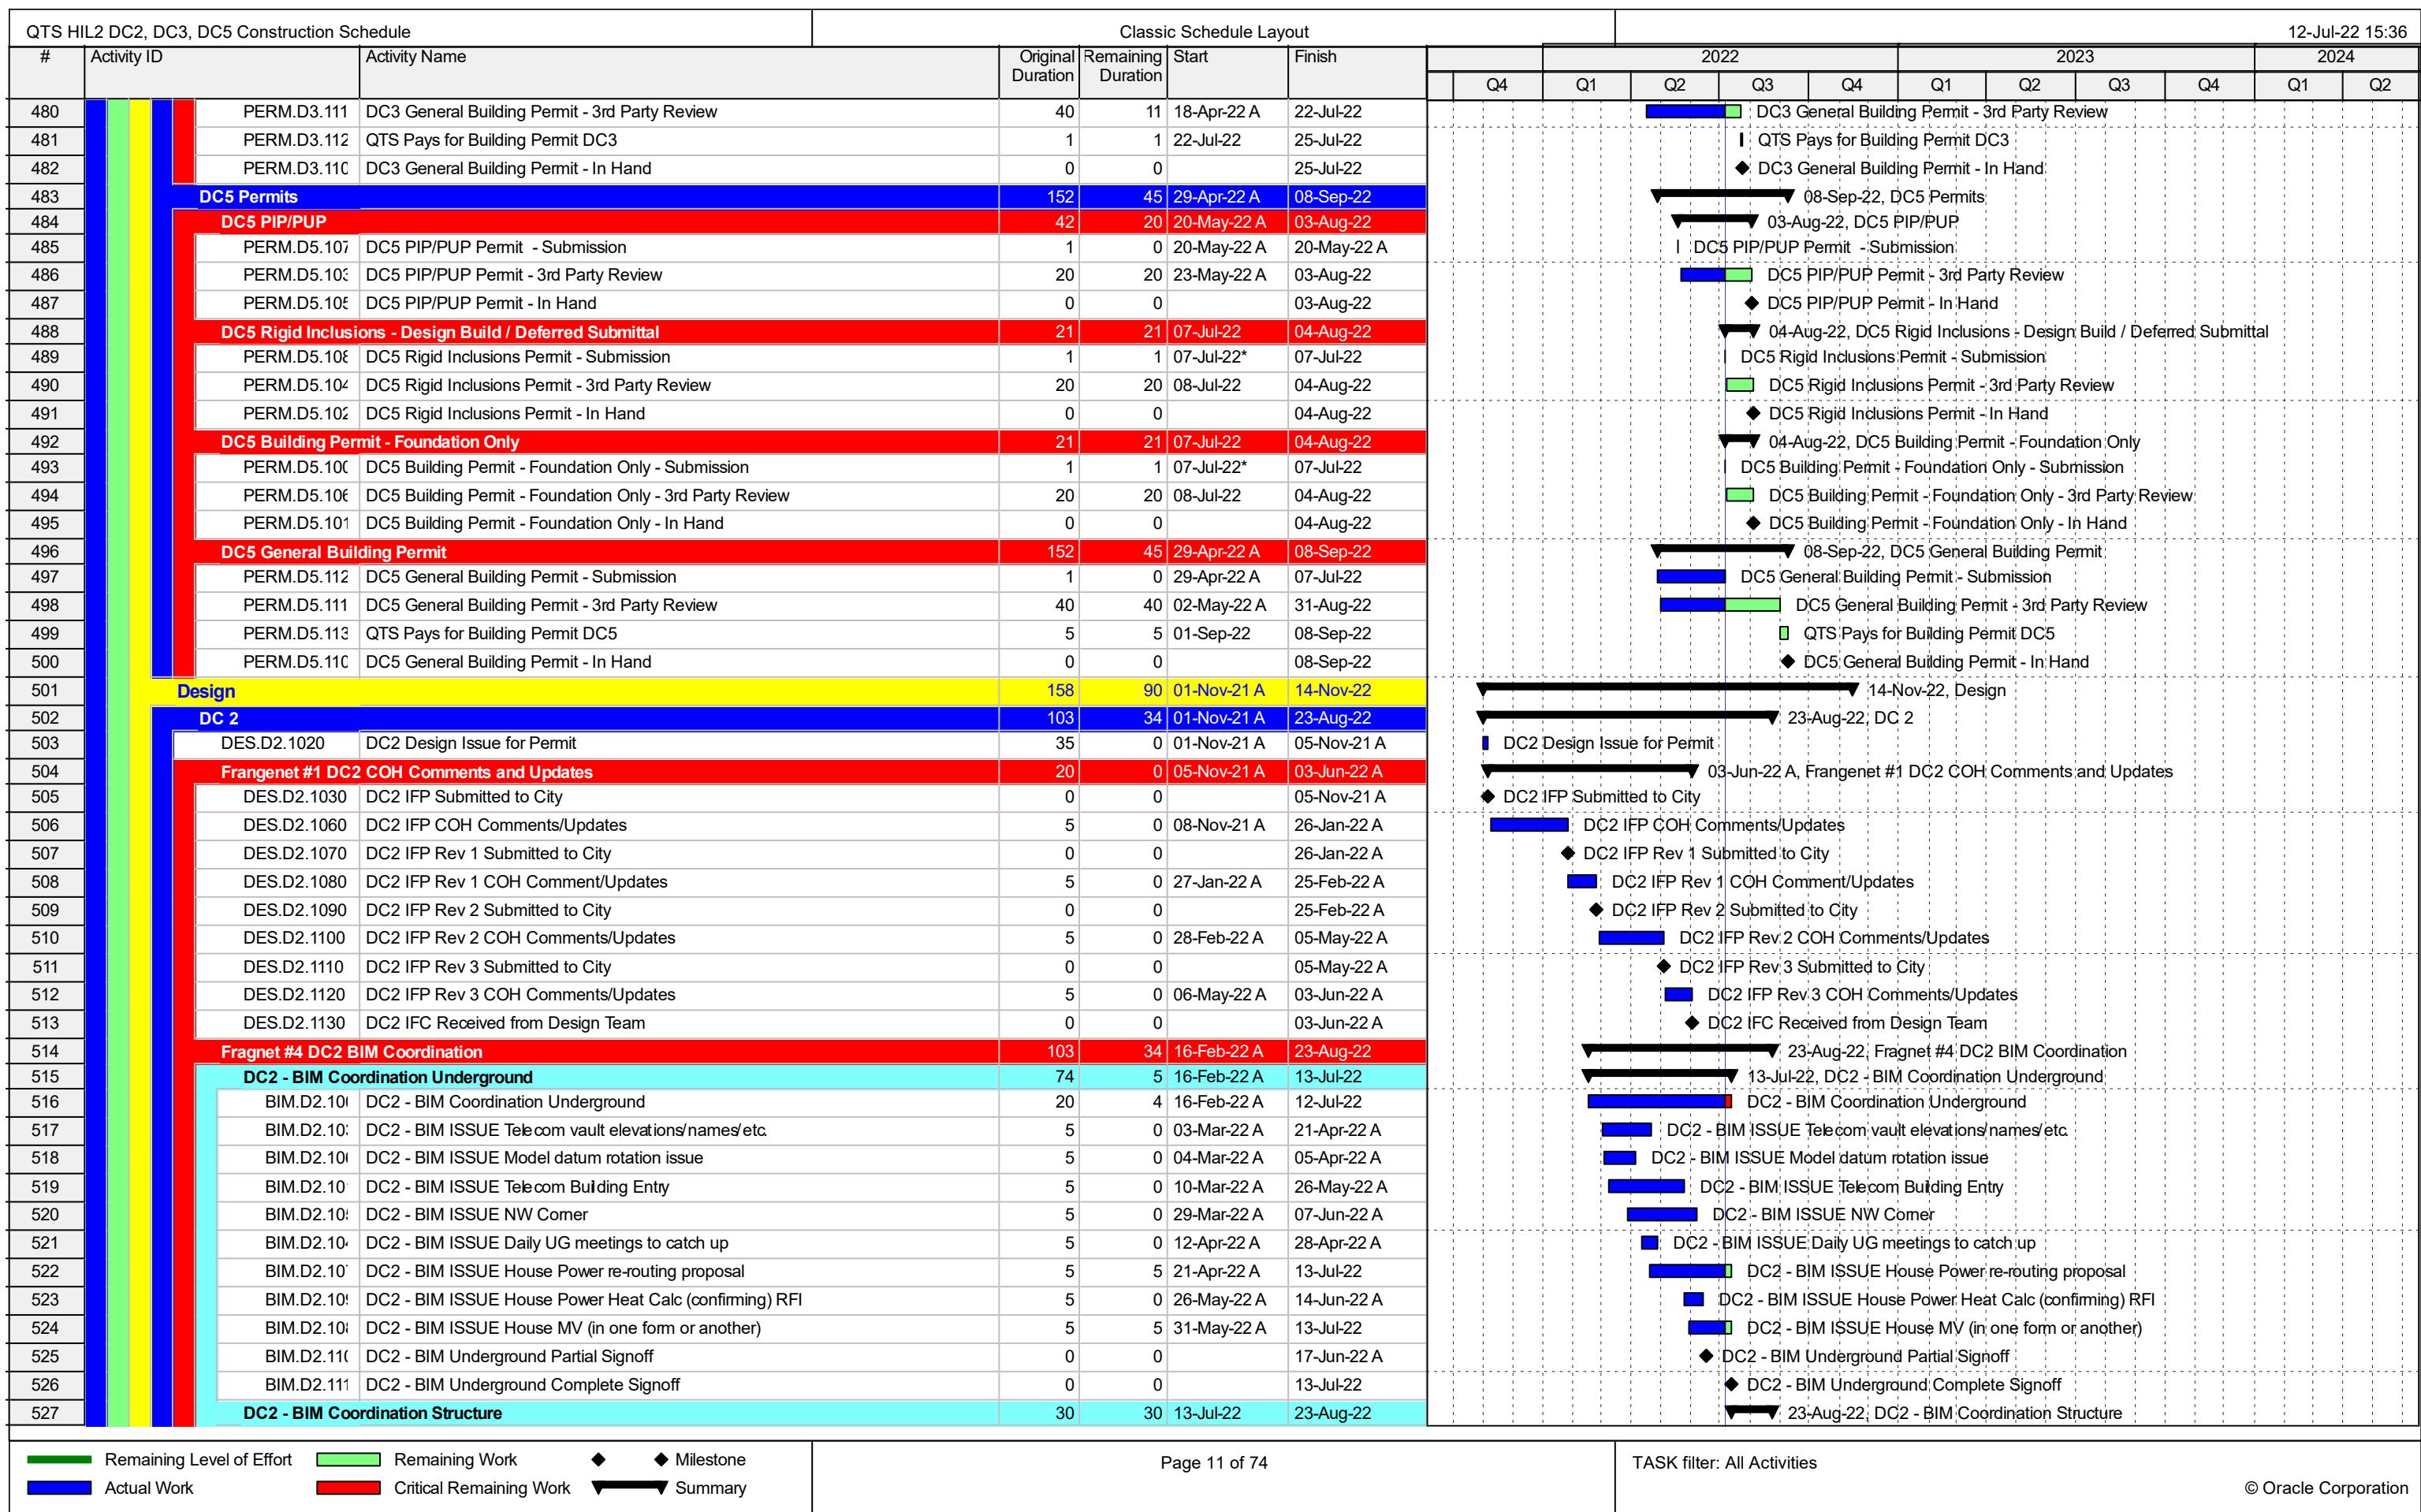

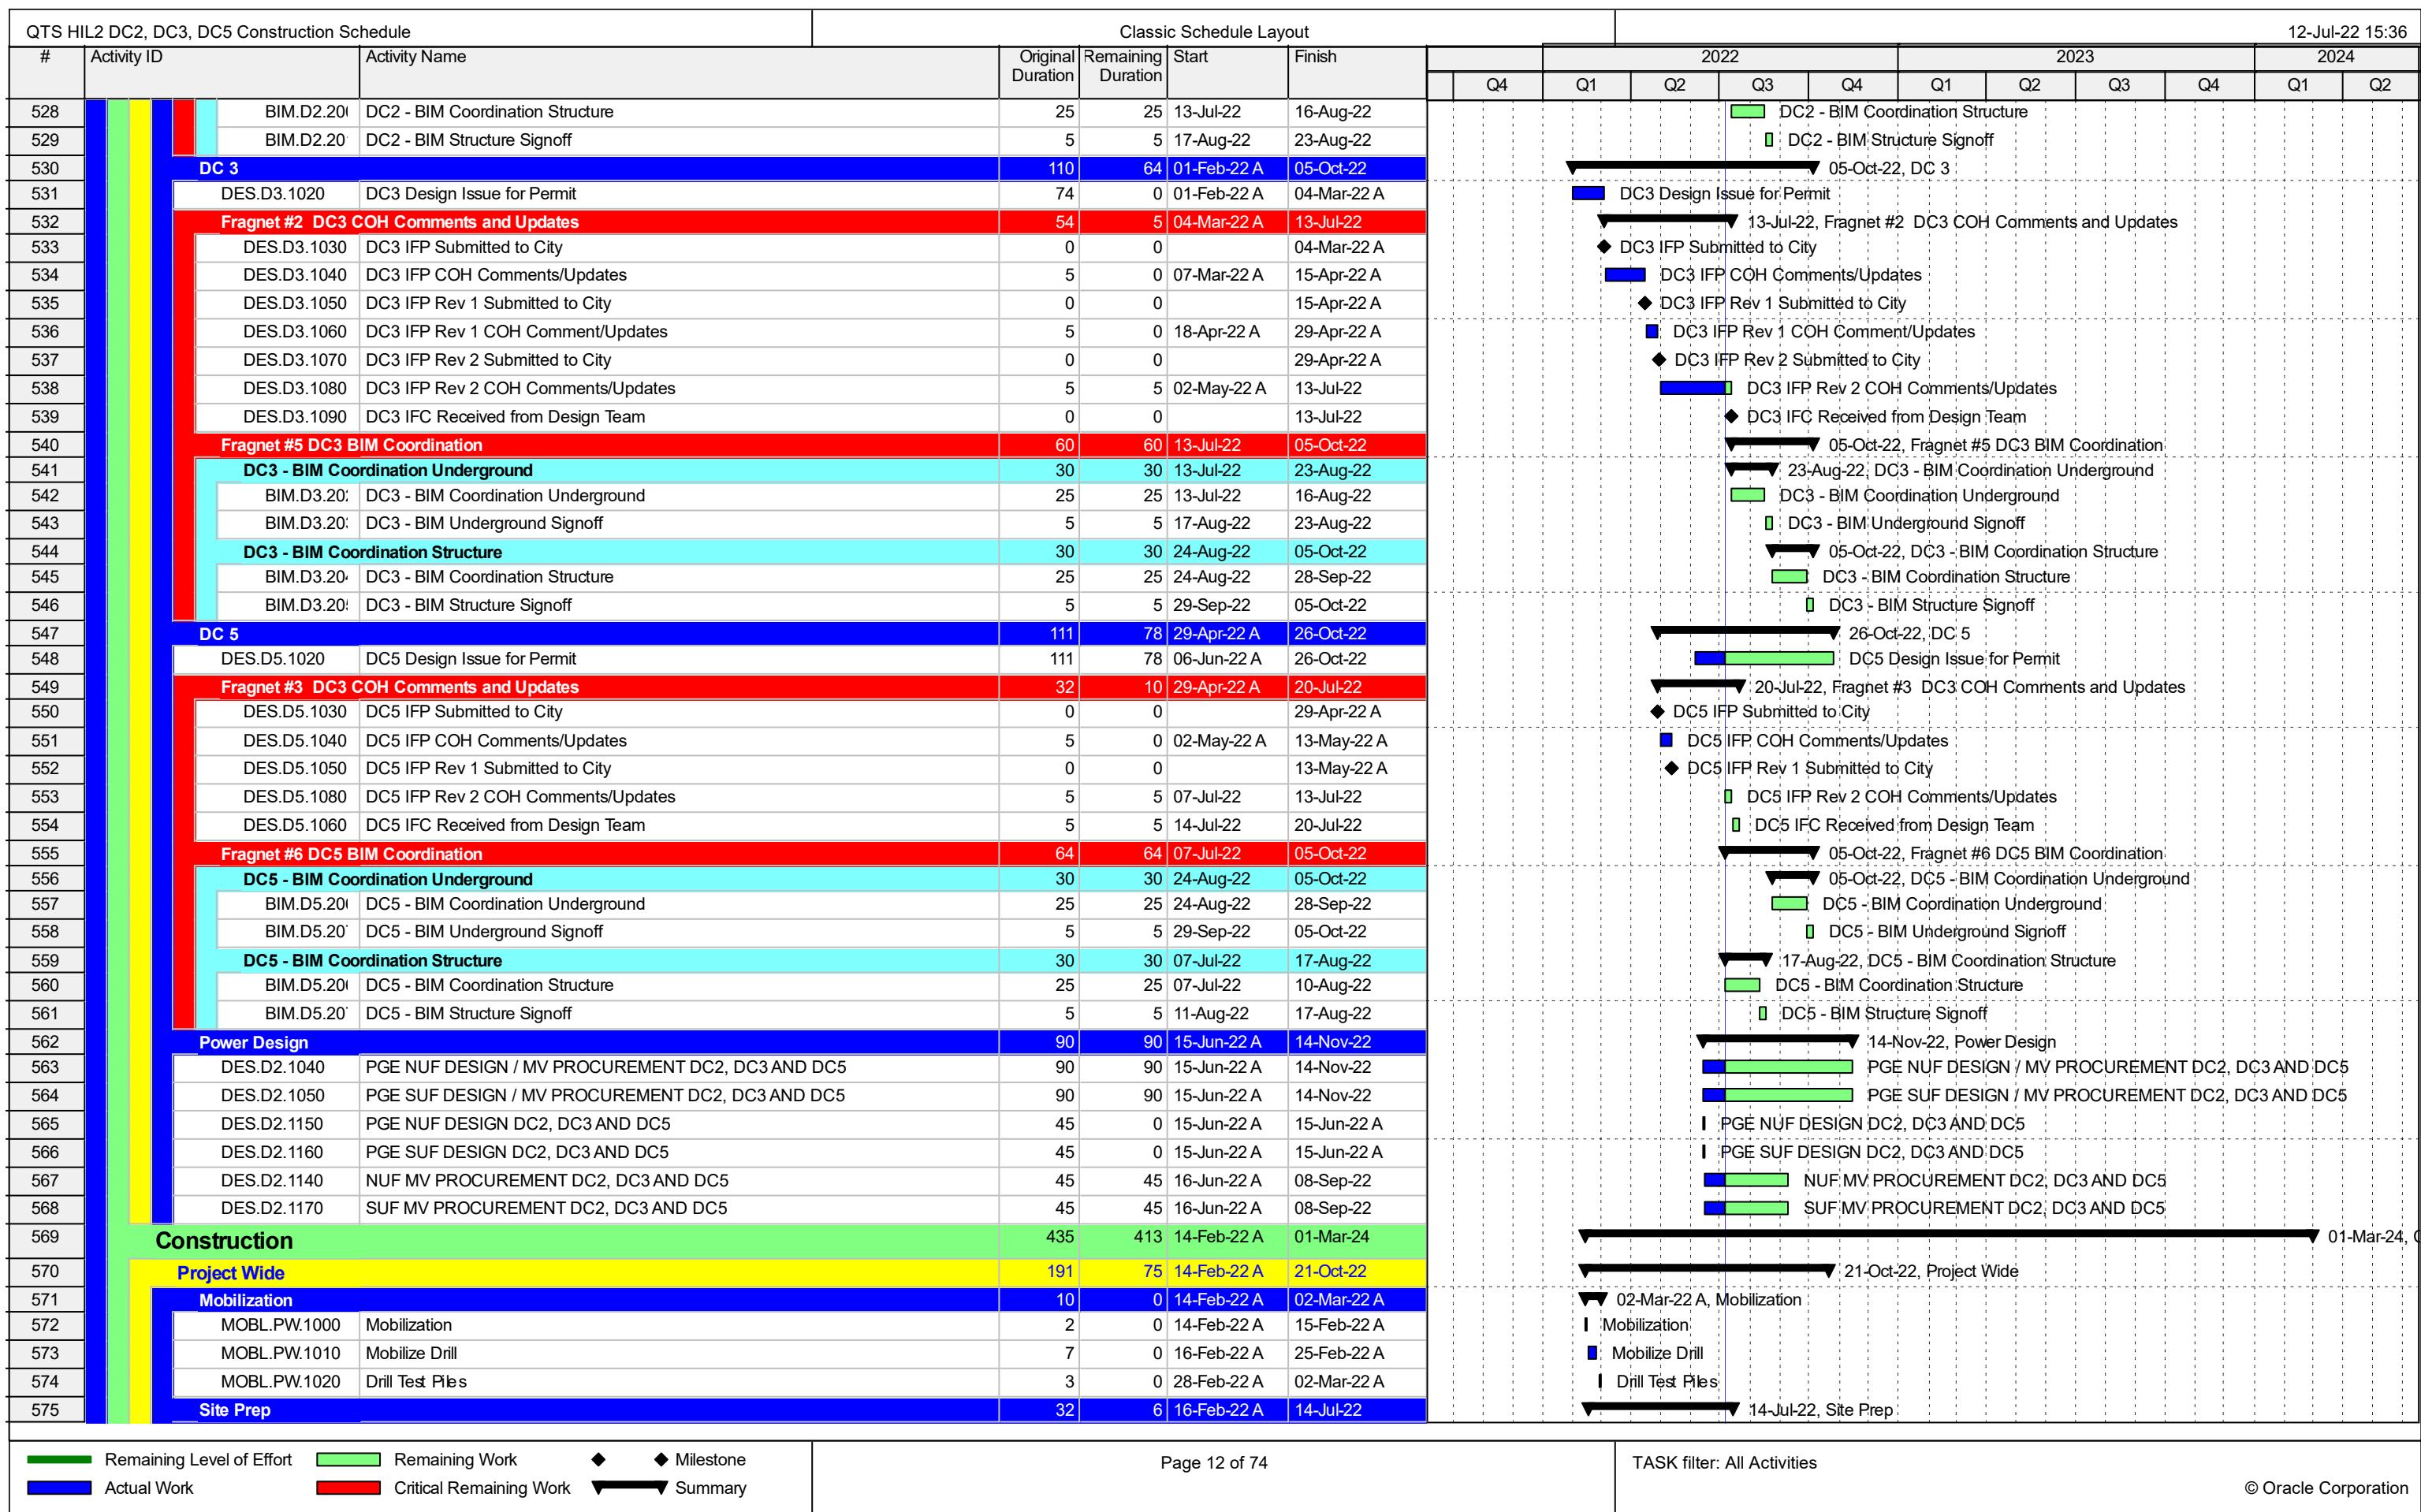

QTS HIL2 DC2, DC3, DC5 Construction Schedule				Classic Schedule Layout					12-Jul-22 15:36										
#	Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish		2022					2023					2024	
					Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2				
576	PREP.PW.1030	Install Tree Protection Fence	1	0	16-Feb-22 A	16-Feb-22 A													
577	PREP.PW.1160	Cut Trees		3	0	21-Feb-22 A	04-Mar-22 A												
578	PREP.PW.1070	Install Construction Entrances		3	0	31-Mar-22 A	02-Apr-22 A												
579	PREP.PW.1080	Install Haul Roads		10	0	31-Mar-22 A	22-Apr-22 A												
580	PREP.PW.1130	Strip and Rock Tailor Park		5	0	31-Mar-22 A	09-Apr-22 A												
581	PREP.PW.1110	Strip Organics to Stockpile		17	3	01-Apr-22 A	11-Jul-22												
582	PREP.PW.1060	Install Security fence		5	0	04-Apr-22 A	07-Apr-22 A												
583	PREP.PW.1100	Tree Removal / Site Clearing		20	0	08-Apr-22 A	28-May-22 A												
584	PREP.PW.1170	Foundation Start		0	0	31-May-22 A													
585	PREP.PW.1120	Install Conduits for Temp Power		5	1	22-Jun-22 A	07-Jul-22												
586	PREP.PW.1140	Strip and Rock Trade Parking		6	6	07-Jul-22	14-Jul-22												
587	PREP.PW.1150	Install walk/Cart Paths		4	4	07-Jul-22	12-Jul-22												
588	Erosion Control			5	0	30-Mar-22 A	01-Apr-22 A												
589	PREP.PW.1040	Install Inlet Protection		1	0	30-Mar-22 A	30-Mar-22 A												
590	PREP.PW.1050	Install Silt Fence		5	0	30-Mar-22 A	01-Apr-22 A												
591	Site Improvements			169	75	21-Apr-22 A	21-Oct-22												
592	Dry Utilities			152	75	14-Jun-22 A	21-Oct-22												
593	Telecommunications			118	38	20-Jun-22 A	02-Sep-22												
594	Excavation			114	36	20-Jun-22 A	31-Aug-22												
595	EXCV.P	Telecom Excavation - TMH-6 TO THM-35		4	0	20-Jun-22 A	21-Jun-22 A												
596	EXCV.P	Telecom Excavation - TMH-7 TO TMH-34		4	0	21-Jun-22 A	22-Jun-22 A												
597	EXCV.P	Telecom Excavation - BUILDING TO BEV-05		4	0	01-Jul-22 A	06-Jul-22 A												
598	EXCV.P	Telecom Excavation - BEV-08 TO BUILDING		4	1	05-Jul-22 A	01-Aug-22												
599	EXCV.P	Telecom Excavation - BUILDING TO BEV-06		4	3	07-Jul-22 A	25-Jul-22												
600	EXCV.P	Telecom Excavation - TMH-7, TMH-34		2	2	13-Jul-22	14-Jul-22												
601	EXCV.P	Telecom Excavation - TMH-34 TO TMH-35		2	2	13-Jul-22	14-Jul-22												
602	EXCV.P	Telecom Excavation - BEV-07,BEV-09		3	3	13-Jul-22	15-Jul-22												
603	EXCV.P	Telecom Excavation - BEV-09 TO BEV-10		3	3	13-Jul-22	15-Jul-22												
604	EXCV.P	Telecom Excavation - BEV-08 TO TMH-14		3	3	13-Jul-22	15-Jul-22												
605	EXCV.P	Telecom Excavation - TMH-17,TMH-14,TMH-15,TMH-16		3	3	13-Jul-22	15-Jul-22												
606	EXCV.P	Telecom Excavation - BEV-10, BEV-08		3	3	14-Jul-22	18-Jul-22												
607	EXCV.P	Telecom Excavation - TMH-32 TO TMH-33		2	2	15-Jul-22	18-Jul-22												
608	EXCV.P	Telecom Excavation - TMH-15 TO MMV-03 existing		3	3	18-Jul-22	20-Jul-22												
609	EXCV.P	Telecom Excavation - TMH-33, TMH-34		2	2	19-Jul-22	20-Jul-22												
610	EXCV.P	Telecom Excavation - TMH-14 TO TMH-08 existing		2	2	21-Jul-22	22-Jul-22												
611	EXCV.P	Telecom Excavation - TMH-15 TO TMH-16		2	2	25-Jul-22	26-Jul-22												
612	EXCV.P	Telecom Excavation - BEV-07 TO BUILDING		4	4	26-Jul-22	29-Jul-22												
613	EXCV.P	Telecom Excavation - TMH-17 TO TMH-16		2	2	27-Jul-22	28-Jul-22												
614	EXCV.P	Telecom Excavation - TMH-14 TO TMH-15		2	2	29-Jul-22	01-Aug-22												
615	EXCV.P	Telecom Excavation - BEV-09 TO TMH-33		3	3	02-Aug-22	04-Aug-22												
616	EXCV.P	Telecom Excavation - TMH-17 TO TMH-14		2	2	02-Aug-22	03-Aug-22												
617	EXCV.P	Telecom Excavation - BEV-07 TO TMH-34		3	3	05-Aug-22	09-Aug-22												
618	EXCV.P	Telecom Excavation - BEV-10 TO TMH-17		3	3	10-Aug-22	12-Aug-22												
619	EXCV.P	Telecom Excavation - BEV-112 TO BUILDING		2	2	15-Aug-22	16-Aug-22												
620	EXCV.P	Telecom Excavation - BEV-112		2	2	16-Aug-22	17-Aug-22												
621	EXCV.P	Telecom Excavation - BEV-112 TO Future		2	2	18-Aug-22	19-Aug-22												
622	EXCV.P	Telecom Excavation - BEV-112 TO TMH-120		2	2	19-Aug-22	22-Aug-22												

Remaining Level of Effort Remaining Work Milestone
 Actual Work Critical Remaining Work Summary


QTS HIL2 DC2, DC3, DC5 Construction Schedule				Classic Schedule Layout					12-Jul-22 15:36									
#	Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish		2022				2023				2024		
					Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2			
718		UTIL.PW.11 Install Sanitary - Public Underground	6	6	15-Aug-22*	22-Aug-22												
719		Fresh Water Utilities		20	20	18-Jul-22	12-Aug-22											
720		UTIL.PW.11 Fire - Private Underground		13	13	18-Jul-22	03-Aug-22											
721		UTIL.PW.11 Fire - Public Underground		3	3	04-Aug-22	08-Aug-22											
722		UTIL.PW.11 Domestic - Public Underground		1	1	09-Aug-22	09-Aug-22											
723		UTIL.PW.11 Domestic - Private Underground		3	3	10-Aug-22	12-Aug-22											
724		DC2	284	274	14-Apr-22 A	08-Aug-23												08-Aug-23, DC2
725		DC2 Milestones		0	0	15-Feb-23	15-Feb-23											15-Feb-23, DC2 Milestones
726	MILE.D2.1000	Substantially Weathertight		0	0		15-Feb-23											Substantially Weathertight
727		Earthwork	44	6	14-Apr-22 A	14-Jul-22												14-Jul-22, Earthwork
728		Site Development		32	6	14-Apr-22 A	14-Jul-22											14-Jul-22, Site Development
729	SITE.D2.1020	Place Imported Fill Materials		26	0	14-Apr-22 A	16-May-22 A											Place Imported Fill Materials
730	SITE.D2.1080	Fragnet ## DC2 Over Excavation of Organic Soil and Additional Fills		27	0	21-Apr-22 A	27-May-22 A											Fragnet ## DC2 Over Excavation of Organic Soil and Additional Fills
731	SITE.D2.1000	Earthwork Onsite Cut to Fill		6	0	25-Apr-22 A	03-May-22 A											Earthwork Onsite Cut to Fill
732	SITE.D2.1010	Earthwork Onsite CTS Site Fills		4	0	28-Apr-22 A	31-May-22 A											Earthwork Onsite CTS Site Fills
733	SITE.D2.1030	Place Surcharge		6	0	16-May-22 A	06-Jun-22 A											Place Surcharge
734	SITE.D2.1040	Surcharge Waiting Period		30	6	18-May-22 A	14-Jul-22											Surcharge Waiting Period
735	SITE.D2.1050	DC2 Surcharge Waiting Period zone1		10	0	18-May-22 A	27-Jun-22 A											DC2 Surcharge Waiting Perbd zone1
736	SITE.D2.1060	DC2 Surcharge Waiting Period Zone 2		10	6	25-May-22 A	14-Jul-22											DC2 Surcharge Waiting Perbd Zone 2
737	SITE.D2.1070	DC2 Surcharge Waiting Period Zone 3		10	4	04-Jun-22 A	12-Jul-22											DC2 Surcharge Waiting Perbd Zone 3
738		Rigid Inclusions	37	0	29-Apr-22 A	22-Jun-22 A												22-Jun-22 A, Rigid Inclusions
739	RIGD.D2.1020	Drill / Pour RI-CL L2 to CL Q		10	0	29-Apr-22 A	07-Jun-22 A											Drill / Pour RI-CL L2 to CL Q
740	RIGD.D2.1010	Drill / Pour RI-CL C to CL L.2		10	0	03-May-22 A	03-Jun-22 A											Drill / Pour RI-CL C to CL L.2
741	RIGD.D2.1000	Drill / Pour RI-CL A to C		7	0	11-May-22 A	19-May-22 A											Drill / Pour RI-CL A to C
742	RIGD.D2.1030	Drill / Pour RI-CL Q to CL Z		10	0	06-Jun-22 A	22-Jun-22 A											Drill / Pour RI-CL Q to CL Z
743		Foundation	119	111	28-May-22 A	15-Dec-22												15-Dec-22, Foundation
744		Building Pad Prep		27	27	07-Jul-22	12-Aug-22											12-Aug-22, Building Pad Prep
745		Area Wide		21	21	15-Jul-22	12-Aug-22											12-Aug-22, Area Wide
746	FOND.D2.1	Move Surcharge to DC3		5	5	15-Jul-22	21-Jul-22											Move Surcharge to DC3
747	FOND.D2.1	Compact Subgrade And Place Stone		5	5	08-Aug-22	12-Aug-22											Compact Subgrade And Place Stone
748		Grid A - C		11	11	07-Jul-22	21-Jul-22											21-Jul-22, Grid A - C
749	UTIL.D2.1C	Under-slab Utilities CL A to C		14	5	25-JUL-22	5-AUG-22											Under-slab Utilities CL A to C
750	UTIL.D2.1C	Deep Underground Utilities		10	10	08-Jul-22	21-Jul-22											Deep Underground Utilities
751	FOND.D2.1	Backfill/Compact CL A to C		5	5	14-Jul-22	20-Jul-22											Backfill/Compact CL A to C
752		Grid C - L		10	10	14-Jul-22	27-Jul-22											27-Jul-22, Grid C - L
753	UTIL.D2.1C	Under-slab Utilities CL C to L2	After Line 929 FS	14	5	12-SEP-22	20-Jul-22											Under-slab Utilities CL C to L2
754	FOND.D2.1	Backfill/Compact CL C to L2		5	5	21-Jul-22	27-Jul-22											Backfill/Compact CL C to L2
755		Grid L - Q.1		10	10	21-Jul-22	03-Aug-22											03-Aug-22, Grid L - Q.1
756	UTIL.D2.1C	Under-slab Utilities CL L.2 to Q	After Line 786 FS	12	5	8-AUG-22	15-AUG-22											Under-slab Utilities CL L.2 to Q
757	FOND.D2.1	Backfill/Compact CL L.2 to Q		5	5	28-Jul-22	03-Aug-22											Backfill/Compact CL L.2 to Q
758		Grid Q.1 - Z		10	10	28-Jul-22	10-Aug-22											10-Aug-22, Grid Q.1 - Z
759	UTIL.D2.1C	Under-slab Utilities CL Q to Z	After Line 940 FS	20	5	18-OCT-22	03-Aug-22											Under-slab Utilities CL Q to Z
760	FOND.D2.1	Backfill/Compact CL Q to Z		5	5	04-Aug-22	10-Aug-22											Backfill/Compact CL Q to Z
761		DC2 Foundations		41	33	28-May-22 A	22-Aug-22											22-Aug-22, DC2 Foundations
762		Grid A-C		18	11	28-May-22 A	21-Jul-22											21-Jul-22, Grid A-C
763	FOND.D2.1	Found A-C - Survey Footing Excavation		1	0	28-May-22 A	30-May-22 A											Found A-C - Survey Footing Excavation
764	FOND.D2.1	Found A-C - Dig Footings		3	0	31-May-22 A	07-Jun-22 A											Found A-C - Dig Footings
765	FOND.D2.1	Found A-C - Form Foundations (#1 Formwork Delivery)		5	0	08-Jun-22 A	22-Jun-22 A											Found A-C - Form Foundations (#1 Formwork Delivery)

QTS HIL2 DC2, DC3, DC5 Construction Schedule				Classic Schedule Layout					12-Jul-22 15:36										
#	Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish		2022					2023					2024	
								Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	
766	FOND.D2.1	Found A-C - Survey Formwork	1	0	08-Jun-22 A	22-Jun-22 A													
767	FOND.D2.1	Found A-C - Install Anchor Bolts		5	0	13-Jun-22 A	29-Jun-22 A												
768	FOND.D2.1	Found A-C - Install Reinforcement		5	0	14-Jun-22 A	29-Jun-22 A												
769	FOND.D2.1	Found A-C - Place Foundations		1	0	23-Jun-22 A	30-Jun-22 A												
770	FOND.D2.1	Found A-C - Strip Foundations		4	1	24-Jun-22 A	07-Jul-22												
771	FOND.D2.1	Found A-C - Install Elevator Pit		5	5	07-Jul-22	13-Jul-22												
772	FOND.D2.1	Found A-C - Plinths and Grade Beams		5	5	07-Jul-22	13-Jul-22												
773	FOND.D2.1	Found A-C - Waterproof/Insulate		3	3	14-Jul-22	18-Jul-22												
774	FOND.D2.1	Found A-C - Backfill Foundations		3	3	19-Jul-22	21-Jul-22												
775	Grid C-L			30	22	24-Jun-22 A	05-Aug-22												
776	FOND.D2.1	Found C-L - Survey Footing Excavation		1	0	24-Jun-22 A	07-Jul-22												
777	FOND.D2.1	Found C-L - Dig Footings		1	0	24-Jun-22 A	07-Jul-22												
778	FOND.D2.1	Found C-L - Form Foundations (#2 Formwork Delivery)		6	2	06-Jul-22 A	08-Jul-22												
779	FOND.D2.1	Found C-L - Install Reinforcement		6	5	06-Jul-22 A	13-Jul-22												
780	FOND.D2.1	Found C-L - Survey Formwork		1	1	06-Jul-22 A	07-Jul-22												
781	FOND.D2.1	Found C-L - Install Anchor Bolts		6	6	07-Jul-22	14-Jul-22												
782	FOND.D2.1	Found C-L - Place Foundations		2	2	15-Jul-22	18-Jul-22												
783	FOND.D2.1	Found C-L - Strip Foundations		6	6	19-Jul-22	26-Jul-22												
784	FOND.D2.1	Found C-L - Plinths and Grade Beams		6	6	19-Jul-22	26-Jul-22												
785	FOND.D2.1	Found C-L - Waterproof/Insulate		3	3	27-Jul-22	29-Jul-22												
786	FOND.D2.1	Found C-L - Backfill Foundations		5	5	01-Aug-22	05-Aug-22												
787	Grid L-Q.1			21	21	15-Jul-22	12-Aug-22												
788	FOND.D2.1	Found L-Q.1 - Survey Footing Excavation		1	1	15-Jul-22	15-Jul-22												
789	FOND.D2.1	Found L-Q.1 - Dig Footings		3	3	18-Jul-22	20-Jul-22												
790	FOND.D2.1	Found L-Q.1 - Survey Formwork		1	1	21-Jul-22	21-Jul-22												
791	FOND.D2.1	Found L-Q.1 - Form Foundations (Formwork From A-C)		6	6	22-Jul-22	29-Jul-22												
792	FOND.D2.1	Found L-Q.1 - Install Anchor Bolts		5	5	22-Jul-22	28-Jul-22												
793	FOND.D2.1	Found L-Q.1 - Install Reinforcement		5	5	25-Jul-22	29-Jul-22												
794	FOND.D2.1	Found L-Q.1 - Place Foundations		1	1	01-Aug-22	01-Aug-22												
795	FOND.D2.1	Found L-Q.1 - Strip Foundations		3	3	02-Aug-22	04-Aug-22												
796	FOND.D2.1	Found L-Q.1 - Plinths and Grade Beams		5	5	02-Aug-22	08-Aug-22												
797	FOND.D2.1	Found L-Q.1 - Waterproof/Insulate		3	3	05-Aug-22	09-Aug-22												
798	FOND.D2.1	Found L-Q.1 - Backfill Foundations		3	3	10-Aug-22	12-Aug-22												
799	Grid Q.1-Z			29	29	13-Jul-22	22-Aug-22												
800	FOND.D2.1	Grid Q.1-Z - Survey Footing Excavation		1	1	13-Jul-22	13-Jul-22												
801	FOND.D2.1	Grid Q.1-Z - Dig Footings		3	3	22-Jul-22	26-Jul-22												
802	FOND.D2.1	Grid Q.1-Z - Survey Formwork		1	1	27-Jul-22	27-Jul-22												
803	FOND.D2.1	Grid Q.1-Z - Form Foundations (Formwork From C-L)		6	6	01-Aug-22	08-Aug-22												
804	FOND.D2.1	Grid Q.1-Z - Install Anchor Bolts		5	5	01-Aug-22	05-Aug-22												
805	FOND.D2.1	Grid Q.1-Z - Install Reinforcement		5	5	02-Aug-22	08-Aug-22												
806	FOND.D2.1	Grid Q.1-Z - Place Foundations		1	1	09-Aug-22	09-Aug-22												
807	FOND.D2.1	Grid Q.1-Z - Strip Foundations		3	3	10-Aug-22	12-Aug-22												
808	FOND.D2.1	Grid Q.1-Z - Plinths and Grade Beams		5	5	10-Aug-22	16-Aug-22												
809	FOND.D2.1	Grid Q.1-Z - Waterproof/Insulate		3	3	15-Aug-22	17-Aug-22												
810	FOND.D2.1	Grid Q.1-Z - Backfill Foundations		3	3	18-Aug-22	22-Aug-22												
811	DC2 Slab On Grade			100	100	22-Jul-22	15-Dec-22												
812	Grid A-C			50	50	22-Jul-22	30-Sep-22												
813	Pour 1			50	50	22-Jul-22	30-Sep-22												

Remaining Level of Effort Remaining Work Milestone Critical Remaining Work Summary

QTS HIL2 DC2, DC3, DC5 Construction Schedule				Classic Schedule Layout					12-Jul-22 15:36									
#	Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish		Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2
862	SOG.D2	SOG Q.1-Z P6 - Place SOG	1	1	08-Dec-22	08-Dec-22							I	SOG Q.1-Z P6 - Place SOG				
863	SOG.D2	SOG Q.1-Z P6 - Cure SOG		5	5	09-Dec-22	15-Dec-22						I	SOG Q.1-Z P6 - Cure SOG				
864	DC2 SOMD			66	66	29-Aug-22	05-Dec-22						▼	05-Dec-22, DC2 SOMD				
865	A-Z			66	66	29-Aug-22	05-Dec-22						▼	05-Dec-22, A-Z				
866	Grid A - C			9	9	29-Aug-22	09-Sep-22						▼	09-Sep-22, Grid A - C				
867	Pour 1 A - C			9	9	29-Aug-22	09-Sep-22						▼	09-Sep-22, Pour 1 A - C				
868	SOM	SOMD A-C P1 - As-Built Structure	1	1	29-Aug-22	29-Aug-22							I	SOMD A-C P1 - As-Built Structure				
869	SOM	SOMD A-C P1 - MEP		3	3	30-Aug-22	01-Sep-22						I	SOMD A-C P1 - MEP				
870	SOM	SOMD A-C P1 - Edgeforms/Embeds		3	3	30-Aug-22	01-Sep-22						I	SOMD A-C P1 - Edgeforms/Embeds				
871	SOM	SOMD A-C P1 - Install Reinforcement		3	3	02-Sep-22	07-Sep-22						I	SOMD A-C P1 - Install Reinforcement				
872	SOM	SOMD A-C P1 - MEP Final		1	1	08-Sep-22	08-Sep-22						I	SOMD A-C P1 - MEP Final				
873	SOM	SOMD A-C P1 - Place Slab		1	1	09-Sep-22	09-Sep-22						I	SOMD A-C P1 - Place Slab				
874	Grid C - L			21	21	02-Sep-22	03-Oct-22						▼	03-Oct-22, Grid C - L				
875	Pour 2 C - F.4			9	9	02-Sep-22	15-Sep-22						▼	15-Sep-22, Pour 2 C - F.4				
876	SOM	SOMD C-F.4 P2 - MEP		2	2	02-Sep-22	06-Sep-22						I	SOMD C-F.4 P2 - MEP				
877	SOM	SOMD C-F.4 P2 - Edgeforms/Embeds		2	2	07-Sep-22	08-Sep-22						I	SOMD C-F.4 P2 - Edgeforms/Embeds				
878	SOM	SOMD C-F.4 P2 - Install Reinforcement		3	3	09-Sep-22	13-Sep-22						I	SOMD C-F.4 P2 - Install Reinforcement				
879	SOM	SOMD C-F.4 P2 - MEP Final		1	1	14-Sep-22	14-Sep-22						I	SOMD C-F.4 P2 - MEP Final				
880	SOM	SOMD C-F.4 P2 - Place Slab		1	1	15-Sep-22	15-Sep-22						I	SOMD C-F.4 P2 - Place Slab				
881	Pour 3 F.4 - J.8			8	8	09-Sep-22	20-Sep-22						▼	20-Sep-22, Pour 3 F.4 - J.8				
882	SOM	SOMD F.4-J.8 P3 - Edgeforms/Embeds		2	2	09-Sep-22	12-Sep-22						I	SOMD F.4-J.8 P3 - Edgeforms/Embeds				
883	SOM	SOMD F.4-J.8 P3 - Install Reinforcement		3	3	14-Sep-22	16-Sep-22						I	SOMD F.4-J.8 P3 - Install Reinforcement				
884	SOM	SOMD F.4-J.8 P3 - MEP		2	2	19-Sep-22	20-Sep-22						I	SOMD F.4-J.8 P3 - MEP				
885	SOM	SOMD F.4-J.8 P3 - MEP Final		1	1	19-Sep-22	19-Sep-22						I	SOMD F.4-J.8 P3 - MEP Final				
886	SOM	SOMD F.4-J.8 P3 - Place Slab		1	1	20-Sep-22	20-Sep-22						I	SOMD F.4-J.8 P3 - Place Slab				
887	Pour 4 J.8 - M.5			7	7	23-Sep-22	03-Oct-22						▼	03-Oct-22, Pour 4 J.8 - M.5				
888	SOM	SOMD J.8-M.5 P4 - MEP		2	2	23-Sep-22	26-Sep-22						I	SOMD J.8-M.5 P4 - MEP				
889	SOM	SOMD J.8-M.5 P4 - Edgeforms/Embeds		2	2	23-Sep-22	26-Sep-22						I	SOMD J.8-M.5 P4 - Edgeforms/Embeds				
890	SOM	SOMD J.8-M.5 P4 - Install Reinforcement		3	3	27-Sep-22	29-Sep-22						I	SOMD J.8-M.5 P4 - Install Reinforcement				
891	SOM	SOMD J.8-M.5 P4 - MEP Final		1	1	30-Sep-22	30-Sep-22						I	SOMD J.8-M.5 P4 - MEP Final				
892	SOM	SOMD J.8-M.5 P4 - Place Slab		1	1	03-Oct-22	03-Oct-22						I	SOMD J.8-M.5 P4 - Place Slab				
893	Grid L - Q.1			7	7	03-Oct-22	12-Oct-22						▼	12-Oct-22, Grid L - Q.1				
894	Pour 5 M.5 - Q			7	7	03-Oct-22	12-Oct-22						▼	12-Oct-22, Pour 5 M.5 - Q				
895	SOM	SOMD M.5-Q P5 - MEP		2	2	03-Oct-22	04-Oct-22						I	SOMD M.5-Q P5 - MEP				
896	SOM	SOMD M.5-Q P5 - Edgeforms/Embeds		2	2	03-Oct-22	04-Oct-22						I	SOMD M.5-Q P5 - Edgeforms/Embeds				
897	SOM	SOMD M.5-Q P5 - Install Reinforcement		3	3	05-Oct-22	07-Oct-22						I	SOMD M.5-Q P5 - Install Reinforcement				
898	SOM	SOMD M.5-Q P5 - MEP Final		1	1	11-Oct-22	11-Oct-22						I	SOMD M.5-Q P5 - MEP Final				
899	SOM	SOMD M.5-Q P5 - Place Slab		1	1	12-Oct-22	12-Oct-22						I	SOMD M.5-Q P5 - Place Slab				
900	Grid Q.1 - Z			34	34	14-Oct-22	05-Dec-22						▼	05-Dec-22, Grid Q.1 - Z				
901	Pour 6 Q - T.3			8	8	14-Oct-22	25-Oct-22						▼	25-Oct-22, Pour 6 Q - T.3				
902	SOM	SOMD Q-T.3 P6 - As-Built Structure		1	1	14-Oct-22	14-Oct-22						I	SOMD Q-T.3 P6 - As-Built Structure				
903	SOM	SOMD Q-T.3 P6 - MEP		2	2	17-Oct-22	18-Oct-22						I	SOMD Q-T.3 P6 - MEP				
904	SOM	SOMD Q-T.3 P6 - Edgeforms/Embeds		2	2	17-Oct-22	18-Oct-22						I	SOMD Q-T.3 P6 - Edgeforms/Embeds				
905	SOM	SOMD Q-T.3 P6 - Install Reinforcement		3	3	19-Oct-22	21-Oct-22						I	SOMD Q-T.3 P6 - Install Reinforcement				
906	SOM	SOMD Q-T.3 P6 - MEP Final		1	1	24-Oct-22	24-Oct-22						I	SOMD Q-T.3 P6 - MEP Final				
907	SOM	SOMD Q-T.3 P6 - Place Slab		1	1	25-Oct-22	25-Oct-22						I	SOMD Q-T.3 P6 - Place Slab				
908	Pour 7 T.3 - W.3			20	20	19-Oct-22	16-Nov-22						▼	16-Nov-22, Pour 7 T.3 - W.3				
909	SOM	SOMD T.3-W.3 P7 - MEP		2	2	19-Oct-22	20-Oct-22						I	SOMD T.3-W.3 P7 - MEP				

█ Remaining Level of Effort █ Remaining Work ◆ Milestone
█ Actual Work █ Critical Remaining Work ▼ Summary

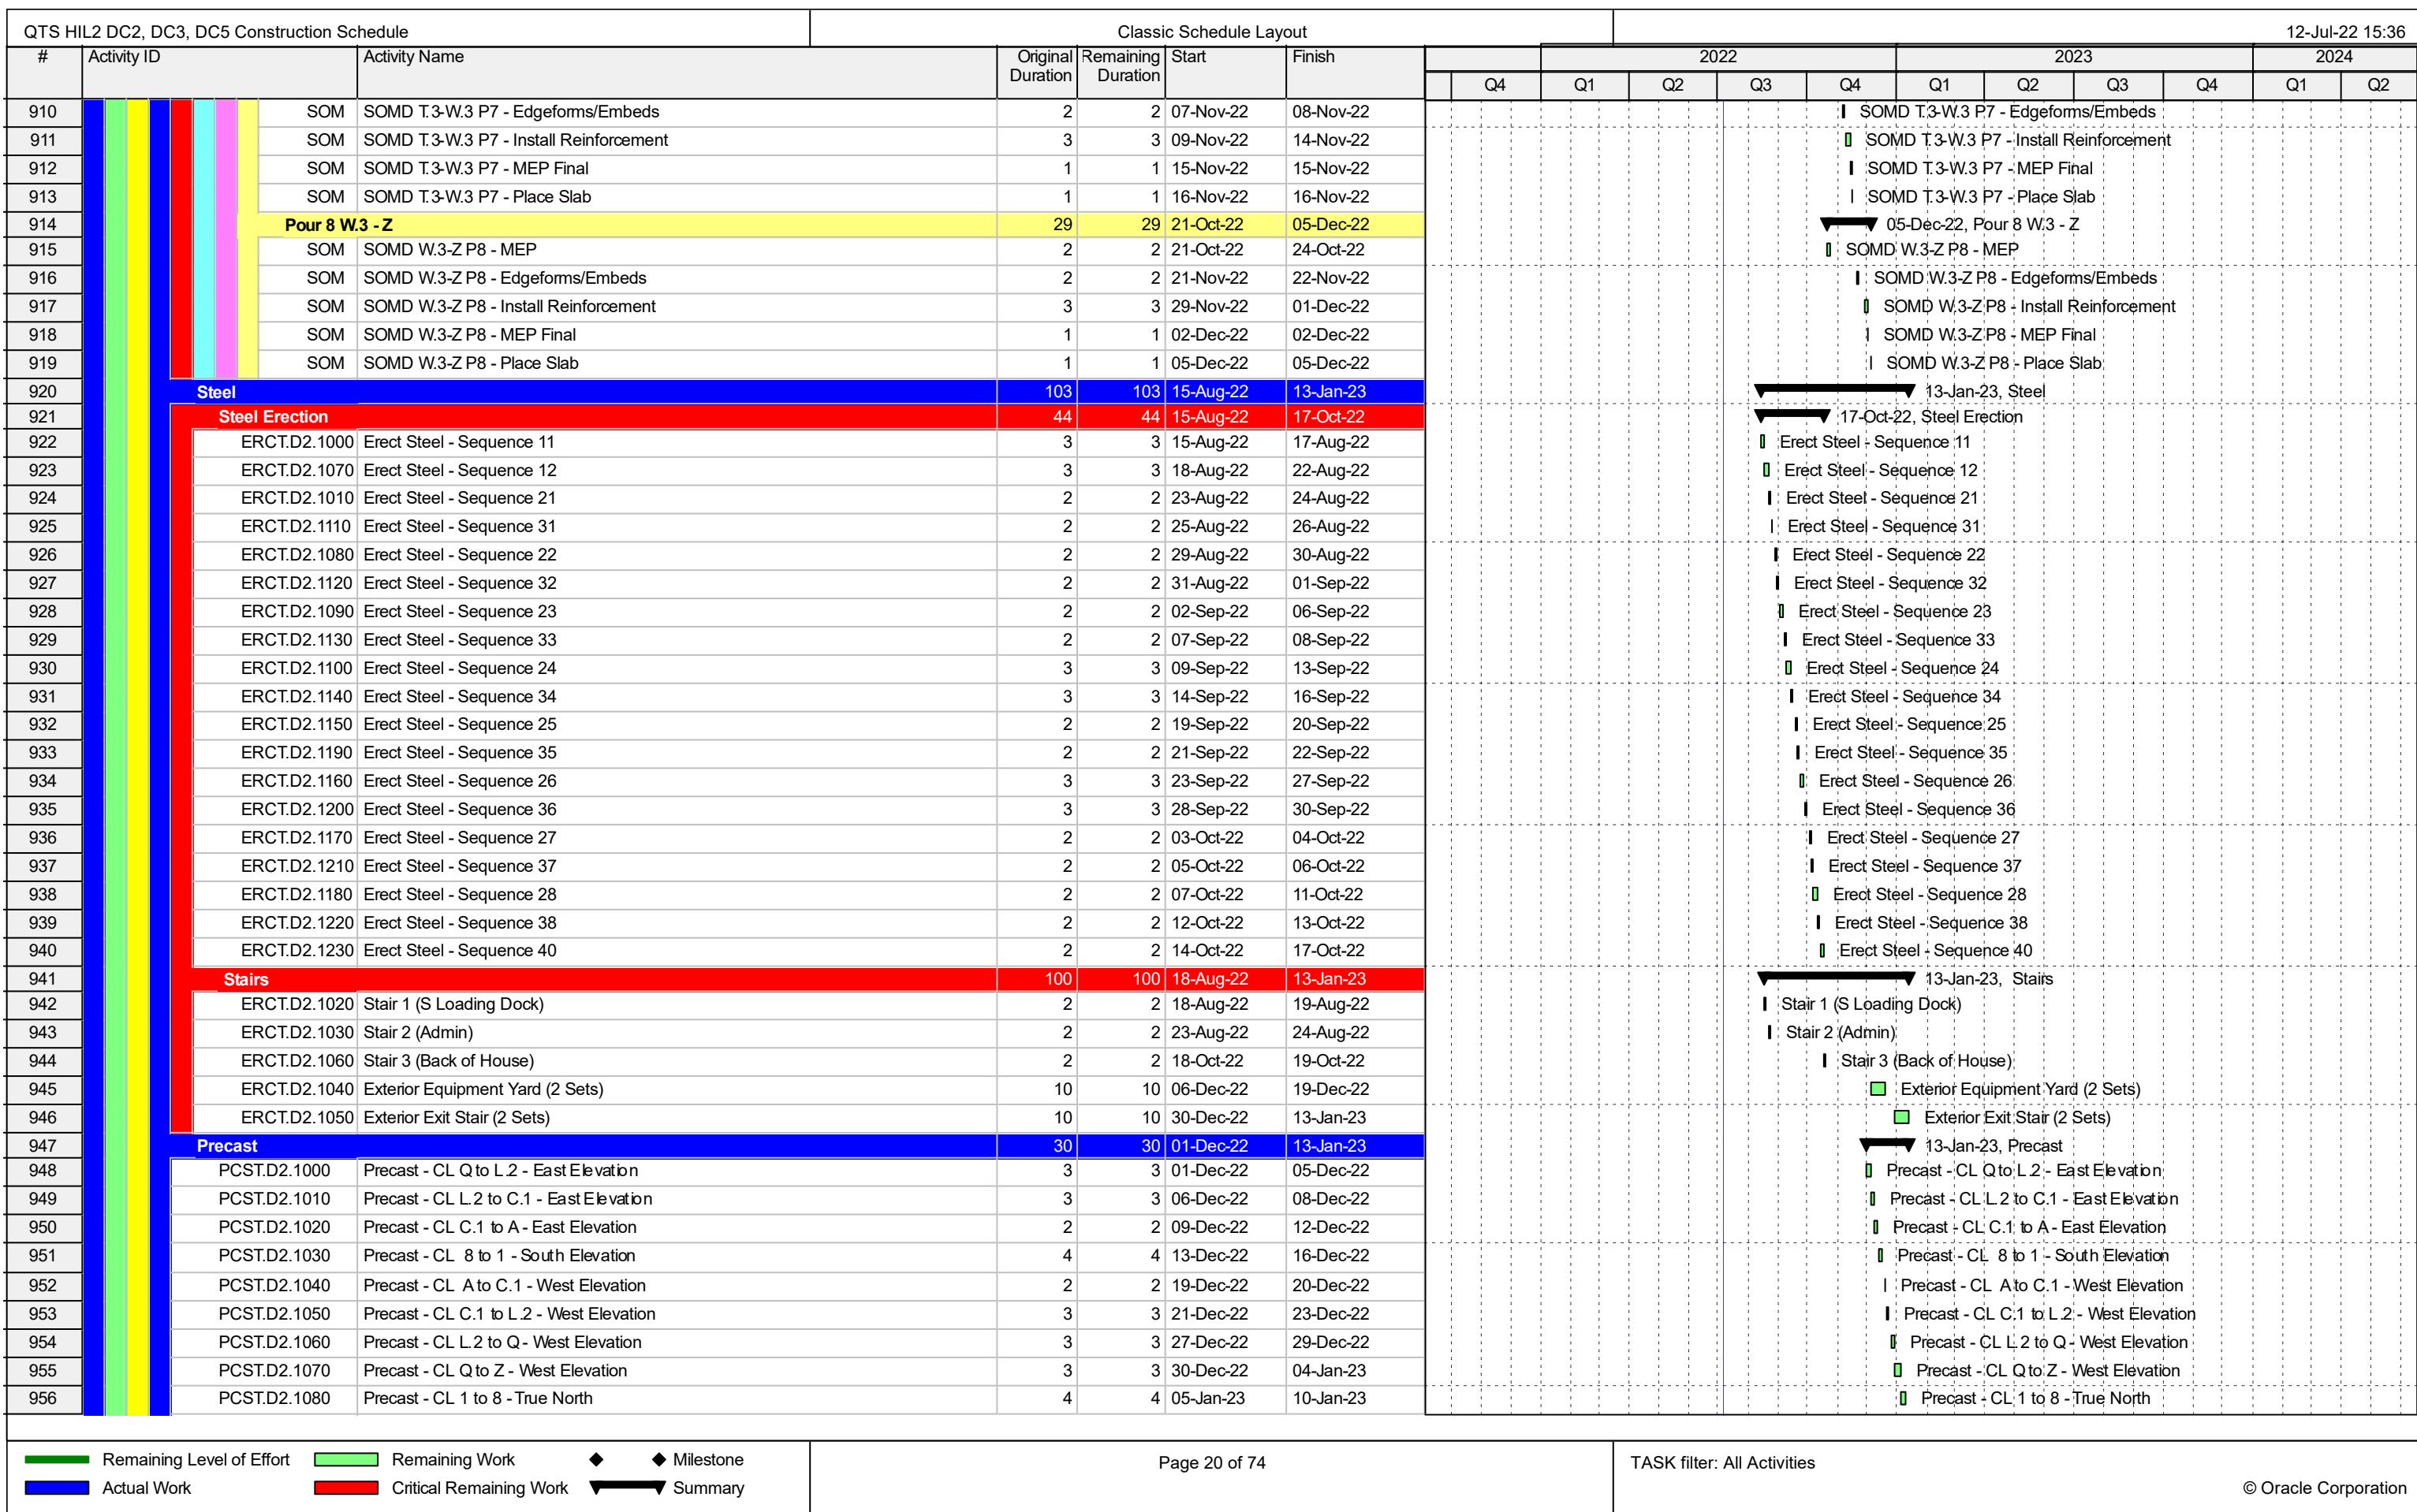



QTS HIL2 DC2, DC3, DC5 Construction Schedule				Classic Schedule Layout					12-Jul-22 15:36									
#	Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	2022					2023					2024	
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	
1005		EQPT.D2.1970 House - Mechanical RTU Final Connections	5	5	15-Dec-22	21-Dec-22												
1006		MPOE/BDF		20	20	25-Oct-22	22-Nov-22											
1007		MEP2 MPOE/BDF - Rough In Roof MEP		20	5	25-Oct-22	31-Oct-22											
1008		EQPT.D2.2000 MPOE/BDF - Set Rooftop ACCU Equipment		5	5	01-Nov-22	07-Nov-22											
1009		EQPT.D2.2010 MPOE/BDF - Pull and Terminate ACCU Feeders		5	5	08-Nov-22	15-Nov-22											
1010		EQPT.D2.2020 MPOE/BDF - Mechanical ACCU Final Connections		5	5	16-Nov-22	22-Nov-22											
1011		DH A - B		78	78	30-Sep-22	25-Jan-23											
1012		MEP3 DH A/B - Rough In Roof MEP		20	5	30-Sep-22	06-Oct-22											
1013		EQPT.D2.2080 DH A/B - Set Rooftop ACCU Equipment		5	5	05-Jan-23	11-Jan-23											
1014		EQPT.D2.2070 DH A/B - Pull and Terminate ACCU Feeders		5	5	12-Jan-23	18-Jan-23											
1015		EQPT.D2.2060 Mechanical ACCU Final Connections DH AB		5	5	19-Jan-23	25-Jan-23											
1016		DH C - D		20	20	08-Nov-22	08-Dec-22											
1017		MEP4 DH C/D - Rough In Roof MEP		20	5	08-Nov-22	15-Nov-22											
1018		EQPT.D2.2030 DH C/D - Set Rooftop ACCU Equipment		5	5	16-Nov-22	22-Nov-22											
1019		EQPT.D2.2040 DH C/D - Pull and Terminate ACCU Feeders		5	5	23-Nov-22	01-Dec-22											
1020		EQPT.D2.2050 DH C/D - Mechanical ACCU Final Connections		5	5	02-Dec-22	08-Dec-22											
1021		Equipment Yard		164	164	19-Jul-22	15-Mar-23											
1022		Medium Voltage Ductbank		57	57	19-Jul-22	06-Oct-22											
1023		EXCV.D2.1000 Excavate Medium Voltage Underground - Sequence 1		3	3	19-Jul-22	21-Jul-22											
1024		EXCV.D2.1010 Excavate Medium Voltage Underground - Sequence 2		9	9	22-Jul-22	03-Aug-22											
1025		MVDP.D2.100 Install Medium Voltage Underground - Sequence 1		2	2	22-Jul-22	25-Jul-22											
1026		EXCV.D2.1020 Excavate Medium Voltage Underground - Sequence 3		7	7	04-Aug-22	12-Aug-22											
1027		MVDP.D2.101 Install Medium Voltage Underground - Sequence 2		8	8	04-Aug-22	15-Aug-22											
1028		EXCV.D2.1030 Excavate Medium Voltage Underground - Sequence 4		8	8	15-Aug-22	24-Aug-22											
1029		MVDP.D2.102 Install Medium Voltage Underground - Sequence 3		7	7	15-Aug-22	23-Aug-22											
1030		EXCV.D2.1040 Excavate Medium Voltage Underground - Sequence 5		16	16	25-Aug-22	16-Sep-22											
1031		MVDP.D2.103 Install Medium Voltage Underground - Sequence 4		8	8	25-Aug-22	06-Sep-22											
1032		EXCV.D2.1050 Excavate Medium Voltage Underground - North Vault Group 1		5	5	19-Sep-22	23-Sep-22											
1033		MVDP.D2.104 Install Medium Voltage Underground - Sequence 5		14	14	19-Sep-22	06-Oct-22											
1034		EXCV.D2.1060 Excavate Medium Voltage Underground - North Vault Group 2		5	5	26-Sep-22	30-Sep-22											
1035		MVDP.D2.105 Install Medium Voltage Underground - North Vault Group 1		4	4	26-Sep-22	29-Sep-22											
1036		MVDP.D2.106 Install Medium Voltage Underground - North Vault Group 2		4	4	03-Oct-22	06-Oct-22											
1037		Equipment Yard Pads and Set Equipment		69	69	06-Dec-22	15-Mar-23											
1038		MPOE/BDF Pads and Set Equipment		28	28	06-Dec-22	16-Jan-23											
1039		SURV.D2.1 Survey MPOE/BDF Equipment Foundations		1	1	06-Dec-22	06-Dec-22											
1040		Pod Pads and Set Equipment		25	25	07-Dec-22	12-Jan-23											
1041		EXCV.D Yard MPOE/BDF - Excavate UPS Pod Foundations		2	2	07-Dec-22	08-Dec-22											
1042		CONC.I Yard MPOE/BDF - Form UPS Pod Foundations MPOE BDF		2	2	08-Dec-22	09-Dec-22											
1043		CONC.I Yard MPOE/BDF - Rebar UPS Pod Foundations		2	2	09-Dec-22	12-Dec-22											
1044		CONC.I Yard MPOE/BDF - Pour UPS Pod Foundations		3	3	13-Dec-22	15-Dec-22											
1045		CONC.I Yard MPOE/BDF - Cure UPS Pod Foundations		5	5	16-Dec-22	22-Dec-22											
1046		CONC.I Yard MPOE/BDF - Install Steel Rails UPS Pod Foundations		3	3	23-Dec-22	28-Dec-22											
1047		EQPT.D Yard MPOE/BDF - Set UPS Pods		5	5	29-Dec-22	05-Jan-23											
1048		EQPT.D Yard MPOE/BDF - Pull and Terminate UPS Pods		5	5	06-Jan-23	12-Jan-23											
1049		Transformer Pads and Set Equipment		23	23	07-Dec-22	10-Jan-23											
1050		EXCV.D Yard MPOE/BDF - Excavation Transformer Foundations		2	2	07-Dec-22	08-Dec-22											
1051		CONC.I Yard MPOE/BDF - Form Transformer Foundations		2	2	08-Dec-22	09-Dec-22											
1052		CONC.I Yard MPOE/BDF - Rebar Transformer Foundations		2	2	09-Dec-22	12-Dec-22											

█ Remaining Level of Effort █ Remaining Work ◆ Milestone
█ Actual Work █ Critical Remaining Work ▼ Summary

QTS HIL2 DC2, DC3, DC5 Construction Schedule				Classic Schedule Layout					Timeline View									
#	Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	2022					2023				2024		
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	
1053		CONC.I Yard MPOE/BDF - Pour Transformer Foundations	1	1	16-Dec-22	16-Dec-22						I	Yard MPOE/BDF - Pour Transformer Foundations					
1054		CONC.I Yard MPOE/BDF - Cure Transformer Foundations		5	5	19-Dec-22	23-Dec-22					I	Yard MPOE/BDF - Cure Transformer Foundations					
1055		EQPT.D Yard MPOE/BDF - Set Transformers		5	5	27-Dec-22	03-Jan-23					■	Yard MPOE/BDF - Set Transformers					
1056		EQPT.D Yard MPOE/BDF - Pull and Terminate Transformers		5	5	04-Jan-23	10-Jan-23					■	Yard MPOE/BDF - Pull and Terminate Transformers					
1057		Generator Pads and Set Equipment		25	25	09-Dec-22	16-Jan-23					▼	16-Jan-23, Generator Pads and Set Equipment					
1058		EXCV.D Yard MPOE/BDF - Excavation Generator Foundations		2	2	09-Dec-22	12-Dec-22					I	Yard MPOE/BDF - Excavation Generator Foundations					
1059		CONC.I Yard MPOE/BDF - Form Generator Foundations		2	2	12-Dec-22	13-Dec-22					I	Yard MPOE/BDF - Form Generator Foundations					
1060		CONC.I Yard MPOE/BDF - Rebar Generator Foundations		3	3	13-Dec-22	15-Dec-22					I	Yard MPOE/BDF - Rebar Generator Foundations					
1061		CONC.I Yard MPOE/BDF - Pour Generator Foundations		4	4	19-Dec-22	22-Dec-22					I	Yard MPOE/BDF - Pour Generator Foundations					
1062		CONC.I Yard MPOE/BDF - Cure Generator Foundations		5	5	23-Dec-22	30-Dec-22					■	Yard MPOE/BDF - Cure Generator Foundations					
1063		EQPT.D Yard MPOE/BDF - Set Generators		5	5	03-Jan-23	09-Jan-23					■	Yard MPOE/BDF - Set Generators					
1064		EQPT.D Yard MPOE/BDF - Pull and Terminate Generators		5	5	10-Jan-23	16-Jan-23					▼	31-Jan-23, Data Hall A and B Pads and Set Equipment					
1065		Data Hall A and B Pads and Set Equipment		36	36	09-Dec-22	31-Jan-23					I	Survey DH A/B - Equipment Foundations					
1066		SURV.D2.1 Survey DH A/B - Equipment Foundations		1	1	09-Dec-22	09-Dec-22					▼	23-Jan-23, Transformer Pads and Set Equipment					
1067		Transformer Pads and Set Equipment		20	20	23-Dec-22	23-Jan-23					■	Yard DH A/B - Excavation Transformer Foundations					
1068		EXCV.D Yard DH A/B - Excavation Transformer Foundations		2	2	23-Dec-22	27-Dec-22					I	Yard DH A/B - Form Transformer Foundations DH AB					
1069		CONC.I Yard DH A/B - Form Transformer Foundations DH AB		2	2	27-Dec-22	28-Dec-22					I	Yard DH A/B - Rebar Transformer Foundations					
1070		CONC.I Yard DH A/B - Rebar Transformer Foundations		2	2	28-Dec-22	29-Dec-22					I	Yard DH A/B - Pour Transformer Foundations					
1071		CONC.I Yard DH A/B - Pour Transformer Foundations		1	1	30-Dec-22	30-Dec-22					■	Yard DH A/B - Cure Transformer Foundations					
1072		CONC.I Yard DH A/B - Cure Transformer Foundations		5	5	03-Jan-23	09-Jan-23					■	Yard DH A/B - Set Transformers					
1073		EQPT.D Yard DH A/B - Set Transformers		5	5	10-Jan-23	16-Jan-23					■	Yard DH A/B - Pull and Terminate Transformers					
1074		EQPT.D Yard DH A/B - Pull and Terminate Transformers		5	5	17-Jan-23	23-Jan-23					▼	31-Jan-23, Generator Pads and Set Equipment					
1075		Generator Pads and Set Equipment		24	24	28-Dec-22	31-Jan-23					I	Yard DH A/B - Excavation Generator Foundations					
1076		EXCV.D Yard DH A/B - Excavation Generator Foundations		2	2	28-Dec-22	29-Dec-22					I	Yard DH A/B - Form Generator Foundations					
1077		CONC.I Yard DH A/B - Form Generator Foundations		2	2	29-Dec-22	30-Dec-22					■	Yard DH A/B - Rebar Generator Foundations					
1078		CONC.I Yard DH A/B - Rebar Generator Foundations		3	3	30-Dec-22	04-Jan-23					I	Yard DH A/B - Pour Generator Foundations					
1079		CONC.I Yard DH A/B - Pour Generator Foundations		4	4	05-Jan-23	10-Jan-23					■	Yard DH A/B - Cure Generator Foundations					
1080		CONC.I Yard DH A/B - Cure Generator Foundations		5	5	11-Jan-23	17-Jan-23					■	Yard DH A/B - Set Generators					
1081		EQPT.D Yard DH A/B - Set Generators		5	5	18-Jan-23	24-Jan-23					■	Yard DH A/B - Pull and Terminate Generators					
1082		EQPT.D Yard DH A/B - Pull and Terminate Generators		5	5	25-Jan-23	31-Jan-23					▼	31-Jan-23, Medium Voltage Pads and Set Equipment					
1083		Medium Voltage Pads and Set Equipment		22	22	30-Dec-22	31-Jan-23					■	Yard DH A/B - Excavation MV Pads					
1084		EXCV.D Yard DH A/B - Excavation MV Pads		2	2	30-Dec-22	03-Jan-23					I	Yard DH A/B - Form MV Pads					
1085		CONC.I Yard DH A/B - Form MV Pads		2	2	04-Jan-23	05-Jan-23					■	Yard DH A/B - Rebar MV Foundations					
1086		CONC.I Yard DH A/B - Rebar MV Foundations		3	3	06-Jan-23	10-Jan-23					I	Yard DH A/B - Pour MV Pads					
1087		CONC.I Yard DH A/B - Pour MV Pads		4	4	11-Jan-23	16-Jan-23					■	Yard DH A/B - Cure MV Pads					
1088		CONC.I Yard DH A/B - Cure MV Pads		5	5	17-Jan-23	23-Jan-23					I	Yard DH A/B - Set MV Equipment					
1089		EQPT.D Yard DH A/B - Set MV Equipment		5	5	24-Jan-23	30-Jan-23					■	Yard DH A/B - Pull and Terminate MV Feeders					
1090		EQPT.D Yard DH A/B - Pull and Terminate MV Feeders		5	5	25-Jan-23	31-Jan-23					▼	31-Jan-23, Data Hall C and D Pads and Set Equipment					
1091		Data Hall C and D Pads and Set Equipment		42	42	16-Jan-23	15-Mar-23					I	Survey DH C/D Equipment Foundations					
1092		SURV.D2.1 Survey DH C/D Equipment Foundations		1	1	16-Jan-23	16-Jan-23					▼	13-Feb-23, Transformer Pads and Set Equipment					
1093		Transformer Pads and Set Equipment		20	20	17-Jan-23	13-Feb-23					I	Yard DH C/D - Excavation Transformer Foundations					
1094		EXCV.D Yard DH C/D - Excavation Transformer Foundations		2	2	17-Jan-23	18-Jan-23					I	Yard DH C/D - Form Transformer Foundations					
1095		CONC.I Yard DH C/D - Form Transformer Foundations		2	2	18-Jan-23	19-Jan-23					I	Yard DH C/D - Rebar Transformer Foundations					
1096		CONC.I Yard DH C/D - Rebar Transformer Foundations		2	2	19-Jan-23	20-Jan-23					I	Yard DH C/D - Pour Transformer Foundations					
1097		CONC.I Yard DH C/D - Pour Transformer Foundations		1	1	23-Jan-23	23-Jan-23					■	Yard DH C/D - Cure Transformer Foundations					
1098		CONC.I Yard DH C/D - Cure Transformer Foundations		5	5	24-Jan-23	30-Jan-23					■	Yard DH C/D - Set Transformers					
1099		EQPT.D Yard DH C/D - Set Transformers		5	5	31-Jan-23	06-Feb-23					■	Yard DH C/D - Pull and Terminate Transformers					
1100		EQPT.D Yard DH C/D - Pull and Terminate Transformers		5	5	07-Feb-23	13-Feb-23											

QTS HIL2 DC2, DC3, DC5 Construction Schedule				Classic Schedule Layout					12-Jul-22 15:36									
#	Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	2022					2023					2024	
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	
1101		Generator Pads and Set Equipment	39	39	19-Jan-23	15-Mar-23												15-Mar-23, Generator Pads and Set Equipment
1102		EXCV.D Yard DH C/D - Excavation Generator Foundations	2	2	19-Jan-23	20-Jan-23												I Yard DH C/D - Excavation Generator Foundations
1103		CONC.I Yard DH C/D - Form Generator Foundations	2	2	20-Jan-23	23-Jan-23												II Yard DH C/D - Form Generator Foundations
1104		CONC.I Yard DH C/D - Rebar Generator Foundations	3	3	23-Jan-23	25-Jan-23												III Yard DH C/D - Rebar Generator Foundations
1105		CONC.I Yard DH C/D - Pour Generator Foundations	4	4	26-Jan-23	31-Jan-23												IV Yard DH C/D - Pour Generator Foundations
1106		CONC.I Yard DH C/D - Cure Generator Foundations	5	5	01-Feb-23	07-Feb-23												V Yard DH C/D - Cure Generator Foundations
1107		EQPT.D Yard DH C/D - Set Generators	5	5	08-Feb-23	14-Feb-23												VI Yard DH C/D - Set Generators
1108		EQPT.D Yard DH C/D - Pull and Terminate Generators	20	20	15-Feb-23	15-Mar-23												VII Yard DH C/D - Pull and Terminate Generators
1109		Medium Voltage Pads and Set Equipment	21	21	23-Jan-23	21-Feb-23												21-Feb-23, Medium Voltage Pads and Set Equipment
1110		EXCV.D Yard DH C/D - Excavation MV Pads	2	2	23-Jan-23	24-Jan-23												I Yard DH C/D - Excavation MV Pads
1111		CONC.I Yard DH C/D - Form MV Pads	2	2	25-Jan-23	26-Jan-23												II Yard DH C/D - Form MV Pads
1112		CONC.I Yard DH C/D - Rebar MV Foundations	2	2	27-Jan-23	30-Jan-23												III Yard DH C/D - Rebar MV Foundations
1113		CONC.I Yard DH C/D - Pour MV Pads	4	4	31-Jan-23	03-Feb-23												IV Yard DH C/D - Pour MV Pads
1114		CONC.I Yard DH C/D - Cure MV Pads	5	5	06-Feb-23	10-Feb-23												V Yard DH C/D - Cure MV Pads
1115		EQPT.D Yard DH C/D - Set MV Equipment	5	5	13-Feb-23	17-Feb-23												VI Yard DH C/D - Set MV Equipment
1116		EQPT.D Yard DH C/D - Pull and Terminate MV Feeders	5	5	14-Feb-23	21-Feb-23												VII Yard DH C/D - Pull and Terminate MV Feeders
1117		House	20	20	23-Dec-22	23-Jan-23												23-Jan-23, House
1118		EXCV.D.1 Yard House - Excavation Transformer Foundations	2	2	23-Dec-22	27-Dec-22												I Yard House - Excavation Transformer Foundations
1119		CONC.D.2. Yard House - Form Transformer Foundations DH AB	2	2	27-Dec-22	28-Dec-22												II Yard House - Form Transformer Foundations DH AB
1120		CONC.D.2. Yard House - Rebar Transformer Foundations	2	2	28-Dec-22	29-Dec-22												III Yard House - Rebar Transformer Foundations
1121		CONC.D.2. Yard House - Pour Transformer Foundations	1	1	30-Dec-22	30-Dec-22												IV Yard House - Pour Transformer Foundations
1122		CONC.D.2. Yard House - Cure Transformer Foundations	5	5	03-Jan-23	09-Jan-23												V Yard House - Cure Transformer Foundations
1123		EQPT.D2.2 Yard House - Set Transformers	5	5	10-Jan-23	16-Jan-23												VI Yard House - Set Transformers
1124		EQPT.D2.2 Yard House - Pull and Terminate Transformers	5	5	17-Jan-23	23-Jan-23												VII Yard House - Pull and Terminate Transformers
1125		Elevators	85	85	01-Dec-22	03-Apr-23												03-Apr-23, Elevators
1126		Freight Elevator E03	61	61	30-Dec-22	28-Mar-23												28-Mar-23, Freight Elevator E03
1127		ELVT.D2.1000 Freight Elev. 3 - Hoisting Equipment	7	7	30-Dec-22	10-Jan-23												I Freight Elev. 3 - Hoisting Equipment
1128		ELVT.D2.1010 Freight Elev. 3 - Pit Rails/Frame/Cab	5	5	11-Jan-23	17-Jan-23												II Freight Elev. 3 - Pit Rails/Frame/Cab
1129		ELVT.D2.1020 Freight Elev. 3 - Tirak & Governor Rope	5	5	18-Jan-23	24-Jan-23												III Freight Elev. 3 - Tirak & Governor Rope
1130		ELVT.D2.1030 Freight Elev. 3 - Rails	8	8	25-Jan-23	03-Feb-23												IV Freight Elev. 3 - Rails
1131		ELVT.D2.1040 Freight Elev. 3 - Door entrances	4	4	06-Feb-23	09-Feb-23												V Freight Elev. 3 - Door entrances
1132		ELVT.D2.1050 Freight Elev. 3 - Duct/Wire Machine/Startup	7	7	10-Feb-23	21-Feb-23												VI Freight Elev. 3 - Duct/Wire Machine/Startup
1133		ELVT.D2.1060 Freight Elev. 3 - Rope Elevator/Remove Tirak	4	4	22-Feb-23	27-Feb-23												VII Freight Elev. 3 - Rope Elevator/Remove Tirak
1134		ELVT.D2.1070 Freight Elev. 3 - Pipe and Wire Hatch Devices	6	6	28-Feb-23	07-Mar-23												VIII Freight Elev. 3 - Pipe and Wire Hatch Devices
1135		ELVT.D2.1080 Freight Elev. 3 - Terminate Devices	8	8	08-Mar-23	17-Mar-23												IX Freight Elev. 3 - Terminate Devices
1136		ELVT.D2.1090 Freight Elev. 3 - Clean Rails	2	2	20-Mar-23	21-Mar-23												X Freight Elev. 3 - Clean Rails
1137		ELVT.D2.1100 Freight Elev. 3 - Inspect	5	5	22-Mar-23	28-Mar-23												XI Freight Elev. 3 - Inspect
1138		Freight Elevator E02A and E02B	85	85	01-Dec-22	03-Apr-23												03-Apr-23, Freight Elevator E02A and E02B
1139		ELVT.D2.1110 Freight Elev. E02A/E02B - Hoisting Equipment	10	10	01-Dec-22	14-Dec-22												I Freight Elev. E02A/E02B - Hoisting Equipment
1140		ELVT.D2.1120 Freight Elev. E02A/E02B - Pit Rails/Frame/Cab	7	7	15-Dec-22	23-Dec-22												II Freight Elev. E02A/E02B - Pit Rails/Frame/Cab
1141		ELVT.D2.1130 Freight Elev. E02A/E02B - Tirak & Governor Rope	7	7	27-Dec-22	05-Jan-23												III Freight Elev. E02A/E02B - Tirak & Governor Rope
1142		ELVT.D2.1140 Freight Elev. E02A/E02B - Rails	10	10	06-Jan-23	19-Jan-23												IV Freight Elev. E02A/E02B - Rails
1143		ELVT.D2.1150 Freight Elev. E02A/E02B - Door entrances	6	6	20-Jan-23	27-Jan-23												V Freight Elev. E02A/E02B - Door entrances
1144		ELVT.D2.1160 Freight Elev. E02A/E02B - Duct/Wire Machine/Startup	9	9	30-Jan-23	09-Feb-23												VI Freight Elev. E02A/E02B - Duct/Wire Machine/Startup
1145		ELVT.D2.1170 Freight Elev. E02A/E02B - Rope Elevator/Remove Tirak	6	6	10-Feb-23	17-Feb-23												VII Freight Elev. E02A/E02B - Rope Elevator/Remove Tirak
1146		ELVT.D2.1180 Freight Elev. E02A/E02B - Pipe and Wire Hatch Devices	8	8	21-Feb-23	02-Mar-23												VIII Freight Elev. E02A/E02B - Pipe and Wire Hatch Devices
1147		ELVT.D2.1190 Freight Elev. E02A/E02B - Terminate Devices	10	10	03-Mar-23	16-Mar-23												IX Freight Elev. E02A/E02B - Terminate Devices
1148		ELVT.D2.1200 Freight Elev. E02A/E02B - Clean Rails	4	4	17-Mar-23	22-Mar-23												X Freight Elev. E02A/E02B - Clean Rails



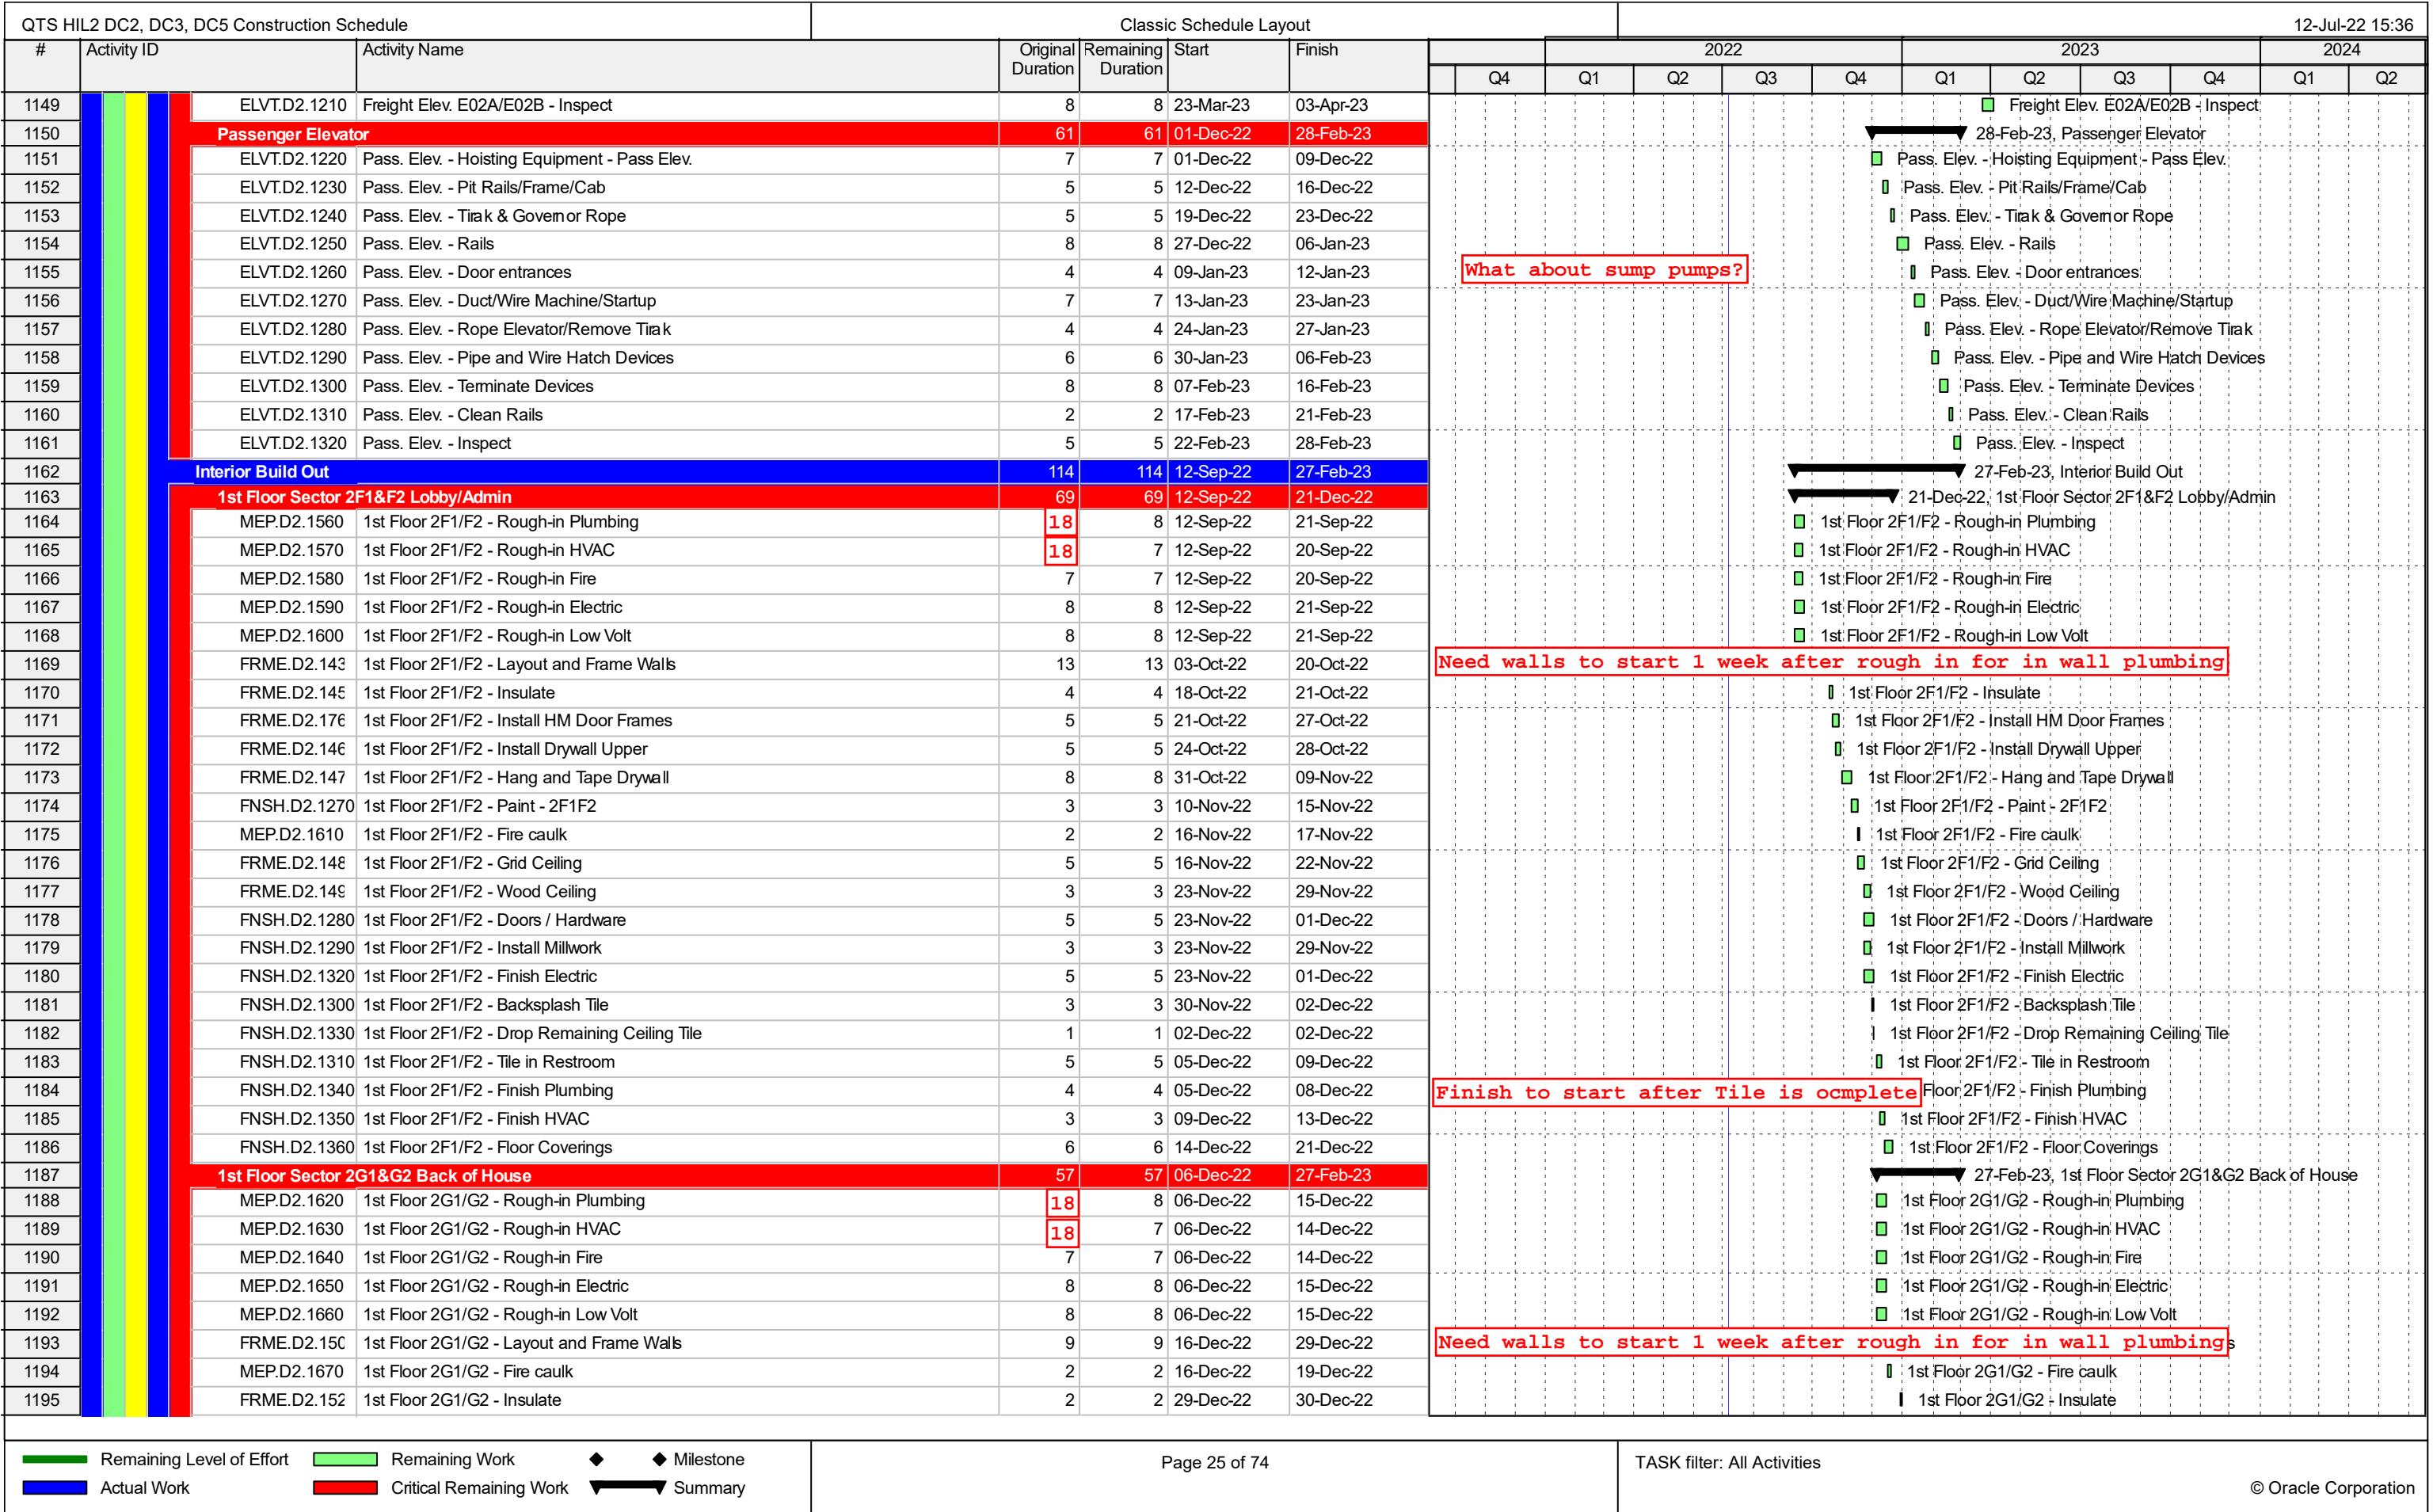

QTS HIL2 DC2, DC3, DC5 Construction Schedule				Classic Schedule Layout					12-Jul-22 15:36									
#	Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	2022					2023				2024		
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	
1196	FRME.D2.153	1st Floor 2G1/G2 - Install Drywall Upper	5	5	03-Jan-23	09-Jan-23						1st Floor 2G1/G2 - Install Drywall Upper						
1197	FRME.D2.154	1st Floor 2G1/G2 - Hang and Tape Drywall	7	7	10-Jan-23	18-Jan-23						1st Floor 2G1/G2 - Hang and Tape Drywall						
1198	FNSH.D2.1390	1st Floor 2G1/G2 - Tile in Restroom	3	3	10-Jan-23	12-Jan-23						1st Floor 2G1/G2 - Tile in Restroom						
1199	FNSH.D2.1400	1st Floor 2G1/G2 - Backsplash Tile	5	5	13-Jan-23	19-Jan-23						1st Floor 2G1/G2 - Backsplash Tile						
1200	FNSH.D2.1370	1st Floor 2G1/G2 - Paint	3	3	19-Jan-23	23-Jan-23						1st Floor 2G1/G2 - Paint						
1201	FRME.D2.155	1st Floor 2G1/G2 - Grid Ceiling	5	5	24-Jan-23	30-Jan-23						1st Floor 2G1/G2 - Grid Ceiling						
1202	FRME.D2.156	1st Floor 2G1/G2 - Wood Ceiling	3	3	31-Jan-23	02-Feb-23						1st Floor 2G1/G2 - Wood Ceiling						
1203	FNSH.D2.1380	1st Floor 2G1/G2 - Doors & Hardware	5	5	31-Jan-23	06-Feb-23						1st Floor 2G1/G2 - Doors & Hardware						
1204	FRME.D2.157	1st Floor 2G1/G2 - Install Millwork	3	3	31-Jan-23	02-Feb-23						1st Floor 2G1/G2 - Install Millwork						
1205	FNSH.D2.1410	1st Floor 2G1/G2 - Finish Electric	5	5	31-Jan-23	06-Feb-23						1st Floor 2G1/G2 - Finish Electric						
1206	FNSH.D2.1420	1st Floor 2G1/G2 - Drop Remaining Ceiling Tile	1	1	07-Feb-23	07-Feb-23						1st Floor 2G1/G2 - Drop Remaining Ceiling Tile						
1207	FNSH.D2.1430	1st Floor 2G1/G2 - Finish Plumbing	4	4	08-Feb-23	13-Feb-23						1st Floor 2G1/G2 - Finish Plumbing						
1208	FNSH.D2.1440	1st Floor 2G1/G2 - Finish HVAC	3	3	14-Feb-23	16-Feb-23						1st Floor 2G1/G2 - Finish HVAC						
1209	FNSH.D2.1450	1st Floor 2G1/G2 - Floor Coverings	6	6	17-Feb-23	27-Feb-23						1st Floor 2G1/G2 - Floor Coverings						
1210	2nd Floor Sector 2F1&F2 Admin			54	54	19-Sep-22	07-Dec-22						07-Dec-22, 2nd Floor Sector 2F1&F2 Admin					
1211	FRME.D2.158	2nd Floor 2F1/F2 - Layout and Frame Walls	13	13	19-Sep-22	05-Oct-22						2nd Floor 2F1/F2 - Layout and Frame Walls						
1212	MEP.D2.1680	2nd Floor 2F1/F2 - Rough-in Plumbing	18	18	19-Sep-22	28-Sep-22						2nd Floor 2F1/F2 - Rough-in Plumbing						
1213	MEP.D2.1690	2nd Floor 2F1/F2 - Rough-in HVAC	18	18	19-Sep-22	27-Sep-22						2nd Floor 2F1/F2 - Rough-in HVAC						
1214	MEP.D2.1700	2nd Floor 2F1/F2 - Rough-in Fire	7	7	19-Sep-22	27-Sep-22						2nd Floor 2F1/F2 - Rough-in Fire						
1215	MEP.D2.1710	2nd Floor 2F1/F2 - Rough-in Electric	8	8	19-Sep-22	28-Sep-22						2nd Floor 2F1/F2 - Rough-in Electric						
1216	MEP.D2.1720	2nd Floor 2F1/F2 - Rough-in Low Volt	8	8	19-Sep-22	28-Sep-22						2nd Floor 2F1/F2 - Rough-in Low Volt						
1217	FRME.D2.182	2nd Floor 2F1/F2 - Install HM Door Frames	5	5	19-Sep-22	23-Sep-22						2nd Floor 2F1/F2 - Install HM Door Frames						
1218	MEP.D2.1730	2nd Floor 2F1/F2 - Fire caulk	2	2	29-Sep-22	30-Sep-22						2nd Floor 2F1/F2 - Fire caulk						
1219	FRME.D2.160	2nd Floor 2F1/F2 - Insulate	4	4	03-Oct-22	06-Oct-22						2nd Floor 2F1/F2 - Insulate						
1220	FRME.D2.161	2nd Floor 2F1/F2 - Install Drywall Upper	5	5	07-Oct-22	14-Oct-22						2nd Floor 2F1/F2 - Install Drywall Upper						
1221	FRME.D2.162	2nd Floor 2F1/F2 - Hang and Tape Drywall	8	8	17-Oct-22	26-Oct-22						2nd Floor 2F1/F2 - Hang and Tape Drywall						
1222	FNSH.D2.1460	2nd Floor 2F1/F2 - Paint	3	3	27-Oct-22	31-Oct-22						2nd Floor 2F1/F2 - Paint						
1223	FRME.D2.163	2nd Floor 2F1/F2 - Grid Ceiling	5	5	01-Nov-22	07-Nov-22						2nd Floor 2F1/F2 - Grid Ceiling						
1224	FNSH.D2.1470	2nd Floor 2F1/F2 - Doors & Hardware	5	5	08-Nov-22	15-Nov-22						2nd Floor 2F1/F2 - Doors & Hardware						
1225	FNSH.D2.1490	2nd Floor 2F1/F2 - Tile in Restroom	5	5	08-Nov-22	15-Nov-22						2nd Floor 2F1/F2 - Tile in Restroom						
1226	FNSH.D2.1500	2nd Floor 2F1/F2 - Finish Electric	5	5	08-Nov-22	15-Nov-22						2nd Floor 2F1/F2 - Finish Electric						
1227	FNSH.D2.1510	2nd Floor 2F1/F2 - Drop Remaining Ceiling Tile	1	1	16-Nov-22	16-Nov-22						2nd Floor 2F1/F2 - Drop Remaining Ceiling Tile						
1228	FNSH.D2.1520	2nd Floor 2F1/F2 - Finish Plumbing	4	4	17-Nov-22	22-Nov-22						2nd Floor 2F1/F2 - Finish Plumbing						
1229	FNSH.D2.1530	2nd Floor 2F1/F2 - Finish HVAC	3	3	23-Nov-22	29-Nov-22						2nd Floor 2F1/F2 - Finish HVAC						
1230	FNSH.D2.1540	2nd Floor 2F1/F2 - Floor Coverings	6	6	30-Nov-22	07-Dec-22						2nd Floor 2F1/F2 - Floor Coverings						
1231	2nd Floor Sector 2G1&G2 Back of House			39	39	06-Dec-22	31-Jan-23						31-Jan-23, 2nd Floor Sector 2G1&G2 Back of House					
1232	FRME.D2.166	2nd Floor 2G1/G2 - Layout and Frame Walls	9	9	06-Dec-22	16-Dec-22						2nd Floor 2G1/G2 - Layout and Frame Walls						
1233	MEP.D2.1740	2nd Floor 2G1/G2 - Rough-in Plumbing	18	18	06-Dec-22	15-Dec-22						2nd Floor 2G1/G2 - Rough-in Plumbing						
1234	MEP.D2.1750	2nd Floor 2G1/G2 - Rough-in HVAC	18	18	06-Dec-22	14-Dec-22						2nd Floor 2G1/G2 - Rough-in HVAC						
1235	MEP.D2.1760	2nd Floor 2G1/G2 - Rough-in Fire	7	7	06-Dec-22	14-Dec-22						2nd Floor 2G1/G2 - Rough-in Fire						
1236	MEP.D2.1770	2nd Floor 2G1/G2 - Rough-in Electric	8	8	06-Dec-22	15-Dec-22						2nd Floor 2G1/G2 - Rough-in Electric						
1237	MEP.D2.1780	2nd Floor 2G1/G2 - Rough-in Low Volt	8	8	06-Dec-22	15-Dec-22						2nd Floor 2G1/G2 - Rough-in Low Volt						
1238	FRME.D2.183	2nd Floor 2G1/G2 - Install HM Door Frame	5	5	06-Dec-22	12-Dec-22						2nd Floor 2G1/G2 - Install HM Door Frame						
1239	MEP.D2.1790	2nd Floor 2G1/G2 - Fire caulk	2	2	16-Dec-22	19-Dec-22						2nd Floor 2G1/G2 - Fire caulk						
1240	FRME.D2.168	2nd Floor 2G1/G2 - Insulate	2	2	20-Dec-22	21-Dec-22						2nd Floor 2G1/G2 - Insulate						
1241	FRME.D2.169	2nd Floor 2G1/G2 - Install Drywall Upper	5	5	22-Dec-22	29-Dec-22						2nd Floor 2G1/G2 - Install Drywall Upper						
1242	FRME.D2.170	2nd Floor 2G1/G2 - Hang and Tape Drywall	7	7	30-Dec-22	10-Jan-23						2nd Floor 2G1/G2 - Hang and Tape Drywall						



QTS HIL2 DC2, DC3, DC5 Construction Schedule				Classic Schedule Layout					12-Jul-22 15:36										
#	Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	2022					2023					2024		
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2		
1243	FNSH.D2.1570	2nd Floor 2G1/G2 - Tile in Restroom	3	3	30-Dec-22	04-Jan-23						2nd Floor 2G1/G2 - Tile in Restroom							
1244	FNSH.D2.1550	2nd Floor 2G1/G2 - Paint	3	3	11-Jan-23	13-Jan-23						2nd Floor 2G1/G2 - Paint							
1245	FRME.D2.172	2nd Floor 2G1/G2 - Wood Ceiling	3	3	16-Jan-23	18-Jan-23						2nd Floor 2G1/G2 - Wood Ceiling							
1246	FNSH.D2.1560	2nd Floor 2G1/G2 - Doors & Hardware	5	5	16-Jan-23	20-Jan-23						2nd Floor 2G1/G2 - Doors & Hardware							
1247	FNSH.D2.1590	2nd Floor 2G1/G2 - Finish Electric	5	5	16-Jan-23	20-Jan-23						2nd Floor 2G1/G2 - Finish Electric							
1248	FNSH.D2.1610	2nd Floor 2G1/G2 - Finish Plumbing	4	4	23-Jan-23	26-Jan-23						2nd Floor 2G1/G2 - Finish Plumbing							
1249	FNSH.D2.1620	2nd Floor 2G1/G2 - Finish HVAC	3	3	27-Jan-23	31-Jan-23						2nd Floor 2G1/G2 - Finish HVAC							
1250	Site Finishes			67	67	23-Dec-22	30-Mar-23						30-Mar-23, Site Finishes						
1251	Trash Enclosure			9	9	23-Dec-22	06-Jan-23						06-Jan-23, Trash Enclosure						
1252	FOND.D2.152	Trash Encl - Dig Footings	1	1	23-Dec-22	23-Dec-22						Trash Encl - Dig Footings							
1253	FOND.D2.153	Trash Encl - Form Footings	1	1	23-Dec-22	23-Dec-22						Trash Encl - Form Footings							
1254	FOND.D2.154	Trash Encl - Install Rebar & Bolards	1	1	27-Dec-22	27-Dec-22						Trash Encl - Install Rebar & Bolards							
1255	FOND.D2.155	Trash Encl - Inspect & Pour	1	1	27-Dec-22	27-Dec-22						Trash Encl - Inspect & Pour							
1256	CONC.D2.134	Trash Encl - Embeds for Gate	3	3	27-Dec-22	29-Dec-22						Trash Encl - Embeds for Gate							
1257	SOG.D2.1420	Trash Encl - SOG	2	2	28-Dec-22	29-Dec-22						Trash Encl - SOG							
1258	CONC.D2.135	Trash Encl - CMU - Trash Enc.	3	3	30-Dec-22	04-Jan-23						Trash Encl - CMU - Trash Enc.							
1259	CONC.D2.136	Trash Encl - Grout CMU	1	1	05-Jan-23	05-Jan-23						Trash Encl - Grout CMU							
1260	FNSH.D2.1640	Trash Encl - Install Gate	1	1	06-Jan-23	06-Jan-23						Trash Encl - Install Gate							
1261	FNSH.D2.1650	Trash Encl - Install Steel Coping	1	1	06-Jan-23	06-Jan-23						Trash Encl - Install Steel Coping							
1262	FNSH.D2.1660	Trash Encl - Paint	1	1	06-Jan-23	06-Jan-23						Trash Encl - Paint							
1263	Parking Lot			23	23	13-Feb-23	16-Mar-23						16-Mar-23, Parking Lot						
1264	UTIL.D2.1040	Park. Lot - Install/Adjust Manhole Covers	3	3	13-Feb-23	15-Feb-23						Park. Lot - Install/Adjust Manhole Covers							
1265	FOND.D2.156	Park. Lot - Rough Grade Parking Lot	2	2	13-Feb-23	14-Feb-23						Park. Lot - Rough Grade Parking Lot							
1266	FNSH.D2.1680	Park. Lot - Landscape Sleeves	3	3	13-Feb-23	15-Feb-23						Park. Lot - Landscape Sleeves							
1267	CONC.D2.136	Park. Lot - Cut Curbs	2	2	15-Feb-23	16-Feb-23						Park. Lot - Cut Curbs							
1268	UTIL.D2.1050	Park. Lot - Install Catch Basins	3	3	17-Feb-23	22-Feb-23						Park. Lot - Install Catch Basins							
1269	MEP.D2.1800	Park. Lot - Street Light Conduits	2	2	23-Feb-23	24-Feb-23						Park. Lot - Street Light Conduits							
1270	CONC.D2.137	Park. Lot - Install Curbs & Inlets	3	3	23-Feb-23	27-Feb-23						Park. Lot - Install Curbs & Inlets							
1271	CONC.D2.138	Park. Lot - Street Light Bases	5	5	27-Feb-23	03-Mar-23						Park. Lot - Street Light Bases							
1272	FOND.D2.157	Park. Lot - Fine Grade Parking Lot	2	2	06-Mar-23	07-Mar-23						Park. Lot - Fine Grade Parking Lot							
1273	ASPV.D2.1000	Park. Lot - 1st Lift Asphalt - DC2	2	2	08-Mar-23	09-Mar-23						Park. Lot - 1st Lift Asphalt - DC2							
1274	CONC.D2.139	Park. Lot - Sidewalks	3	3	10-Mar-23	14-Mar-23						Park. Lot - Sidewalks							
1275	ASPV.D2.1010	Park. Lot - 2nd Lift Asphalt	1	1	15-Mar-23	15-Mar-23						Park. Lot - 2nd Lift Asphalt							
1276	CONC.D2.140	Park. Lot - Wheel Stops	1	1	16-Mar-23	16-Mar-23						Park. Lot - Wheel Stops							
1277	CONC.D2.141	Park. Lot - Strip	1	1	16-Mar-23	16-Mar-23						Park. Lot - Strip							
1278	FNSH.D2.1670	Park. Lot - Signage	1	1	16-Mar-23	16-Mar-23						Park. Lot - Signage							
1279	Landscape and Fencing			15	15	10-Mar-23	30-Mar-23						30-Mar-23, Landscape and Fencing						
1280	CONC.D2.142	Land Scp. - Site Concrete for Fence - DC2	3	3	10-Mar-23	14-Mar-23						Land Scp. - Site Concrete for Fence - DC2							
1281	FNSH.D2.1690	Land Scp. - Landscape Power and Irrigation	10	10	15-Mar-23	28-Mar-23						Land Scp. - Landscape Power and Irrigation							
1282	FNSH.D2.1700	Land Scp. - Fill Planters	2	2	15-Mar-23	16-Mar-23						Land Scp. - Fill Planters							
1283	FNSH.D2.1720	Land Scp. - Ground Cover	5	5	15-Mar-23	21-Mar-23						Land Scp. - Ground Cover							
1284	FNSH.D2.1780	Land Scp. - Install Fence	7	7	15-Mar-23	23-Mar-23						Land Scp. - Install Fence							
1285	FNSH.D2.1710	Land Scp. - Plantings	5	5	17-Mar-23	23-Mar-23						Land Scp. - Plantings							
1286	FNSH.D2.1790	Land Scp. - Gates and Access Control	5	5	24-Mar-23	30-Mar-23						Land Scp. - Gates and Access Control							
1287	1st Floor Data Hall			139	139	14-Sep-22	05-Apr-23						05-Apr-23, 1st Floor Data Hall						
1288	House			124	124	14-Sep-22	15-Mar-23						15-Mar-23, House						
1289	Rough-In			104	104	14-Sep-22	14-Feb-23						14-Feb-23, Rough-In						
1290	FRME.D2.1	1st Floor House - Layout and Frame Walls	10	10	14-Sep-22	27-Sep-22						1st Floor House - Layout and Frame Walls							

█ Remaining Level of Effort █ Remaining Work ◆ Milestone
█ Actual Work █ Critical Remaining Work ▼ Summary

QTS HIL2 DC2, DC3, DC5 Construction Schedule				Classic Schedule Layout					12-Jul-22 15:36										
#	Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	2022					2023					2024		
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2		
1291	FRME.D2.1	1st Floor House - Install Door Frames	3	3	28-Sep-22	30-Sep-22						1st Floor House - Install Door Frames							
1292	MEP.D2.3C	1st Floor House - Install Fire Protection	10	10	17-Nov-22	02-Dec-22						1st Floor House - Install Fire Protection							
1293	MEP.D2.3C	1st Floor House - Install OH Mechanical (Plumbing and HVAC)	20	20	17-Nov-22	16-Dec-22						1st Floor House - Install OH Mechanical (Plumbing and HVAC)							
1294	MEP.D2.3C	1st Floor House - Install OH Electrical	20	20	17-Nov-22	16-Dec-22						1st Floor House - Install OH Electrical							
1295	FRME.D2.1	1st Floor House - Install Drywall Upper	4	4	10-Jan-23	13-Jan-23						1st Floor House - Install Drywall Upper							
1296	MEP.D2.3C	1st Floor House - In-wall Rough-in Electrical	4	4	16-Jan-23	19-Jan-23						1st Floor House - In-wall Rough-in Electrical							
1297	FRME.D2.1	1st Floor House - Install Structural Grid	10	10	16-Jan-23	27-Jan-23						1st Floor House - Install Structural Grid							
1298	FRME.D2.1	1st Floor House - Insulate and Inspect	5	5	20-Jan-23	26-Jan-23						1st Floor House - Insulate and Inspect							
1299	FRME.D2.1	1st Floor House - Hang and Tape Drywall	6	6	27-Jan-23	03-Feb-23						1st Floor House - Hang and Tape Drywall							
1300	MEP.D2.3C	1st Floor House - Install Lighting	5	5	30-Jan-23	03-Feb-23						1st Floor House - Install Lighting							
1301	MEP.D2.3C	1st Floor House - Install Sprinkler Drops	5	5	30-Jan-23	03-Feb-23						1st Floor House - Install Sprinkler Drops							
1302	FNSH.D2.3	1st Floor House - Paint House	2	2	06-Feb-23	07-Feb-23						1st Floor House - Paint House							
1303	FRME.D2.1	1st Floor House - Install Overhead Doors	5	5	06-Feb-23	10-Feb-23						1st Floor House - Install Overhead Doors							
1304	FNSH.D2.3	1st Floor House - Install Finishes	5	5	08-Feb-23	14-Feb-23						1st Floor House - Install Finishes							
1305	FNSH.D2.3	1st Floor House - Trim Out Electrical Devices	5	5	08-Feb-23	14-Feb-23						1st Floor House - Trim Out Electrical Devices							
1306	Equipment			25	25	08-Feb-23	15-Mar-23						15-Mar-23, Equipment						
1307	EQPT.D2.3	1st Floor House - Set CRAC Units		7	5	08-Feb-23	14-Feb-23						1st Floor House - Set CRAC Units						
1308	EQPT.D2.3	1st Floor House - Install HDP Panels	10	10	08-Feb-23	22-Feb-23						1st Floor House - Install HDP Panels							
1309	EQPT.D2.3	1st Floor House - Install COD Boards	5	5	08-Feb-23	14-Feb-23						1st Floor House - Install COD Boards							
1310	EQPT.D2.3	1st Floor House - Install PDU	5	5	08-Feb-23	14-Feb-23						1st Floor House - Install PDU							
1311	EQPT.D2.3	1st Floor House - Set HUM	5	5	15-Feb-23	22-Feb-23						1st Floor House - Set HUM							
1312	EQPT.D2.3	1st Floor House - Final Connections CRAC Units	15	15	23-Feb-23	15-Mar-23						1st Floor House - Final Connections CRAC Units							
1313	MPOE 1 and 2			87	87	07-Nov-22	15-Mar-23						15-Mar-23, MPOE 1 and 2						
1314	Rough-In			67	67	07-Nov-22	14-Feb-23						14-Feb-23, Rough-In						
1315	FRME.D2.1	1st Floor MPOE 1/2 - Layout and Frame Walls	10	10	07-Nov-22	21-Nov-22						1st Floor MPOE 1/2 - Layout and Frame Walls							
1316	MEP.D2.12	1st Floor MPOE 1/2 - Install Fire Protection	10	10	17-Nov-22	02-Dec-22						1st Floor MPOE 1/2 - Install Fire Protection							
1317	MEP.D2.13	1st Floor MPOE 1/2 - Install OH Mechanical (Plumbing and HVAC)	20	20	17-Nov-22	16-Dec-22						1st Floor MPOE 1/2 - Install OH Mechanical (Plumbing and HVAC)							
1318	MEP.D2.13	1st Floor MPOE 1/2 - Install OH Electrical	20	20	17-Nov-22	16-Dec-22						1st Floor MPOE 1/2 - Install OH Electrical							
1319	FRME.D2.1	1st Floor MPOE 1/2 - Install Door Frames	3	3	22-Nov-22	28-Nov-22						1st Floor MPOE 1/2 - Install Door Frames							
1320	FRME.D2.1	1st Floor MPOE 1/2 - Install Drywall Upper	4	4	10-Jan-23	13-Jan-23						1st Floor MPOE 1/2 - Install Drywall Upper							
1321	MEP.D2.12	1st Floor MPOE 1/2 - In-wall Rough-in Electrical	4	4	16-Jan-23	19-Jan-23						1st Floor MPOE 1/2 - In-wall Rough-in Electrical							
1322	FRME.D2.1	1st Floor MPOE 1/2 - Install Structural Grid	10	10	16-Jan-23	27-Jan-23						1st Floor MPOE 1/2 - Install Structural Grid							
1323	FRME.D2.1	1st Floor MPOE 1/2 - Insulate and Inspect	5	5	20-Jan-23	26-Jan-23						1st Floor MPOE 1/2 - Insulate and Inspect							
1324	FRME.D2.1	1st Floor MPOE 1/2 - Hang and Tape Drywall	6	6	27-Jan-23	03-Feb-23						1st Floor MPOE 1/2 - Hang and Tape Drywall							
1325	MEP.D2.18	1st Floor MPOE 1/2 - Install Lighting	5	5	30-Jan-23	03-Feb-23						1st Floor MPOE 1/2 - Install Lighting							
1326	MEP.D2.18	1st Floor MPOE 1/2 - Install Sprinkler Drops	5	5	30-Jan-23	03-Feb-23						1st Floor MPOE 1/2 - Install Sprinkler Drops							
1327	FNSH.D2.1	1st Floor MPOE 1/2 - Paint MPOE	2	2	06-Feb-23	07-Feb-23						1st Floor MPOE 1/2 - Paint MPOE							
1328	FRME.D2.1	1st Floor MPOE 1/2 - Install Overhead Doors	5	5	06-Feb-23	10-Feb-23						1st Floor MPOE 1/2 - Install Overhead Doors							
1329	FNSH.D2.1	1st Floor MPOE 1/2 - Install Finishes	5	5	08-Feb-23	14-Feb-23						1st Floor MPOE 1/2 - Install Finishes							
1330	FNSH.D2.1	1st Floor MPOE 1/2 - Trim Out Electrical Devices	5	5	08-Feb-23	14-Feb-23						1st Floor MPOE 1/2 - Trim Out Electrical Devices							
1331	Equipment			25	25	08-Feb-23	15-Mar-23						15-Mar-23, Equipment						
1332	EQPT.D2.1	1st Floor MPOE 1/2 - Set CRAC Units		7	5	08-Feb-23	14-Feb-23						1st Floor MPOE 1/2 - Set CRAC Units						
1333	EQPT.D2.1	1st Floor MPOE 1/2 - Install HDP Panels	10	10	08-Feb-23	22-Feb-23						1st Floor MPOE 1/2 - Install HDP Panels							
1334	EQPT.D2.1	1st Floor MPOE 1/2 - Install COD Boards	5	5	08-Feb-23	14-Feb-23						1st Floor MPOE 1/2 - Install COD Boards							
1335	EQPT.D2.2	1st Floor MPOE 1/2 - Install Network COD 2000AMP	10	10	08-Feb-23	22-Feb-23						1st Floor MPOE 1/2 - Install Network COD 2000AMP							
1336	EQPT.D2.1	1st Floor MPOE 1/2 - Set HUM		5	5	15-Feb-23	22-Feb-23						1st Floor MPOE 1/2 - Set HUM						
1337	EQPT.D2.1	1st Floor MPOE 1/2 - Final Connections CRAC Units	15	15	23-Feb-23	15-Mar-23						1st Floor MPOE 1/2 - Final Connections CRAC Units							

Remaining Level of Effort
Actual Work

Remaining Work
Critical Remaining Work





QTS HIL2 DC2, DC3, DC5 Construction Schedule				Classic Schedule Layout					12-Jul-22 15:36									
#	Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish		Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2
1338	EQPT.D2.1	1st Floor MPOE 1/2 - Install PDU	5	5	23-Feb-23	01-Mar-23							1st Floor MPOE 1/2 - Install PDU					
1339	Systems Gallery 1001 and 1010 DH A			102	102	03-Oct-22	02-Mar-23						02-Mar-23, Systems Gallery 1001 and 1010 DH A					
1340	Rough-In			80	80	03-Oct-22	30-Jan-23						30-Jan-23, Rough-In					
1341	MEP.D2.14	1st Floor DHA SG1001/1010 - Install Fire Protection	15	15	03-Oct-22	24-Oct-22							1st Floor DHA SG1001/1010 - Install Fire Protection					
1342	MEP.D2.15	1st Floor DHA SG1001/1010 - Install OH Mechanical (Plumbing and HVAC)	20	15	25-Oct-22	15-Nov-22							1st Floor DHA SG1001/1010 - Install OH Mechanical (Plumbing and HVAC)					
1343	MEP.D2.15	1st Floor DHA SG1001/1010 - Install OH Electrical	20	20	25-Oct-22	22-Nov-22							1st Floor DHA SG1001/1010 - Install OH Electrical					
1344	FRME.D2.1	1st Floor DHA SG1001/1010 - Layout and Frame Walls	6	6	28-Dec-22	05-Jan-23							1st Floor DHA SG1001/1010 - Layout and Frame Walls					
1345	FRME.D2.1	1st Floor DHA SG1001/1010 - Install Drywall Upper	6	6	30-Dec-22	09-Jan-23							1st Floor DHA SG1001/1010 - Install Drywall Upper					
1346	MEP.D2.14	1st Floor DHA SG1001/1010 - In-wall Rough-in Electrical	5	5	30-Dec-22	06-Jan-23							1st Floor DHA SG1001/1010 - In-wall Rough-in Electrical					
1347	FRME.D2.1	1st Floor DHA SG1001/1010 - Insulate and Inspect	5	5	09-Jan-23	13-Jan-23							1st Floor DHA SG1001/1010 - Insulate and Inspect					
1348	FRME.D2.1	1st Floor DHA SG1001/1010 - Hang and Tape Drywall	6	6	16-Jan-23	23-Jan-23							1st Floor DHA SG1001/1010 - Hang and Tape Drywall					
1349	FNSH.D2.1	1st Floor DHA SG1001/1010 - Paint - DHA SG	2	2	24-Jan-23	25-Jan-23							1st Floor DHA SG1001/1010 - Paint - DHA SG					
1350	FNSH.D2.1	1st Floor DHA SG1001/1010 - Install Finishes	3	3	26-Jan-23	30-Jan-23							1st Floor DHA SG1001/1010 - Install Finishes					
1351	Equipment			33	33	16-Jan-23	02-Mar-23						02-Mar-23, Equipment					
1352	EQPT.D2.1	1st Floor DHA SG1001/1010 - Install COD Boards	5	5	16-Jan-23	20-Jan-23							1st Floor DHA SG1001/1010 - Install COD Boards					
1353	EQPT.D2.1	1st Floor DHA SG1001/1010 - Install Switch Gear	5	5	24-Jan-23	30-Jan-23							1st Floor DHA SG1001/1010 - Install Switch Gear					
1354	EQPT.D2.1	1st Floor DHA SG1001/1010 - Install ATS	5	5	24-Jan-23	30-Jan-23							1st Floor DHA SG1001/1010 - Install ATS					
1355	EQPT.D2.1	1st Floor DHA SG1001/1010 - Install PDU	5	5	24-Jan-23	30-Jan-23							1st Floor DHA SG1001/1010 - Install PDU					
1356	EQPT.D2.1	1st Floor DHA SG1001/1010 - Install Reserve Busway	5	5	24-Jan-23	30-Jan-23							1st Floor DHA SG1001/1010 - Install Reserve Busway					
1357	EQPT.D2.1	1st Floor DHA SG1001/1010 - Install HDP	5	5	26-Jan-23	01-Feb-23							1st Floor DHA SG1001/1010 - Install HDP					
1358	EQPT.D2.1	1st Floor DHA SG1001/1010 - Pull and Terminate Feeders	15	15	31-Jan-23	21-Feb-23							1st Floor DHA SG1001/1010 - Pull and Terminate Feeders					
1359	EQPT.D2.1	1st Floor DHA SG1001/1010 - Install CRAC Units	7	5	02-Feb-23	08-Feb-23							1st Floor DHA SG1001/1010 - Install CRAC Units					
1360	EQPT.D2.1	1st Floor DHA SG1001/1010 - Final Connections CRAC Units	15	15	09-Feb-23	02-Mar-23							1st Floor DHA SG1001/1010 - Final Connections CRAC Units					
1361	Mechanical Gallery 1002 DH A			105	105	19-Sep-22	21-Feb-23						21-Feb-23, Mechanical Gallery 1002 DH A					
1362	Rough-In			42	42	19-Sep-22	17-Nov-22						17-Nov-22, Rough-In					
1363	MEP.D2.14	1st Floor DHA MG1002 - Install Fire Protection	1	1	19-Sep-22	19-Sep-22							1st Floor DHA MG1002 - Install Fire Protection					
1364	MEP.D2.14	1st Floor DHA MG1002 - Install OH Mechanical (Plumbing and HVAC)	20	3	19-Sep-22	21-Sep-22							1st Floor DHA MG1002 - Install OH Mechanical (Plumbing and HVAC)					
1365	MEP.D2.14	1st Floor DHA MG1002 - Install OH Electrical	5	5	19-Sep-22	23-Sep-22							1st Floor DHA MG1002 - Install OH Electrical					
1366	MEP.D2.14	1st Floor DHA MG1002 - In-wall Rough-in Electrical	3	3	20-Sep-22	22-Sep-22							1st Floor DHA MG1002 - In-wall Rough-in Electrical					
1367	FRME.D2.1	1st Floor DHA MG1002 - Insulate and Inspect	5	5	23-Sep-22	29-Sep-22							1st Floor DHA MG1002 - Insulate and Inspect					
1368	FRME.D2.1	1st Floor DHA MG1002 - Layout and Frame Walls	6	6	17-Oct-22	24-Oct-22							1st Floor DHA MG1002 - Layout and Frame Walls					
1369	FRME.D2.1	1st Floor DHA MG1002 - Install Drywall Upper	6	6	25-Oct-22	01-Nov-22							1st Floor DHA MG1002 - Install Drywall Upper					
1370	FRME.D2.1	1st Floor DHA MG1002 - Hang and Tape Drywall	6	6	02-Nov-22	09-Nov-22							1st Floor DHA MG1002 - Hang and Tape Drywall					
1371	FNSH.D2.1	1st Floor DHA MG1002 - Paint	2	2	10-Nov-22	14-Nov-22							1st Floor DHA MG1002 - Paint					
1372	FNSH.D2.1	1st Floor DHA MG1002 - Install Finishes	3	3	15-Nov-22	17-Nov-22							1st Floor DHA MG1002 - Install Finishes					
1373	Equipment			38	38	28-Dec-22	21-Feb-23						21-Feb-23, Equipment					
1374	EQPT.D2.1	1st Floor DHA MG1002 - Install HDP Boards	5	5	28-Dec-22	04-Jan-23							1st Floor DHA MG1002 - Install HDP Boards					
1375	EQPT.D2.1	1st Floor DHA MG1002 - Pull and Terminate Feeders	15	15	05-Jan-23	25-Jan-23							1st Floor DHA MG1002 - Pull and Terminate Feeders					
1376	EQPT.D2.1	1st Floor DHA MG1002 - Install CRAC Units	7	5	24-Jan-23	30-Jan-23							1st Floor DHA MG1002 - Install CRAC Units					
1377	EQPT.D2.1	1st Floor DHA MG1002 - Final Connections CRAC Units	15	15	31-Jan-23	21-Feb-23							1st Floor DHA MG1002 - Final Connections CRAC Units					
1378	DH A ROOM 1100			41	41	25-Oct-22	23-Dec-22						23-Dec-22, DH A ROOM 1100					
1379	Rough-In			41	41	25-Oct-22	23-Dec-22						23-Dec-22, Rough-In					
1380	FRME.D2.1	1st Floor DHA R1100 - Layout and Frame Walls	10	10	25-Oct-22	07-Nov-22							1st Floor DHA R1100 - Layout and Frame Walls					
1381	FRME.D2.1	1st Floor DHA R1100 - Install Drywall Upper	4	4	08-Nov-22	14-Nov-22							1st Floor DHA R1100 - Install Drywall Upper					
1382	MEP.D2.13	1st Floor DHA R1100 - Rough-In Fire Protection	3	3	15-Nov-22	17-Nov-22							1st Floor DHA R1100 - Rough-In Fire Protection					
1383	MEP.D2.13	1st Floor DHA R1100 - In-wall Rough-in Electrical	4	4	15-Nov-22	18-Nov-22							1st Floor DHA R1100 - In-wall Rough-in Electrical					
1384	MEP.D2.13	1st Floor DHA R1100 - Install OH Mechanical (Plumbing and HVAC)	20	5	21-Nov-22	29-Nov-22							1st Floor DHA R1100 - Install OH Mechanical (Plumbing and HVAC)					
1385	FRME.D2.1	1st Floor DHA R1100 - Insulate and Inspect	5	5	2													


QTS HIL2 DC2, DC3, DC5 Construction Schedule				Classic Schedule Layout						12-Jul-22 15:37							
#	Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	2022					2023				2024	
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2
1434	MEP.D2.13	1st Floor DHD R1200 - Install Fire Protection	3	3	23-Feb-23	27-Feb-23										1st Floor DHD R1200 - Install Fire Protection	
1435		1st Floor DHD R1200 - In-wall Rough-in Electrical	4	4	23-Feb-23	28-Feb-23										1st Floor DHD R1200 - In-wall Rough-in Electrical	
1436		1st Floor DHD R1200 - Install OH Mechanical (Plumbing and HVAC)	5	5	01-Mar-23	07-Mar-23										1st Floor DHD R1200 - Install OH Mechanical (Plumbing and HVAC)	
1437		FRME.D2.1	1st Floor DHD R1200 - Insulate and Inspect	5	5	01-Mar-23	07-Mar-23									1st Floor DHD R1200 - Insulate and Inspect	
1438		MEP.D2.13	1st Floor DHD R1200 - Install OH Electrical	7	7	08-Mar-23	16-Mar-23									1st Floor DHD R1200 - Install OH Electrical	
1439		FRME.D2.1	1st Floor DHD R1200 - Hang and Tape Drywall	6	6	17-Mar-23	24-Mar-23									1st Floor DHD R1200 - Hang and Tape Drywall	
1440		FRME.D2.1	1st Floor DHD R1200 - Install Structural Grid	10	10	17-Mar-23	30-Mar-23									1st Floor DHD R1200 - Install Structural Grid	
1441		FNSH.D2.1	1st Floor DHD R1200 - Paint	2	2	27-Mar-23	28-Mar-23									1st Floor DHD R1200 - Paint	
1442		PROC.PW.	1st Floor DHD R1200 - Install Finishes	3	3	29-Mar-23	31-Mar-23									1st Floor DHD R1200 - Install Finishes	
1443	2nd Floor Data Hall			135	135	04-Oct-22	19-Apr-23									19-Apr-23, 2nd Floor Data Hall	
1444	BDF 1 and 2			102	102	13-Oct-22	13-Mar-23									13-Mar-23, BDF 1 and 2	
1445	Rough-In			40	40	13-Oct-22	12-Dec-22									12-Dec-22, Rough-In	
1446	MEP.D2.10	2nd Floor BDF1/2 - Install Fire Protection	3	3	13-Oct-22	17-Oct-22										2nd Floor BDF1/2 - Install Fire Protection	
1447	MEP.D2.10	2nd Floor BDF1/2 - Install OH Mechanical (Plumbing and HVAC)	20	5	18-Oct-22	24-Oct-22										Everywhere there is a CRAC Unit	Plumbing and HVAC)
1448	MEP.D2.10	2nd Floor BDF1/2 - Install OH Electrical	7	7	18-Oct-22	26-Oct-22										2nd Floor BDF1/2 - Install OH Electrical	
1449	FRME.D2.1	2nd Floor BDF1/2 - Layout and Frame Walls	10	10	27-Oct-22	09-Nov-22										2nd Floor BDF1/2 - Layout and Frame Walls	
1450	FRME.D2.1	2nd Floor BDF1/2 - Install Drywall Upper	4	4	10-Nov-22	16-Nov-22										2nd Floor BDF1/2 - Install Drywall Upper	
1451	MEP.D2.10	2nd Floor BDF1/2 - In-wall Rough-in Electrical	4	4	10-Nov-22	16-Nov-22										2nd Floor BDF1/2 - In-wall Rough-in Electrical	
1452	FRME.D2.1	2nd Floor BDF1/2 - Install Structural Grid	10	10	17-Nov-22	02-Dec-22										2nd Floor BDF1/2 - Install Structural Grid	
1453	FRME.D2.1	2nd Floor BDF1/2 - Insulate and Inspect	5	5	17-Nov-22	23-Nov-22										2nd Floor BDF1/2 - Insulate and Inspect	
1454	FRME.D2.1	2nd Floor BDF1/2 - Hang and Tape Drywall	6	6	28-Nov-22	05-Dec-22										2nd Floor BDF1/2 - Hang and Tape Drywall	
1455	FNSH.D2.1	2nd Floor BDF1/2 - Paint	2	2	06-Dec-22	07-Dec-22										2nd Floor BDF1/2 - Paint	
1456	FNSH.D2.1	2nd Floor BDF1/2 - Install Finishes	3	3	08-Dec-22	12-Dec-22										2nd Floor BDF1/2 - Install Finishes	
1457	Equipment			65	65	08-Dec-22	13-Mar-23									13-Mar-23, Equipment	
1458	EQPT.D2.1	2nd Floor BDF1/2 - Install HDP Panels	10	10	08-Dec-22	21-Dec-22										2nd Floor BDF1/2 - Install HDP Panels	
1459	EQPT.D2.1	2nd Floor BDF1/2 - Set CRAC's	7	5	06-Feb-23	10-Feb-23										2nd Floor BDF1/2 - Set CRAC's	
1460	EQPT.D2.1	2nd Floor BDF1/2 - Set HUM	5	5	13-Feb-23	17-Feb-23										2nd Floor BDF1/2 - Set HUM	
1461	EQPT.D2.1	2nd Floor BDF1/2 - Final Connections CRAC Units	15	15	13-Feb-23	06-Mar-23										2nd Floor BDF1/2 - Final Connections CRAC Units	
1462	EQPT.D2.1	2nd Floor BDF1/2 - Pull and Terminate Feeders	15	15	21-Feb-23	13-Mar-23										2nd Floor BDF1/2 - Pull and Terminate Feeders	
1463	Systems Gallery 2001 and 2010 DH B			100	100	04-Oct-22	01-Mar-23									01-Mar-23, Systems Gallery 2001 and 2010 DH B	
1464	Rough-In			79	79	04-Oct-22	30-Jan-23									30-Jan-23, Rough-In	
1465	MEP.D2.12	2nd Floor DHB SG 2001/2010 - Install Fire Protection	5	5	04-Oct-22	11-Oct-22										2nd Floor DHB SG 2001/2010 - Install Fire Protection	
1466	MEP.D2.12	2nd Floor DHB SG 2001/2010 - Install OH Mechanical (Plumbing and HVAC)	20	15	12-Oct-22	01-Nov-22										2nd Floor DHB SG 2001/2010 - Install OH Mechanical (Plumbing and HVAC)	
1467	MEP.D2.12	2nd Floor DHB SG 2001/2010 - Install OH Electrical	20	20	12-Oct-22	08-Nov-22										2nd Floor DHB SG 2001/2010 - Install OH Electrical	
1468	FRME.D2.1	2nd Floor DHB SG 2001/2010 - Layout and Frame Walls	6	6	28-Dec-22	05-Jan-23										2nd Floor DHB SG 2001/2010 - Layout and Frame Walls	
1469	MEP.D2.12	2nd Floor DHB SG 2001/2010 - In-wall Rough-in Electrical	3	3	30-Dec-22	04-Jan-23										2nd Floor DHB SG 2001/2010 - In-wall Rough-in Electrical	
1470	FRME.D2.1	2nd Floor DHB SG 2001/2010 - Insulate and Inspect	5	5	05-Jan-23	11-Jan-23										2nd Floor DHB SG 2001/2010 - Insulate and Inspect	
1471	FRME.D2.1	2nd Floor DHB SG 2001/2010 - Install Drywall Upper	6	6	06-Jan-23	13-Jan-23										2nd Floor DHB SG 2001/2010 - Install Drywall Upper	
1472	FRME.D2.1	2nd Floor DHB SG 2001/2010 - Hang and Tape Drywall	6	6	16-Jan-23	23-Jan-23										2nd Floor DHB SG 2001/2010 - Hang and Tape Drywall	
1473	FNSH.D2.1	2nd Floor DHB SG 2001/2010 - Paint	2	2	24-Jan-23	25-Jan-23										2nd Floor DHB SG 2001/2010 - Paint	
1474	FNSH.D2.1	2nd Floor DHB SG 2001/2010 - Install Finishes	3	3	26-Jan-23	30-Jan-23										2nd Floor DHB SG 2001/2010 - Install Finishes	
1475	Equipment			41	41	03-Jan-23	01-Mar-23									01-Mar-23, Equipment	
1476	EQPT.D2.1	2nd Floor DHB SG 2001/2010 - Install Switch Gear	5	5	03-Jan-23	09-Jan-23										2nd Floor DHB SG 2001/2010 - Install Switch Gear	
1477	EQPT.D2.1	2nd Floor DHB SG 2001/2010 - Install ATS	5	5	03-Jan-23	09-Jan-23										2nd Floor DHB SG 2001/2010 - Install ATS	
1478	EQPT.D2.1	2nd Floor DHB SG 2001/2010 - Install HDP	5	5	03-Jan-23	09-Jan-23										2nd Floor DHB SG 2001/2010 - Install HDP	
1479	EQPT.D2.1	2nd Floor DHB SG 2001/2010 - Install PDU	5	5	03-Jan-23	09-Jan-23										2nd Floor DHB SG 2001/2010 - Install PDU	
1480	EQPT.D2.1	2nd Floor DHB SG 2001/2010 - Install Reserve Busway	5	5	03-Jan-23	09-Jan-23										2nd Floor DHB SG 2001/2010 - Install Reserve Busway	
1481	EQPT.D2.1</td																

QTS HIL2 DC2, DC3, DC5 Construction Schedule				Classic Schedule Layout					12-Jul-22 15:37									
#	Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	2022					2023				2024		
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	
1482		EQPT.D2.1 2nd Floor DHB SG 2001/2010 - Pull and Terminate Feeders	15	15	23-Jan-23	10-Feb-23												2nd Floor DHB SG 2001/2010 - Pull and Terminate Feeders
1483		EQPT.D2.1 2nd Floor DHB SG 2001/2010 - Install CRAC Units		7	5	01-Feb-23	07-Feb-23											2nd Floor DHB SG 2001/2010 - Install CRAC Units
1484		EQPT.D2.1 2nd Floor DHB SG 2001/2010 - Final Connections CRAC Units		15	15	08-Feb-23	01-Mar-23											2nd Floor DHB SG 2001/2010 - Final Connections CRAC Units
1485		Mechanical Gallery 2002 DH B	100	100	04-Oct-22	01-Mar-23												Cant energize until equipment is connected
1486		Rough-In		85	85	04-Oct-22	07-Feb-23											01-Mar-23, Mechanical Gallery 2002 DH B
1487		FRME.D2.1 2nd Floor DHB MG 2002 - Layout and Frame Walls		6	6	04-Oct-22	12-Oct-22											07-Feb-23, Rough-In
1488		MEP.D2.11 2nd Floor DHB MG 2002 - Install Fire Protection		1	1	04-Oct-22	04-Oct-22											2nd Floor DHB MG 2002 - Layout and Frame Walls
1489		MEP.D2.11 2nd Floor DHB MG 2002 - Install OH Mechanical (Plumbing and HVAC)		20	3	04-Oct-22	06-Oct-22											2nd Floor DHB MG 2002 - Install Fire Protection
1490		MEP.D2.11 2nd Floor DHB MG 2002 - Install OH Electrical		5	5	04-Oct-22	11-Oct-22											2nd Floor DHB MG 2002 - Install OH Mechanical (Plumbing and HVAC)
1491		MEP.D2.11 2nd Floor DHB MG 2002 - In-wall Rough-in Electrical		3	3	05-Oct-22	07-Oct-22											2nd Floor DHB MG 2002 - Install OH Electrical
1492		FRME.D2.1 2nd Floor DHB MG 2002 - Insulate and Inspect		5	5	11-Oct-22	17-Oct-22											2nd Floor DHB MG 2002 - In-wall Rough-in Electrical
1493		FRME.D2.1 2nd Floor DHB MG 2002 - Install Drywall Upper		6	6	13-Oct-22	20-Oct-22											2nd Floor DHB MG 2002 - Insulate and Inspect
1494		FRME.D2.1 2nd Floor DHB MG 2002 - Hang and Tape Drywall		6	6	24-Jan-23	31-Jan-23											2nd Floor DHB MG 2002 - Install Drywall Upper
1495		FNSH.D2.1 2nd Floor DHB MG 2002 - Paint		2	2	01-Feb-23	02-Feb-23											2nd Floor DHB MG 2002 - Hang and Tape Drywall
1496		FNSH.D2.1 2nd Floor DHB MG 2002 - Install Finishes		3	3	03-Feb-23	07-Feb-23											2nd Floor DHB MG 2002 - Paint
1497		Equipment		20	20	01-Feb-23	01-Mar-23											2nd Floor DHB MG 2002 - Install Finishes
1498		EQPT.D2.1 2nd Floor DHB MG 2002 - Install CRAC Units		7	5	01-Feb-23	07-Feb-23											01-Mar-23, Equipment
1499		EQPT.D2.1 2nd Floor DHB MG 2002 - Install HDP Boards		5	5	01-Feb-23	07-Feb-23											2nd Floor DHB MG 2002 - Install CRAC Units
1500		EQPT.D2.1 2nd Floor DHB MG 2002 - Final Connections CRAC Units		15	15	08-Feb-23	01-Mar-23											2nd Floor DHB MG 2002 - Install HDP Boards
1501		EQPT.D2.1 2nd Floor DHB MG 2002 - Pull and Terminate Feeders		15	15	08-Feb-23	01-Mar-23											2nd Floor DHB MG 2002 - Final Connections CRAC Units
1502		DH B ROOM 2100		85	85	13-Oct-22	15-Feb-23											2nd Floor DHB MG 2002 - Pull and Terminate Feeders
1503		Rough-In		85	85	13-Oct-22	15-Feb-23											15-Feb-23, DH B ROOM 2100
1504		FRME.D2.1 2nd Floor DHB R2100 - Layout and Frame Walls		10	10	13-Oct-22	26-Oct-22											15-Feb-23, Rough-In
1505		MEP.D2.10 2nd Floor DHB R2100 - Install Fire Protection		3	3	13-Oct-22	17-Oct-22											2nd Floor DHB R2100 - Layout and Frame Walls
1506		MEP.D2.10 2nd Floor DHB R2100 - Install OH Electrical		7	7	13-Oct-22	21-Oct-22											2nd Floor DHB R2100 - Install Fire Protection
1507		FRME.D2.1 2nd Floor DHB R2100 - Install Structural Grid		10	10	24-Oct-22	04-Nov-22											2nd Floor DHB R2100 - Install OH Electrical
1508		FRME.D2.1 2nd Floor DHB R2100 - Install Drywall Upper		4	4	27-Oct-22	01-Nov-22											2nd Floor DHB R2100 - Install Structural Grid
1509		MEP.D2.10 2nd Floor DHB R2100 - In-wall Rough-in Electrical		4	4	02-Nov-22	07-Nov-22											2nd Floor DHB R2100 - Install Drywall Upper
1510		FRME.D2.1 2nd Floor DHB R2100 - Insulate and Inspect		5	5	08-Nov-22	15-Nov-22											2nd Floor DHB R2100 - In-wall Rough-in Electrical
1511		FRME.D2.1 2nd Floor DHB R2100 - Hang and Tape Drywall		6	6	01-Feb-23	08-Feb-23											2nd Floor DHB R2100 - Insulate and Inspect
1512		FNSH.D2.1 2nd Floor DHB R2100 - Paint		2	2	09-Feb-23	10-Feb-23											2nd Floor DHB R2100 - Hang and Tape Drywall
1513		FNSH.D2.1 2nd Floor DHB R2100 - Install Finishes		3	3	13-Feb-23	15-Feb-23											2nd Floor DHB R2100 - Paint
1514		Systems Gallery 2020 and 2003 DH C		94	94	06-Dec-22	19-Apr-23											2nd Floor DHB R2100 - Install Finishes
1515		Rough-In		59	59	06-Dec-22	01-Mar-23											19-Apr-23, Systems Gallery 2020 and 2003 DH C
1516		MEP.D2.12 2nd Floor DHC 2020/2003 - Install Fire Protection		5	5	06-Dec-22	12-Dec-22											01-Mar-23, Rough-In
1517		MEP.D2.12 2nd Floor DHC 2020/2003 - Install OH Mechanical (Plumbing and HVAC)		20	15	13-Dec-22	04-Jan-23											2nd Floor DHC 2020/2003 - Install Fire Protection
1518		MEP.D2.12 2nd Floor DHC 2020/2003 - Install OH Electrical		20	20	13-Dec-22	11-Jan-23											2nd Floor DHC 2020/2003 - Install OH Mechanical (Plumbing and HVAC)
1519		FRME.D2.1 2nd Floor DHC 2020/2003 - Layout and Frame Walls		6	6	17-Jan-23	24-Jan-23											2nd Floor DHC 2020/2003 - Install OH Electrical
1520		FRME.D2.1 2nd Floor DHC 2020/2003 - Install Drywall Upper		6	6	25-Jan-23	01-Feb-23											2nd Floor DHC 2020/2003 - Layout and Frame Walls
1521		MEP.D2.12 2nd Floor DHC 2020/2003 - In-wall Rough-in Electrical		3	3	02-Feb-23	06-Feb-23											2nd Floor DHC 2020/2003 - Install Drywall Upper
1522		FRME.D2.1 2nd Floor DHC 2020/2003 - Insulate and Inspect		5	5	07-Feb-23	13-Feb-23											2nd Floor DHC 2020/2003 - In-wall Rough-in Electrical
1523		FRME.D2.1 2nd Floor DHC 2020/2003 - Hang and Tape Drywall		6	6	14-Feb-23	22-Feb-23											2nd Floor DHC 2020/2003 - Insulate and Inspect
1524		FNSH.D2.1 2nd Floor DHC 2020/2003 - Paint		2	2	23-Feb-23	24-Feb-23											2nd Floor DHC 2020/2003 - Hang and Tape Drywall
1525		FNSH.D2.1 2nd Floor DHC 2020/2003 - Install Finishes		3	3	27-Feb-23	01-Mar-23											2nd Floor DHC 2020/2003 - Paint
1526		Equipment		66	66	17-Jan-23	19-Apr-23											2nd Floor DHC 2020/2003 - Install Finishes
1527		EQPT.D2.1 2nd Floor DHC 2020/2003 - Install ATS		5	5	17-Jan-23	23-Jan-23											19-Apr-23, Equipment
1528		EQPT.D2.1 2nd Floor DHC 2020/2003 - Install HDP		5	5	17-Jan-23	23-Jan-23											2nd Floor DHC 2020/2003 - Install ATS
1529																		

QTS HIL2 DC2, DC3, DC5 Construction Schedule				Classic Schedule Layout					12-Jul-22 15:37								
#	Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	2022					2023				2024	
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2
1530	EQPT.D2.1	EQPT.D2.1	5	5	17-Jan-23	23-Jan-23										2nd Floor DHC 2020/2003 - Install Reserve Busway	
1531		2nd Floor DHC 2020/2003 - Install COD Boards	10	10	23-Feb-23	08-Mar-23										2nd Floor DHC 2020/2003 - Install COD Boards	
1532		2nd Floor DHC 2020/2003 - Install CRAC Units	7	5	23-Feb-23	01-Mar-23										2nd Floor DHC 2020/2003 - Install CRAC Units	
1533		2nd Floor DHC 2020/2003 - Final Connections CRAC Units	15	15	02-Mar-23	22-Mar-23										2nd Floor DHC 2020/2003 - Final Connections CRAC Units	
1534		2nd Floor DHC 2020/2003 - Install Switch Gear	5	5	09-Mar-23	15-Mar-23										2nd Floor DHC 2020/2003 - Install Switch Gear	
1535		2nd Floor DHC 2020/2003 - Pull and Terminate Feeders	25	25	16-Mar-23	19-Apr-23										2nd Floor DHC 2020/2003 - Pull and Terminate Feeders	
1536		Mechanical Gallery 2003 DH C	74	74	06-Dec-22	22-Mar-23										22-Mar-23, Mechanical Gallery 2003 DH C	
1537	Rough-In	Rough-In	30	30	06-Dec-22	18-Jan-23										18-Jan-23, Rough-In	
1538		FRME.D2.1	2nd Floor DHC MG 2003 - Layout and Frame Walls	5	5	06-Dec-22	12-Dec-22									2nd Floor DHC MG 2003 - Layout and Frame Walls	
1539		MEP.D2.11	2nd Floor DHC MG 2003 - Install Fire Protection	1	1	06-Dec-22	06-Dec-22									2nd Floor DHC MG 2003 - Install Fire Protection	
1540		MEP.D2.11	2nd Floor DHC MG 2003 - Install OH Mechanical (Plumbing and HVAC)	20	3	06-Dec-22	08-Dec-22									2nd Floor DHC MG 2003 - Install OH Mechanical (Plumbing and HVAC)	
1541		MEP.D2.11	2nd Floor DHC MG 2003 - Install OH Electrical	5	5	06-Dec-22	12-Dec-22									2nd Floor DHC MG 2003 - Install OH Electrical	
1542		MEP.D2.11	2nd Floor DHC MG 2003 - In-wall Rough-in Electrical	3	3	07-Dec-22	09-Dec-22									2nd Floor DHC MG 2003 - In-wall Rough-in Electrical	
1543		FRME.D2.1	2nd Floor DHC MG 2003 - Insulate and Inspect	5	5	12-Dec-22	16-Dec-22									2nd Floor DHC MG 2003 - Insulate and Inspect	
1544		FRME.D2.1	2nd Floor DHC MG 2003 - Install Drywall Upper	6	6	13-Dec-22	20-Dec-22									2nd Floor DHC MG 2003 - Install Drywall Upper	
1545		FRME.D2.1	2nd Floor DHC MG 2003 - Hang and Tape Drywall	6	6	21-Dec-22	29-Dec-22									2nd Floor DHC MG 2003 - Hang and Tape Drywall	
1546		FNSH.D2.1	2nd Floor DHC MG 2003 - Paint	2	2	30-Dec-22	03-Jan-23									2nd Floor DHC MG 2003 - Paint	
1547		FNSH.D2.1	2nd Floor DHC MG 2003 - Install Finishes	3	3	16-Jan-23	18-Jan-23									2nd Floor DHC MG 2003 - Install Finishes	
1548	Equipment	Equipment	55	55	04-Jan-23	22-Mar-23										22-Mar-23, Equipment	
1549		EQPT.D2.1	2nd Floor DHC MG 2003 - Ducting	4	4	04-Jan-23	09-Jan-23									2nd Floor DHC MG 2003 - Ducting	
1550		EQPT.D2.1	2nd Floor DHC MG 2003 - Install HDP Boards	5	5	17-Jan-23	23-Jan-23									2nd Floor DHC MG 2003 - Install HDP Boards	
1551		EQPT.D2.1	2nd Floor DHC MG 2003 - Pull and Terminate Feeders	15	15	24-Jan-23	13-Feb-23									2nd Floor DHC MG 2003 - Pull and Terminate Feeders	
1552		EQPT.D2.1	2nd Floor DHC MG 2003 - Install CRAC Units	7	5	23-Feb-23	01-Mar-23									2nd Floor DHC MG 2003 - Install CRAC Units	
1553		EQPT.D2.1	2nd Floor DHC MG 2003 - Final Connections CRAC Units	15	15	02-Mar-23	22-Mar-23									2nd Floor DHC MG 2003 - Final Connections CRAC Units	
1554	DH C ROOM 2200	DH C ROOM 2200	34	34	13-Dec-22	31-Jan-23										31-Jan-23, DH C ROOM 2200	
1555		Rough-In	34	34	13-Dec-22	31-Jan-23										31-Jan-23, Rough-In	
1556		FRME.D2.1	2nd Floor DHC R2200 - Layout and Frame Walls	10	10	13-Dec-22	27-Dec-22									2nd Floor DHC R2200 - Layout and Frame Walls	
1557		MEP.D2.1C	2nd Floor DHC R2200 - Install Fire Protection	3	3	13-Dec-22	15-Dec-22									2nd Floor DHC R2200 - Install Fire Protection	
1558		MEP.D2.11	2nd Floor DHC R2200 - Install OH Electrical	7	7	13-Dec-22	21-Dec-22									2nd Floor DHC R2200 - Install OH Electrical	
1559		FRME.D2.1	2nd Floor DHC R2200 - Install Structural Grid	10	10	22-Dec-22	06-Jan-23									2nd Floor DHC R2200 - Install Structural Grid	
1560		FRME.D2.1	2nd Floor DHC R2200 - Install Drywall Upper	4	4	28-Dec-22	03-Jan-23									2nd Floor DHC R2200 - Install Drywall Upper	
1561		MEP.D2.1C	2nd Floor DHC R2200 - In-wall Rough-in Electrical	4	4	04-Jan-23	09-Jan-23									2nd Floor DHC R2200 - In-wall Rough-in Electrical	
1562		FRME.D2.1	2nd Floor DHC R2200 - Insulate and Inspect	5	5	10-Jan-23	16-Jan-23									2nd Floor DHC R2200 - Insulate and Inspect	
1563		FRME.D2.1	2nd Floor DHC R2200 - Hang and Tape Drywall	6	6	17-Jan-23	24-Jan-23									2nd Floor DHC R2200 - Hang and Tape Drywall	
1564		FNSH.D2.1	2nd Floor DHC R2200 - Paint	2	2	25-Jan-23	26-Jan-23									2nd Floor DHC R2200 - Paint	
1565		FNSH.D2.1	2nd Floor DHC R2200 - Install Finishes	3	3	27-Jan-23	31-Jan-23									2nd Floor DHC R2200 - Install Finishes	
1566	Closeout and Final Inspections	Closeout and Final Inspections	78	78	02-Mar-23	20-Jun-23										20-Jun-23, Closeout and Final Inspections	
1567		PNCH.D2.1080	Punch DH B	15	15	02-Mar-23	22-Mar-23									Punch DH B	
1568		PNCH.D2.1070	Punch - DH A	15	15	03-Mar-23	23-Mar-23									Punch - DH A	
1569		PNCH.D2.1110	Punch House	15	15	17-Mar-23	06-Apr-23									Punch House	
1570		PNCH.D2.1090	Punch DH C	15	15	23-Mar-23	12-Apr-23									Punch DH C	
1571		PNCH.D2.1100	Punch DH D	15	15	03-Apr-23	21-Apr-23									Punch DH D	
1572		PNCH.D2.1020	Elevators Final Inspections	5	5	04-Apr-23	10-Apr-23									Elevators Final Inspections	
1573		PNCH.D2.1060	Punch MPOE/BDF	15	15	25-Apr-23	15-May-23									Punch MPOE/BDF	
1574		PNCH.D2.1000	Electrical Final Inspections - DC2	5	5	25-May-23	01-Jun-23									Electrical Final Inspections - DC2	
1575		PNCH.D2.1030	Fire and Life Safety Final Inspections	5	5	25-May-23	01-Jun-23									Fire and Life Safety Final Inspections	
1576		PNCH.D2.1050	Low Voltage Final Inspections	5	5	25-May-23	01-Jun-23									Low Voltage Final Inspections	
1577		PNCH.D2.1010	Mechanical Final Inspections	5	5	31-May-23	06-Jun-23									Mechanical Final Inspections	



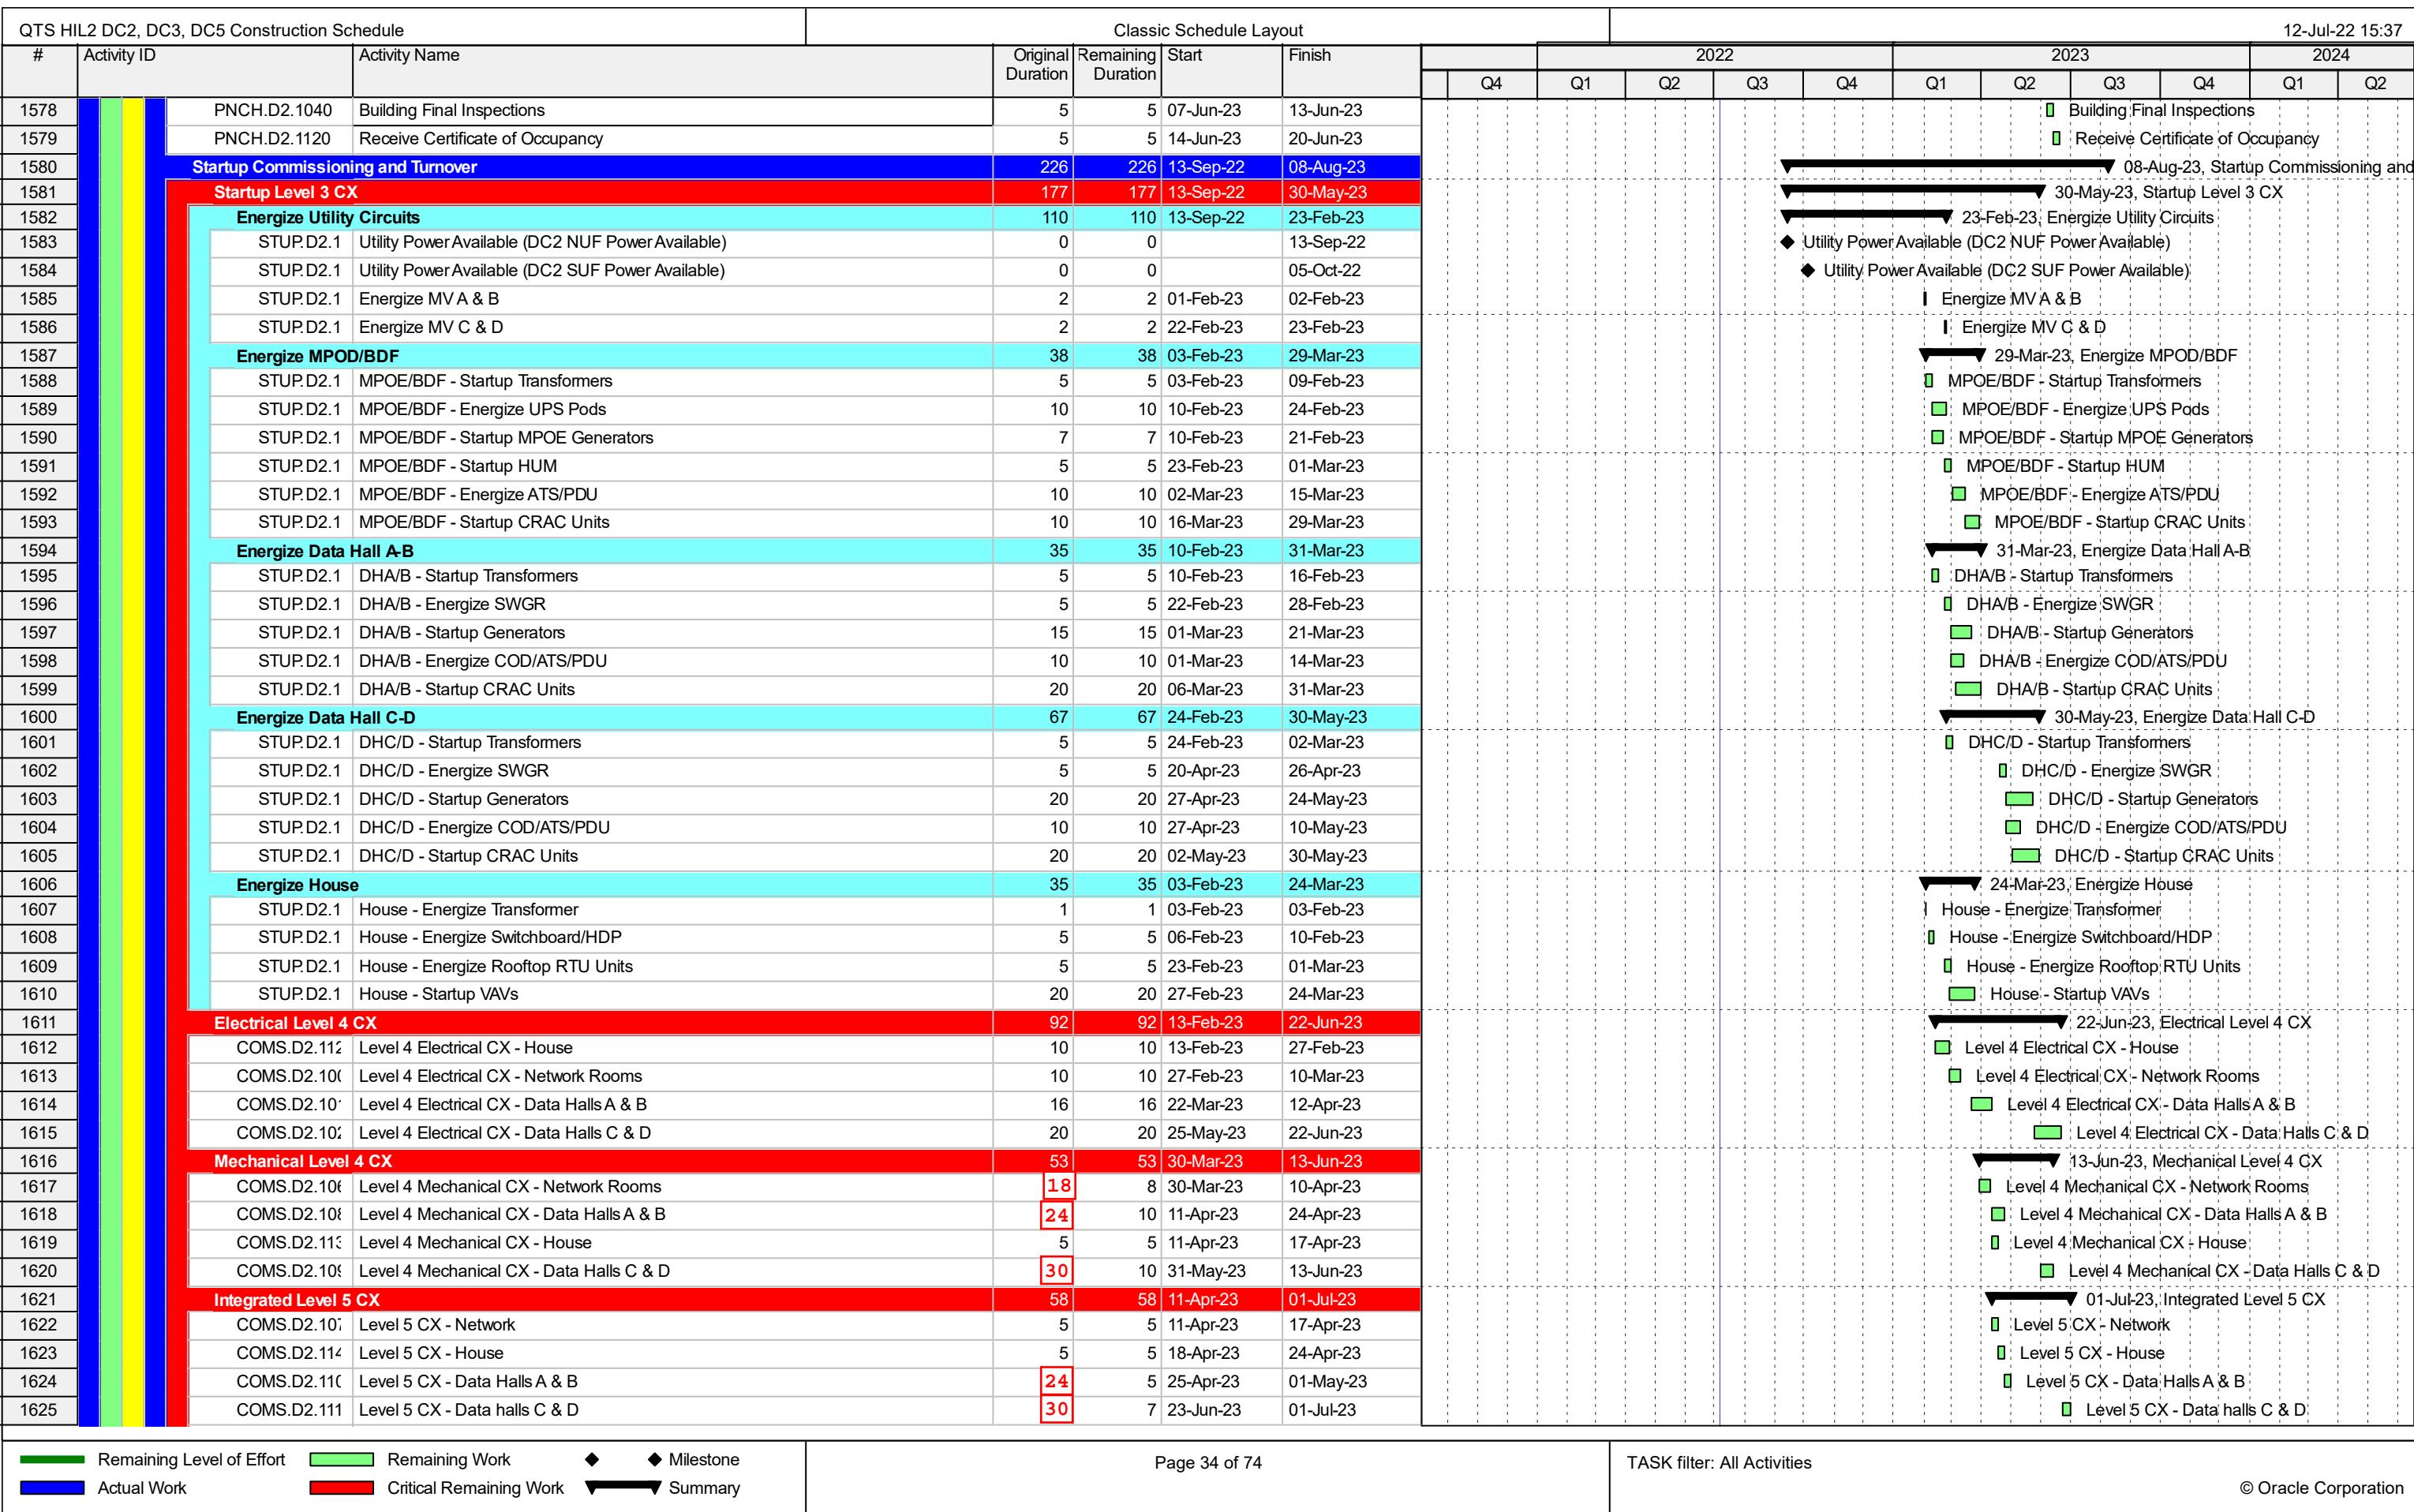

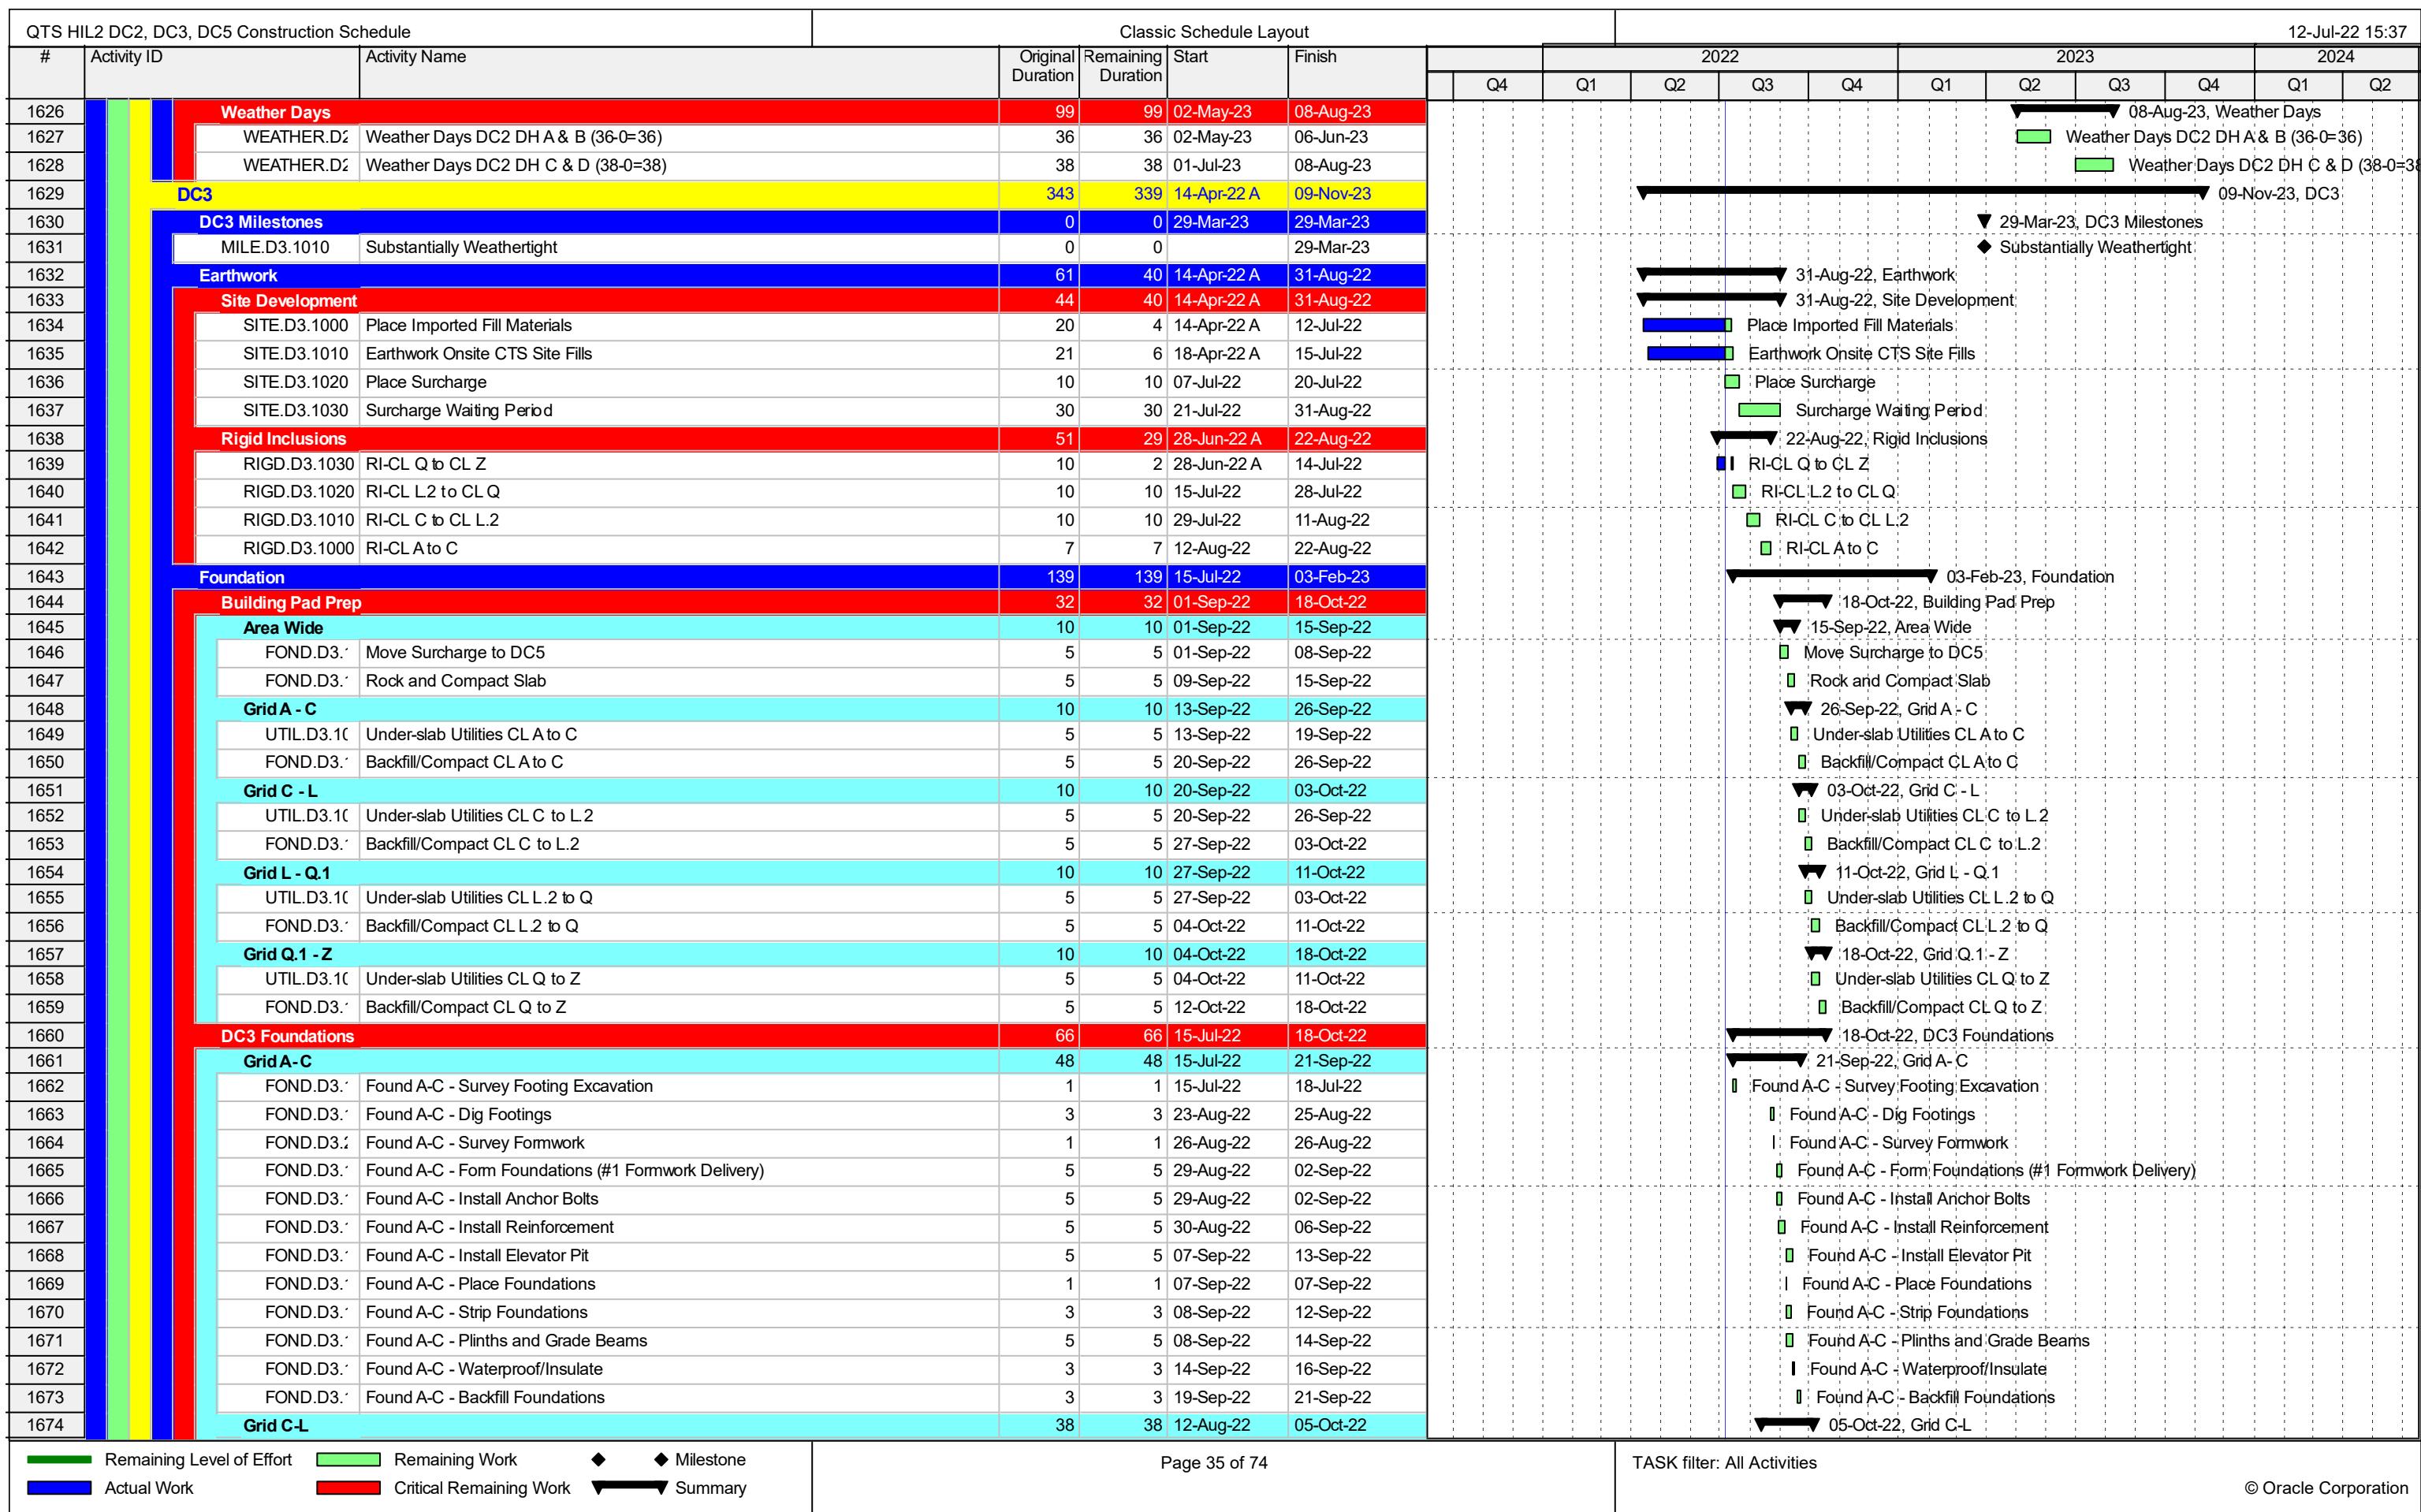

The legend consists of six items arranged horizontally. From left to right: a green bar labeled 'Remaining Level of Effort'; a light green bar labeled 'Remaining Work'; a black diamond symbol labeled 'Milestone'; a blue bar labeled 'Actual Work'; a red bar labeled 'Critical Remaining Work'; and a black arrow symbol labeled 'Summary'.

Page 36 of 74

TASK filter: All Activities

© Oracle Corporation


QTS HIL2 DC2, DC3, DC5 Construction Schedule				Classic Schedule Layout					12-Jul-22 15:37									
#	Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish			2022				2023				2024	
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	
1723	SOG.D3	SOG C-L P2 - Edgeforms/Diamonds	2	2	12-Oct-22	13-Oct-22					I	SOG C-L P2 - Edgeforms/Diamonds						
1724	SOG.D3	SOG C-L P2 - Vapor Barrier		1	1	14-Oct-22	14-Oct-22				I	SOG C-L P2 - Vapor Barrier						
1725	SOG.D3	SOG C-L P2 - Install reinforcement		3	3	17-Oct-22	19-Oct-22				I	SOG C-L P2 - Install reinforcement						
1726	SOG.D3	SOG C-L P2 - MEP Final Set		1	1	20-Oct-22	20-Oct-22				I	SOG C-L P2 - MEP Final Set						
1727	SOG.D3	SOG C-L P2 - Place SOG		1	1	21-Oct-22	21-Oct-22				I	SOG C-L P2 - Place SOG						
1728	SOG.D3	SOG C-L P2 - Cure SOG		5	5	24-Oct-22	28-Oct-22				I	SOG C-L P2 - Cure SOG						
1729	Pour 3			16	16	06-Oct-22	28-Oct-22						▼	28-Oct-22, Pour 3				
1730	SOG.D3	SOG C-L P3 - Fine Grade		3	3	06-Oct-22	11-Oct-22				I	SOG C-L P3 - Fine Grade						
1731	SOG.D3	SOG C-L P3 - Edgeforms/Diamonds		2	2	12-Oct-22	13-Oct-22				I	SOG C-L P3 - Edgeforms/Diamonds						
1732	SOG.D3	SOG C-L P3 - Vapor Barrier		1	1	14-Oct-22	14-Oct-22				I	SOG C-L P3 - Vapor Barrier						
1733	SOG.D3	SOG C-L P3 - Install reinforcement		3	3	17-Oct-22	19-Oct-22				I	SOG C-L P3 - Install reinforcement						
1734	SOG.D3	SOG C-L P3 - MEP Final Set		1	1	20-Oct-22	20-Oct-22				I	SOG C-L P3 - MEP Final Set						
1735	SOG.D3	SOG C-L P3 - Place SOG		1	1	21-Oct-22	21-Oct-22				I	SOG C-L P3 - Place SOG						
1736	SOG.D3	SOG C-L P3 - Cure SOG		5	5	24-Oct-22	28-Oct-22				I	SOG C-L P3 - Cure SOG						
1737	Grid L-Q.1			16	16	12-Oct-22	02-Nov-22						▼	02-Nov-22, Grid L-Q.1				
1738	Pour 4			16	16	12-Oct-22	02-Nov-22						▼	02-Nov-22, Pour 4				
1739	SOG.D3	SOG L-Q.1 P4 - Fine Grade		3	3	12-Oct-22	14-Oct-22				I	SOG L-Q.1 P4 - Fine Grade						
1740	SOG.D3	SOG L-Q.1 P4 - Edgeforms/Diamonds		2	2	17-Oct-22	18-Oct-22				I	SOG L-Q.1 P4 - Edgeforms/Diamonds						
1741	SOG.D3	SOG L-Q.1 P4 - Vapor Barrier		1	1	19-Oct-22	19-Oct-22				I	SOG L-Q.1 P4 - Vapor Barrier						
1742	SOG.D3	SOG L-Q.1 P4 - Install reinforcement		3	3	20-Oct-22	24-Oct-22				I	SOG L-Q.1 P4 - Install reinforcement						
1743	SOG.D3	SOG L-Q.1 P4 - MEP Final Set		1	1	25-Oct-22	25-Oct-22				I	SOG L-Q.1 P4 - MEP Final Set						
1744	SOG.D3	SOG L-Q.1 P4 - Place SOG		1	1	26-Oct-22	26-Oct-22				I	SOG L-Q.1 P4 - Place SOG						
1745	SOG.D3	SOG L-Q.1 P4 - Cure SOG		5	5	27-Oct-22	02-Nov-22				I	SOG L-Q.1 P4 - Cure SOG						
1746	Grid Q.1-Z			16	16	19-Oct-22	09-Nov-22						▼	09-Nov-22, Grid Q.1-Z				
1747	Pour 5			16	16	19-Oct-22	09-Nov-22						▼	09-Nov-22, Pour 5				
1748	SOG.D3	SOG Q.1-Z P5 - Fine Grade		3	3	19-Oct-22	21-Oct-22				I	SOG Q.1-Z P5 - Fine Grade						
1749	SOG.D3	SOG Q.1-Z P5 - Edgeforms/Diamonds		2	2	24-Oct-22	25-Oct-22				I	SOG Q.1-Z P5 - Edgeforms/Diamonds						
1750	SOG.D3	SOG Q.1-Z P5 - Vapor Barrier		1	1	26-Oct-22	26-Oct-22				I	SOG Q.1-Z P5 - Vapor Barrier						
1751	SOG.D3	SOG Q.1-Z P5 - Install reinforcement		3	3	27-Oct-22	31-Oct-22				I	SOG Q.1-Z P5 - Install reinforcement						
1752	SOG.D3	SOG Q.1-Z P5 - MEP Final Set		1	1	01-Nov-22	01-Nov-22				I	SOG Q.1-Z P5 - MEP Final Set						
1753	SOG.D3	SOG Q.1-Z P5 - Place SOG		1	1	02-Nov-22	02-Nov-22				I	SOG Q.1-Z P5 - Place SOG						
1754	SOG.D3	SOG Q.1-Z P5 - Cure SOG		5	5	03-Nov-22	09-Nov-22				I	SOG Q.1-Z P5 - Cure SOG						
1755	Pour 6			16	16	19-Oct-22	09-Nov-22						▼	09-Nov-22, Pour 6				
1756	SOG.D3	SOG Q.1-Z P6 - Fine Grade		3	3	19-Oct-22	21-Oct-22				I	SOG Q.1-Z P6 - Fine Grade						
1757	SOG.D3	SOG Q.1-Z P6 - Edgeforms/Diamonds		2	2	24-Oct-22	25-Oct-22				I	SOG Q.1-Z P6 - Edgeforms/Diamonds						
1758	SOG.D3	SOG Q.1-Z P6 - Vapor Barrier		1	1	26-Oct-22	26-Oct-22				I	SOG Q.1-Z P6 - Vapor Barrier						
1759	SOG.D3	SOG Q.1-Z P6 - Install reinforcement		3	3	27-Oct-22	31-Oct-22				I	SOG Q.1-Z P6 - Install reinforcement						
1760	SOG.D3	SOG Q.1-Z P6 - MEP Final Set		1	1	01-Nov-22	01-Nov-22				I	SOG Q.1-Z P6 - MEP Final Set						
1761	SOG.D3	SOG Q.1-Z P6 - Place SOG		1	1	02-Nov-22	02-Nov-22				I	SOG Q.1-Z P6 - Place SOG						
1762	SOG.D3	SOG Q.1-Z P6 - Cure SOG		5	5	03-Nov-22	09-Nov-22				I	SOG Q.1-Z P6 - Cure SOG						
1763	Leave Out			49	49	23-Nov-22	03-Feb-23						▼	03-Feb-23, Leave Out				
1764	Leave Out Pour 1 C-F.4			16	16	23-Nov-22	16-Dec-22						▼	16-Dec-22, Leave Out Pour 1 C-F.4				
1765	SOG.D3	SOG Leave Out P2 - Fine Grade CL C-F.4		3	3	23-Nov-22	29-Nov-22				I	SOG Leave Out P2 - Fine Grade CL C-F.4						
1766	SOG.D3	SOG Leave Out P2 - Edgeforms/Diamonds		2	2	30-Nov-22	01-Dec-22				I	SOG Leave Out P2 - Edgeforms/Diamonds						
1767	SOG.D3	SOG Leave Out P2 - Vapor Barrier		1	1	02-Dec-22	02-Dec-22				I	SOG Leave Out P2 - Vapor Barrier						
1768	SOG.D3	SOG Leave Out P2 - Install reinforcement		3	3	05-Dec-22	07-Dec-22				I	SOG Leave Out P2 - Install reinforcement						
1769	SOG.D3	SOG Leave Out P2 - MEP Final Set		1	1	08-Dec-22	08-Dec-22				I	SOG Leave Out P2 - MEP Final Set						
1770	SOG.D3	SOG Leave Out P2 - Place SOG		1	1	09-Dec-22	09-Dec-22				I	SOG Leave Out P2 - Place SOG						
Remaining Level of Effort				Remaining Work	◆	◆ Milestone	Page 37 of 74					TASK filter: All Activities					© Oracle Corporation	
Actual Work				Critical Remaining Work	▼	Summary												

QTS HIL2 DC2, DC3, DC5 Construction Schedule				Classic Schedule Layout						12-Jul-22 15:37							
#	Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	2022					2023				2024	
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2
1771	SOG.D3	SOG Leave Out P2 - Cure SOG	5	5	12-Dec-22	16-Dec-22											
1772	Leave Out Pour 2 F.4-J.8			16	16	01-Dec-22	22-Dec-22										
1773	SOG.D3	SOG Leave Out P3 - Fine Grade CL F.4-J.8	3	3	01-Dec-22	05-Dec-22											
1774	SOG.D3	SOG Leave Out P3 - Edgeforms/Diamonds	2	2	06-Dec-22	07-Dec-22											
1775	SOG.D3	SOG Leave Out P3 - Vapor Barrier	1	1	08-Dec-22	08-Dec-22											
1776	SOG.D3	SOG Leave Out P3 - Install reinforcement	3	3	09-Dec-22	13-Dec-22											
1777	SOG.D3	SOG Leave Out P3 - MEP Final Set	1	1	14-Dec-22	14-Dec-22											
1778	SOG.D3	SOG Leave Out P3 - Place SOG	1	1	15-Dec-22	15-Dec-22											
1779	SOG.D3	SOG Leave Out P3 - Cure SOG	5	5	16-Dec-22	22-Dec-22											
1780	Leave Out Pour 3 J.8-M.5			16	16	09-Dec-22	03-Jan-23										
1781	SOG.D3	SOG Leave Out P4 - Fine Grade CL J.8-M.5	3	3	09-Dec-22	13-Dec-22											
1782	SOG.D3	SOG Leave Out P4 - Edgeforms/Diamonds	2	2	14-Dec-22	15-Dec-22											
1783	SOG.D3	SOG Leave Out P4 - Vapor Barrier	1	1	16-Dec-22	16-Dec-22											
1784	SOG.D3	SOG Leave Out P4 - Install reinforcement	3	3	19-Dec-22	21-Dec-22											
1785	SOG.D3	SOG Leave Out P4 - MEP Final Set	1	1	22-Dec-22	22-Dec-22											
1786	SOG.D3	SOG Leave Out P4 - Place SOG	1	1	23-Dec-22	23-Dec-22											
1787	SOG.D3	SOG Leave Out P4 - Cure SOG	5	5	27-Dec-22	03-Jan-23											
1788	Leave Out Pour 4 M.5-Q			16	16	06-Jan-23	27-Jan-23										
1789	SOG.D3	SOG Leave Out P5 - Fine Grade M.5-Q	3	3	06-Jan-23	10-Jan-23											
1790	SOG.D3	SOG Leave Out P5 - Edgeforms/Diamonds	2	2	11-Jan-23	12-Jan-23											
1791	SOG.D3	SOG Leave Out P5 - Vapor Barrier	1	1	13-Jan-23	13-Jan-23											
1792	SOG.D3	SOG Leave Out P5 - Install reinforcement	3	3	16-Jan-23	18-Jan-23											
1793	SOG.D3	SOG Leave Out P5 - MEP Final Set	1	1	19-Jan-23	19-Jan-23											
1794	SOG.D3	SOG Leave Out P5 - Place SOG	1	1	20-Jan-23	20-Jan-23											
1795	SOG.D3	SOG Leave Out P5 - Cure SOG	5	5	23-Jan-23	27-Jan-23											
1796	Leave Out Pour 5 Q-Z			21	21	06-Jan-23	03-Feb-23										
1797	SOG.D3	SOG Leave Out P6 - Fine Grade CL Q-Z	3	3	06-Jan-23	10-Jan-23											
1798	SOG.D3	SOG Leave Out P6 - Edgeforms/Diamonds	2	2	11-Jan-23	12-Jan-23											
1799	SOG.D3	SOG Leave Out P6 - Vapor Barrier	1	1	13-Jan-23	13-Jan-23											
1800	SOG.D3	SOG Leave Out P6 - Install reinforcement	3	3	16-Jan-23	18-Jan-23											
1801	SOG.D3	SOG Leave Out P6 - MEP Final Set	1	1	19-Jan-23	19-Jan-23											
1802	SOG.D3	SOG Leave Out P6 - Place SOG	1	1	20-Jan-23	20-Jan-23											
1803	SOG.D3	SOG Leave Out P6 - Cure SOG	5	5	30-Jan-23	03-Feb-23											
1804	DC3 SOMD			45	45	08-Nov-22	16-Jan-23										
1805	A-Z			45	45	08-Nov-22	16-Jan-23										
1806	Grid A - C			9	9	08-Nov-22	21-Nov-22										
1807	Pour 1 A - C			9	9	08-Nov-22	21-Nov-22										
1808	SOM	SOMD A-C P1 - As-Built Structure	1	1	08-Nov-22	08-Nov-22											
1809	SOM	SOMD A-C P1 - MEP	3	3	09-Nov-22	14-Nov-22											
1810	SOM	SOMD A-C P1 - Edgeforms/Embeds	3	3	09-Nov-22	14-Nov-22											
1811	SOM	SOMD A-C P1 - Install Reinforcement	3	3	15-Nov-22	17-Nov-22											
1812	SOM	SOMD A-C P1 - MEP Final	1	1	18-Nov-22	18-Nov-22											
1813	SOM	SOMD A-C P1 - Place Slab	1	1	21-Nov-22	21-Nov-22											
1814	Grid C - L			17	17	21-Nov-22	15-Dec-22										
1815	Pour 2 C - F.4			7	7	21-Nov-22	01-Dec-22										
1816	SOM	SOMD C-F.4 P2 - MEP	2	2	21-Nov-22	22-Nov-22											
1817	SOM	SOMD C-F.4 P2 - Edgeforms/Embeds	2	2	21-Nov-22	22-Nov-22											
1818	SOM	SOMD C-F.4 P2 - Install Reinforcement	3	3	23-Nov-22	29-Nov-22											
Remaining Level of Effort				Remaining Work				Milestone				TASK filter: All Activities				© Oracle Corporation	
Actual Work				Critical Remaining Work				Summary									

QTS HIL2 DC2, DC3, DC5 Construction Schedule				Classic Schedule Layout					12-Jul-22 15:37										
#	Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	2022					2023					2024		
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2		
1819	SOM	SOMD C-F.4 P2 - MEP Final	1	1	30-Nov-22	30-Nov-22						I	SOMD C-F.4 P2 -MEP Final						
1820	SOM	SOMD C-F.4 P2 - Place Slab	1	1	01-Dec-22	01-Dec-22						I	SOMD C-F.4 P2 -Place Slab						
1821	Pour 3 F.4 - J.8						7	7	29-Nov-22	07-Dec-22						▼	07-Dec-22, Pour 3 F.4 - J.8		
1822	SOM	SOMD F.4-J.8 P3 - MEP	2	2	29-Nov-22	30-Nov-22						I	SOMD F.4-J.8 P3 - MEP						
1823	SOM	SOMD F.4-J.8 P3 - Edgeforms/Embeds	2	2	29-Nov-22	30-Nov-22						I	SOMD F.4-J.8 P3 - Edgeforms/Embeds						
1824	SOM	SOMD F.4-J.8 P3 - Install Reinforcement	3	3	01-Dec-22	05-Dec-22						I	SOMD F.4-J.8 P3 - Install Reinforcement						
1825	SOM	SOMD F.4-J.8 P3 - MEP Final	1	06-Dec-22	06-Dec-22							I	SOMD F.4-J.8 P3 - MEP Final						
1826	SOM	SOMD F.4-J.8 P3 - Place Slab	1	1	07-Dec-22	07-Dec-22						I	SOMD F.4-J.8 P3 - Place Slab						
1827	Pour 4 J.8 - M.5						7	7	07-Dec-22	15-Dec-22						▼	15-Dec-22, Pour 4 J.8 - M.5		
1828	SOM	SOMD J.8-M.5 P4 - MEP	2	2	07-Dec-22	08-Dec-22						I	SOMD J.8-M.5 P4 - MEP						
1829	SOM	SOMD J.8-M.5 P4 - Edgeforms/Embeds	2	2	07-Dec-22	08-Dec-22						I	SOMD J.8-M.5 P4 - Edgeforms/Embeds						
1830	SOM	SOMD J.8-M.5 P4 - Install Reinforcement	3	3	09-Dec-22	13-Dec-22						I	SOMD J.8-M.5 P4 - Install Reinforcement						
1831	SOM	SOMD J.8-M.5 P4 - MEP Final	1	1	14-Dec-22	14-Dec-22						I	SOMD J.8-M.5 P4 - MEP Final						
1832	SOM	SOMD J.8-M.5 P4 - Place Slab	1	1	15-Dec-22	15-Dec-22						I	SOMD J.8-M.5 P4 -Place Slab						
1833	Grid L - Q.1						7	7	13-Dec-22	21-Dec-22						▼	21-Dec-22, Grid L - Q.1		
1834	Pour 5 M.5 - Q						7	7	13-Dec-22	21-Dec-22						▼	21-Dec-22, Pour 5 M.5 - Q		
1835	SOM	SOMD M.5-Q P5 - MEP	2	2	13-Dec-22	14-Dec-22						I	SOMD M.5-Q P5 - MEP						
1836	SOM	SOMD M.5-Q P5 - Edgeforms/Embeds	2	2	13-Dec-22	14-Dec-22						I	SOMD M.5-Q P5 - Edgeforms/Embeds						
1837	SOM	SOMD M.5-Q P5 - Install Reinforcement	3	3	15-Dec-22	19-Dec-22						I	SOMD M.5-Q P5 - Install Reinforcement						
1838	SOM	SOMD M.5-Q P5 - MEP Final	1	1	20-Dec-22	20-Dec-22						I	SOMD M.5-Q P5 - MEP Final						
1839	SOM	SOMD M.5-Q P5 - Place Slab	1	1	21-Dec-22	21-Dec-22						I	SOMD M.5-Q P5 - Place Slab						
1840	Grid Q.1 - Z						13	13	28-Dec-22	16-Jan-23						▼	16-Jan-23, Grid Q.1 - Z		
1841	Pour 6 Q - T.3						8	8	28-Dec-22	09-Jan-23						▼	09-Jan-23, Pour 6 Q - T.3		
1842	SOM	SOMD Q-T.3 P6 - As-Built Structure	1	1	28-Dec-22	28-Dec-22						I	SOMD Q-T.3 P6 - As-Built Structure						
1843	SOM	SOMD Q-T.3 P6 - MEP	2	2	29-Dec-22	30-Dec-22						I	SOMD Q-T.3 P6 - MEP						
1844	SOM	SOMD Q-T.3 P6 - Edgeforms/Embeds	2	2	29-Dec-22	30-Dec-22						I	SOMD Q-T.3 P6 - Edgeforms/Embeds						
1845	SOM	SOMD Q-T.3 P6 - Install Reinforcement	3	3	03-Jan-23	05-Jan-23						I	SOMD Q-T.3 P6 - Install Reinforcement						
1846	SOM	SOMD Q-T.3 P6 - MEP Final	1	1	06-Jan-23	06-Jan-23						I	SOMD Q-T.3 P6 - MEP Final						
1847	SOM	SOMD Q-T.3 P6 - Place Slab	1	1	09-Jan-23	09-Jan-23						I	SOMD Q-T.3 P6- Place Slab						
1848	Pour 7 T.3 - W.3						7	7	04-Jan-23	12-Jan-23						▼	12-Jan-23, Pour 7 T.3 - W.3		
1849	SOM	SOMD T.3-W.3 P7 - MEP	2	2	04-Jan-23	05-Jan-23						I	SOMD T.3-W.3 P7 - MEP						
1850	SOM	SOMD T.3-W.3 P7 - Edgeforms/Embeds	2	2	04-Jan-23	05-Jan-23						I	SOMD T.3-W.3 P7 - Edgeforms/Embeds						
1851	SOM	SOMD T.3-W.3 P7 - Install Reinforcement	3	3	06-Jan-23	10-Jan-23						I	SOMD T.3-W.3 P7 - Install Reinforcement						
1852	SOM	SOMD T.3-W.3 P7 - MEP Final	1	1	11-Jan-23	11-Jan-23						I	SOMD T.3-W.3 P7 - MEP Final						
1853	SOM	SOMD T.3-W.3 P7 - Place Slab	1	1	12-Jan-23	12-Jan-23						I	SOMD T.3-W.3 P7 - Place Slab						
1854	Pour 8 W.3 - Z						7	7	06-Jan-23	16-Jan-23						▼	16-Jan-23, Pour 8 W.3 -Z		
1855	SOM	SOMD W.3-Z P8 - MEP	2	2	06-Jan-23	09-Jan-23						I	SOMD W.3-Z P8 - MEP						
1856	SOM	SOMD W.3-Z P8 - Edgeforms/Embeds	2	2	06-Jan-23	09-Jan-23						I	SOMD W.3-Z P8 - Edgeforms/Embeds						
1857	SOM	SOMD W.3-Z P8 - Install Reinforcement	3	3	10-Jan-23	12-Jan-23						I	SOMD W.3-Z P8 - Install Reinforcement						
1858	SOM	SOMD W.3-Z P8 - MEP Final	1	1	13-Jan-23	13-Jan-23						I	SOMD W.3-Z P8 - MEP Final						
1859	SOM	SOMD W.3-Z P8 - Place Slab	1	1	16-Jan-23	16-Jan-23						I	SOMD W.3-Z P8 - Place Slab						
1860	Steel						78	78	31-Oct-22	23-Feb-23						►	23-Feb-23, Steel		
1861	Steel Erection						44	44	31-Oct-22	05-Jan-23						►	05-Jan-23, Steel Erection		
1862	ERCT.D3.1290	Erect Steel - Sequence 11		3	3	31-Oct-22	02-Nov-22						I	Erect Steel - Sequence 11					
1863	ERCT.D3.1310	Erect Steel - Sequence 12		3	3	03-Nov-22	07-Nov-22						I	Erect Steel - Sequence 12					
1864	ERCT.D3.1300	Erect Steel - Sequence 21		2	2	08-Nov-22	09-Nov-22						I	Erect Steel - Sequence 21					
1865	ERCT.D3.1350	Erect Steel - Sequence 31		2	2	10-Nov-22	14-Nov-22						I	Erect Steel - Sequence 31					
1866	ERCT.D3.1320	Erect Steel - Sequence 22		2	2	15-Nov-22	16-Nov-22						I	Erect Steel - Sequence 22	</td				

QTS HIL2 DC2, DC3, DC5 Construction Schedule				Classic Schedule Layout					12-Jul-22 15:37										
#	Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	2022					2023					2024		
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2		
1867	ERCT.D3.1360	Erect Steel - Sequence 32	2	2	17-Nov-22	18-Nov-22						I	Erect Steel - Sequence 32						
1868	ERCT.D3.1330	Erect Steel - Sequence 23	2	2	21-Nov-22	22-Nov-22						I	Erect Steel - Sequence 23						
1869	ERCT.D3.1370	Erect Steel - Sequence 33	2	2	23-Nov-22	28-Nov-22						■	Erect Steel - Sequence 33						
1870	ERCT.D3.1340	Erect Steel - Sequence 24	3	3	29-Nov-22	01-Dec-22						■	Erect Steel - Sequence 24						
1871	ERCT.D3.1380	Erect Steel - Sequence 34	3	3	02-Dec-22	06-Dec-22						■	Erect Steel - Sequence 34						
1872	ERCT.D3.1390	Erect Steel - Sequence 25	2	2	07-Dec-22	08-Dec-22						I	Erect Steel - Sequence 25						
1873	ERCT.D3.1430	Erect Steel - Sequence 35	2	2	09-Dec-22	12-Dec-22						■	Erect Steel - Sequence 35						
1874	ERCT.D3.1400	Erect Steel - Sequence 26	3	3	13-Dec-22	15-Dec-22						I	Erect Steel - Sequence 26						
1875	ERCT.D3.1440	Erect Steel - Sequence 36	3	3	16-Dec-22	20-Dec-22						■	Erect Steel - Sequence 36						
1876	ERCT.D3.1410	Erect Steel - Sequence 27	2	2	21-Dec-22	22-Dec-22						I	Erect Steel - Sequence 27						
1877	ERCT.D3.1450	Erect Steel - Sequence 37	2	2	23-Dec-22	27-Dec-22						■	Erect Steel - Sequence 37						
1878	ERCT.D3.1420	Erect Steel - Sequence 28	2	2	28-Dec-22	29-Dec-22						I	Erect Steel - Sequence 28						
1879	ERCT.D3.1460	Erect Steel - Sequence 38	2	2	30-Dec-22	03-Jan-23						■	Erect Steel - Sequence 38						
1880	ERCT.D3.1470	Erect Steel - Sequence 40	2	2	04-Jan-23	05-Jan-23						I	Erect Steel - Sequence 40						
1881	Stairs			75	75	03-Nov-22	23-Feb-23						23-Feb-23	Stairs					
1882	ERCT.D3.1240	Stair 1 (S Loading Dock)	2	2	03-Nov-22	04-Nov-22						I	Stair 1 (S Loading Dock)						
1883	ERCT.D3.1250	Stair 2 (Admin)	2	2	08-Nov-22	09-Nov-22						I	Stair 2 (Admin)						
1884	ERCT.D3.1280	Stair 3 (Back of House)	2	2	06-Jan-23	09-Jan-23						■	Stair 3 (Back of House)						
1885	ERCT.D3.1260	Exterior Equipment Yard (2 Sets)	10	10	17-Jan-23	30-Jan-23						■	Exterior Equipment Yard (2 Sets)						
1886	ERCT.D3.1270	Exterior Exit Stair (2 Sets)	10	10	09-Feb-23	23-Feb-23						■	Exterior Exit Stair (2 Sets)						
1887	Precast			30	30	12-Jan-23	23-Feb-23						23-Feb-23	Precast					
1888	PCST.D3.1100	Precast - CL Q to L.2 - East Elevation	3	3	12-Jan-23	16-Jan-23						■	Precast - CL Q to L.2 - East Elevation						
1889	PCST.D3.1110	Precast - CL L.2 to C.1 - East Elevation	3	3	17-Jan-23	19-Jan-23						■	Precast - CL L.2 to C.1 - East Elevation						
1890	PCST.D3.1120	Precast - CL C.1 to A - East Elevation	2	2	20-Jan-23	23-Jan-23						■	Precast - CL C.1 to A - East Elevation						
1891	PCST.D3.1130	Precast - CL 8 to 1 - South Elevation	4	4	24-Jan-23	27-Jan-23						■	Precast - CL 8 to 1 - South Elevation						
1892	PCST.D3.1140	Precast - CL A to C.1 - West Elevation	2	2	30-Jan-23	31-Jan-23						■	Precast - CL A to C.1 - West Elevation						
1893	PCST.D3.1150	Precast - CL C.1 to L.2 - West Elevation	3	3	01-Feb-23	03-Feb-23						■	Precast - CL C.1 to L.2 - West Elevation						
1894	PCST.D3.1160	Precast - CL L.2 to Q - West Elevation	3	3	06-Feb-23	08-Feb-23						■	Precast - CL L.2 to Q - West Elevation						
1895	PCST.D3.1170	Precast - CL Q to Z - West Elevation	3	3	09-Feb-23	13-Feb-23						■	Precast - CL Q to Z - West Elevation						
1896	PCST.D3.1180	Precast - CL 1 to 8 - True North	4	4	14-Feb-23	17-Feb-23						■	Precast - CL 1 to 8 - True North						
1897	PCST.D3.1190	Precast - CL Z to Q - East Elevation	3	3	21-Feb-23	23-Feb-23						■	Precast - CL Z to Q - East Elevation						
1898	Glazing and Metal Paneling			42	42	30-Jan-23	29-Mar-23						29-Mar-23	Glazing and Metal Paneling					
1899	GZMP.D3.1040	Metal Paneling - S Elevation	15	15	30-Jan-23	17-Feb-23						■	Metal Paneling - S Elevation						
1900	GZMP.D3.1060	Precast Field Verification for Glazing	2	2	30-Jan-23	31-Jan-23						I	Precast Field Verification for Glazing						
1901	GZMP.D3.1030	Install Glazing - S Elevation CL-8 to CL-1	15	15	02-Mar-23	22-Mar-23						■	Install Glazing - S Elevation CL-8 to CL-1						
1902	GZMP.D3.1050	Install Glazing - W Elevation CL-C to CL-A	5	5	23-Mar-23	29-Mar-23						■	Install Glazing - W Elevation CL-C to CL-A						
1903	Roof			78	78	08-Nov-22	03-Mar-23						03-Mar-23	Roof					
1904	CL A to CL C			62	62	08-Nov-22	08-Feb-23						08-Feb-23	CL A to CL C					
1905	ROOF.D3.132	Roof A-C - Install Curbs	5	5	08-Nov-22	15-Nov-22						■	Roof A-C - Install Curbs						
1906	ROOF.D3.135	Roof A-C - Temp Roof	2	2	15-Nov-22	16-Nov-22						■	Roof A-C - Temp Roof						
1907	ROOF.D3.133	Roof A-C - Roof Penetrations	3	3	16-Nov-22	18-Nov-22						■	Roof A-C - Roof Penetrations						
1908	ROOF.D3.136	Roof A-C - Foam Insulation	5	5	17-Nov-22	23-Nov-22						■	Roof A-C - Foam Insulation						
1909	ROOF.D3.134	Roof A-C - Inspect/Punch/QAAC	1	1	18-Nov-22	18-Nov-22						■	Roof A-C - Inspect/Punch/QAAC						
1910	ROOF.D3.137	Roof A-C - Install Roofing Material	5	5	28-Nov-22	02-Dec-22						■	Roof A-C - Install Roofing Material						
1911	ROOF.D3.138	Roof A-C - Interior Wall Covering	5	5	26-Jan-23	01-Feb-23						■	Roof A-C - Interior Wall Covering						
1912	ROOF.D3.139	Roof A-C - Wall Cap	5	5	02-Feb-23	08-Feb-23						■	Roof A-C - Wall Cap						
1913	CL C to CL L			57	57	21-Nov-22	13-Feb-23						13-Feb-23	CL C to CL L					
1914	ROOF.D3.140	Roof C-L - Install Curbs	5	5	21-Nov-22	29-Nov-22						■	Roof C-L - Install Curbs						

█ Remaining Level of Effort █ Remaining Work ◆ Milestone
█ Actual Work █ Critical Remaining Work ▼ Summary

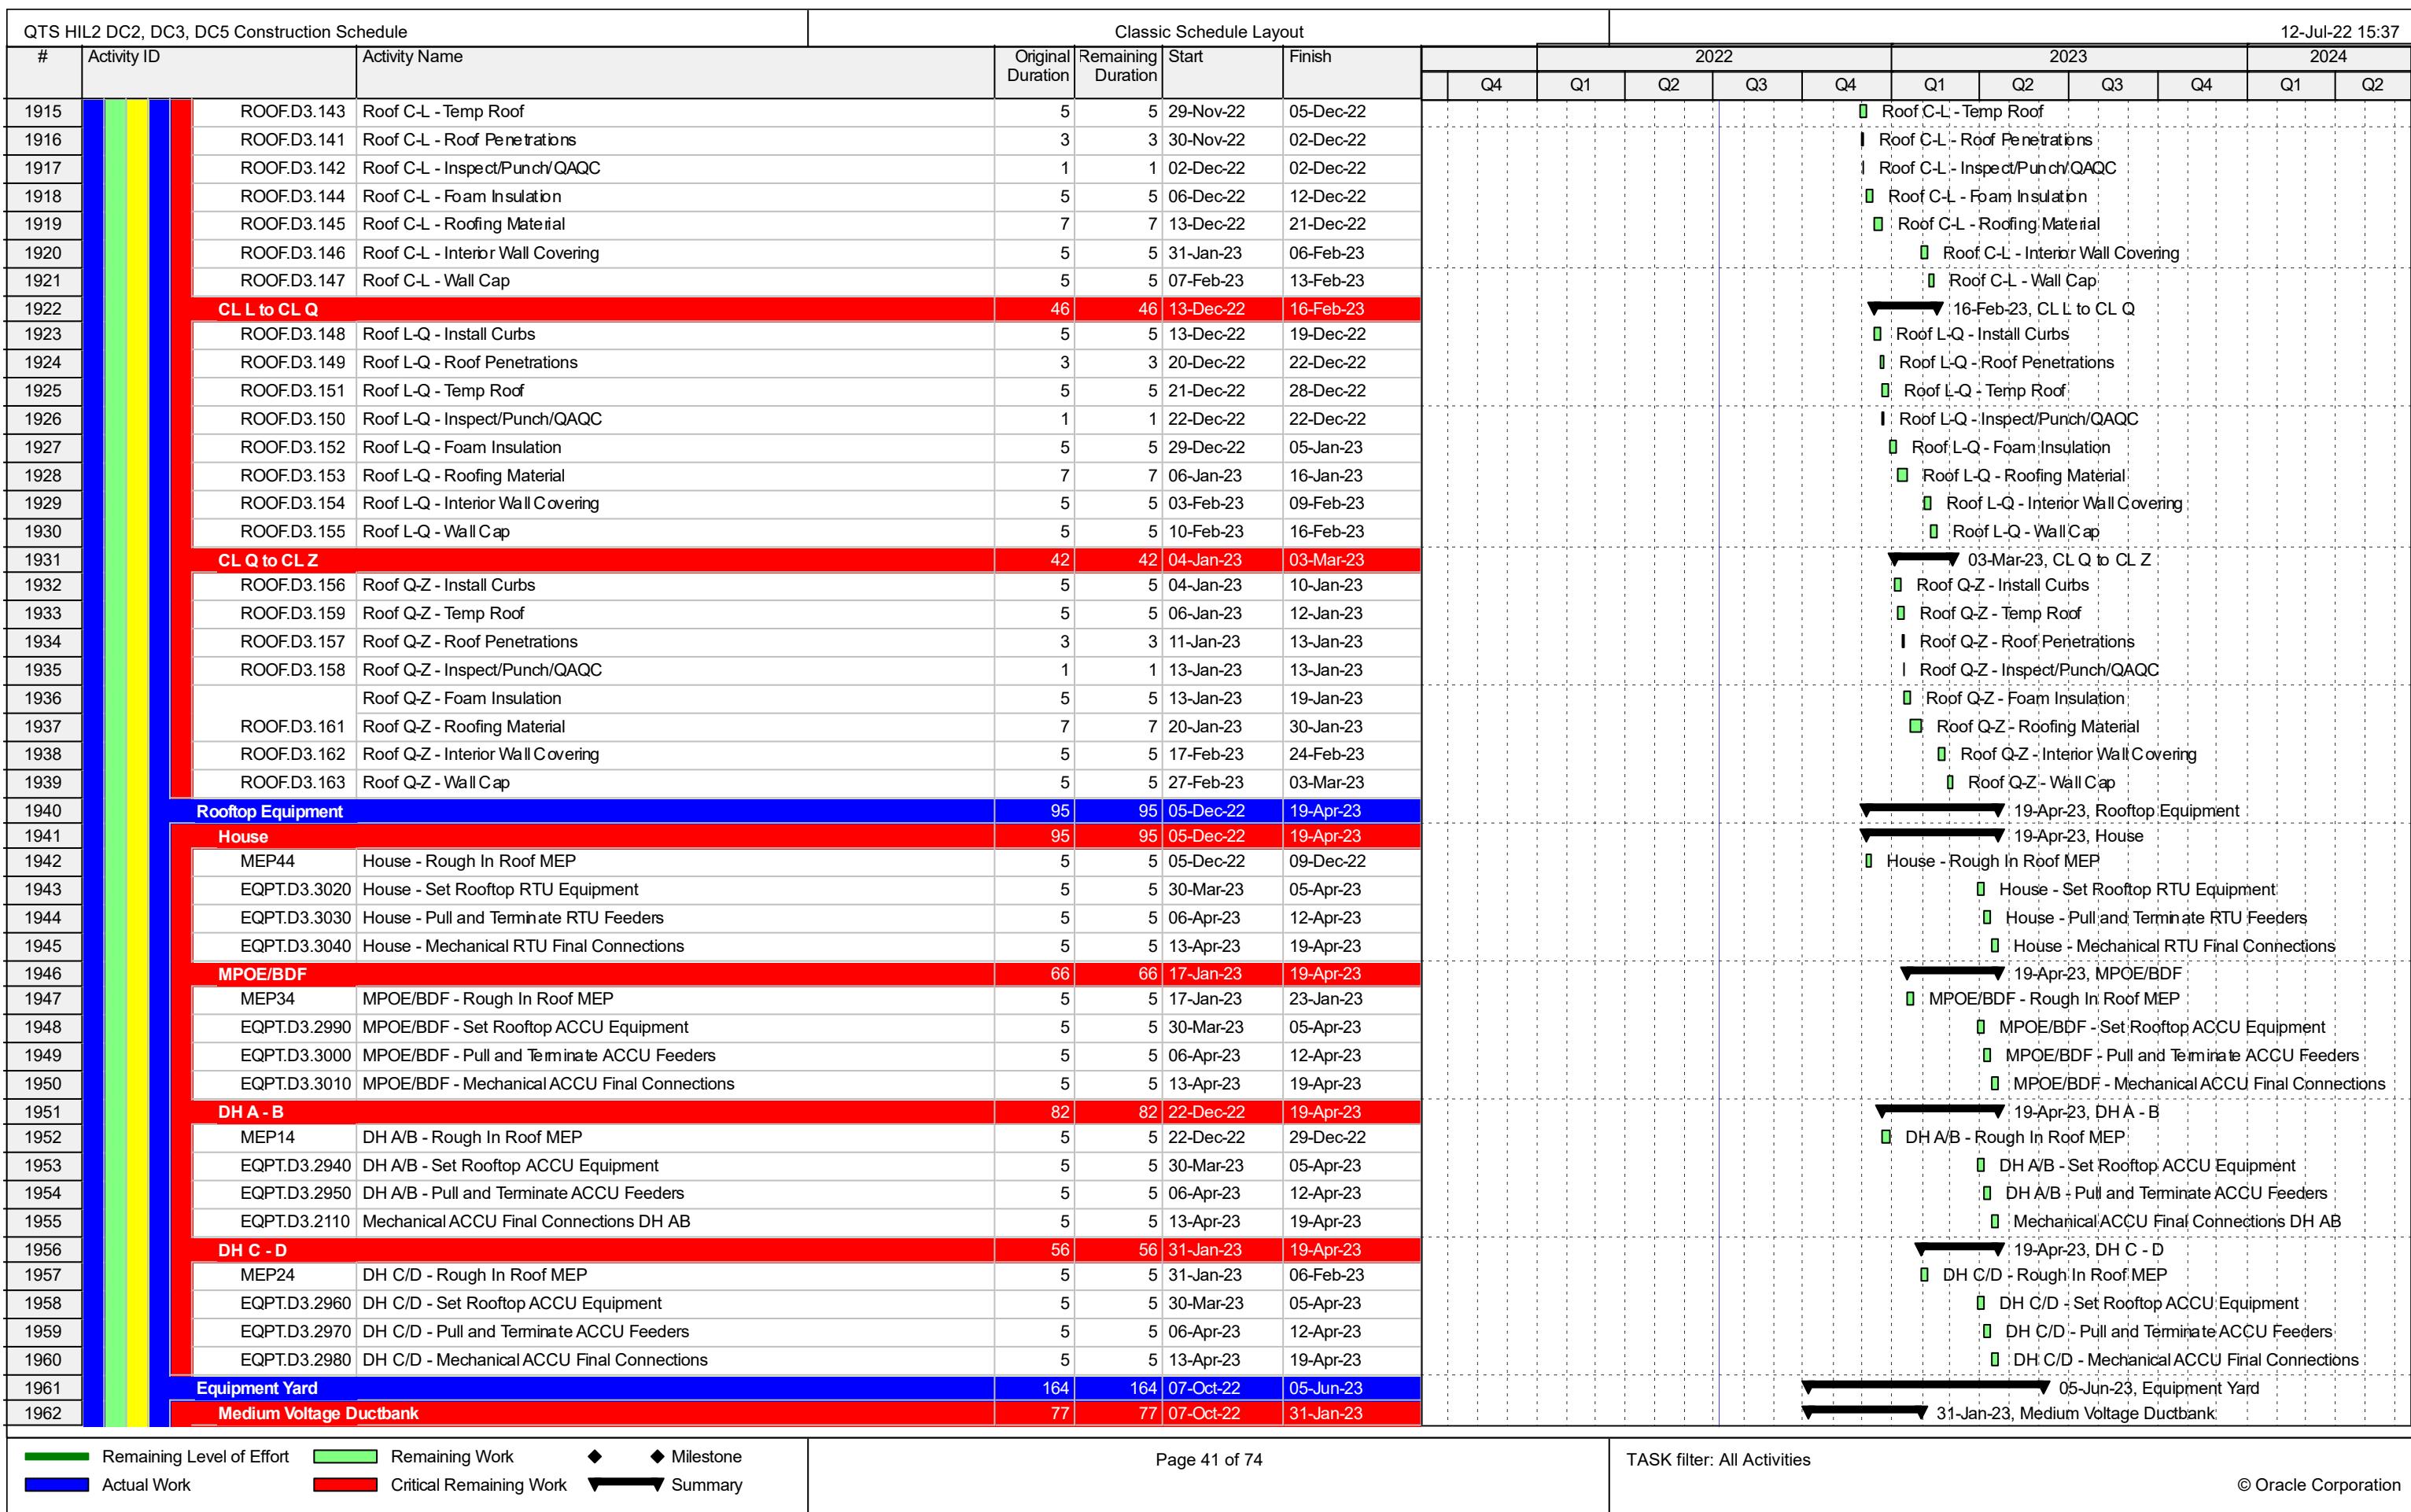


QTS HIL2 DC2, DC3, DC5 Construction Schedule				Classic Schedule Layout					12-Jul-22 15:37									
#	Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	2022					2023					2024	
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	
1963		EXCV.D3.1250 Excavate Medium Voltage Underground - Sequence 1	6	6	07-Oct-22	17-Oct-22												
1964		EXCV.D3.1260 Excavate Medium Voltage Underground - Sequence 2	14	14	18-Oct-22	04-Nov-22												
1965		MVDP.D3.107 Install Medium Voltage Underground - Sequence 1	2	2	18-Oct-22	19-Oct-22												
1966		EXCV.D3.1270 Excavate Medium Voltage Underground - Sequence 3	13	13	07-Nov-22	28-Nov-22												
1967		MVDP.D3.108 Install Medium Voltage Underground - Sequence 2	8	8	07-Nov-22	17-Nov-22												
1968		EXCV.D3.1280 Excavate Medium Voltage Underground - Sequence 4	13	13	29-Nov-22	15-Dec-22												
1969		MVDP.D3.109 Install Medium Voltage Underground - Sequence 3	7	7	29-Nov-22	07-Dec-22												
1970		EXCV.D3.1290 Excavate Medium Voltage Underground - Sequence 5	17	17	16-Dec-22	11-Jan-23												
1971		MVDP.D3.110 Install Medium Voltage Underground - Sequence 4	8	8	16-Dec-22	28-Dec-22												
1972		EXCV.D3.1300 Excavate Medium Voltage Underground - North Vault Group 1	5	5	12-Jan-23	18-Jan-23												
1973		MVDP.D3.111 Install Medium Voltage Underground - Sequence 5	14	14	12-Jan-23	31-Jan-23												
1974		Excavate Medium Voltage Underground - North Vault Group 2	5	5	19-Jan-23	25-Jan-23												
1975		MVDP.D3.112 Install Medium Voltage Underground - North Vault Group 1	4	4	19-Jan-23	24-Jan-23												
1976		MVDP.D3.113 Install Medium Voltage Underground - North Vault Group 2	4	4	26-Jan-23	31-Jan-23												
1977		Equipment Yard Pads and Set Equipment	98	98	17-Jan-23	05-Jun-23												
1978		House	20	20	03-Feb-23	03-Mar-23												
1979		EXCV.D3.4 Yard House - Excavation Transformer Foundations	2	2	03-Feb-23	06-Feb-23												
1980		CONC.D3. Yard House - Form Transformer Foundations DH AB	2	2	06-Feb-23	07-Feb-23												
1981		CONC.D3. Yard House - Rebar Transformer Foundations	2	2	07-Feb-23	08-Feb-23												
1982		CONC.D3. Yard House - Pour Transformer Foundations	1	1	09-Feb-23	09-Feb-23												
1983		CONC.D3. Yard House - Cure Transformer Foundations	5	5	10-Feb-23	16-Feb-23												
1984		EQPT.D3.4 Yard House - Set Transformers	5	5	17-Feb-23	24-Feb-23												
1985		EQPT.D3.4 Yard House - Pull and Terminate Transformers	5	5	27-Feb-23	03-Mar-23												
1986		MPOE/BDF Pads and Set Equipment	38	38	17-Jan-23	10-Mar-23												
1987		SURV.D3.1 Survey MPOE/BDF Equipment Foundations	1	1	17-Jan-23	17-Jan-23												
1988		Pod Pads and Set Equipment	35	35	18-Jan-23	08-Mar-23												
1989		EXCV.D Yard MPOE/BDF - Excavate UPS Pod Foundations	2	2	18-Jan-23	19-Jan-23												
1990		CONC.I Yard MPOE/BDF - Form UPS Pod Foundations MPOE BDF	2	2	19-Jan-23	20-Jan-23												
1991		CONC.I Yard MPOE/BDF - Rebar UPS Pod Foundations	2	2	20-Jan-23	23-Jan-23												
1992		CONC.I Yard MPOE/BDF - Pour UPS Pod Foundations	3	3	24-Jan-23	26-Jan-23												
1993		CONC.I Yard MPOE/BDF - Cure UPS Pod Foundations	5	5	27-Jan-23	02-Feb-23												
1994		CONC.I Yard MPOE/BDF - Install Steel Rails UPS Pod Foundations	3	3	03-Feb-23	07-Feb-23												
1995		EQPT.D Yard MPOE/BDF - Set UPS Pods	5	5	08-Feb-23	14-Feb-23												
1996		EQPT.D Yard MPOE/BDF - Pull and Terminate UPS Pods	15	15	15-Feb-23	08-Mar-23												
1997		Transformer Pads and Set Equipment	28	28	18-Jan-23	27-Feb-23												
1998		EXCV.D Yard MPOE/BDF - Excavation Transformer Foundations	2	2	18-Jan-23	19-Jan-23												
1999		CONC.I Yard MPOE/BDF - Form Transformer Foundations	2	2	19-Jan-23	20-Jan-23												
2000		CONC.I Yard MPOE/BDF - Rebar Transformer Foundations	2	2	20-Jan-23	23-Jan-23												
2001		CONC.I Yard MPOE/BDF - Pour Transformer Foundations	1	1	27-Jan-23	27-Jan-23												
2002		CONC.I Yard MPOE/BDF - Cure Transformer Foundations	5	5	30-Jan-23	03-Feb-23												
2003		EQPT.D Yard MPOE/BDF - Set Transformers	5	5	06-Feb-23	10-Feb-23												
2004		EQPT.D Yard MPOE/BDF - Pull and Terminate Transformers	10	10	13-Feb-23	27-Feb-23												
2005		Generator Pads and Set Equipment	35	35	20-Jan-23	10-Mar-23												
2006		EXCV.D Yard MPOE/BDF - Excavation Generator Foundations	2	2	20-Jan-23	23-Jan-23												
2007		CONC.I Yard MPOE/BDF - Form Generator Foundations	2	2	23-Jan-23	24-Jan-23												
2008		CONC.I Yard MPOE/BDF - Rebar Generator Foundations	3	3	24-Jan-23	26-Jan-23												
2009		CONC.I Yard MPOE/BDF - Pour Generator Foundations	4	4	30-Jan-23	02-Feb-23												
2010		CONC.I Yard MPOE/BDF - Cure Generator Foundations	5	5	03-Feb-23	09-Feb-23												

Remaining Level of Effort Remaining Work Milestone Critical Remaining Work Summary

QTS HIL2 DC2, DC3, DC5 Construction Schedule				Classic Schedule Layout						12-Jul-22 15:37							
#	Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	2022					2023				2024	
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2
2011		EQPT.D Yard MPOE/BDF - Set Generators	5	5	10-Feb-23	16-Feb-23											
2012		EQPT.D Yard MPOE/BDF - Pull and Terminate Generators	15	15	17-Feb-23	10-Mar-23											
2013		Data Hall A and B Pads and Set Equipment			51	51	20-Jan-23	03-Apr-23									
2014		SURV.D3.1 Survey DH A/B - Equipment Foundations	1	1	20-Jan-23	20-Jan-23											
2015		Transformer Pads and Set Equipment			30	30	03-Feb-23	17-Mar-23									
2016		EXCV.D Yard DH A/B - Excavation Transformer Foundations	2	2	03-Feb-23	06-Feb-23											
2017		CONC.I Yard DH A/B - Form Transformer Foundations DH AB	2	2	06-Feb-23	07-Feb-23											
2018		CONC.I Yard DH A/B - Rebar Transformer Foundations	2	2	07-Feb-23	08-Feb-23											
2019		CONC.I Yard DH A/B - Pour Transformer Foundations	1	1	09-Feb-23	09-Feb-23											
2020		CONC.I Yard DH A/B - Cure Transformer Foundations	5	5	10-Feb-23	16-Feb-23											
2021		EQPT.D Yard DH A/B - Set Transformers	5	5	17-Feb-23	24-Feb-23											
2022		EQPT.D Yard DH A/B - Pull and Terminate Transformers	15	15	27-Feb-23	17-Mar-23											
2023		Generator Pads and Set Equipment			39	39	07-Feb-23	03-Apr-23									
2024		EXCV.D Yard DH A/B - Excavation Generator Foundations	2	2	07-Feb-23	08-Feb-23											
2025		CONC.I Yard DH A/B - Form Generator Foundations	2	2	08-Feb-23	09-Feb-23											
2026		CONC.I Yard DH A/B - Rebar Generator Foundations	3	3	09-Feb-23	13-Feb-23											
2027		CONC.I Yard DH A/B - Pour Generator Foundations	4	4	14-Feb-23	17-Feb-23											
2028		CONC.I Yard DH A/B - Cure Generator Foundations	5	5	21-Feb-23	27-Feb-23											
2029		EQPT.D Yard DH A/B - Set Generators	5	5	28-Feb-23	06-Mar-23											
2030		EQPT.D Yard DH A/B - Pull and Terminate Generators	20	20	07-Mar-23	03-Apr-23											
2031		Medium Voltage Pads and Set Equipment			32	32	09-Feb-23	27-Mar-23									
2032		EXCV.D Yard DH A/B - Excavation MV Pads	2	2	09-Feb-23	10-Feb-23											
2033		CONC.I Yard DH A/B - Form MV Pads	2	2	13-Feb-23	14-Feb-23											
2034		CONC.I Yard DH A/B - Rebar MV Foundations	3	3	15-Feb-23	17-Feb-23											
2035		CONC.I Yard DH A/B - Pour MV Pads	4	4	21-Feb-23	24-Feb-23											
2036		CONC.I Yard DH A/B - Cure MV Pads	5	5	27-Feb-23	03-Mar-23											
2037		EQPT.D Yard DH A/B - Set MV Equipment	5	5	06-Mar-23	10-Mar-23											
2038		EQPT.D Yard DH A/B - Pull and Terminate MV Feeders	15	15	07-Mar-23	27-Mar-23											
2039		Data Hall C and D Pads and Set Equipment			71	71	24-Feb-23	05-Jun-23									
2040		SURV.D3.1 Survey DH C/D Equipment Foundations	1	1	24-Feb-23	24-Feb-23											
2041		Transformer Pads and Set Equipment			30	30	27-Feb-23	07-Apr-23									
2042		EXCV.D Yard DH C/D - Excavation Transformer Foundations	2	2	27-Feb-23	28-Feb-23											
2043		CONC.I Yard DH C/D - Form Transformer Foundations	2	2	28-Feb-23	01-Mar-23											
2044		CONC.I Yard DH C/D - Rebar Transformer Foundations	2	2	01-Mar-23	02-Mar-23											
2045		CONC.I Yard DH C/D - Pour Transformer Foundations	1	1	03-Mar-23	03-Mar-23											
2046		CONC.I Yard DH C/D - Cure Transformer Foundations	5	5	06-Mar-23	10-Mar-23											
2047		EQPT.D Yard DH C/D - Set Transformers	5	5	13-Mar-23	17-Mar-23											
2048		EQPT.D Yard DH C/D - Pull and Terminate Transformers	15	15	20-Mar-23	07-Apr-23											
2049		Generator Pads and Set Equipment			48	48	01-Mar-23	05-May-23									
2050		EXCV.D Yard DH C/D - Excavation Generator Foundations	2	2	01-Mar-23	02-Mar-23											
2051		CONC.I Yard DH C/D - Form Generator Foundations	2	2	02-Mar-23	03-Mar-23											
2052		CONC.I Yard DH C/D - Rebar Generator Foundations	3	3	03-Mar-23	07-Mar-23											
2053		CONC.I Yard DH C/D - Pour Generator Foundations	4	4	08-Mar-23	13-Mar-23											
2054		CONC.I Yard DH C/D - Cure Generator Foundations	5	5	14-Mar-23	20-Mar-23											
2055		EQPT.D Yard DH C/D - Set Generators	5	5	21-Mar-23	27-Mar-23											
2056		EQPT.D Yard DH C/D - Pull and Terminate Generators	20	20	10-Apr-23	05-May-23											
2057		Medium Voltage Pads and Set Equipment			66	66	03-Mar-23	05-Jun-23									
2058		EXCV.D Yard DH C/D - Excavation MV Pads	2	2	03-Mar-23	06-Mar-23											

 Remaining Level of Effort
  Remaining Work
  Milestone
  Actual Work
  Critical Remaining Work
  Summary

QTS HIL2 DC2, DC3, DC5 Construction Schedule				Classic Schedule Layout						12-Jul-22 15:37							
#	Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	2022					2023				2024	
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2
2059	CONC.I	Yard DH C/D - Form MV Pads	2	2	07-Mar-23	08-Mar-23						I	Yard DH C/D - Form MV Pads				
2060		Yard DH C/D - Rebar MV Foundations	2	2	09-Mar-23	10-Mar-23						I	Yard DH C/D - Rebar MV Foundations				
2061		Yard DH C/D - Pour MV Pads	4	4	13-Mar-23	16-Mar-23						I	Yard DH C/D - Pour MV Pads				
2062		Yard DH C/D - Cure MV Pads	5	5	17-Mar-23	23-Mar-23						I	Yard DH C/D - Cure MV Pads				
2063		EQPT.D	Yard DH C/D - Set MV Equipment	5	5	24-Mar-23	30-Mar-23					I	Yard DH C/D - Set MV Equipment				
2064		EQPT.D	Yard DH C/D - Pull and Terminate MV Feeders	20	20	08-May-23	05-Jun-23					I	Yard DH C/D - Pull and Terminate MV Feeders				
2065	Elevators			85	85	23-Feb-23	22-Jun-23										
2066	Freight Elevator E03			61	61	23-Feb-23	18-May-23										
2067	ELVT.D3.1330	Freight Elev. 3 - Hoisting Equipment	7	7	23-Feb-23	03-Mar-23						I	Freight Elev. 3 - Hoisting Equipment				
2068	ELVT.D3.1340	Freight Elev. 3 - Pit Rails/Frame/Cab	5	5	06-Mar-23	10-Mar-23						I	Freight Elev. 3 - Pit Rails/Frame/Cab				
2069	ELVT.D3.1350	Freight Elev. 3 - Tirak & Governor Rope	5	5	13-Mar-23	17-Mar-23						I	Freight Elev. 3 - Tirak & Governor Rope				
2070	ELVT.D3.1360	Freight Elev. 3 - Rails	8	8	20-Mar-23	29-Mar-23						I	Freight Elev. 3 - Rails				
2071	ELVT.D3.1370	Freight Elev. 3 - Door entrances	4	4	30-Mar-23	04-Apr-23						I	Freight Elev. 3 - Door entrances				
2072	ELVT.D3.1380	Freight Elev. 3 - Duct/Wire Machine/Startup	7	7	05-Apr-23	13-Apr-23						I	Freight Elev. 3 - Duct/Wire Machine/Startup				
2073	ELVT.D3.1390	Freight Elev. 3 - Rope Elevator/Remove Tirak	4	4	14-Apr-23	19-Apr-23						I	Freight Elev. 3 - Rope Elevator/Remove Tirak				
2074	ELVT.D3.1400	Freight Elev. 3 - Pipe and Wire Hatch Devices	6	6	20-Apr-23	27-Apr-23						I	Freight Elev. 3 - Pipe and Wire Hatch Devices				
2075	ELVT.D3.1410	Freight Elev. 3 - Terminate Devices	8	8	28-Apr-23	09-May-23						I	Freight Elev. 3 - Terminate Devices				
2076	ELVT.D3.1420	Freight Elev. 3 - Clean Rails	2	2	10-May-23	11-May-23						I	Freight Elev. 3 - Clean Rails				
2077	ELVT.D3.1430	Freight Elev. 3 - Inspect	5	5	12-May-23	18-May-23						I	Freight Elev. 3 - Inspect				
2078	Freight Elevator E02A and E02B			85	85	23-Feb-23	22-Jun-23										
2079	ELVT.D3.1440	Freight Elev. E02A/E02B - Hoisting Equipment	10	10	23-Feb-23	08-Mar-23						I	Freight Elev. E02A/E02B - Hoisting Equipment				
2080	ELVT.D3.1450	Freight Elev. E02A/E02B - Pit Rails/Frame/Cab	7	7	09-Mar-23	17-Mar-23						I	Freight Elev. E02A/E02B - Pit Rails/Frame/Cab				
2081	ELVT.D3.1460	Freight Elev. E02A/E02B - Tirak & Governor Rope	7	7	20-Mar-23	28-Mar-23						I	Freight Elev. E02A/E02B - Tirak & Governor Rope				
2082	ELVT.D3.1470	Freight Elev. E02A/E02B - Rails	10	10	29-Mar-23	11-Apr-23						I	Freight Elev. E02A/E02B - Rails				
2083	ELVT.D3.1480	Freight Elev. E02A/E02B - Door entrances	6	6	12-Apr-23	19-Apr-23						I	Freight Elev. E02A/E02B - Door entrances				
2084	ELVT.D3.1490	Freight Elev. E02A/E02B - Duct/Wire Machine/Startup	9	9	20-Apr-23	02-May-23						I	Freight Elev. E02A/E02B - Duct/Wire Machine/Startup				
2085	ELVT.D3.1500	Freight Elev. E02A/E02B - Rope Elevator/Remove Tirak	6	6	03-May-23	10-May-23						I	Freight Elev. E02A/E02B - Rope Elevator/Remove Tirak				
2086	ELVT.D3.1510	Freight Elev. E02A/E02B - Pipe and Wire Hatch Devices	8	8	11-May-23	22-May-23						I	Freight Elev. E02A/E02B - Pipe and Wire Hatch Devices				
2087	ELVT.D3.1520	Freight Elev. E02A/E02B - Terminate Devices	10	10	23-May-23	06-Jun-23						I	Freight Elev. E02A/E02B - Terminate Devices				
2088	ELVT.D3.1530	Freight Elev. E02A/E02B - Clean Rails	4	4	07-Jun-23	12-Jun-23						I	Freight Elev. E02A/E02B - Clean Rails				
2089	ELVT.D3.1540	Freight Elev. E02A/E02B - Inspect	8	8	13-Jun-23	22-Jun-23						I	Freight Elev. E02A/E02B - Inspect				
2090	Passenger Elevator			61	61	23-Feb-23	18-May-23										
2091	ELVT.D3.1550	Pass. Elev. - Hoisting Equipment - Pass Elev.	7	7	23-Feb-23	03-Mar-23						I	Pass. Elev. - Hoisting Equipment - Pass Elev.				
2092	ELVT.D3.1560	Pass. Elev. - Pit Rails/Frame/Cab	5	5	06-Mar-23	10-Mar-23						I	Pass. Elev. - Pit Rails/Frame/Cab				
2093	ELVT.D3.1570	Pass. Elev. - Tirak & Governor Rope	5	5	13-Mar-23	17-Mar-23						I	Pass. Elev. - Tirak & Governor Rope				
2094	ELVT.D3.1580	Pass. Elev. - Rails	8	8	20-Mar-23	29-Mar-23						I	Pass. Elev. - Rails				
2095	ELVT.D3.1590	Pass. Elev. - Door entrances	4	4	30-Mar-23	04-Apr-23						I	Pass. Elev. - Door entrances				
2096	ELVT.D3.1600	Pass. Elev. - Duct/Wire Machine/Startup	7	7	05-Apr-23	13-Apr-23						I	Pass. Elev. - Duct/Wire Machine/Startup				
2097	ELVT.D3.1610	Pass. Elev. - Rope Elevator/Remove Tirak	4	4	14-Apr-23	19-Apr-23						I	Pass. Elev. - Rope Elevator/Remove Tirak				
2098	ELVT.D3.1620	Pass. Elev. - Pipe and Wire Hatch Devices	6	6	20-Apr-23	27-Apr-23						I	Pass. Elev. - Pipe and Wire Hatch Devices				
2099	ELVT.D3.1630	Pass. Elev. - Terminate Devices	8	8	28-Apr-23	09-May-23						I	Pass. Elev. - Terminate Devices				
2100	ELVT.D3.1640	Pass. Elev. - Clean Rails	2	2	10-May-23	11-May-23						I	Pass. Elev. - Clean Rails				
2101	ELVT.D3.1650	Pass. Elev. - Inspect	5	5	12-May-23	18-May-23						I	Pass. Elev. - Inspect				
2102	Interior Buildout			85	85	22-Nov-22	27-Mar-23										
2103	1st Floor Sector 2F1&F2 Lobby/Admin			54	54	22-Nov-22	09-Feb-23										
2104	FRME.D3.262	1st Floor 2F1/F2 - Layout and Frame Walls	13	13	22-Nov-22	12-Dec-22						I	1st Floor 2F1/F2 - Layout and Frame Walls				
2105	MEP.D3.2390	1st Floor 2F1/F2 - Rough-in Plumbing	8	8	22-Nov-22	05-Dec-22						I	1st Floor 2F1/F2 - Rough-in Plumbing				
2106	MEP.D3.2400	1st Floor 2F1/F2 - Rough-in HVAC	7	7	22-Nov-22	02-Dec-22						I	1st Floor 2F1/F2 - Rough-in HVAC				



QTS HIL2 DC2, DC3, DC5 Construction Schedule				Classic Schedule Layout					12-Jul-22 15:37											
#	Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	2022					2023					2024			
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2			
2154	MEP.D3.2530	2nd Floor 2F1/F2 - Rough-in Fire	7	7	07-Dec-22	15-Dec-22														
2155		2nd Floor 2F1/F2 - Rough-in Electric	8	8	07-Dec-22	16-Dec-22														
2156		MEP.D3.2550	2nd Floor 2F1/F2 - Rough-in Low Volt	8	8	07-Dec-22	16-Dec-22													
2157		FRME.D3.281	2nd Floor 2F1/F2 - Install HM Door Frames	5	5	07-Dec-22	13-Dec-22													
2158		MEP.D3.2560	2nd Floor 2F1/F2 - Fire caulk	2	2	19-Dec-22	20-Dec-22													
2159		FRME.D3.277	2nd Floor 2F1/F2 - Insulate	4	4	21-Dec-22	27-Dec-22													
2160		FRME.D3.278	2nd Floor 2F1/F2 - Install Drywall Upper	5	5	28-Dec-22	04-Jan-23													
2161		FRME.D3.279	2nd Floor 2F1/F2 - Hang and Tape Drywall	8	8	05-Jan-23	16-Jan-23													
2162		FNSH.D3.2280	2nd Floor 2F1/F2 - Paint	3	3	17-Jan-23	19-Jan-23													
2163		FRME.D3.280	2nd Floor 2F1/F2 - Grid Ceiling	5	5	20-Jan-23	26-Jan-23													
2164		FNSH.D3.2290	2nd Floor 2F1/F2 - Doors & Hardware	5	5	27-Jan-23	02-Feb-23													
2165		FNSH.D3.2300	2nd Floor 2F1/F2 - Tile in Restroom	5	5	27-Jan-23	02-Feb-23													
2166		FNSH.D3.2310	2nd Floor 2F1/F2 - Finish Electric	5	5	27-Jan-23	02-Feb-23													
2167		FNSH.D3.2320	2nd Floor 2F1/F2 - Drop Remaining Ceiling Tile	1	1	03-Feb-23	03-Feb-23													
2168		FNSH.D3.2330	2nd Floor 2F1/F2 - Finish Plumbing	4	4	06-Feb-23	09-Feb-23													
2169		FNSH.D3.2340	2nd Floor 2F1/F2 - Finish HVAC	3	3	10-Feb-23	14-Feb-23													
2170		2nd Floor 2F1/F2 - Floor Coverings		6	6	15-Feb-23	23-Feb-23													
2171	2nd Floor Sector 2G1&G2 Back of House				39	39	17-Jan-23	13-Mar-23												
2172	FRME.D3.282	2nd Floor 2G1/G2 - Layout and Frame Walls	9	9	17-Jan-23	27-Jan-23														
2173	MEP.D3.2570	2nd Floor 2G1/G2 - Rough-in Plumbing	8	8	17-Jan-23	26-Jan-23														
2174	MEP.D3.2580	2nd Floor 2G1/G2 - Rough-in HVAC	7	7	17-Jan-23	25-Jan-23														
2175	MEP.D3.2590	2nd Floor 2G1/G2 - Rough-in Fire	7	7	17-Jan-23	25-Jan-23														
2176	MEP.D3.2600	2nd Floor 2G1/G2 - Rough-in Electric	8	8	17-Jan-23	26-Jan-23														
2177	MEP.D3.2610	2nd Floor 2G1/G2 - Rough-in Low Volt	8	8	17-Jan-23	26-Jan-23														
2178	FRME.D3.287	2nd Floor 2G1/G2 - Install HM Door Frame	5	5	17-Jan-23	23-Jan-23														
2179	MEP.D3.2620	2nd Floor 2G1/G2 - Fire caulk	2	2	27-Jan-23	30-Jan-23														
2180	FRME.D3.283	2nd Floor 2G1/G2 - Insulate	2	2	31-Jan-23	01-Feb-23														
2181	FRME.D3.284	2nd Floor 2G1/G2 - Install Drywall Upper	5	5	02-Feb-23	08-Feb-23														
2182	FRME.D3.285	2nd Floor 2G1/G2 - Hang and Tape Drywall	7	7	09-Feb-23	17-Feb-23														
2183	FNSH.D3.2380	2nd Floor 2G1/G2 - Tile in Restroom	3	3	09-Feb-23	13-Feb-23														
2184	FNSH.D3.2360	2nd Floor 2G1/G2 - Paint	3	3	21-Feb-23	23-Feb-23														
2185	FRME.D3.286	2nd Floor 2G1/G2 - Wood Ceiling	3	3	24-Feb-23	28-Feb-23														
2186	FNSH.D3.2370	2nd Floor 2G1/G2 - Doors & Hardware	5	5	24-Feb-23	02-Mar-23														
2187	FNSH.D3.2390	2nd Floor 2G1/G2 - Finish Electric	5	5	24-Feb-23	02-Mar-23														
2188	FNSH.D3.2400	2nd Floor 2G1/G2 - Finish Plumbing	4	4	03-Mar-23	08-Mar-23														
2189	FNSH.D3.2410	2nd Floor 2G1/G2 - Finish HVAC	3	3	09-Mar-23	13-Mar-23														
2190	Site Finishes				68	68	03-Feb-23	10-May-23												
2191	Trash Enclosure	15-Feb-23, Trash Enclosure				9	9	03-Feb-23	15-Feb-23											
2192		FOND.D3.205	Trash Encl - Dig Footings	1	1	03-Feb-23	03-Feb-23													
2193		FOND.D3.206	Trash Encl - Form Footings	1	1	03-Feb-23	03-Feb-23													
2194		FOND.D3.207	Trash Encl - Install Rebar & Bolards	1	1	06-Feb-23	06-Feb-23													
2195		FOND.D3.208	Trash Encl - Inspect & Pour	1	1	06-Feb-23	06-Feb-23													
2196		CONC.D3.18t	Trash Encl - Embeds for Gate	3	3	06-Feb-23	08-Feb-23													
2197		SOG.D3.1850	Trash Encl - SOG	2	2	07-Feb-23	08-Feb-23													
2198		CONC.D3.18t	Trash Encl - CMU - Trash Enc.	3	3	09-Feb-23	13-Feb-23													
2199		CONC.D3.18t	Trash Encl - Grout CMU	1	1	14-Feb-23	14-Feb-23													
2200		FNSH.D3.2420	Trash Encl - Install Gate	1	1	15-Feb-23	15-Feb-23													
Remaining Level of Effort				Remaining Work				Milestone				Page 46 of 74					TASK filter: All Activities			
Actual Work				Critical Remaining Work				Summary									© Oracle Corporation			

QTS HIL2 DC2, DC3, DC5 Construction Schedule				Classic Schedule Layout					12-Jul-22 15:37									
#	Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	2022					2023					2024	
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	
2249		EQPT.D3.5 1st Floor House - Set CRAC Units	5	5	30-Mar-23	05-Apr-23										1st Floor House - Set CRAC Units		
2250		EQPT.D3.5 1st Floor House - Install COD Boards	5	5	30-Mar-23	05-Apr-23										1st Floor House - Install COD Boards		
2251		EQPT.D3.5 1st Floor House - Final Connections CRAC Units	15	15	04-Apr-23	24-Apr-23										1st Floor House - Final Connections CRAC Units		
2252		EQPT.D3.5 1st Floor House - Set HUM	5	5	06-Apr-23	12-Apr-23										1st Floor House - Set HUM		
2253		MPOE 1 and 2	78	78	04-Jan-23	24-Apr-23										24-Apr-23, MPOE 1 and 2		
2254		Rough-In	58	58	04-Jan-23	27-Mar-23										27-Mar-23, Rough-In		
2255	FRME.D3.1	1st Floor MPOE 1/2 - Layout and Frame Walls	10	10	04-Jan-23	17-Jan-23										1st Floor MPOE 1/2 - Layout and Frame Walls		
2256	MEP.D3.18	1st Floor MPOE 1/2 - Install Fire Protection	10	10	13-Jan-23	26-Jan-23										1st Floor MPOE 1/2 - Install Fire Protection		
2257	MEP.D3.18	1st Floor MPOE 1/2 - Install OH Mechanical (Plumbing and HVAC)	20	20	13-Jan-23	09-Feb-23										1st Floor MPOE 1/2 - Install OH Mechanical (Plumbing and HVAC)		
2258	MEP.D3.18	1st Floor MPOE 1/2 - Install OH Electrical	20	20	13-Jan-23	09-Feb-23										1st Floor MPOE 1/2 - Install OH Electrical		
2259	FRME.D3.2	1st Floor MPOE 1/2 - Install Door Frames	3	3	18-Jan-23	20-Jan-23										1st Floor MPOE 1/2 - Install Door Frames		
2260	FRME.D3.2	1st Floor MPOE 1/2 - Install Drywall Upper	4	4	17-Feb-23	23-Feb-23										1st Floor MPOE 1/2 - Install Drywall Upper		
2261	MEP.D3.18	1st Floor MPOE 1/2 - In-wall Rough-in Electrical	4	4	24-Feb-23	01-Mar-23										1st Floor MPOE 1/2 - In-wall Rough-in Electrical		
2262	FRME.D3.2	1st Floor MPOE 1/2 - Install Structural Grid	10	10	24-Feb-23	09-Mar-23										1st Floor MPOE 1/2 - Install Structural Grid		
2263	FRME.D3.2	1st Floor MPOE 1/2 - Insulate and Inspect	5	5	02-Mar-23	08-Mar-23										1st Floor MPOE 1/2 - Insulate and Inspect		
2264	FRME.D3.2	1st Floor MPOE 1/2 - Hang and Tape Drywall	6	6	09-Mar-23	16-Mar-23										1st Floor MPOE 1/2 - Hang and Tape Drywall		
2265	MEP.D3.18	1st Floor MPOE 1/2 - Install Lighting	5	5	10-Mar-23	16-Mar-23										1st Floor MPOE 1/2 - Install Lighting		
2266	MEP.D3.18	1st Floor MPOE 1/2 - Install Sprinkler Drops	5	5	10-Mar-23	16-Mar-23										1st Floor MPOE 1/2 - Install Sprinkler Drops		
2267	FNSH.D3.1	1st Floor MPOE 1/2 - Paint MPOE	2	2	17-Mar-23	20-Mar-23										1st Floor MPOE 1/2 - Paint MPOE		
2268	FRME.D3.2	1st Floor MPOE 1/2 - Install Overhead Doors	5	5	17-Mar-23	23-Mar-23										1st Floor MPOE 1/2 - Install Overhead Doors		
2269	FNSH.D3.1	1st Floor MPOE 1/2 - Install Finishes	5	5	21-Mar-23	27-Mar-23										1st Floor MPOE 1/2 - Install Finishes		
2270	FNSH.D3.1	1st Floor MPOE 1/2 - Trim Out Electrical Devices	5	5	21-Mar-23	27-Mar-23										1st Floor MPOE 1/2 - Trim Out Electrical Devices		
2271	Equipment		25	25	21-Mar-23	24-Apr-23										24-Apr-23, Equipment		
2272	EQPT.D3.2	1st Floor MPOE 1/2 - Set CRAC Units	5	5	21-Mar-23	27-Mar-23										1st Floor MPOE 1/2 - Set CRAC Units		
2273	EQPT.D3.2	1st Floor MPOE 1/2 - Install HDP Panels	10	10	21-Mar-23	03-Apr-23										1st Floor MPOE 1/2 - Install HDP Panels		
2274	EQPT.D3.3	1st Floor MPOE 1/2 - Install Network COD 2000AMP	10	10	21-Mar-23	03-Apr-23										1st Floor MPOE 1/2 - Install Network COD 2000AMP		
2275	EQPT.D3.2	1st Floor MPOE 1/2 - Set HUM	5	5	28-Mar-23	03-Apr-23										1st Floor MPOE 1/2 - Set HUM		
2276	EQPT.D3.2	1st Floor MPOE 1/2 - Install COD Boards	5	5	30-Mar-23	05-Apr-23										1st Floor MPOE 1/2 - Install COD Boards		
2277	EQPT.D3.2	1st Floor MPOE 1/2 - Final Connections CRAC Units	15	15	04-Apr-23	24-Apr-23										1st Floor MPOE 1/2 - Final Connections CRAC Units		
2278	EQPT.D3.2	1st Floor MPOE 1/2 - Install PDU	5	5	04-Apr-23	10-Apr-23										1st Floor MPOE 1/2 - Install PDU		
2279	Systems Gallery 1001 and 1010 DHA		101	101	02-Dec-22	26-Apr-23										26-Apr-23, Systems Gallery 1001 and 1010 DHA		
2280	Rough-In		68	68	02-Dec-22	10-Mar-23										10-Mar-23, Rough-In		
2281	MEP.D3.20	1st Floor DHA SG1001/1010 - Install Fire Protection	15	15	02-Dec-22	22-Dec-22										1st Floor DHA SG1001/1010 - Install Fire Protection		
2282	MEP.D3.20	1st Floor DHA SG1001/1010 - Install OH Mechanical (Plumbing and HVAC)	15	15	23-Dec-22	16-Jan-23										1st Floor DHA SG1001/1010 - Install OH Mechanical (Plumbing and HVAC)		
2283	MEP.D3.20	1st Floor DHA SG1001/1010 - Install OH Electrical	20	20	23-Dec-22	23-Jan-23										1st Floor DHA SG1001/1010 - Install OH Electrical		
2284	FRME.D3.2	1st Floor DHA SG1001/1010 - Layout and Frame Walls	6	6	07-Feb-23	14-Feb-23										1st Floor DHA SG1001/1010 - Layout and Frame Walls		
2285	FRME.D3.2	1st Floor DHA SG1001/1010 - Install Drywall Upper	6	6	09-Feb-23	16-Feb-23										1st Floor DHA SG1001/1010 - Install Drywall Upper		
2286	MEP.D3.20	1st Floor DHA SG1001/1010 - In-wall Rough-in Electrical	5	5	09-Feb-23	15-Feb-23										1st Floor DHA SG1001/1010 - In-wall Rough-in Electrical		
2287	FRME.D3.2	1st Floor DHA SG1001/1010 - Insulate and Inspect	5	5	16-Feb-23	23-Feb-23										1st Floor DHA SG1001/1010 - Insulate and Inspect		
2288	FRME.D3.2	1st Floor DHA SG1001/1010 - Hang and Tape Drywall	6	6	24-Feb-23	03-Mar-23										1st Floor DHA SG1001/1010 - Hang and Tape Drywall		
2289	FNSH.D3.1	1st Floor DHA SG1001/1010 - Paint - DHA SG	2	2	06-Mar-23	07-Mar-23										1st Floor DHA SG1001/1010 - Paint - DHA SG		
2290	FNSH.D3.1	1st Floor DHA SG1001/1010 - Install Finishes	3	3	08-Mar-23	10-Mar-23										1st Floor DHA SG1001/1010 - Install Finishes		
2291	Equipment		38	38	06-Mar-23	26-Apr-23										26-Apr-23, Equipment		
2292	EQPT.D3.2	1st Floor DHA SG1001/1010 - Install Switch Gear	5	5	06-Mar-23	10-Mar-23										1st Floor DHA SG1001/1010 - Install Switch Gear		
2293	EQPT.D3.2	1st Floor DHA SG1001/1010 - Install ATS	5	5	06-Mar-23	10-Mar-23										1st Floor DHA SG1001/1010 - Install ATS		
2294	EQPT.D3.2	1st Floor DHA SG1001/1010 - Install PDU	5	5	06-Mar-23	10-Mar-23										1st Floor DHA SG1001/1010 - Install PDU		
2295	EQPT.D3.2	1st Floor DHA SG1001/1010 - Install Reserve Busway	5	5	06-Mar-23	10-Mar-												


QTS HIL2 DC2, DC3, DC5 Construction Schedule				Classic Schedule Layout						12-Jul-22 15:37							
#	Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	2022					2023				2024	
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2
2345	EQPT.D3.2	1st Floor DHD SG1003/1020 - Install Reserve Busway	5	5	21-Mar-23	27-Mar-23										1st Floor DHD SG1003/1020 - Install Reserve Busway	
2346		1st Floor DHD SG1003/1020 - Install ATS	5	5	28-Mar-23	03-Apr-23										1st Floor DHD SG1003/1020 - Install ATS	
2347		1st Floor DHD SG1003/1020 - Install COD Boards	5	5	30-Mar-23	05-Apr-23										1st Floor DHD SG1003/1020 - Install COD Boards	
2348		1st Floor DHD SG1003/1020 - Install CRAC Units	5	5	31-Mar-23	06-Apr-23										1st Floor DHD SG1003/1020 - Install CRAC Units	
2349		1st Floor DHD SG1003/1020 - Install HDP	5	5	06-Apr-23	12-Apr-23										1st Floor DHD SG1003/1020 - Install HDP	
2350		1st Floor DHD SG1003/1020 - Install PDU	5	5	06-Apr-23	12-Apr-23										1st Floor DHD SG1003/1020 - Install PDU	
2351		1st Floor DHD SG1003/1020 - Final Connections CRAC Units	15	15	07-Apr-23	27-Apr-23										1st Floor DHD SG1003/1020 - Final Connections CRAC Units	
2352		1st Floor DHD SG1003/1020 - Pull and Terminate Feeders	15	15	13-Apr-23	03-May-23										1st Floor DHD SG1003/1020 - Pull and Terminate Feeders	
2353	Mechanical Gallery 1004 DH D			72	72	17-Jan-23	27-Apr-23									27-Apr-23, Mechanical Gallery 1004 DH D	
2354	Rough-In			57	57	17-Jan-23	06-Apr-23									06-Apr-23, Rough-In	
2355	MEP.D3.2C			1st Floor DHD MG1004 - Install Fire Protection	5	5	17-Jan-23	23-Jan-23								1st Floor DHD MG1004 - Install Fire Protection	
2356	MEP.D3.2C			1st Floor DHD MG1004 - In-wall Rough-in Electrical	3	3	24-Jan-23	26-Jan-23								1st Floor DHD MG1004 - In-wall Rough-in Electrical	
2357	MEP.D3.2C			1st Floor DHD MG1004 - Install OH Mechanical (Plumbing and HVAC)	5	5	24-Jan-23	30-Jan-23								1st Floor DHD MG1004 - Install OH Mechanical (Plumbing and HVAC)	
2358	FRME.D3.2			1st Floor DHD MG1004 - Insulate and Inspect	5	5	27-Jan-23	02-Feb-23								1st Floor DHD MG1004 - Insulate and Inspect	
2359	MEP.D3.2C			1st Floor DHD MG1004 - Install OH Electrical	5	5	31-Jan-23	06-Feb-23								1st Floor DHD MG1004 - Install OH Electrical	
2360	FRME.D3.2			1st Floor DHD MG1004 - Layout and Frame Walls	6	6	07-Mar-23	14-Mar-23								1st Floor DHD MG1004 - Layout and Frame Walls	
2361	FRME.D3.2			1st Floor DHD MG1004 - Install Drywall Upper	6	6	15-Mar-23	22-Mar-23								1st Floor DHD MG1004 - Install Drywall Upper	
2362	FRME.D3.2			1st Floor DHD MG1004 - Hang and Tape Drywall	6	6	23-Mar-23	30-Mar-23								1st Floor DHD MG1004 - Hang and Tape Drywall	
2363	FNSH.D3.1			1st Floor DHD MG1004 - Paint	2	2	31-Mar-23	03-Apr-23								1st Floor DHD MG1004 - Paint	
2364	FNSH.D3.1			1st Floor DHD MG1004 - Install Finishes	3	3	04-Apr-23	06-Apr-23								1st Floor DHD MG1004 - Install Finishes	
2365	Equipment				20	20	31-Mar-23	27-Apr-23								27-Apr-23, Equipment	
2366	EQPT.D3.2			1st Floor DHD MG1004 - Install CRAC Units	5	5	31-Mar-23	06-Apr-23								1st Floor DHD MG1004 - Install CRAC Units	
2367	EQPT.D3.2			1st Floor DHD MG1004 - Install HDP Boards	5	5	31-Mar-23	06-Apr-23								1st Floor DHD MG1004 - Install HDP Boards	
2368	EQPT.D3.2			1st Floor DHD MG1004 - Final Connections CRAC Units	15	15	07-Apr-23	27-Apr-23								1st Floor DHD MG1004 - Final Connections CRAC Units	
2369	EQPT.D3.2			1st Floor DHD MG1004 - Pull and Terminate Feeders	15	15	07-Apr-23	27-Apr-23								1st Floor DHD MG1004 - Pull and Terminate Feeders	
2370	DH D ROOM 1200				41	41	15-Mar-23	10-May-23								10-May-23, DH D ROOM 1200	
2371	Rough-In				41	41	15-Mar-23	10-May-23								10-May-23, Rough-In	
2372	FRME.D3.2			1st Floor DHD R1200 - Layout and Frame Walls	10	10	15-Mar-23	28-Mar-23								1st Floor DHD R1200 - Layout and Frame Walls	
2373	FRME.D3.2			1st Floor DHD R1200 - Install Drywall Upper	4	4	29-Mar-23	03-Apr-23								1st Floor DHD R1200 - Install Drywall Upper	
2374	MEP.D3.19			1st Floor DHD R1200 - Install Fire Protection	3	3	04-Apr-23	06-Apr-23								1st Floor DHD R1200 - Install Fire Protection	
2375	MEP.D3.19			1st Floor DHD R1200 - In-wall Rough-in Electrical	4	4	04-Apr-23	07-Apr-23								1st Floor DHD R1200 - In-wall Rough-in Electrical	
2376	MEP.D3.19			1st Floor DHD R1200 - Install OH Mechanical (Plumbing and HVAC)	5	5	10-Apr-23	14-Apr-23								1st Floor DHD R1200 - Install OH Mechanical (Plumbing and HVAC)	
2377	FRME.D3.2			1st Floor DHD R1200 - Insulate and Inspect	5	5	10-Apr-23	14-Apr-23								1st Floor DHD R1200 - Insulate and Inspect	
2378	MEP.D3.19			1st Floor DHD R1200 - Install OH Electrical	7	7	17-Apr-23	25-Apr-23								1st Floor DHD R1200 - Install OH Electrical	
2379	FRME.D3.2			1st Floor DHD R1200 - Hang and Tape Drywall	6	6	26-Apr-23	03-May-23								1st Floor DHD R1200 - Hang and Tape Drywall	
2380	FRME.D3.2			1st Floor DHD R1200 - Install Structural Grid	10	10	26-Apr-23	09-May-23								1st Floor DHD R1200 - Install Structural Grid	
2381	FNSH.D3.1			1st Floor DHD R1200 - Paint	2	2	04-May-23	05-May-23								1st Floor DHD R1200 - Paint	
2382																	

QTS HIL2 DC2, DC3, DC5 Construction Schedule				Classic Schedule Layout						12-Jul-22 15:37							
#	Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	2022					2023				2024	
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2
2393		FRME.D3.2 2nd Floor BDF1/2 - Insulate and Inspect	5	5	02-Feb-23	08-Feb-23											
2394		FRME.D3.2 2nd Floor BDF1/2 - Hang and Tape Drywall	6	6	09-Feb-23	16-Feb-23											
2395		FNSH.D3.1 2nd Floor BDF1/2 - Paint	2	2	17-Feb-23	21-Feb-23											
2396		FNSH.D3.1 2nd Floor BDF1/2 - Install Finishes	3	3	22-Feb-23	24-Feb-23											
2397		Equipment			51	51	22-Feb-23	03-May-23									
2398		EQPT.D3.2 2nd Floor BDF1/2 - Install HDP Panels	10	10	22-Feb-23	07-Mar-23											
2399		EQPT.D3.2 2nd Floor BDF1/2 - Set CRAC's	5	5	30-Mar-23	05-Apr-23											
2400		EQPT.D3.2 2nd Floor BDF1/2 - Set HUM	5	5	06-Apr-23	12-Apr-23											
2401		EQPT.D3.2 2nd Floor BDF1/2 - Final Connections CRAC Units	15	15	06-Apr-23	26-Apr-23											
2402		EQPT.D3.2 2nd Floor BDF1/2 - Pull and Terminate Feeders	15	15	13-Apr-23	03-May-23											
2403		Systems Gallery 2001 and 2010 DH B			91	91	16-Dec-22	26-Apr-23									
2404		Rough-In			58	58	16-Dec-22	10-Mar-23									
2405		MEP.D3.23 2nd Floor DHB SG 2001/2010 - Install Fire Protection	5	5	16-Dec-22	22-Dec-22											
2406		MEP.D3.23 2nd Floor DHB SG 2001/2010 - Install OH Mechanical (Plumbing and HVAC)	15	15	23-Dec-22	16-Jan-23											
2407		MEP.D3.23 2nd Floor DHB SG 2001/2010 - Install OH Electrical	20	20	23-Dec-22	23-Jan-23											
2408		FRME.D3.2 2nd Floor DHB SG 2001/2010 - Layout and Frame Walls	6	6	07-Feb-23	14-Feb-23											
2409		MEP.D3.23 2nd Floor DHB SG 2001/2010 - In-wall Rough-in Electrical	3	3	09-Feb-23	13-Feb-23											
2410		FRME.D3.2 2nd Floor DHB SG 2001/2010 - Insulate and Inspect	5	5	14-Feb-23	21-Feb-23											
2411		FRME.D3.2 2nd Floor DHB SG 2001/2010 - Install Drywall Upper	6	6	15-Feb-23	23-Feb-23											
2412		FRME.D3.2 2nd Floor DHB SG 2001/2010 - Hang and Tape Drywall	6	6	24-Feb-23	03-Mar-23											
2413		FNSH.D3.2 2nd Floor DHB SG 2001/2010 - Paint	2	2	06-Mar-23	07-Mar-23											
2414		FNSH.D3.2 2nd Floor DHB SG 2001/2010 - Install Finishes	3	3	08-Mar-23	10-Mar-23											
2415		Equipment			53	53	10-Feb-23	26-Apr-23									
2416		EQPT.D3.2 2nd Floor DHB SG 2001/2010 - Install Switch Gear	5	5	10-Feb-23	16-Feb-23											
2417		EQPT.D3.2 2nd Floor DHB SG 2001/2010 - Install ATS	5	5	10-Feb-23	16-Feb-23											
2418		EQPT.D3.2 2nd Floor DHB SG 2001/2010 - Install HDP	5	5	10-Feb-23	16-Feb-23											
2419		EQPT.D3.2 2nd Floor DHB SG 2001/2010 - Install PDU	5	5	10-Feb-23	16-Feb-23											
2420		EQPT.D3.2 2nd Floor DHB SG 2001/2010 - Install Reserve Busway	5	5	10-Feb-23	16-Feb-23											
2421		EQPT.D3.2 2nd Floor DHB SG 2001/2010 - Install COD Boards	5	5	30-Mar-23	05-Apr-23											
2422		EQPT.D3.2 2nd Floor DHB SG 2001/2010 - Install CRAC Units	5	5	30-Mar-23	05-Apr-23											
2423		EQPT.D3.2 2nd Floor DHB SG 2001/2010 - Final Connections CRAC Units	15	15	06-Apr-23	26-Apr-23											
2424		EQPT.D3.2 2nd Floor DHB SG 2001/2010 - Pull and Terminate Feeders	15	15	06-Apr-23	26-Apr-23											
2425		Mechanical Gallery 2002 DH B			91	91	16-Dec-22	26-Apr-23									
2426		Rough-In			64	64	16-Dec-22	20-Mar-23									
2427		FRME.D3.2 2nd Floor DHB MG 2002 - Layout and Frame Walls	6	6	16-Dec-22	23-Dec-22											
2428		MEP.D3.22 2nd Floor DHB MG 2002 - Install Fire Protection	1	1	16-Dec-22	16-Dec-22											
2429		MEP.D3.22 2nd Floor DHB MG 2002 - Install OH Mechanical (Plumbing and HVAC)	3	3	16-Dec-22	20-Dec-22											
2430		MEP.D3.22 2nd Floor DHB MG 2002 - Install OH Electrical	5	5	16-Dec-22	22-Dec-22											
2431		MEP.D3.22 2nd Floor DHB MG 2002 - In-wall Rough-in Electrical	3	3	19-Dec-22	21-Dec-22											
2432		FRME.D3.2 2nd Floor DHB MG 2002 - Insulate and Inspect	5	5	22-Dec-22	29-Dec-22											
2433		FRME.D3.2 2nd Floor DHB MG 2002 - Install Drywall Upper	6	6	27-Dec-22	04-Jan-23											
2434		FRME.D3.2 2nd Floor DHB MG 2002 - Hang and Tape Drywall	6	6	06-Mar-23	13-Mar-23											
2435		FNSH.D3.2 2nd Floor DHB MG 2002 - Paint	2	2	14-Mar-23	15-Mar-23											
2436		FNSH.D3.2 2nd Floor DHB MG 2002 - Install Finishes	3	3	16-Mar-23	20-Mar-23											
2437		Equipment			32	32	14-Mar-23	26-Apr-23									
2438		EQPT.D3.2 2nd Floor DHB MG 2002 - Install HDP Boards	5	5	14-Mar-23	20-Mar-23											
2439		EQPT.D3.2 2nd Floor DHB MG 2002 - Pull and Terminate Feeders	15	15	21-Mar-23	10-Apr-23											
2440		EQPT.D3.2 2nd Floor DHB MG 2002 - Install CRAC Units	5	5	30-Mar-23	05-Apr-23											



QTS HIL2 DC2, DC3, DC5 Construction Schedule				Classic Schedule Layout						12-Jul-22 15:37							
#	Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	2022					2023				2024	
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2
2441	EQPT.D3.2	2nd Floor DHB MG 2002 - Final Connections CRAC Units	15	15	06-Apr-23	26-Apr-23										2nd Floor DHB MG 2002 -Final Connections CRAC U	
2442	DH B ROOM 2100			64	64	27-Dec-22	28-Mar-23									28-Mar-23; DH B ROOM 2100	
2443	Rough-In			64	64	27-Dec-22	28-Mar-23									28-Mar-23, Rough-In	
2444	FRME.D3.2	2nd Floor DHB R2100 - Layout and Frame Walls	10	10	27-Dec-22	10-Jan-23										2nd Floor DHB R2100 - Layout and Frame Walls	
2445	MEP.D3.21	2nd Floor DHB R2100 - Install Fire Protection	3	3	27-Dec-22	29-Dec-22										2nd Floor DHB R2100 - Install Fire Protection	
2446	MEP.D3.21	2nd Floor DHB R2100 - Install OH Electrical	7	7	27-Dec-22	05-Jan-23										2nd Floor DHB R2100 - Install OH Electrical	
2447	FRME.D3.2	2nd Floor DHB R2100 - Install Structural Grid	10	10	06-Jan-23	19-Jan-23										2nd Floor DHB R2100 - Install Structural Grid	
2448	FRME.D3.2	2nd Floor DHB R2100 - Install Drywall Upper	4	4	11-Jan-23	16-Jan-23										2nd Floor DHB R2100 -Install Drywall Upper	
2449	MEP.D3.21	2nd Floor DHB R2100 - In-wall Rough-in Electrical	4	4	17-Jan-23	20-Jan-23										2nd Floor DHB R2100 - In-wall Rough-in Electrical	
2450	FRME.D3.2	2nd Floor DHB R2100 - Insulate and Inspect	5	5	23-Jan-23	27-Jan-23										2nd Floor DHB R2100 - Insulate and Inspect	
2451	FRME.D3.2	2nd Floor DHB R2100 - Hang and Tape Drywall	6	6	14-Mar-23	21-Mar-23										2nd Floor DHB R2100 - Hang and Tape Drywall	
2452	FNSH.D3.1	2nd Floor DHB R2100 - Paint	2	2	22-Mar-23	23-Mar-23										2nd Floor DHB R2100 - Paint	
2453	FNSH.D3.1	2nd Floor DHB R2100 - Install Finishes	3	3	24-Mar-23	28-Mar-23										2nd Floor DHB R2100- Install Finishes	
2454	Systems Gallery 2020 and 2003 DH C			79	79	17-Jan-23	08-May-23									08-May-23, Systems Gallery 2020 and 2003 DH C	
2455	Rough-In			59	59	17-Jan-23	10-Apr-23									10-Apr-23, Rough-In	
2456	MEP.D3.23	2nd Floor DHC 2020/2003 - Install Fire Protection	5	5	17-Jan-23	23-Jan-23										2nd Floor DHC 2020/2003- Install Fire Protection	
2457	MEP.D3.23	2nd Floor DHC 2020/2003 - Install OH Mechanical (Plumbing and HVAC)	15	15	24-Jan-23	13-Feb-23										2nd Floor DHC 2020/2003 -Install OH Mechanical (Plumbing a	
2458	MEP.D3.23	2nd Floor DHC 2020/2003 - Install OH Electrical	20	20	24-Jan-23	21-Feb-23										2nd Floor DHC 2020/2003 - Install OH Electrical	
2459	FRME.D3.2	2nd Floor DHC 2020/2003 - Layout and Frame Walls	6	6	27-Feb-23	06-Mar-23										2nd Floor DHC 2020/2003 - Layout and Frame Walls	
2460	FRME.D3.2	2nd Floor DHC 2020/2003 - Install Drywall Upper	6	6	07-Mar-23	14-Mar-23										2nd Floor DHC 2020/2003 - Install Drywall Upper	
2461	MEP.D3.23	2nd Floor DHC 2020/2003 - In-wall Rough-in Electrical	3	3	15-Mar-23	17-Mar-23										2nd Floor DHC 2020/2003 -In-wall Rough-in Electrical	
2462	FRME.D3.2	2nd Floor DHC 2020/2003 - Insulate and Inspect	5	5	20-Mar-23	24-Mar-23										2nd Floor DHC 2020/2003 - Insulate and Inspect	
2463	FRME.D3.2	2nd Floor DHC 2020/2003 - Hang and Tape Drywall	6	6	27-Mar-23	03-Apr-23										2nd Floor DHC 2020/2003 - Hang and Tape Drywall	
2464	FNSH.D3.2	2nd Floor DHC 2020/2003 - Paint	2	2	04-Apr-23	05-Apr-23										2nd Floor DHC 2020/2003 - Paint	
2465	FNSH.D3.2	2nd Floor DHC 2020/2003 - Install Finishes	3	3	06-Apr-23	10-Apr-23										2nd Floor DHC 2020/2003 - Install Finishes	
2466	Equipment			51	51	27-Feb-23	08-May-23									08-May-23, Equipment	
2467	EQPT.D3.2	2nd Floor DHC 2020/2003 - Install ATS	5	5	27-Feb-23	03-Mar-23										2nd Floor DHC 2020/2003 - Install ATS	
2468	EQPT.D3.2	2nd Floor DHC 2020/2003 - Install HDP	5	5	27-Feb-23	03-Mar-23										2nd Floor DHC 2020/2003 - Install HDP	
2469	EQPT.D3.2	2nd Floor DHC 2020/2003 - Install PDU	5	5	27-Feb-23	03-Mar-23										2nd Floor DHC 2020/2003 - Install PDU	
2470	EQPT.D3.2	2nd Floor DHC 2020/2003 - Install Reserve Busway	5	5	27-Feb-23	03-Mar-23										2nd Floor DHC 2020/2003 - Install Reserve Busway	
2471	EQPT.D3.2	2nd Floor DHC 2020/2003 - Install COD Boards	5	5	04-Apr-23	10-Apr-23										2nd Floor DHC 2020/2003 - Install COD Boards	
2472	EQPT.D3.2	2nd Floor DHC 2020/2003 - Install CRAC Units	5	5	04-Apr-23	10-Apr-23										2nd Floor DHC 2020/2003 - Install CRAC Units	
2473	EQPT.D3.2	2nd Floor DHC 2020/2003 - Install Switch Gear	5	5	11-Apr-23	17-Apr-23										2nd Floor DHC 2020/2003 - Install Switch Gear	
2474	EQPT.D3.2	2nd Floor DHC 2020/2003 - Final Connections CRAC Units	15	15	11-Apr-23	01-May-23										2nd Floor DHC 2020/2003 - Final Connections CRA	
2475	EQPT.D3.2	2nd Floor DHC 2020/2003 - Pull and Terminate Feeders	15	15	18-Apr-23	08-May-23										2nd Floor DHC 2020/2003 - Pull and Terminate Fee	
2476	Mechanical Gallery 2003 DH C			74	74	17-Jan-23	01-May-23									01-May-23, Mechanical Gallery 2003 DH C	
2477	Rough-In			30	30	17-Jan-23	28-Feb-23									28-Feb-23, Rough-In	
2478	FRME.D3.2	2nd Floor DHC MG 2003 - Layout and Frame Walls	5	5	17-Jan-23	23-Jan-23										2nd Floor DHC MG 2003 - Layout and Frame Walls	
2479	MEP.D3.22	2nd Floor DHC MG 2003 - Install Fire Protection	1	1	17-Jan-23	17-Jan-23										2nd Floor DHC MG 2003 - Install Fire Protection	
2480	MEP.D3.22	2nd Floor DHC MG 2003 - Install OH Mechanical (Plumbing and HVAC)	3	3	17-Jan-23	19-Jan-23										2nd Floor DHC MG 2003 - Install OH Mechanical (Plumbi	
2481	MEP.D3.23	2nd Floor DHC MG 2003 - Install OH Electrical	5	5	17-Jan-23	23-Jan-23										2nd Floor DHC MG 2003 - Install OH Electrical	
2482	MEP.D3.22	2nd Floor DHC MG 2003 - In-wall Rough-in Electrical	3	3	18-Jan-23	20-Jan-23										2nd Floor DHC MG 2003 - In-wall Rough-in Electrical	
2483	FRME.D3.2	2nd Floor DHC MG 2003 - Insulate and Inspect	5	5	23-Jan-23	27-Jan-23										2nd Floor DHC MG 2003 - Insulate and Inspect	
2484	FRME.D3.2	2nd Floor DHC MG 2003 - Install Drywall Upper	6	6	24-Jan-23	31-Jan-23										2nd Floor DHC MG 2003 - Install Drywall Upper	
2485	FRME.D3.2	2nd Floor DHC MG 2003 - Hang and Tape Drywall	6	6	01-Feb-23	08-Feb-23										2nd Floor DHC MG 2003 - Hang and Tape Drywall	
2486	FNSH.D3.2	2nd Floor DHC MG 2003 - Paint	2	2	09-Feb-23	10-Feb-23										2nd Floor DHC MG 2003 - Paint	
2487	FNSH.D3.2	2nd Floor DHC MG 2003 - Install Finishes	3	3	24-Feb-23	28-Feb-23				</							

QTS HIL2 DC2, DC3, DC5 Construction Schedule				Classic Schedule Layout					12-Jul-22 15:37									
#	Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	2022					2023					2024	
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	
2489	EQPT.D3.2	2nd Floor DHC MG 2003 - Ducting	4	4	13-Feb-23	16-Feb-23												
2490	EQPT.D3.2	2nd Floor DHC MG 2003 - Install HDP Boards		5	5	27-Feb-23	03-Mar-23											
2491	EQPT.D3.2	2nd Floor DHC MG 2003 - Pull and Terminate Feeders		15	15	06-Mar-23	24-Mar-23											
2492	EQPT.D3.2	2nd Floor DHC MG 2003 - Install CRAC Units		5	5	04-Apr-23	10-Apr-23											
2493	EQPT.D3.2	2nd Floor DHC MG 2003 - Final Connections CRAC Units		15	15	11-Apr-23	01-May-23											
2494	DH C ROOM 2200			34	34	24-Jan-23	13-Mar-23											
2495	Rough-In			34	34	24-Jan-23	13-Mar-23											
2496	FRME.D3.1	2nd Floor DHC R2200 - Layout and Frame Walls		10	10	24-Jan-23	06-Feb-23											
2497	MEP.D3.22	2nd Floor DHC R2200 - Install Fire Protection		3	3	24-Jan-23	26-Jan-23											
2498	MEP.D3.22	2nd Floor DHC R2200 - Install OH Electrical		7	7	24-Jan-23	01-Feb-23											
2499	FRME.D3.1	2nd Floor DHC R2200 - Install Structural Grid		10	10	02-Feb-23	15-Feb-23											
2500	FRME.D3.1	2nd Floor DHC R2200 - Install Drywall Upper		4	4	07-Feb-23	10-Feb-23											
2501	MEP.D3.22	2nd Floor DHC R2200 - In-wall Rough-in Electrical		4	4	13-Feb-23	16-Feb-23											
2502	FRME.D3.1	2nd Floor DHC R2200 - Insulate and Inspect		5	5	17-Feb-23	24-Feb-23											
2503	FRME.D3.1	2nd Floor DHC R2200 - Hang and Tape Drywall		6	6	27-Feb-23	06-Mar-23											
2504	FNSH.D3.1	2nd Floor DHC R2200 - Paint		2	2	07-Mar-23	08-Mar-23											
2505	FNSH.D3.2	2nd Floor DHC R2200 - Install Finishes		3	3	09-Mar-23	13-Mar-23											
2506	Closeout and Final Inspections			84	84	27-Apr-23	24-Aug-23											
2507	PNCH.D3.1190	Punch MPOE/BDF		15	15	27-Apr-23	17-May-23											
2508	PNCH.D3.1200	Punch DH A		15	15	27-Apr-23	17-May-23											
2509	PNCH.D3.1210	Punch DH B		15	15	27-Apr-23	17-May-23											
2510	PNCH.D3.1240	Punch House		15	15	27-Apr-23	17-May-23											
2511	PNCH.D3.1220	Punch DH C		15	15	02-May-23	22-May-23											
2512	PNCH.D3.1230	Punch DH D		15	15	11-May-23	01-Jun-23											
2513	PNCH.D3.1150	Elevators Final Inspections		5	5	23-Jun-23	29-Jun-23											
2514	PNCH.D3.1130	Electrical Final Inspections - DC2		5	5	02-Aug-23	08-Aug-23											
2515	PNCH.D3.1160	Fire and Life Safety Final Inspections		5	5	02-Aug-23	08-Aug-23											
2516	PNCH.D3.1180	Low Voltage Final Inspections		5	5	02-Aug-23	08-Aug-23											
2517	PNCH.D3.1140	Mechanical Final Inspections		5	5	04-Aug-23	10-Aug-23											
2518	PNCH.D3.1170	Building Final Inspections		5	5	11-Aug-23	17-Aug-23											
2519	PNCH.D3.1250	Receive Certificate of Occupancy		5	5	18-Aug-23	24-Aug-23											
2520	Startup Commissioning and Turnover			296	296	06-Sep-22	09-Nov-23											
2521	Startup Level 3CX			228	228	06-Sep-22	03-Aug-23											
2522	Energize Utility Circuits			196	196	06-Sep-22	19-Jun-23											
2523	STUP.D3.1	Utility Power Available (DC3 NUF Power Available)		0	0		06-Sep-22											
2524	STUP.D3.1	Utility Power Available (DC3 SUF Power Available)		0	0		05-Oct-22											
2525	STUP.D3.1	Energize MV A & B		10	10	28-Mar-23	10-Apr-23											
2526	STUP.D3.1	Energize MV D & C		10	10	06-Jun-23	19-Jun-23											
2527	Energize MPOD/BDF			39	39	11-Apr-23	05-Jun-23											
2528	STUP.D3.1	MPOE/BDF - Startup Transformers		10	10	11-Apr-23	24-Apr-23											
2529	STUP.D3.1	MPOE/BDF - Startup HUM		5	5	13-Apr-23	19-Apr-23											
2530	STUP.D3.1	MPOE/BDF - Energize UPS Pods		13	13	25-Apr-23	11-May-23											
2531	STUP.D3.1	MPOE/BDF - Startup MPOE Generators		10	10	25-Apr-23	08-May-23											
2532	STUP.D3.1	MPOE/BDF - Energize ATS/PDU		15	15	12-May-23	01-Jun-23											
2533	STUP.D3.1	MPOE/BDF - Startup CRAC Units		15	15	15-May-23	05-Jun-23											
2534	Energize Data Hall A-B			33	33	25-Apr-23	09-Jun-23											
2535	STUP.D3.1	DHA/B - Startup Transformers		5	5	25-Apr-23	01-May-23											
2536	STUP.D3.1	DHA/B - Energize SWGR		5	5	02-May-23	08-May-23											
Remaining Level of Effort				Remaining Work		Milestone												
Actual Work				Critical Remaining Work		Summary												
Page 53 of 74											TASK filter: All Activities							
© Oracle Corporation																		

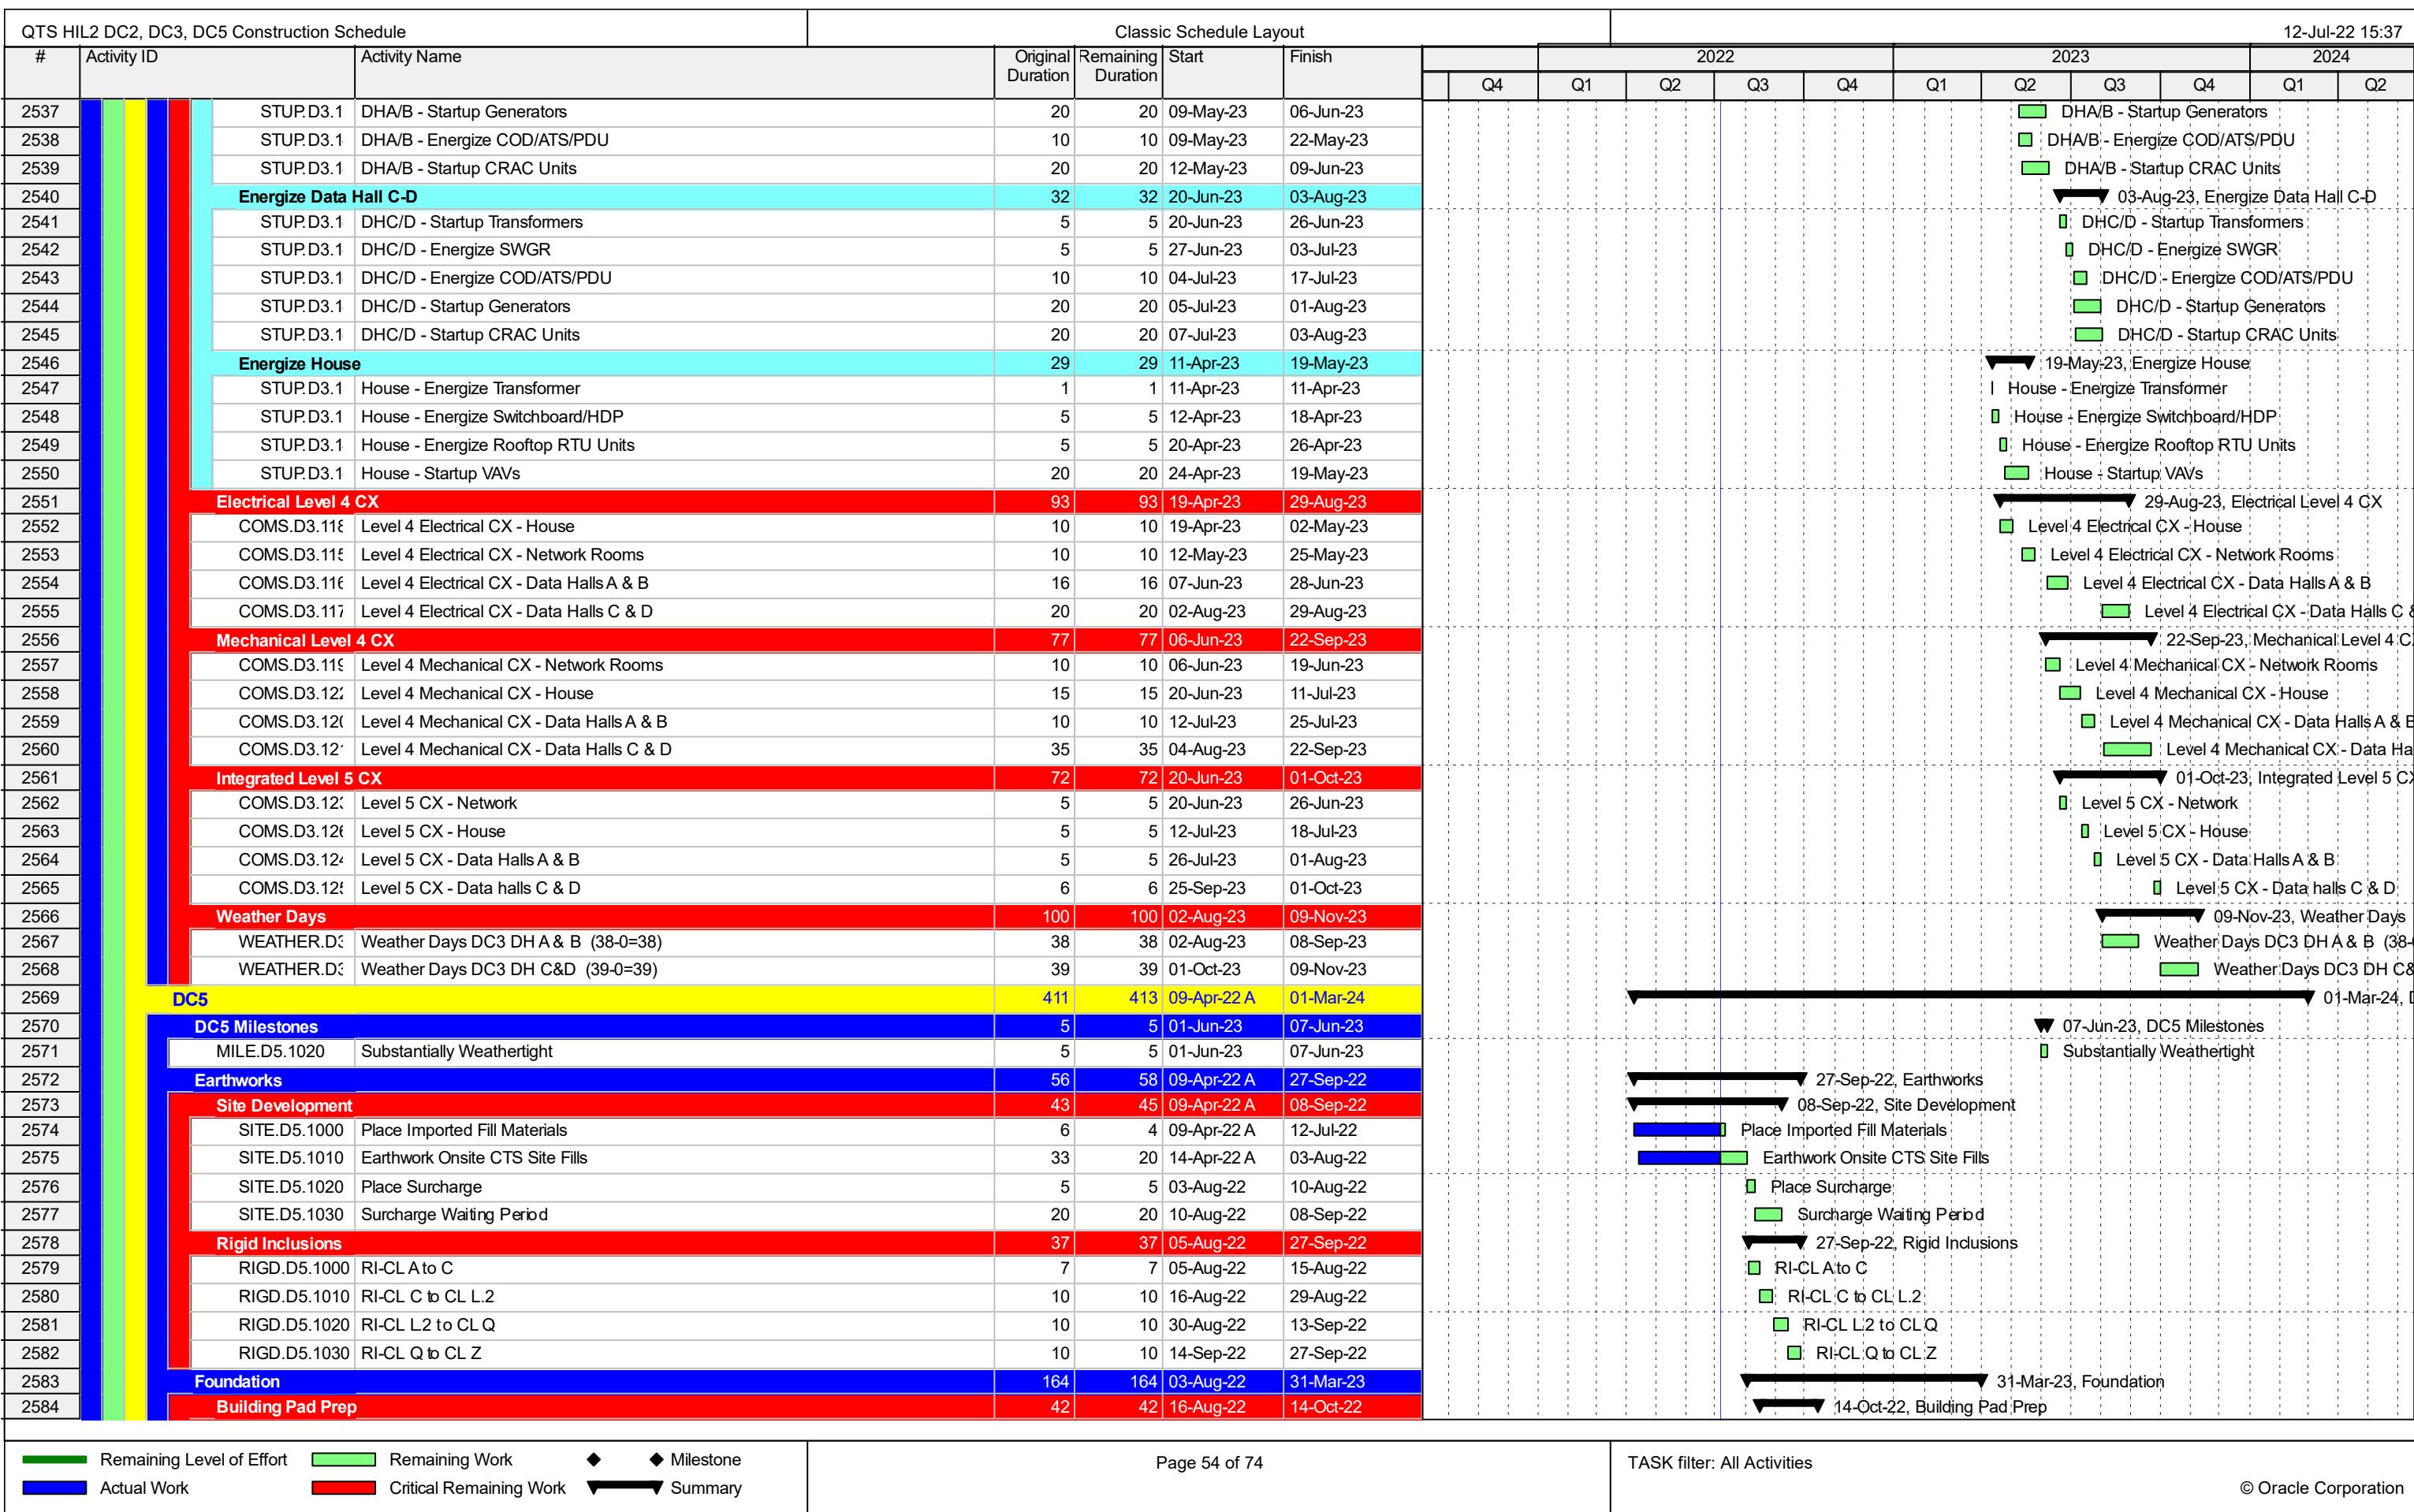

QTS HIL2 DC2, DC3, DC5 Construction Schedule				Classic Schedule Layout						12-Jul-22 15:37								
#	Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish		2022				2023				2024		
								Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2
2585		Area Wide	10	10	16-Aug-22	29-Aug-22												
2586	FOND.D5.1	Move Surcharge to DC5	5	5	16-Aug-22	22-Aug-22												
2587	FOND.D5.1	Rock and Compact Slab	5	5	23-Aug-22	29-Aug-22												
2588		Grid A - C	10	10	09-Sep-22	22-Sep-22												
2589	UTIL.D5.11	Under-slab Utilities CL A to C	5	5	09-Sep-22	15-Sep-22												
2590	FOND.D5.1	Backfill/Compact CL A to C	5	5	16-Sep-22	22-Sep-22												
2591		Grid C - L	10	10	16-Sep-22	29-Sep-22												
2592	UTIL.D5.11	Under-slab Utilities CL C to L2	5	5	16-Sep-22	22-Sep-22												
2593	FOND.D5.1	Backfill/Compact CL C to L2	5	5	23-Sep-22	29-Sep-22												
2594		Grid L - Q.1	10	10	23-Sep-22	06-Oct-22												
2595	UTIL.D5.11	Under-slab Utilities CL L.2 to Q	5	5	23-Sep-22	29-Sep-22												
2596	FOND.D5.1	Backfill/Compact CL L.2 to Q	5	5	30-Sep-22	06-Oct-22												
2597		Grid Q.1 - Z	10	10	30-Sep-22	14-Oct-22												
2598	UTIL.D5.11	Under-slab Utilities CL Q to Z	5	5	30-Sep-22	06-Oct-22												
2599	FOND.D5.1	Backfill/Compact CL Q to Z	5	5	07-Oct-22	14-Oct-22												
2600		DC5 Foundations	85	85	03-Aug-22	07-Dec-22												
2601		Grid A-C	69	69	03-Aug-22	10-Nov-22												
2602	FOND.D5.1	Found A-C - Survey Footing Excavation	3	3	03-Aug-22	08-Aug-22												
2603	FOND.D5.1	Found A-C - Dig Footings	3	3	13-Oct-22	17-Oct-22												
2604	FOND.D5.1	Found A-C - Survey Formwork	1	1	18-Oct-22	18-Oct-22												
2605	FOND.D5.1	Found A-C - Form Foundations (#1 Formwork Delivery)	5	5	19-Oct-22	25-Oct-22												
2606	FOND.D5.1	Found A-C - Install Anchor Bolts	5	5	19-Oct-22	25-Oct-22												
2607	FOND.D5.1	Found A-C - Install Reinforcement	5	5	20-Oct-22	26-Oct-22												
2608	FOND.D5.1	Found A-C - Install Elevator Pit	5	5	27-Oct-22	02-Nov-22												
2609	FOND.D5.1	Found A-C - Place Foundations	1	1	27-Oct-22	27-Oct-22												
2610	FOND.D5.1	Found A-C - Strip Foundations	3	3	28-Oct-22	01-Nov-22												
2611	FOND.D5.1	Found A-C - Plinths and Grade Beams	5	5	28-Oct-22	03-Nov-22												
2612	FOND.D5.1	Found A-C - Waterproof/Insulate	3	3	03-Nov-22	07-Nov-22												
2613	FOND.D5.1	Found A-C - Backfill Foundations	3	3	08-Nov-22	10-Nov-22												
2614		Grid C-L	77	77	03-Aug-22	23-Nov-22												
2615	FOND.D5.1	Found C-L - Survey Footing Excavation	3	3	03-Aug-22	08-Aug-22												
2616	FOND.D5.1	Found C-L - Dig Footings	3	3	18-Oct-22	20-Oct-22												
2617	FOND.D5.1	Found C-L - Survey Formwork	1	1	21-Oct-22	21-Oct-22												
2618	FOND.D5.1	Found C-L - Form Foundations (#2 Formwork Delivery)	5	5	26-Oct-22	01-Nov-22												
2619	FOND.D5.1	Found C-L - Instal Anchor Bolts	5	5	26-Oct-22	01-Nov-22												
2620	FOND.D5.1	Found C-L - Instal Reinforcement	5	5	02-Nov-22	08-Nov-22												
2621	FOND.D5.1	Found C-L - Place Foundations	1	1	09-Nov-22	09-Nov-22												
2622	FOND.D5.1	Found C-L - Strip Foundations	3	3	10-Nov-22	15-Nov-22												
2623	FOND.D5.1	Found C-L - Plinths and Grade Beams	5	5	10-Nov-22	17-Nov-22												
2624	FOND.D5.1	Found C-L - Waterproof/Insulate	3	3	16-Nov-22	18-Nov-22												
2625	FOND.D5.1	Found C-L - Backfill Foundations	3	3	21-Nov-22	23-Nov-22												
2626		Grid L-Q.1	78	78	03-Aug-22	28-Nov-22												
2627	FOND.D5.1	Found L-Q.1 - Survey Footing Excavation	3	3	03-Aug-22	08-Aug-22												
2628	FOND.D5.1	Found L-Q.1 - Dig Footings	3	3	14-Sep-22	16-Sep-22												
2629	FOND.D5.1	Found L-Q.1 - Survey Formwork	1	1	19-Sep-22	19-Sep-22												
2630	FOND.D5.1	Found L-Q.1 - Form Foundations (Formwork From A-C)	5	5	02-Nov-22	08-Nov-22												
2631	FOND.D5.1	Found L-Q.1 - Install Anchor Bolts	5	5	02-Nov-22	08-Nov-22												
2632	FOND.D5.1	Found L-Q.1 - Install Reinforcement	5	5	03-Nov-22	09-Nov-22												



QTS HIL2 DC2, DC3, DC5 Construction Schedule				Classic Schedule Layout						12-Jul-22 15:37									
#	Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	2022				2023				2024				
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2		
2633	FOND.D5.1	Found L-Q.1 - Place Foundations	1	1	10-Nov-22	10-Nov-22													
2634		Found L-Q.1 - Strip Foundations		3	3	14-Nov-22													
2635		Found L-Q.1 - Plinths and Grade Beams		5	5	14-Nov-22													
2636		Found L-Q.1 - Waterproof/Insulate		3	3	17-Nov-22													
2637		Found L-Q.1 - Backfill Foundations		3	3	22-Nov-22													
2638		Grid Q.1-Z	60	60	08-Sep-22	07-Dec-22													
2639		FOND.D5.1 Grid Q.1-Z - Survey Footing Excavation		3	3	08-Sep-22													
2640		FOND.D5.1 Grid Q.1-Z - Dig Footings		3	3	28-Sep-22													
2641		FOND.D5.1 Grid Q.1-Z - Survey Formwork		1	1	03-Oct-22													
2642		FOND.D5.1 Grid Q.1-Z - Form Foundations (Formwork From C-L)		5	5	14-Nov-22													
2643		FOND.D5.1 Grid Q.1-Z - Install Anchor Bolts		5	5	14-Nov-22													
2644		FOND.D5.1 Grid Q.1-Z - Install Reinforcement		5	5	15-Nov-22													
2645		FOND.D5.1 Grid Q.1-Z - Place Foundations		1	1	22-Nov-22													
2646		FOND.D5.1 Grid Q.1-Z - Strip Foundations		3	3	23-Nov-22													
2647		FOND.D5.1 Grid Q.1-Z - Plinths and Grade Beams		5	5	23-Nov-22													
2648		FOND.D5.1 Grid Q.1-Z - Waterproof/Insulate		3	3	30-Nov-22													
2649		FOND.D5.1 Grid Q.1-Z - Backfill Foundations		3	3	05-Dec-22													
2650	DC5 Slab On Grade	DC5 Slab On Grade	95	95	14-Nov-22	31-Mar-23													
2651		Grid A-C	16	16	14-Nov-22	07-Dec-22													
2652		Pour 1	16	16	14-Nov-22	07-Dec-22													
2653		SOG.D5 SOG A-C P1 - Fine Grade CLA to C		3	3	14-Nov-22													
2654		SOG.D5 SOG A-C P1 - Edgeforms/Diamonds		2	2	17-Nov-22													
2655		SOG.D5 SOG A-C P1 - Vapor Barrier		1	1	21-Nov-22													
2656		SOG.D5 SOG A-C P1 - Install reinforcement		3	3	22-Nov-22													
2657		SOG.D5 SOG A-C P1 - MEP Final Set		1	1	29-Nov-22													
2658		SOG.D5 SOG A-C P1 - Place SOG		1	1	30-Nov-22													
2659		SOG.D5 SOG A-C P1 - Cure SOG		5	5	01-Dec-22													
2660		Grid C-L	16	16	28-Nov-22	19-Dec-22													
2661		Pour 2	16	16	28-Nov-22	19-Dec-22													
2662		SOG.D5 SOG C-L P2 - Fine Grade		3	3	28-Nov-22													
2663		SOG.D5 SOG C-L P2 - Edgeforms/Diamonds		2	2	01-Dec-22													
2664		SOG.D5 SOG C-L P2 - Vapor Barrier		1	1	05-Dec-22													
2665		SOG.D5 SOG C-L P2 - Install reinforcement		3	3	06-Dec-22													
2666		SOG.D5 SOG C-L P2 - MEP Final Set		1	1	09-Dec-22													
2667		SOG.D5 SOG C-L P2 - Place SOG		1	1	12-Dec-22													
2668		SOG.D5 SOG C-L P2 - Cure SOG		5	5	13-Dec-22													
2669		Pour 3	16	16	28-Nov-22	19-Dec-22													
2670		SOG.D5 SOG C-L P3 - Fine Grade		3	3	28-Nov-22													
2671		SOG.D5 SOG C-L P3 - Edgeforms/Diamonds		2	2	01-Dec-22													
2672		SOG.D5 SOG C-L P3 - Vapor Barrier		1	1	05-Dec-22													
2673		SOG.D5 SOG C-L P3 - Install reinforcement		3	3	06-Dec-22													
2674		SOG.D5 SOG C-L P3 - MEP Final Set		1	1	09-Dec-22													
2675		SOG.D5 SOG C-L P3 - Place SOG		1	1	12-Dec-22													
2676		SOG.D5 SOG C-L P3 - Cure SOG		5	5	13-Dec-22													
2677	Grid L-Q.1	Grid L-Q.1	16	16	29-Nov-22	20-Dec-22													
2678		Pour 4	16	16	29-Nov-22	20-Dec-22													
2679		SOG.D5 SOG L-Q.1 P4 - Fine Grade		3	3	29-Nov-22													
2680		SOG.D5 SOG L-Q.1 P4 - Edgeforms/Diamonds		2	2	02-Dec-22													

Remaining Level of Effort	Remaining Work	Milestone	Actual Work	Critical Remaining Work	Summary	Page 56 of 74	TASK filter: All Activities	© Oracle Corporation
---------------------------	----------------	-----------	-------------	-------------------------	---------	---------------	-----------------------------	----------------------

QTS HIL2 DC2, DC3, DC5 Construction Schedule				Classic Schedule Layout					12-Jul-22 15:37										
#	Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	2022					2023				2024			
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2		
2681		SOG.D5 SOG L-Q.1 P4 - Vapor Barrier	1	1	06-Dec-22	06-Dec-22						I	SOG L-Q.1 P4 - Vapor Barrier						
2682		SOG.D5 SOG L-Q.1 P4 - Install reinforcement		3	3	07-Dec-22	09-Dec-22					I	SOG L-Q.1 P4 - Install reinforcement						
2683		SOG.D5 SOG L-Q.1 P4 - MEP Final Set		1	1	12-Dec-22	12-Dec-22					I	SOG L-Q.1 P4 - MEP Final Set						
2684		SOG.D5 SOG L-Q.1 P4 - Place SOG		1	1	13-Dec-22	13-Dec-22					I	SOG L-Q.1 P4 - Place SOG						
2685		SOG.D5 SOG L-Q.1 P4 - Cure SOG		5	5	14-Dec-22	20-Dec-22					I	SOG L-Q.1 P4 - Cure SOG						
2686	Grid Q.1-Z			16	16	08-Dec-22	30-Dec-22					▼	30-Dec-22, Grid Q.1-Z						
2687	Pour 5			16	16	08-Dec-22	30-Dec-22					▼	30-Dec-22, Pour 5						
2688		SOG.D5 SOG Q.1-Z P5 - Fine Grade		3	3	08-Dec-22	12-Dec-22					I	SOG Q.1-Z P5 - Fine Grade						
2689		SOG.D5 SOG Q.1-Z P5 - Edgeforms/Diamonds		2	2	13-Dec-22	14-Dec-22					I	SOG Q.1-Z P5 - Edgeforms/Diamonds						
2690		SOG.D5 SOG Q.1-Z P5 - Vapor Barrier		1	1	15-Dec-22	15-Dec-22					I	SOG Q.1-Z P5 - Vapor Barrier						
2691		SOG.D5 SOG Q.1-Z P5 - Install reinforcement		3	3	16-Dec-22	20-Dec-22					I	SOG Q.1-Z P5 - Install reinforcement						
2692		SOG.D5 SOG Q.1-Z P5 - MEP Final Set		1	1	21-Dec-22	21-Dec-22					I	SOG Q.1-Z P5 - MEP Final Set						
2693		SOG.D5 SOG Q.1-Z P5 - Place SOG		1	1	22-Dec-22	22-Dec-22					I	SOG Q.1-Z P5 - Place SOG						
2694		SOG.D5 SOG Q.1-Z P5 - Cure SOG		5	5	23-Dec-22	30-Dec-22					I	SOG Q.1-Z P5 - Cure SOG						
2695	Pour 6			16	16	08-Dec-22	30-Dec-22					▼	30-Dec-22, Pour 6						
2696		SOG.D5 SOG Q.1-Z P6 - Fine Grade		3	3	08-Dec-22	12-Dec-22					I	SOG Q.1-Z P6 - Fine Grade						
2697		SOG.D5 SOG Q.1-Z P6 - Edgeforms/Diamonds		2	2	13-Dec-22	14-Dec-22					I	SOG Q.1-Z P6 - Edgeforms/Diamonds						
2698		SOG.D5 SOG Q.1-Z P6 - Vapor Barrier		1	1	15-Dec-22	15-Dec-22					I	SOG Q.1-Z P6 - Vapor Barrier						
2699		SOG.D5 SOG Q.1-Z P6 - Install reinforcement		3	3	16-Dec-22	20-Dec-22					I	SOG Q.1-Z P6 - Install reinforcement						
2700		SOG.D5 SOG Q.1-Z P6 - MEP Final Set		1	1	21-Dec-22	21-Dec-22					I	SOG Q.1-Z P6 - MEP Final Set						
2701		SOG.D5 SOG Q.1-Z P6 - Place SOG		1	1	22-Dec-22	22-Dec-22					I	SOG Q.1-Z P6 - Place SOG						
2702		SOG.D5 SOG Q.1-Z P6 - Cure SOG		5	5	23-Dec-22	30-Dec-22					I	SOG Q.1-Z P6 - Cure SOG						
2703	Leave Out			44	44	30-Jan-23	31-Mar-23					▼	31-Mar-23, Leave Out						
2704	Leave Out Pour 1 C-F.4			16	16	30-Jan-23	21-Feb-23					▼	21-Feb-23, Leave Out Pour 1 C-F.4						
2705		SOG.D5 SOG Leave Out P2 - Fine Grade CLC-F.4		3	3	30-Jan-23	01-Feb-23					I	SOG Leave Out P2 - Fine Grade CLC-F.4						
2706		SOG.D5 SOG Leave Out P2 - Edgeforms/Diamonds		2	2	02-Feb-23	03-Feb-23					I	SOG Leave Out P2 - Edgeforms/Diamonds						
2707		SOG.D5 SOG Leave Out P2 - Vapor Barrier		1	1	06-Feb-23	06-Feb-23					I	SOG Leave Out P2 - Vapor Barrier						
2708		SOG.D5 SOG Leave Out P2 - Install reinforcement		3	3	07-Feb-23	09-Feb-23					I	SOG Leave Out P2 - Install reinforcement						
2709		SOG.D5 SOG Leave Out P2 - MEP Final Set		1	1	10-Feb-23	10-Feb-23					I	SOG Leave Out P2 - MEP Final Set						
2710		SOG.D5 SOG Leave Out P2 - Place SOG		1	1	13-Feb-23	13-Feb-23					I	SOG Leave Out P2 - Place SOG						
2711		SOG.D5 SOG Leave Out P2 - Cure SOG		5	5	14-Feb-23	21-Feb-23					I	SOG Leave Out P2 - Cure SOG						
2712	Leave Out Pour 2 F.4-J.8			16	16	03-Feb-23	27-Feb-23					▼	27-Feb-23, Leave Out Pour 2 F.4-J.8						
2713		SOG.D5 SOG Leave Out P3 - Fine Grade CL F.4-J.8		3	3	03-Feb-23	07-Feb-23					I	SOG Leave Out P3 - Fine Grade CL F.4-J.8						
2714		SOG.D5 SOG Leave Out P3 - Edgeforms/Diamonds		2	2	08-Feb-23	09-Feb-23					I	SOG Leave Out P3 - Edgeforms/Diamonds						
2715		SOG.D5 SOG Leave Out P3 - Vapor Barrier		1	1	10-Feb-23	10-Feb-23					I	SOG Leave Out P3 - Vapor Barrier						
2716		SOG.D5 SOG Leave Out P3 - Install reinforcement		3	3	13-Feb-23	15-Feb-23					I	SOG Leave Out P3 - Install reinforcement						
2717		SOG.D5 SOG Leave Out P3 - MEP Final Set		1	1	16-Feb-23	16-Feb-23					I	SOG Leave Out P3 - MEP Final Set						
2718		SOG.D5 SOG Leave Out P3 - Place SOG		1	1	17-Feb-23	17-Feb-23					I	SOG Leave Out P3 - Place SOG						
2719		SOG.D5 SOG Leave Out P3 - Cure SOG		5	5	21-Feb-23	27-Feb-23					I	SOG Leave Out P3 - Cure SOG						
2720	Leave Out Pour 3 J.8 - M.5			16	16	13-Feb-23	07-Mar-23					▼	07-Mar-23, Leave Out Pour 3 J.8 - M.5						
2721		SOG.D5 SOG Leave Out P4 - Fine Grade CL J.8 - M.5		3	3	13-Feb-23	15-Feb-23					I	SOG Leave Out P4 - Fine Grade CL J.8 - M.5						
2722		SOG.D5 SOG Leave Out P4 - Edgeforms/Diamonds		2	2	16-Feb-23	17-Feb-23					I	SOG Leave Out P4 - Edgeforms/Diamonds						
2723		SOG.D5 SOG Leave Out P4 - Vapor Barrier		1	1	21-Feb-23	21-Feb-23					I	SOG Leave Out P4 - Vapor Barrier						
2724		SOG.D5 SOG Leave Out P4 - Install reinforcement		3	3	22-Feb-23	24-Feb-23					I	SOG Leave Out P4 - Install reinforcement						
2725		SOG.D5 SOG Leave Out P4 - MEP Final Set		1	1	27-Feb-23	27-Feb-23					I	SOG Leave Out P4 - MEP Final Set						
2726		SOG.D5 SOG Leave Out P4 - Place SOG		1	1	28-Feb-23	28-Feb-23					I	SOG Leave Out P4 - Place SOG						
2727		SOG.D5 SOG Leave Out P4 - Cure SOG		5	5	01-Mar-23	07-Mar-23					I	SOG Leave Out P4 - Cure SOG						
2728	Leave Out Pour 4 M.5 - Q			16	16	17-Feb-23	13-Mar-23					▼	13-Mar-23, Leave Out Pour 4 M.5 - Q						
Remaining Level of Effort				Remaining Work	◆	◆ Milestone	Page 57 of 74								TASK filter: All Activities				
Actual Work				Critical Remaining Work	▼	Summary									© Oracle Corporation				

QTS HIL2 DC2, DC3, DC5 Construction Schedule				Classic Schedule Layout						12-Jul-22 15:37								
#	Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	2022		2023				2024					
					Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2			
2729	SOG.D5	SOG Leave Out P5 - Fine Grade CL M.5 - Q	3	3	17-Feb-23	22-Feb-23											SOG Leave Out P5 - Fine Grade CL M.5 - Q	
2730	SOG.D5	SOG Leave Out P5 - Edgeforms/Diamonds	2	2	23-Feb-23	24-Feb-23											SOG Leave Out P5 - Edgeforms/Diamonds	
2731	SOG.D5	SOG Leave Out P5 - Vapor Barrier	1	1	27-Feb-23	27-Feb-23											SOG Leave Out P5 - Vapor Barrier	
2732	SOG.D5	SOG Leave Out P5 - Install reinforcement	3	3	28-Feb-23	02-Mar-23											SOG Leave Out P5 - Install reinforcement	
2733	SOG.D5	SOG Leave Out P5 - MEP Final Set	1	1	03-Mar-23	03-Mar-23											SOG Leave Out P5 - MEP Final Set	
2734	SOG.D5	SOG Leave Out P5 - Place SOG	1	1	06-Mar-23	06-Mar-23											SOG Leave Out P5 - Place SOG	
2735	SOG.D5	SOG Leave Out P5 - Cure SOG	5	5	07-Mar-23	13-Mar-23											SOG Leave Out P5 - Cure SOG	
2736	Leave Out Pour 5 Q - Z			16	16	10-Mar-23	31-Mar-23										31-Mar-23, Leave Out Pour 5 Q - Z	
2737	SOG.D5	SOG Leave Out P6 - Fine Grade CL Q - Z	3	3	10-Mar-23	14-Mar-23											SOG Leave Out P6 - Fine Grade CL Q - Z	
2738	SOG.D5	SOG Leave Out P6 - Edgeforms/Diamonds	2	2	15-Mar-23	16-Mar-23											SOG Leave Out P6 - Edgeforms/Diamonds	
2739	SOG.D5	SOG Leave Out P6 - Vapor Barrier	1	1	17-Mar-23	17-Mar-23											SOG Leave Out P6 - Vapor Barrier	
2740	SOG.D5	SOG Leave Out P6 - Install reinforcement	3	3	20-Mar-23	22-Mar-23											SOG Leave Out P6 - Install reinforcement	
2741	SOG.D5	SOG Leave Out P6 - MEP Final Set	1	1	23-Mar-23	23-Mar-23											SOG Leave Out P6 - MEP Final Set	
2742	SOG.D5	SOG Leave Out P6 - Place SOG	1	1	24-Mar-23	24-Mar-23											SOG Leave Out P6 - Place SOG	
2743	SOG.D5	SOG Leave Out P6 - Cure SOG	5	5	27-Mar-23	31-Mar-23											SOG Leave Out P6 - Cure SOG	
2744	DC5 SOMD			45	45	16-Jan-23	20-Mar-23										20-Mar-23, DC5 SOMD	
2745	A-Z			45	45	16-Jan-23	20-Mar-23										20-Mar-23, A-Z	
2746	Grid A - C			9	9	16-Jan-23	26-Jan-23										26-Jan-23, Grid A - C	
2747	Pour 1 A - C			9	9	16-Jan-23	26-Jan-23										26-Jan-23, Pour 1 A - C	
2748	SOM	SOMD A-C P1 - As-Built Structure	1	1	16-Jan-23	16-Jan-23											SOMD A-C P1 - As-Built Structure	
2749	SOM	SOMD A-C P1 - MEP	3	3	17-Jan-23	19-Jan-23											SOMD A-C P1 - MEP	
2750	SOM	SOMD A-C P1 - Edgeforms/Embeds	3	3	17-Jan-23	19-Jan-23											SOMD A-C P1 - Edgeforms/Embeds	
2751	SOM	SOMD A-C P1 - Install Reinforcement	3	3	20-Jan-23	24-Jan-23											SOMD A-C P1 - Install Reinforcement	
2752	SOM	SOMD A-C P1 - MEP Final	1	1	25-Jan-23	25-Jan-23											SOMD A-C P1 - MEP Final	
2753	SOM	SOMD A-C P1 - Place Slab	1	1	26-Jan-23	26-Jan-23											SOMD A-C P1 - Place Slab	
2754	Grid C - L			17	17	26-Jan-23	17-Feb-23										17-Feb-23, Grid C - L	
2755	Pour 2 C - F.4			7	7	26-Jan-23	03-Feb-23										03-Feb-23, Pour 2 C - F.4	
2756	SOM	SOMD C-F.4 P2 - MEP	2	2	26-Jan-23	27-Jan-23											SOMD C-F.4 P2 - MEP	
2757	SOM	SOMD C-F.4 P2 - Edgeforms/Embeds	2	2	26-Jan-23	27-Jan-23											SOMD C-F.4 P2 - Edgeforms/Embeds	
2758	SOM	SOMD C-F.4 P2 - Install Reinforcement	3	3	30-Jan-23	01-Feb-23											SOMD C-F.4 P2 - Install Reinforcement	
2759	SOM	SOMD C-F.4 P2 - MEP Final	1	1	02-Feb-23	02-Feb-23											SOMD C-F.4 P2 - MEP Final	
2760	SOM	SOMD C-F.4 P2 - Place Slab	1	1	03-Feb-23	03-Feb-23											SOMD C-F.4 P2 - Place Slab	
2761	Pour 3 F.4 - J.8			7	7	01-Feb-23	09-Feb-23										09-Feb-23, Pour 3 F.4 - J.8	
2762	SOM	SOMD F.4-J.8 P3 - MEP	2	2	01-Feb-23	02-Feb-23											SOMD F.4-J.8 P3 - MEP	
2763	SOM	SOMD F.4-J.8 P3 - Edgeforms/Embeds	2	2	01-Feb-23	02-Feb-23											SOMD F.4-J.8 P3 - Edgeforms/Embeds	
2764	SOM	SOMD F.4-J.8 P3 - Install Reinforcement	3	3	03-Feb-23	07-Feb-23											SOMD F.4-J.8 P3 - Install Reinforcement	
2765	SOM	SOMD F.4-J.8 P3 - MEP Final	1	1	08-Feb-23	08-Feb-23											SOMD F.4-J.8 P3 - MEP Final	
2766	SOM	SOMD F.4-J.8 P3 - Place Slab	1	1	09-Feb-23	09-Feb-23											SOMD F.4-J.8 P3 - Place Slab	
2767	Pour 4 J.8 - M.5			7	7	09-Feb-23	17-Feb-23										17-Feb-23, Pour 4 J.8 - M.5	
2768	SOM	SOMD J.8-M.5 P4 - MEP	2	2	09-Feb-23	10-Feb-23											SOMD J.8-M.5 P4 - MEP	
2769	SOM	SOMD J.8-M.5 P4 - Edgeforms/Embeds	2	2	09-Feb-23	10-Feb-23											SOMD J.8-M.5 P4 - Edgeforms/Embeds	
2770	SOM	SOMD J.8-M.5 P4 - Install Reinforcement	3	3	13-Feb-23	15-Feb-23											SOMD J.8-M.5 P4 - Install Reinforcement	
2771	SOM	SOMD J.8-M.5 P4 - MEP Final	1	1	16-Feb-23	16-Feb-23											SOMD J.8-M.5 P4 - MEP Final	
2772	SOM	SOMD J.8-M.5 P4 - Place Slab	1	1	17-Feb-23	17-Feb-23											SOMD J.8-M.5 P4 - Place Slab	
2773	Grid L - Q.1			7	7	15-Feb-23	24-Feb-23										24-Feb-23, Grid L - Q.1	
2774	Pour 5 M.5 - Q			7	7	15-Feb-23	24-Feb-23										24-Feb-23, Pour 5 M.5 - Q	
2775	SOM	SOMD M.5-Q P5 - MEP	2	2	15-Feb-23	16-Feb-23											SOMD M.5-Q P5 - MEP	
2776	SOM	SOMD M.5-Q P5 - Edgeforms/Embeds	2	2	15-Feb-23	16-Feb-23											SOMD M.5-Q P5 - Edgeforms/Embeds	

Remaining Level of Effort
Actual Work

Remaining Work
Critical Remaining Work

◆ Milestone
▼ Summary

QTS HIL2 DC2, DC3, DC5 Construction Schedule				Classic Schedule Layout					12-Jul-22 15:37									
#	Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	2022					2023				2024		
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	
2777	SOM	SOMD M.5-Q P5 - Install Reinforcement	3	3	17-Feb-23	22-Feb-23						I	SOMD M.5-Q P5 - Install Reinforcement					
2778	SOM	SOMD M.5-Q P5 - MEP Final	1	1	23-Feb-23	23-Feb-23						I	SOMD M.5-Q P5 - MEP Final					
2779	SOM	SOMD M.5-Q P5 - Place Slab	1	1	24-Feb-23	24-Feb-23						I	SOMD M.5-Q P5 - Place Slab					
2780	Grid Q.1 - Z		13	13	02-Mar-23	20-Mar-23						▼	20-Mar-23, Grid Q.1 - Z					
2781	Pour 6 Q - T.3		8	8	02-Mar-23	13-Mar-23						▼	13-Mar-23, Pour 6 Q - T.3					
2782	SOM	SOMD Q-T.3 P6 - As-Built Structure	1	1	02-Mar-23	02-Mar-23						I	SOMD Q-T.3 P6 - As-Built Structure					
2783	SOM	SOMD Q-T.3 P6 - MEP	2	2	03-Mar-23	06-Mar-23						I	SOMD Q-T.3 P6 - MEP					
2784	SOM	SOMD Q-T.3 P6 - Edgeforms/Embeds	2	2	03-Mar-23	06-Mar-23						I	SOMD Q-T.3 P6 - Edgeforms/Embeds					
2785	SOM	SOMD Q-T.3 P6 - Install Reinforcement	3	3	07-Mar-23	09-Mar-23						I	SOMD Q-T.3 P6 - Install Reinforcement					
2786	SOM	SOMD Q-T.3 P6 - MEP Final	1	1	10-Mar-23	10-Mar-23						I	SOMD Q-T.3 P6 - MEP Final					
2787	SOM	SOMD Q-T.3 P6 - Place Slab	1	1	13-Mar-23	13-Mar-23						I	SOMD Q-T.3 P6 - Place Slab					
2788	Pour 7 T.3 - W.3		7	7	08-Mar-23	16-Mar-23						▼	16-Mar-23, Pour 7 T.3 - W.3					
2789	SOM	SOMD T.3-W.3 P7 - MEP	2	2	08-Mar-23	09-Mar-23						I	SOMD T.3-W.3 P7 - MEP					
2790	SOM	SOMD T.3-W.3 P7 - Edgeforms/Embeds	2	2	08-Mar-23	09-Mar-23						I	SOMD T.3-W.3 P7 - Edgeforms/Embeds					
2791	SOM	SOMD T.3-W.3 P7 - Install Reinforcement	3	3	10-Mar-23	14-Mar-23						I	SOMD T.3-W.3 P7 - Install Reinforcement					
2792	SOM	SOMD T.3-W.3 P7 - MEP Final	1	1	15-Mar-23	15-Mar-23						I	SOMD T.3-W.3 P7 - MEP Final					
2793	SOM	SOMD T.3-W.3 P7 - Place Slab	1	1	16-Mar-23	16-Mar-23						I	SOMD T.3-W.3 P7 - Place Slab					
2794	Pour 8 W.3 - Z		7	7	10-Mar-23	20-Mar-23						▼	20-Mar-23, Pour 8 W.3 - Z					
2795	SOM	SOMD W.3-Z P8 - MEP	2	2	10-Mar-23	13-Mar-23						I	SOMD W.3-Z P8 - MEP					
2796	SOM	SOMD W.3-Z P8 - Edgeforms/Embeds	2	2	10-Mar-23	13-Mar-23						I	SOMD W.3-Z P8 - Edgeforms/Embeds					
2797	SOM	SOMD W.3-Z P8 - Install Reinforcement	3	3	14-Mar-23	16-Mar-23						I	SOMD W.3-Z P8 - Install Reinforcement					
2798	SOM	SOMD W.3-Z P8 - MEP Final	1	1	17-Mar-23	17-Mar-23						I	SOMD W.3-Z P8 - MEP Final					
2799	SOM	SOMD W.3-Z P8 - Place Slab	1	1	20-Mar-23	20-Mar-23						I	SOMD W.3-Z P8 - Place Slab					
2800	Steel		78	78	06-Jan-23	26-Apr-23						▼	26-Apr-23, Steel					
2801	Steel Erection		44	44	06-Jan-23	09-Mar-23						▼	09-Mar-23, Steel Erection					
2802	ERCT.D5.1530	Erect Steel - Sequence 11	3	3	06-Jan-23	10-Jan-23						I	Erect Steel - Sequence 11					
2803	ERCT.D5.1550	Erect Steel - Sequence 12	3	3	11-Jan-23	13-Jan-23						I	Erect Steel - Sequence 12					
2804	ERCT.D5.1540	Erect Steel - Sequence 21	2	2	16-Jan-23	17-Jan-23						I	Erect Steel - Sequence 21					
2805	ERCT.D5.1590	Erect Steel - Sequence 31	2	2	18-Jan-23	19-Jan-23						I	Erect Steel - Sequence 31					
2806	ERCT.D5.1560	Erect Steel - Sequence 22	2	2	20-Jan-23	23-Jan-23						I	Erect Steel - Sequence 22					
2807	ERCT.D5.1600	Erect Steel - Sequence 32	2	2	24-Jan-23	25-Jan-23						I	Erect Steel - Sequence 32					
2808	ERCT.D5.1570	Erect Steel - Sequence 23	2	2	26-Jan-23	27-Jan-23						I	Erect Steel - Sequence 23					
2809	ERCT.D5.1610	Erect Steel - Sequence 33	2	2	30-Jan-23	31-Jan-23						I	Erect Steel - Sequence 33					
2810	ERCT.D5.1580	Erect Steel - Sequence 24	3	3	01-Feb-23	03-Feb-23						I	Erect Steel - Sequence 24					
2811	ERCT.D5.1620	Erect Steel - Sequence 34	3	3	06-Feb-23	08-Feb-23						I	Erect Steel - Sequence 34					
2812	ERCT.D5.1630	Erect Steel - Sequence 25	2	2	09-Feb-23	10-Feb-23						I	Erect Steel - Sequence 25					
2813	ERCT.D5.1670	Erect Steel - Sequence 35	2	2	13-Feb-23	14-Feb-23						I	Erect Steel - Sequence 35					
2814	ERCT.D5.1640	Erect Steel - Sequence 26	3	3	15-Feb-23	17-Feb-23						I	Erect Steel - Sequence 26					
2815	ERCT.D5.1680	Erect Steel - Sequence 36	3	3	21-Feb-23	23-Feb-23						I	Erect Steel - Sequence 36					
2816	ERCT.D5.1650	Erect Steel - Sequence 27	2	2	24-Feb-23	27-Feb-23						I	Erect Steel - Sequence 27					
2817	ERCT.D5.1690	Erect Steel - Sequence 37	2	2	28-Feb-23	01-Mar-23						I	Erect Steel - Sequence 37					
2818	ERCT.D5.1660	Erect Steel - Sequence 28	2	2	02-Mar-23	03-Mar-23						I	Erect Steel - Sequence 28					
2819	ERCT.D5.1700	Erect Steel - Sequence 38	2	2	06-Mar-23	07-Mar-23						I	Erect Steel - Sequence 38					
2820	ERCT.D5.1710	Erect Steel - Sequence 40	2	2	08-Mar-23	09-Mar-23						I	Erect Steel - Sequence 40					
2821	Stairs		75	75	11-Jan-23	26-Apr-23						▼	26-Apr-23, Stairs					
2822	ERCT.D5.1480	Stair 1 (S Loading Dock)	2	2	11-Jan-23	12-Jan-23						I	Stair 1 (S Loading Dock)					
2823	ERCT.D5.1490	Stair 2 (Admin)	2	2	16-Jan-23	17-Jan-23						I	Stair 2 (Admin)					
2824	ERCT.D5.1520	Stair 3 (Back of House)	2	2	10-Mar-23	13-Mar-23						I	Stair 3 (Back of House)					

█ Remaining Level of Effort █ Remaining Work ◆ Milestone █ Critical Remaining Work ► Summary
█ Actual Work


Page 59 of 74 TASK filter: All Activities © Oracle Corporation

QTS HIL2 DC2, DC3, DC5 Construction Schedule				Classic Schedule Layout							12-Jul-22 15:37								
#	Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	2022					2023					2024		
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2		
2825	ERCT.D5.1500	Exterior Equipment Yard (2 Sets)	10	10	21-Mar-23	03-Apr-23											Exterior Equipment Yard (2 Sets) Exterior Exit Stair (2 Sets) 26-Apr-23, Precast Precast - CL Q to L.2 - East Elevation Precast - CL L.2 to C.1 - East Elevation Precast - CL C.1 to A - East Elevation Precast - CL 8 to 1 - South Elevation Precast - CL A to C.1 - West Elevation Precast - CL C.1 to L.2 - West Elevation Precast - CL L.2 to Q - West Elevation Precast - CL Q to Z - West Elevation Precast - CL 1 to 8 - True North Precast - CL Z to Q - East Elevation 31-May-23, Glazing and Metal Paneling Metal Paneling - S Elevation Precast Field Verification for Glazing Install Glazing - S Elevation CL-8 to CL-1 Install Glazing - W Elevation CL-C to CL-A 04-May-23, Roof 12-Apr-23, CL A to CL C Roof A-C - Install Curbs Roof A-C - Roof Penetrations Roof A-C - Temp Roof Roof A-C - Inspect/Punch/QAQC Roof A-C - Foam Insulation Roof A-C - Install Roofing Material Roof A-C - Interior Wall Covering Roof A-C - Wall Cap Roof C-L - Install Curbs Roof C-L - Roof Penetrations Roof C-L - Temp Roof Roof C-L - Inspect/Punch/QAQC Roof C-L - Foam Insulation Roof C-L - Roofing Material Roof C-L - Interior Wall Covering Roof C-L - Wall Cap 20-Apr-23, CL L to CL Q Roof L-Q - Install Curbs Roof L-Q - Roof Penetrations Roof L-Q - Inspect/Punch/QAQC Roof L-Q - Temp Roof Roof L-Q - Foam Insulation Roof L-Q - Roofing Material Roof L-Q - Interior Wall Covering Roof L-Q - Wall Cap 04-May-23, CL Q to CL Z Roof Q-Z - Install Curbs		
2826		ERCT.D5.1510	Exterior Exit Stair (2 Sets)	10	10	13-Apr-23	26-Apr-23												
2827		Precast	30	30	16-Mar-23	26-Apr-23													
2828		PCST.D5.1200	Precast - CL Q to L.2 - East Elevation	3	3	16-Mar-23	20-Mar-23												
2829		PCST.D5.1210	Precast - CL L.2 to C.1 - East Elevation	3	3	21-Mar-23	23-Mar-23												
2830		PCST.D5.1220	Precast - CL C.1 to A - East Elevation	2	2	24-Mar-23	27-Mar-23												
2831		PCST.D5.1230	Precast - CL 8 to 1 - South Elevation	4	4	28-Mar-23	31-Mar-23												
2832		PCST.D5.1240	Precast - CL A to C.1 - West Elevation	2	2	03-Apr-23	04-Apr-23												
2833		PCST.D5.1250	Precast - CL C.1 to L.2 - West Elevation	3	3	05-Apr-23	07-Apr-23												
2834		PCST.D5.1260	Precast - CL L.2 to Q - West Elevation	3	3	10-Apr-23	12-Apr-23												
2835		PCST.D5.1270	Precast - CL Q to Z - West Elevation	3	3	13-Apr-23	17-Apr-23												
2836		PCST.D5.1280	Precast - CL 1 to 8 - True North	4	4	18-Apr-23	21-Apr-23												
2837		PCST.D5.1290	Precast - CL Z to Q - East Elevation	3	3	24-Apr-23	26-Apr-23												
2838		Glazing and Metal Paneling		42	42	03-Apr-23	31-May-23												
2839		GZMP.D5.1070	Metal Paneling - S Elevation	15	15	03-Apr-23	21-Apr-23												
2840		GZMP.D5.1050	Precast Field Verification for Glazing	2	2	03-Apr-23	04-Apr-23												
2841		GZMP.D5.1060	Install Glazing - S Elevation CL-8 to CL-1	15	15	03-May-23	23-May-23												
2842		GZMP.D5.1080	Install Glazing - W Elevation CL-C to CL-A	5	5	24-May-23	31-May-23												
2843		Roof		78	78	16-Jan-23	04-May-23												
2844		CL A to CL C		62	62	16-Jan-23	12-Apr-23												
2845		ROOF.D5.164	Roof A-C - Install Curbs	3	3	16-Jan-23	18-Jan-23												
2846		ROOF.D5.165	Roof A-C - Roof Penetrations	3	3	19-Jan-23	23-Jan-23												
2847		ROOF.D5.167	Roof A-C - Temp Roof	2	2	20-Jan-23	23-Jan-23												
2848		ROOF.D5.166	Roof A-C - Inspect/Punch/QAQC	1	1	23-Jan-23	23-Jan-23												
2849		ROOF.D5.168	Roof A-C - Foam Insulation	5	5	24-Jan-23	30-Jan-23												
2850		ROOF.D5.169	Roof A-C - Install Roofing Material	5	5	31-Jan-23	06-Feb-23												
2851		ROOF.D5.170	Roof A-C - Interior Wall Covering	5	5	30-Mar-23	05-Apr-23												
2852		ROOF.D5.171	Roof A-C - Wall Cap	5	5	06-Apr-23	12-Apr-23												
2853		CL C to CLL		57	57	26-Jan-23	17-Apr-23												
2854		ROOF.D5.172	Roof C-L - Install Curbs	3	3	26-Jan-23	30-Jan-23												
2855		ROOF.D5.173	Roof C-L - Roof Penetrations	3	3	31-Jan-23	02-Feb-23												
2856		ROOF.D5.175	Roof C-L - Temp Roof	5	5	01-Feb-23	07-Feb-23												
2857		ROOF.D5.174	Roof C-L - Inspect/Punch/QAQC	1	1	02-Feb-23	02-Feb-23												
2858		ROOF.D5.176	Roof C-L - Foam Insulation	5	5	08-Feb-23	14-Feb-23												
2859		ROOF.D5.177	Roof C-L - Roofing Material	5	5	15-Feb-23	22-Feb-23												
2860		ROOF.D5.178	Roof C-L - Interior Wall Covering	5	5	04-Apr-23	10-Apr-23												
2861		ROOF.D5.179	Roof C-L - Wall Cap	5	5	11-Apr-23	17-Apr-23												
2862		CL L to CL Q		46	46	15-Feb-23	20-Apr-23												
2863		ROOF.D5.180	Roof L-Q - Install Curbs	3	3	15-Feb-23	17-Feb-23												
2864		ROOF.D5.181	Roof L-Q - Roof Penetrations	3	3	21-Feb-23	23-Feb-23												
2865		ROOF.D5.182	Roof L-Q - Inspect/Punch/QAQC	1	1	23-Feb-23	23-Feb-23												
2866		ROOF.D5.183	Roof L-Q - Temp Roof	5	5	24-Feb-23	02-Mar-23												
2867		ROOF.D5.184	Roof L-Q - Foam Insulation	5	5	03-Mar-23	09-Mar-23												
2868		ROOF.D5.185	Roof L-Q - Roofing Material	5	5	10-Mar-23	16-Mar-23												
2869		ROOF.D5.186	Roof L-Q - Interior Wall Covering	5	5	07-Apr-23	13-Apr-23												
2870		ROOF.D5.187	Roof L-Q - Wall Cap	5	5	14-Apr-23	20-Apr-23												
2871		CL Q to CL Z		42	42	08-Mar-23	04-May-23												
2872		ROOF.D5.188	Roof Q-Z - Install Curbs	3	3	08-Mar-23	10-Mar-23												


Remaining Level of Effort Remaining Work


QTS HIL2 DC2, DC3, DC5 Construction Schedule			Classic Schedule Layout						12-Jul-22 15:37										
#	Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish		2022					2023					2024	
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2		
2873	ROOF.D5.191	Roof Q-Z - Temp Roof	5	5	10-Mar-23	16-Mar-23												Roof Q-Z - Temp Roof	
2874		Roof Q-Z - Roof Penetrations	3	3	13-Mar-23	15-Mar-23												Roof Q-Z - Roof Penetrations	
2875		Roof Q-Z - Inspect/Punch/QAAC	1	1	15-Mar-23	15-Mar-23												Roof Q-Z - Inspect/Punch/QAAC	
2876		Roof Q-Z - Foam Insulation	5	5	17-Mar-23	23-Mar-23												Roof Q-Z - Foam Insulation	
2877		Roof Q-Z - Roofing Material	5	5	24-Mar-23	30-Mar-23												Roof Q-Z - Roofing Material	
2878		Roof Q-Z - Interior Wall Covering	5	5	21-Apr-23	27-Apr-23												Roof Q-Z - Interior Wall Covering	
2879		Roof Q-Z - Wall Cap	5	5	28-Apr-23	04-May-23												Roof Q-Z - Wall Cap	
2880	Rooftop Equipment			102	102	07-Feb-23	28-Jun-23											28-Jun-23; Rooftop Equipment	
2881				102	102	07-Feb-23	28-Jun-23											28-Jun-23; House	
2882	MEP84	House - Rough In Roof MEP	5	5	07-Feb-23	13-Feb-23												House - Rough In Roof MEP	
2883	EQPT.D5.3960	House - Set Rooftop RTU Equipment	5	5	08-Jun-23	14-Jun-23												House - Set Rooftop RTU Equipment	
2884	EQPT.D5.3970	House - Pull and Terminate RTU Feeders	5	5	15-Jun-23	21-Jun-23												House - Pull and Terminate RTU Feeders	
2885	EQPT.D5.3980	House - Mechanical RTU Final Connections	5	5	22-Jun-23	28-Jun-23												House - Mechanical RTU Final Connections	
2886	MPOE/BDF			74	74	17-Mar-23	28-Jun-23											28-Jun-23; MPOE/BDF	
2887	MEP74	MPOE/BDF - Rough In Roof MEP	5	5	17-Mar-23	23-Mar-23												MPOE/BDF - Rough In Roof MEP	
2888	EQPT.D5.3930	MPOE/BDF - Set Rooftop ACCU Equipment	5	5	08-Jun-23	14-Jun-23												MPOE/BDF - Set Rooftop ACCU Equipment	
2889	EQPT.D5.3940	MPOE/BDF - Pull and Terminate ACCU Feeders	5	5	15-Jun-23	21-Jun-23												MPOE/BDF - Pull and Terminate ACCU Feeders	
2890	EQPT.D5.3950	MPOE/BDF - Mechanical ACCU Final Connections	5	5	22-Jun-23	28-Jun-23												MPOE/BDF - Mechanical ACCU Final Connections	
2891	DH A-B			90	90	23-Feb-23	28-Jun-23											28-Jun-23; DH A-B	
2892	MEP54	DH A/B - Rough In Roof MEP	5	5	23-Feb-23	01-Mar-23												DH A/B - Rough In Roof MEP	
2893	EQPT.D5.3880	DH A/B - Set Rooftop ACCU Equipment	5	5	08-Jun-23	14-Jun-23												DH A/B - Set Rooftop ACCU Equipment	
2894	EQPT.D5.3890	DH A/B - Pull and Terminate ACCU Feeders	5	5	15-Jun-23	21-Jun-23												DH A/B - Pull and Terminate ACCU Feeders	
2895	EQPT.D5.3050	Mechanical ACCU Final Connections DH AB	5	5	22-Jun-23	28-Jun-23												Mechanical ACCU Final Connections DH AB	
2896	DH C-D			64	64	31-Mar-23	28-Jun-23											28-Jun-23; DH C-D	
2897	MEP64	DH C/D - Rough In Roof MEP	5	5	31-Mar-23	06-Apr-23												DH C/D - Rough In Roof MEP	
2898	EQPT.D5.3900	DH C/D - Set Rooftop ACCU Equipment	5	5	08-Jun-23	14-Jun-23												DH C/D - Set Rooftop ACCU Equipment	
2899	EQPT.D5.3910	DH C/D - Pull and Terminate ACCU Feeders	5	5	15-Jun-23	21-Jun-23												DH C/D - Pull and Terminate ACCU Feeders	
2900	EQPT.D5.3920	DH C/D - Mechanical ACCU Final Connections	5	5	22-Jun-23	28-Jun-23												DH C/D - Mechanical ACCU Final Connections	
2901	Equipment Yard			101	101	01-Feb-23	23-Jun-23											23-Jun-23; Equipment Yard	
2902	Medium Voltage Ductbank			77	77	01-Feb-23	19-May-23											19-May-23; Medium Voltage Ductbank	
2903	EXCV.D5.1410	Excavate Medium Voltage Underground - Sequence 1	6	6	01-Feb-23	08-Feb-23												Excavate Medium Voltage Underground - Sequence 1	
2904	EXCV.D5.1420	Excavate Medium Voltage Underground - Sequence 2	14	14	09-Feb-23	01-Mar-23												Excavate Medium Voltage Underground - Sequence 2	
2905	MVDP.D5.114	Install Medium Voltage Underground - Sequence 1	2	2	09-Feb-23	10-Feb-23												Install Medium Voltage Underground - Sequence 1	
2906	EXCV.D5.1430	Excavate Medium Voltage Underground - Sequence 3	13	13	02-Mar-23	20-Mar-23												Excavate Medium Voltage Underground - Sequence 3	
2907	MVDP.D5.115	Install Medium Voltage Underground - Sequence 2	8	8	02-Mar-23	13-Mar-23												Install Medium Voltage Underground - Sequence 2	
2908	EXCV.D5.1440	Excavate Medium Voltage Underground - Sequence 4	13	13	21-Mar-23	06-Apr-23												Excavate Medium Voltage Underground - Sequence 4	
2909	MVDP.D5.116	Install Medium Voltage Underground - Sequence 3	7	7	21-Mar-23	29-Mar-23												Install Medium Voltage Underground - Sequence 3	
2910	EXCV.D5.1450	Excavate Medium Voltage Underground - Sequence 5	17	17	07-Apr-23	01-May-23												Excavate Medium Voltage Underground - Sequence 5	
2911	MVDP.D5.117	Install Medium Voltage Underground - Sequence 4	8	8	07-Apr-23	18-Apr-23												Install Medium Voltage Underground - Sequence 4	
2912	EXCV.D5.1460	Excavate Medium Voltage Underground - North Vault Group 1	5	5	02-May-23	08-May-23												Excavate Medium Voltage Underground - North Vault Group 1	
2913	MVDP.D5.118	Install Medium Voltage Underground - Sequence 5	14	14	02-May-23	19-May-23												Install Medium Voltage Underground - Sequence 5	
2914	EXCV.D5.1470	Excavate Medium Voltage Underground - North Vault Group 2	5	5	09-May-23	15-May-23												Excavate Medium Voltage Underground - North Vault Group 2	
2915	MVDP.D5.119	Install Medium Voltage Underground - North Vault Group 1	4	4	09-May-23	12-May-23												Install Medium Voltage Underground - North Vault Group 1	
2916	MVDP.D5.120	Install Medium Voltage Underground - North Vault Group 2	4	4	16-May-23	19-May-23												Install Medium Voltage Underground - North Vault Group 2	
2917	Equipment Yard Pads and Set Equipment			68	68	21-Mar-23	23-Jun-23											23-Jun-23; Equipment Yard Pads and Set Equipment	
2918	House			20	20	07-Apr-23	04-May-23											04-May-23, House	
2919	EXCV.D5.1	Yard House - Excavation Transformer Foundations	2	2	07-Apr-23	10-Apr-23												Yard House - Excavation Transformer Foundations	
2920	CONC.D5.	Yard House - Form Transformer Foundations DH AB	2	2	10-Apr-23	11-Apr-23												Yard House - Form Transformer Foundations DH AB	

QTS HIL2 DC2, DC3, DC5 Construction Schedule				Classic Schedule Layout						12-Jul-22 15:37								
#	Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	2022					2023				2024		
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	
2921		CONC.D5. Yard House - Rebar Transformer Foundations	2	2	11-Apr-23	12-Apr-23										I	Yard House - Rebar Transformer Foundations	
2922		CONC.D5. Yard House - Pour Transformer Foundations	1	1	13-Apr-23	13-Apr-23										I	Yard House - Pour Transformer Foundations	
2923		CONC.D5. Yard House - Cure Transformer Foundations	5	5	14-Apr-23	20-Apr-23										■	Yard House - Cure Transformer Foundations	
2924		EQPT.D5.2 Yard House - Set Transformers	5	5	21-Apr-23	27-Apr-23										■	Yard House - Set Transformers	
2925		EQPT.D5.2 Yard House - Pull and Terminate Transformers	5	5	28-Apr-23	04-May-23										■	Yard House - Pull and Terminate Transformers	
2926		MPOE/BDF Pads and Set Equipment			28	28	21-Mar-23	27-Apr-23								▼	27-Apr-23, MPOE/BDF Pads and Set Equipment	
2927		SURV.D5.1 Survey MPOE/BDF Equipment Foundations		1	1	21-Mar-23	21-Mar-23									▼	Survey MPOE/BDF Equipment Foundations	
2928		Pod Pads and Set Equipment			25	25	22-Mar-23	25-Apr-23								▼	25-Apr-23, Pod Pads and Set Equipment	
2929		EXCV.D Yard MPOE/BDF - Excavate UPS Pod Foundations	2	2	22-Mar-23	23-Mar-23										I	Yard MPOE/BDF - Excavate UPS Pod Foundations	
2930		CONC.I Yard MPOE/BDF - Form UPS Pod Foundations MPOE BDF	2	2	23-Mar-23	24-Mar-23										I	Yard MPOE/BDF - Form UPS Pod Foundations MPOE BDF	
2931		CONC.I Yard MPOE/BDF - Rebar UPS Pod Foundations	2	2	24-Mar-23	27-Mar-23										I	Yard MPOE/BDF - Rebar UPS Pod Foundations	
2932		CONC.I Yard MPOE/BDF - Pour UPS Pod Foundations	3	3	28-Mar-23	30-Mar-23										I	Yard MPOE/BDF - Pour UPS Pod Foundations	
2933		CONC.I Yard MPOE/BDF - Cure UPS Pod Foundations	5	5	31-Mar-23	06-Apr-23										■	Yard MPOE/BDF - Cure UPS Pod Foundations	
2934		CONC.I Yard MPOE/BDF - Install Steel Rails UPS Pod Foundations	3	3	07-Apr-23	11-Apr-23										■	Yard MPOE/BDF - Install Steel Rails UPS Pod Foundations	
2935		EQPT.D Yard MPOE/BDF - Set UPS Pods	5	5	12-Apr-23	18-Apr-23										■	Yard MPOE/BDF - Set UPS Pods	
2936		EQPT.D Yard MPOE/BDF - Pull and Terminate UPS Pods	5	5	19-Apr-23	25-Apr-23										■	Yard MPOE/BDF - Pull and Terminate UPS Pods	
2937		Transformer Pads and Set Equipment			23	23	22-Mar-23	21-Apr-23								▼	21-Apr-23, Transformer Pads and Set Equipment	
2938		EXCV.D Yard MPOE/BDF - Excavation Transformer Foundations	2	2	22-Mar-23	23-Mar-23										I	Yard MPOE/BDF - Excavation Transformer Foundations	
2939		CONC.I Yard MPOE/BDF - Form Transformer Foundations	2	2	23-Mar-23	24-Mar-23										I	Yard MPOE/BDF - Form Transformer Foundations	
2940		CONC.I Yard MPOE/BDF - Rebar Transformer Foundations	2	2	24-Mar-23	27-Mar-23										■	Yard MPOE/BDF - Rebar Transformer Foundations	
2941		CONC.I Yard MPOE/BDF - Pour Transformer Foundations	1	1	31-Mar-23	31-Mar-23										I	Yard MPOE/BDF - Pour Transformer Foundations	
2942		CONC.I Yard MPOE/BDF - Cure Transformer Foundations	5	5	03-Apr-23	07-Apr-23										■	Yard MPOE/BDF - Cure Transformer Foundations	
2943		EQPT.D Yard MPOE/BDF - Set Transformers	5	5	10-Apr-23	14-Apr-23										■	Yard MPOE/BDF - Set Transformers	
2944		EQPT.D Yard MPOE/BDF - Pull and Terminate Transformers	5	5	17-Apr-23	21-Apr-23										▼	21-Apr-23, Generator Pads and Set Equipment	
2945		Generator Pads and Set Equipment			25	25	24-Mar-23	27-Apr-23									I	Yard MPOE/BDF - Excavation Generator Foundations
2946		EXCV.D Yard MPOE/BDF - Excavation Generator Foundations	2	2	24-Mar-23	27-Mar-23										I	Yard MPOE/BDF - Form Generator Foundations	
2947		CONC.I Yard MPOE/BDF - Form Generator Foundations	2	2	27-Mar-23	28-Mar-23										I	Yard MPOE/BDF - Rebar Generator Foundations	
2948		CONC.I Yard MPOE/BDF - Pour Generator Foundations	3	3	28-Mar-23	30-Mar-23										I	Yard MPOE/BDF - Cure Generator Foundations	
2949		CONC.I Yard MPOE/BDF - Set Generators	5	5	03-Apr-23	06-Apr-23										■	Yard MPOE/BDF - Set Generators	
2950		EQPT.D Yard MPOE/BDF - Pull and Terminate Generators	5	5	14-Apr-23	20-Apr-23										■	Yard MPOE/BDF - Pull and Terminate Generators	
2951		Data Hall A and B Pads and Set Equipment			61	61	24-Mar-23	19-Jun-23								▼	19-Jun-23, Data Hall A and B Pads and Set Equipment	
2952		SURV.D5.1 Survey DH A/B - Equipment Foundations		1	1	24-Mar-23	24-Mar-23									I	Survey DH A/B - Equipment Foundations	
2953		Transformer Pads and Set Equipment			20	20	07-Apr-23	04-May-23								▼	04-May-23, Transformer Pads and Set Equipment	
2954		EXCV.D Yard DH A/B - Excavation Transformer Foundations	2	2	07-Apr-23	10-Apr-23										I	Yard DH A/B - Excavation Transformer Foundations	
2955		CONC.I Yard DH A/B - Form Transformer Foundations DH AB	2	2	10-Apr-23	11-Apr-23										I	Yard DH A/B - Form Transformer Foundations DH AB	
2956		CONC.I Yard DH A/B - Rebar Transformer Foundations	2	2	11-Apr-23	12-Apr-23										I	Yard DH A/B - Rebar Transformer Foundations	
2957		CONC.I Yard DH A/B - Pour Transformer Foundations	1	1	13-Apr-23	13-Apr-23										I	Yard DH A/B - Pour Transformer Foundations	
2958		CONC.I Yard DH A/B - Cure Transformer Foundations	5	5	14-Apr-23	20-Apr-23										■	Yard DH A/B - Cure Transformer Foundations	
2959		EQPT.D Yard DH A/B - Set Transformers	5	5	21-Apr-23	27-Apr-23										■	Yard DH A/B - Set Transformers	
2960		EQPT.D Yard DH A/B - Pull and Terminate Transformers	5	5	28-Apr-23	04-May-23										▼	12-May-23, Generator Pads and Set Equipment	
2961		Generator Pads and Set Equipment			24	24	11-Apr-23	12-May-23								I	Yard DH A/B - Excavation Generator Foundations	
2962		EXCV.D Yard DH A/B - Excavation Generator Foundations	2	2	11-Apr-23	12-Apr-23										I	Yard DH A/B - Form Generator Foundations	
2963		CONC.I Yard DH A/B - Rebar Generator Foundations	3	3	12-Apr-23	17-Apr-23										■	Yard DH A/B - Rebar Generator Foundations	
2964		CONC.I Yard DH A/B - Pour Generator Foundations	4	4	18-Apr-23	21-Apr-23										■	Yard DH A/B - Pour Generator Foundations	
2965		CONC.I Yard DH A/B - Cure Generator Foundations	5	5	24-Apr-23	28-Apr-23										I	Yard DH A/B - Cure Generator Foundations	



QTS HIL2 DC2, DC3, DC5 Construction Schedule				Classic Schedule Layout						12-Jul-22 15:37								
#	Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	2022					2023				2024		
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	
2969	EQPT.D	Yard DH A/B - Set Generators	5	5	01-May-23	05-May-23										[Color: Green]	Yard DH A/B - Set Generators	
2970	EQPT.D	Yard DH A/B - Pull and Terminate Generators	5	5	08-May-23	12-May-23										[Color: Green]	Yard DH A/B - Pull and Terminate Generators	
2971	Medium Voltage Pads and Set Equipment			47	47	13-Apr-23	19-Jun-23											[Color: Black] 19-Jun-23, Medium Voltage Pads and Set Equipment
2972	EXCV.D	Yard DH A/B - Excavation MV Pads	2	2	13-Apr-23	14-Apr-23												[Color: Blue] Yard DH A/B - Excavation MV Pads
2973	CONC.I	Yard DH A/B - Form MV Pads	2	2	17-Apr-23	18-Apr-23												[Color: Blue] Yard DH A/B - Form MV Pads
2974	CONC.I	Yard DH A/B - Rebar MV Foundations	3	3	19-Apr-23	21-Apr-23												[Color: Blue] Yard DH A/B - Rebar MV Foundations
2975	CONC.I	Yard DH A/B - Pour MV Pads	4	4	22-May-23	25-May-23												[Color: Red] Yard DH A/B - Pour MV Pads
2976	CONC.I	Yard DH A/B - Cure MV Pads	5	5	26-May-23	02-Jun-23												[Color: Red] Yard DH A/B - Cure MV Pads
2977	EQPT.D	Yard DH A/B - Set MV Equipment	5	5	05-Jun-23	09-Jun-23												[Color: Red] Yard DH A/B - Set MV Equipment
2978	EQPT.D	Yard DH A/B - Pull and Terminate MV Feeders	10	10	06-Jun-23	19-Jun-23												[Color: Red] Yard DH A/B - Pull and Terminate MV Feeders
2979	Data Hall C and D Pads and Set Equipment			41	41	27-Apr-23	23-Jun-23											[Color: Black] 23-Jun-23, Data Hall C and D Pads and Set Equipment
2980	SURV.D5.1	Survey DH C/D Equipment Foundations	1	1	27-Apr-23	27-Apr-23												[Color: Blue] Survey DH C/D Equipment Foundations
2981	Transformer Pads and Set Equipment			20	20	28-Apr-23	25-May-23											[Color: Black] 25-May-23, Transformer Pads and Set Equipment
2982	EXCV.D	Yard DH C/D - Excavation Transformer Foundations	2	2	28-Apr-23	01-May-23												[Color: Blue] Yard DH C/D - Excavation Transformer Foundations
2983	CONC.I	Yard DH C/D - Form Transformer Foundations	2	2	01-May-23	02-May-23												[Color: Blue] Yard DH C/D - Form Transformer Foundations
2984	CONC.I	Yard DH C/D - Rebar Transformer Foundations	2	2	02-May-23	03-May-23												[Color: Blue] Yard DH C/D - Rebar Transformer Foundations
2985	CONC.I	Yard DH C/D - Pour Transformer Foundations	1	1	04-May-23	04-May-23												[Color: Blue] Yard DH C/D - Pour Transformer Foundations
2986	CONC.I	Yard DH C/D - Cure Transformer Foundations	5	5	05-May-23	11-May-23												[Color: Green] Yard DH C/D - Cure Transformer Foundations
2987	EQPT.D	Yard DH C/D - Set Transformers	5	5	12-May-23	18-May-23												[Color: Green] Yard DH C/D - Set Transformers
2988	EQPT.D	Yard DH C/D - Pull and Terminate Transformers	5	5	19-May-23	25-May-23												[Color: Green] Yard DH C/D - Pull and Terminate Transformers
2989	Generator Pads and Set Equipment			24	24	02-May-23	05-Jun-23											[Color: Black] 05-Jun-23, Generator Pads and Set Equipment
2990	EXCV.D	Yard DH C/D - Excavation Generator Foundations	2	2	02-May-23	03-May-23												[Color: Blue] Yard DH C/D - Excavation Generator Foundations
2991	CONC.I	Yard DH C/D - Form Generator Foundations	2	2	03-May-23	04-May-23												[Color: Blue] Yard DH C/D - Form Generator Foundations
2992	CONC.I	Yard DH C/D - Rebar Generator Foundations	3	3	04-May-23	08-May-23												[Color: Blue] Yard DH C/D - Rebar Generator Foundations
2993	CONC.I	Yard DH C/D - Pour Generator Foundations	4	4	09-May-23	12-May-23												[Color: Blue] Yard DH C/D - Pour Generator Foundations
2994	CONC.I	Yard DH C/D - Cure Generator Foundations	5	5	15-May-23	19-May-23												[Color: Blue] Yard DH C/D - Cure Generator Foundations
2995	EQPT.D	Yard DH C/D - Set Generators	5	5	22-May-23	26-May-23												[Color: Green] Yard DH C/D - Set Generators
2996	EQPT.D	Yard DH C/D - Pull and Terminate Generators	5	5	30-May-23	05-Jun-23												[Color: Green] Yard DH C/D - Pull and Terminate Generators
2997	Medium Voltage Pads and Set Equipment			36	36	04-May-23	23-Jun-23											[Color: Black] 23-Jun-23, Medium Voltage Pads and Set Equipment
2998	EXCV.D	Yard DH C/D - Excavation MV Pads	2	2	04-May-23	05-May-23												[Color: Blue] Yard DH C/D - Excavation MV Pads
2999	CONC.I	Yard DH C/D - Form MV Pads	2	2	22-May-23	23-May-23												[Color: Blue] Yard DH C/D - Form MV Pads
3000	CONC.I	Yard DH C/D - Rebar MV Foundations	2	2	24-May-23	25-May-23												[Color: Blue] Yard DH C/D - Rebar MV Foundations
3001	CONC.I	Yard DH C/D - Pour MV Pads	4	4	26-May-23	01-Jun-23												[Color: Green] Yard DH C/D - Pour MV Pads
3002	CONC.I	Yard DH C/D - Cure MV Pads	5	5	02-Jun-23	08-Jun-23												[Color: Green] Yard DH C/D - Cure MV Pads
3003	EQPT.D	Yard DH C/D - Set MV Equipment	5	5	09-Jun-23	15-Jun-23												[Color: Green] Yard DH C/D - Set MV Equipment
3004	EQPT.D	Yard DH C/D - Pull and Terminate MV Feeders	10	10	12-Jun-23	23-Jun-23												[Color: Green] Yard DH C/D - Pull and Terminate MV Feeders
3005	Elevators			86	86	09-Mar-23	10-Jul-23											[Color: Black] 10-Jul-23, Elevators
3006	Freight Elevator E03			61	61	13-Apr-23	10-Jul-23											[Color: Black] 10-Jul-23, Freight Elevator E03
3007	ELVT.D5.1660	Freight Elev. 3 - Hoisting Equipment	7	7	13-Apr-23	21-Apr-23												[Color: Green] Freight Elev. 3 - Hoisting Equipment
3008	ELVT.D5.1670	Freight Elev. 3 - Pit Rails/Frame/Cab	5	5	24-Apr-23	28-Apr-23												[Color: Blue] Freight Elev. 3 - Pit Rails/Frame/Cab
3009	ELVT.D5.1680	Freight Elev. 3 - Tirak & Governor Rope	5	5	01-May-23	05-May-23												[Color: Green] Freight Elev. 3 - Tirak & Governor Rope
3010	ELVT.D5.1690	Freight Elev. 3 - Rails	8	8	08-May-23	17-May-23												[Color: Green] Freight Elev. 3 - Rails
3011	ELVT.D5.1700	Freight Elev. 3 - Door entrances	4	4	18-May-23	23-May-23												[Color: Green] Freight Elev. 3 - Door entrances
3012	ELVT.D5.1710	Freight Elev. 3 - Duct/Wire Machine/Startup	7	7	24-May-23	02-Jun-23												[Color: Green] Freight Elev. 3 - Duct/Wire Machine/Startup
3013	ELVT.D5.1720	Freight Elev. 3 - Rope Elevator/Remove Tirak	4	4	05-Jun-23	08-Jun-23												[Color: Blue] Freight Elev. 3 - Rope Elevator/Remove Tirak
3014	ELVT.D5.1730	Freight Elev. 3 - Pipe and Wire Hatch Devices	6	6	09-Jun-23	16-Jun-23												[Color: Green] Freight Elev. 3 - Pipe and Wire Hatch Devices
3015	ELVT.D5.1740	Freight Elev. 3 - Terminate Devices	8	8	19-Jun-23	28-Jun-23												[Color: Green] Freight Elev. 3 - Terminate Devices
3016	ELVT.D5.1750	Freight Elev. 3 - Clean Rails	2	2	29-Jun-23	30-Jun-23												[Color: Green] Freight Elev. 3 - Clean Rails



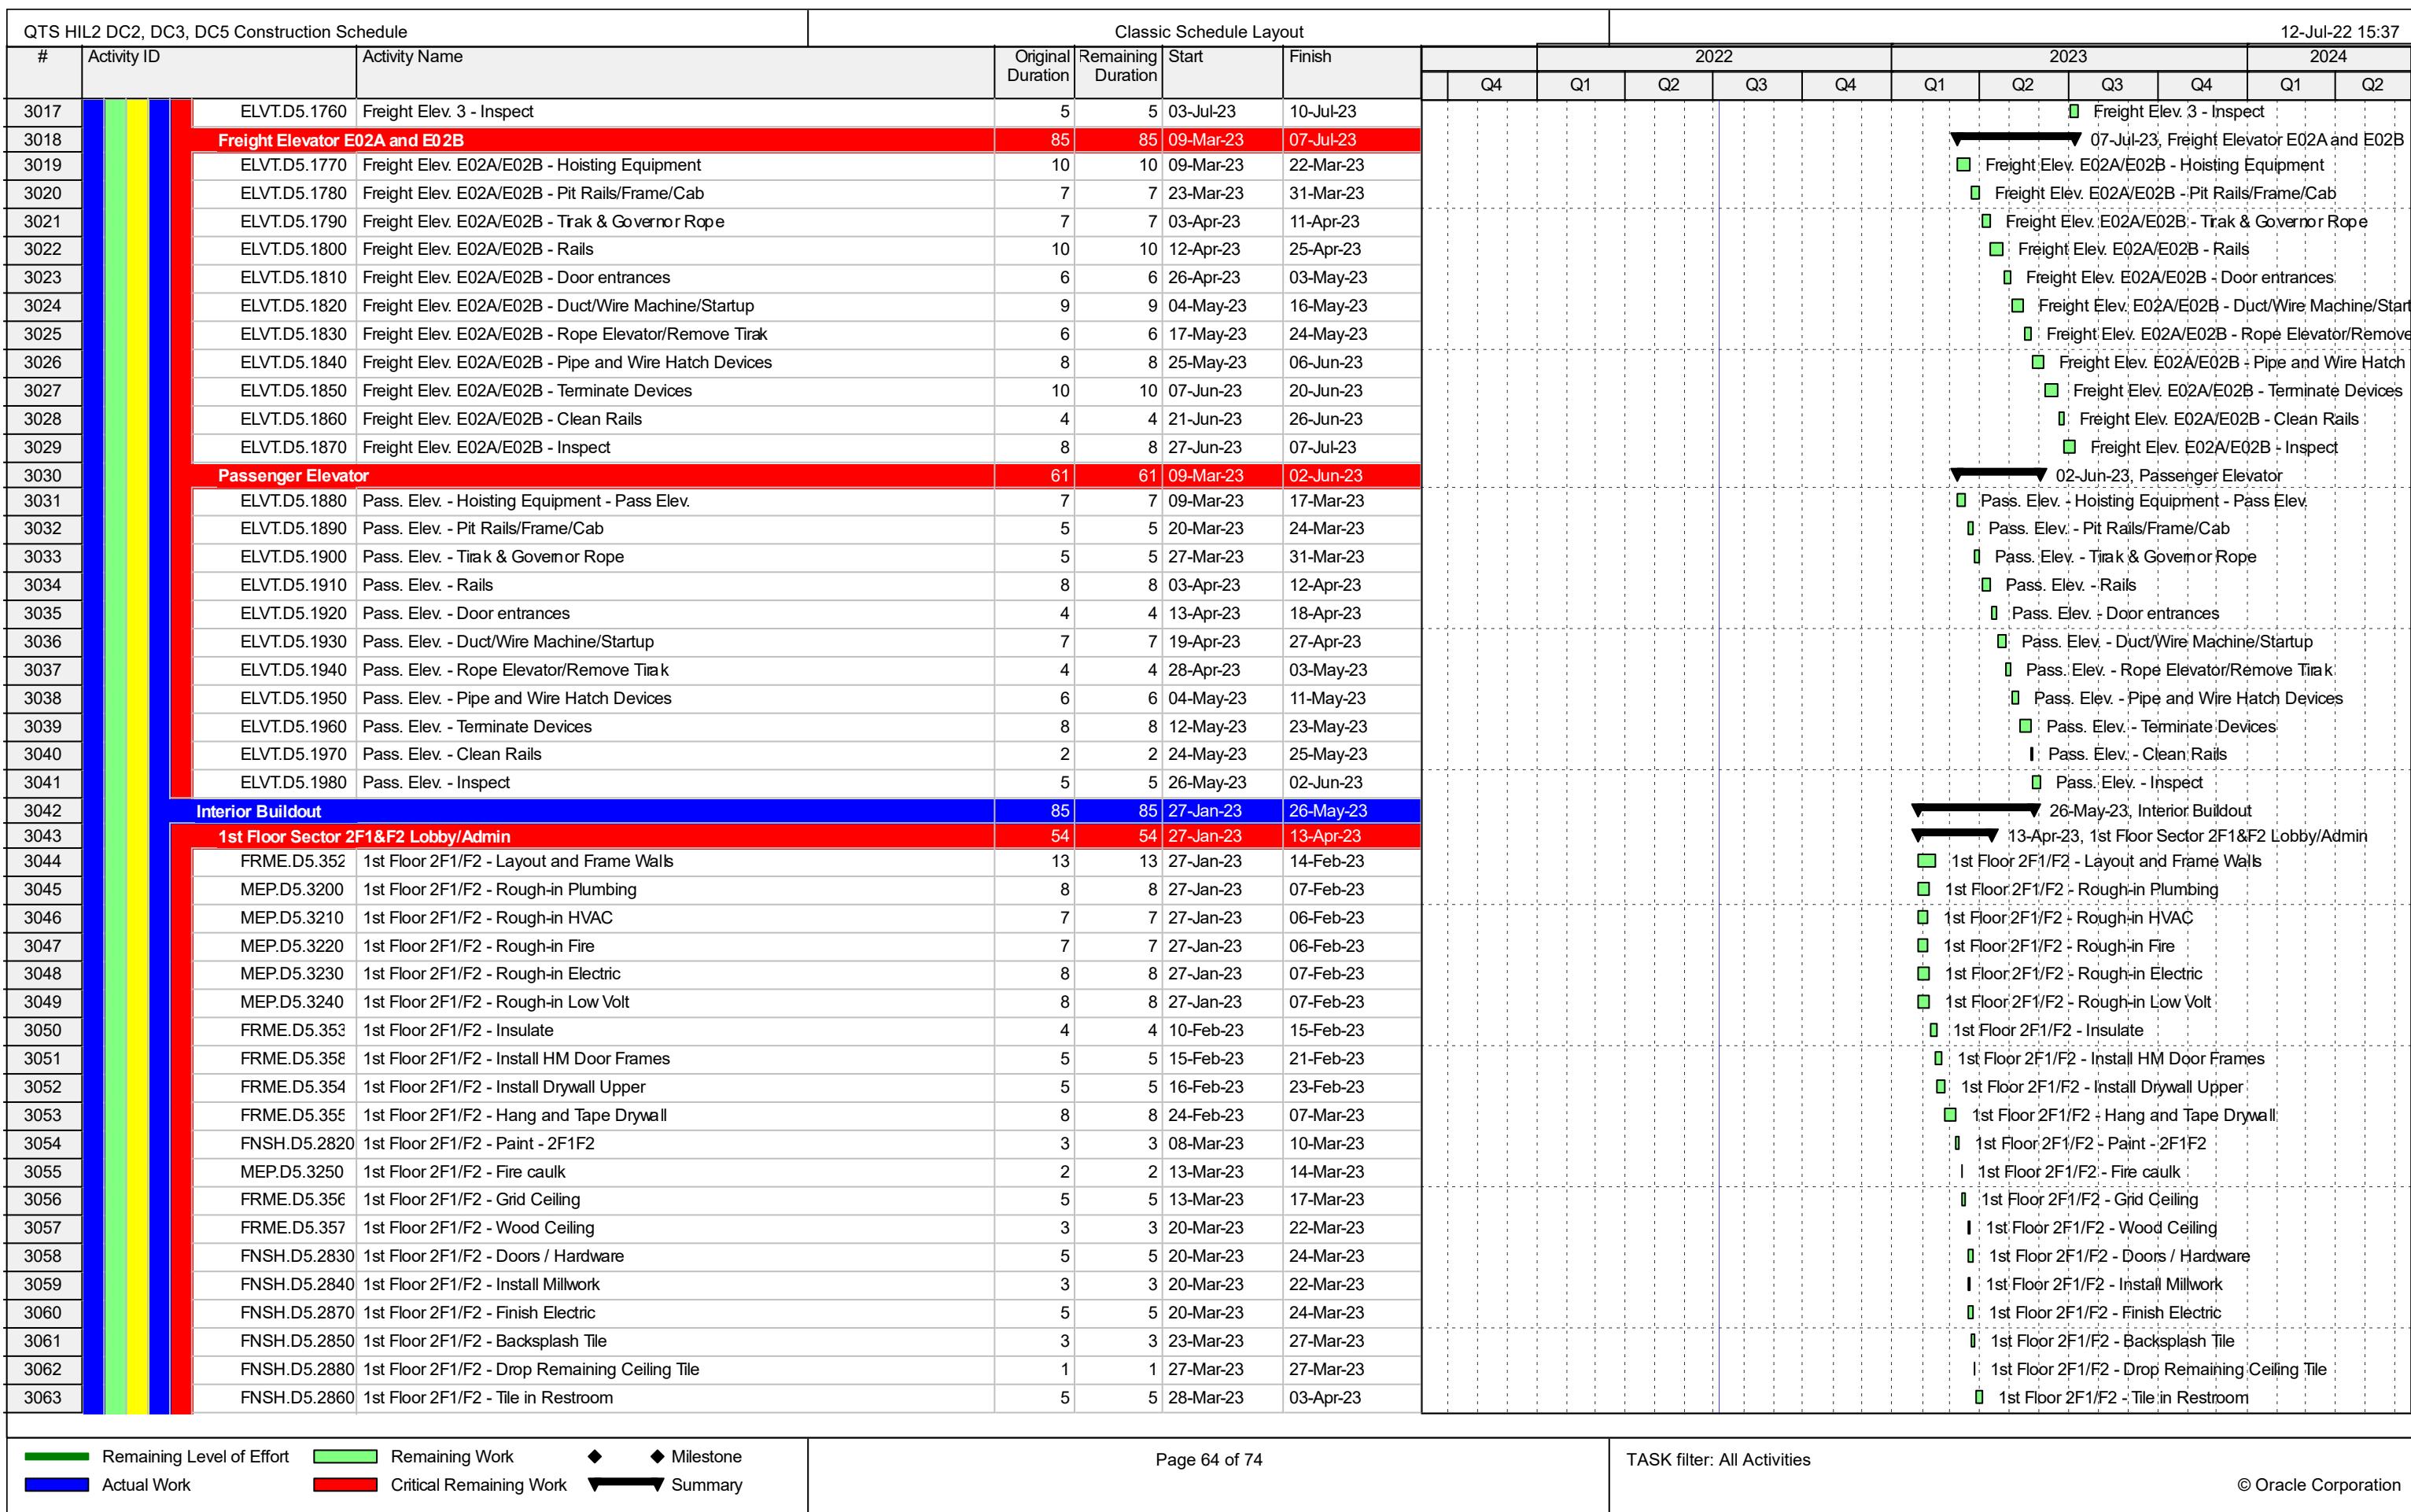

QTS HIL2 DC2, DC3, DC5 Construction Schedule				Classic Schedule Layout							12-Jul-22 15:37									
#	Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish			2022				2023				2024			
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2			
3064		FNSH.D5.2890 1st Floor 2F1/F2 - Finish Plumbing	4	4	28-Mar-23	31-Mar-23										1st Floor 2F1/F2 - Finish Plumbing				
3065		FNSH.D5.2900 1st Floor 2F1/F2 - Finish HVAC		3	3	03-Apr-23										1st Floor 2F1/F2 - Finish HVAC				
3066		FNSH.D5.2910 1st Floor 2F1/F2 - Floor Coverings		6	6	06-Apr-23										1st Floor 2F1/F2 - Floor Coverings				
3067		1st Floor Sector 2G1&G2 Back of House			49	49	21-Mar-23										26-May-23, 1st Floor Sector 2G1&G2 Back of House			
3068		FRME.D5.359 1st Floor 2G1/G2 - Layout and Frame Walls		9	9	21-Mar-23											1st Floor 2G1/G2 - Layout and Frame Walls			
3069		MEP.D5.3260 1st Floor 2G1/G2 - Rough-in Plumbing		8	8	21-Mar-23											1st Floor 2G1/G2 - Rough-in Plumbing			
3070		MEP.D5.3270 1st Floor 2G1/G2 - Rough-in HVAC		7	7	21-Mar-23											1st Floor 2G1/G2 - Rough-in HVAC			
3071		MEP.D5.3280 1st Floor 2G1/G2 - Rough-in Fire		7	7	21-Mar-23											1st Floor 2G1/G2 - Rough-in Fire			
3072		MEP.D5.3290 1st Floor 2G1/G2 - Rough-in Electric		8	8	21-Mar-23											1st Floor 2G1/G2 - Rough-in Electric			
3073		MEP.D5.3300 1st Floor 2G1/G2 - Rough-in Low Volt		8	8	21-Mar-23											1st Floor 2G1/G2 - Rough-in Low Volt			
3074		MEP.D5.3310 1st Floor 2G1/G2 - Fire caulk		2	2	31-Mar-23											1st Floor 2G1/G2 - Fire caulk			
3075		FRME.D5.360 1st Floor 2G1/G2 - Insulate		2	2	31-Mar-23											1st Floor 2G1/G2 - Insulate			
3076		FRME.D5.361 1st Floor 2G1/G2 - Install Drywall Upper		5	5	04-Apr-23											1st Floor 2G1/G2 - Install Drywall Upper			
3077		FRME.D5.362 1st Floor 2G1/G2 - Hang and Tape Drywall		7	7	11-Apr-23											1st Floor 2G1/G2 - Hang and Tape Drywall			
3078		FNSH.D5.2940 1st Floor 2G1/G2 - Tile in Restroom		3	3	11-Apr-23											1st Floor 2G1/G2 - Tile in Restroom			
3079		FNSH.D5.2950 1st Floor 2G1/G2 - Backsplash Tile		5	5	14-Apr-23											1st Floor 2G1/G2 - Backsplash Tile			
3080		FNSH.D5.2920 1st Floor 2G1/G2 - Paint		3	3	20-Apr-23											1st Floor 2G1/G2 - Paint			
3081		FRME.D5.363 1st Floor 2G1/G2 - Grid Ceiling		5	5	25-Apr-23											1st Floor 2G1/G2 - Grid Ceiling			
3082		FRME.D5.364 1st Floor 2G1/G2 - Wood Ceiling		3	3	02-May-23											1st Floor 2G1/G2 - Wood Ceiling			
3083		FNSH.D5.2930 1st Floor 2G1/G2 - Doors & Hardware		5	5	02-May-23											1st Floor 2G1/G2 - Doors & Hardware			
3084		FRME.D5.365 1st Floor 2G1/G2 - Install Millwork		3	3	02-May-23											1st Floor 2G1/G2 - Install Millwork			
3085		FNSH.D5.2960 1st Floor 2G1/G2 - Finish Electric		5	5	02-May-23											1st Floor 2G1/G2 - Finish Electric			
3086		FNSH.D5.2970 1st Floor 2G1/G2 - Drop Remaining Ceiling Tile		1	1	09-May-23											1st Floor 2G1/G2 - Drop Remaining Ceiling Tile			
3087		FNSH.D5.2980 1st Floor 2G1/G2 - Finish Plumbing		4	4	10-May-23											1st Floor 2G1/G2 - Finish Plumbing			
3088		FNSH.D5.2990 1st Floor 2G1/G2 - Finish HVAC		3	3	16-May-23											1st Floor 2G1/G2 - Finish HVAC			
3089		FNSH.D5.3000 1st Floor 2G1/G2 - Floor Coverings		6	6	19-May-23											1st Floor 2G1/G2 - Floor Coverings			
3090		2nd Floor Sector 2F1&F2 Admin			54	54	09-Feb-23											26-Apr-23, 2nd Floor Sector 2F1&F2 Admin		
3091		FRME.D5.366 2nd Floor 2F1/F2 - Layout and Frame Walls		13	13	09-Feb-23												2nd Floor 2F1/F2 - Layout and Frame Walls		
3092		MEP.D5.3320 2nd Floor 2F1/F2 - Rough-in Plumbing		8	8	09-Feb-23											2nd Floor 2F1/F2 - Rough-in Plumbing			
3093		MEP.D5.3330 2nd Floor 2F1/F2 - Rough-in HVAC		7	7	09-Feb-23											2nd Floor 2F1/F2 - Rough-in HVAC			
3094		MEP.D5.3340 2nd Floor 2F1/F2 - Rough-in Fire		7	7	09-Feb-23											2nd Floor 2F1/F2 - Rough-in Fire			
3095		MEP.D5.3350 2nd Floor 2F1/F2 - Rough-in Electric		8	8	09-Feb-23											2nd Floor 2F1/F2 - Rough-in Electric			
3096		MEP.D5.3360 2nd Floor 2F1/F2 - Rough-in Low Volt		8	8	09-Feb-23											2nd Floor 2F1/F2 - Rough-in Low Volt			
3097		FRME.D5.371 2nd Floor 2F1/F2 - Install HM Door Frames		5	5	09-Feb-23											2nd Floor 2F1/F2 - Install HM Door Frames			
3098		MEP.D5.3370 2nd Floor 2F1/F2 - Fire caulk		2	2	22-Feb-23											2nd Floor 2F1/F2 - Fire caulk			
3099		FRME.D5.367 2nd Floor 2F1/F2 - Insulate		4	4	24-Feb-23											2nd Floor 2F1/F2 - Insulate			
3100		FRME.D5.368 2nd Floor 2F1/F2 - Install Drywall Upper		5	5	02-Mar-23											2nd Floor 2F1/F2 - Install Drywall Upper			
3101		FRME.D5.369 2nd Floor 2F1/F2 - Hang and Tape Drywall		8	8	09-Mar-23											2nd Floor 2F1/F2 - Hang and Tape Drywall			
3102		FNSH.D5.3010 2nd Floor 2F1/F2 - Paint		3	3	21-Mar-23											2nd Floor 2F1/F2 - Paint			
3103		FRME.D5.37C 2nd Floor 2F1/F2 - Grid Ceiling		5	5	24-Mar-23											2nd Floor 2F1/F2 - Grid Ceiling			
3104		FNSH.D5.3020 2nd Floor 2F1/F2 - Doors & Hardware		5	5	31-Mar-23											2nd Floor 2F1/F2 - Doors & Hardware			
3105		FNSH.D5.3030 2nd Floor 2F1/F2 - Tile in Restroom		5	5	31-Mar-23											2nd Floor 2F1/F2 - Tile in Restroom			
3106		FNSH.D5.3040 2nd Floor 2F1/F2 - Finish Electric		5	5	31-Mar-23											2nd Floor 2F1/F2 - Finish Electric			
3107		FNSH.D5.3050 2nd Floor 2F1/F2 - Drop Remaining Ceiling Tile		1	1	07-Apr-23											2nd Floor 2F1/F2 - Drop Remaining Ceiling Tile			
3108		FNSH.D5.3060 2nd Floor 2F1/F2 - Finish Plumbing		4	4	10-Apr-23											2nd Floor 2F1/F2 - Finish Plumbing			
3109		FNSH.D5.3070 2nd Floor 2F1/F2 - Finish HVAC		3	3	14-Apr-23											2nd Floor 2F1/F2 - Finish HVAC			
3110		FNSH.D5.3080 2nd Floor 2F1/F2 - Floor Coverings		6	6	19-Apr-23											2nd Floor 2F1/F2 - Floor Coverings			


Remaining Level of Effort

Remaining Work

Milestone

QTS HIL2 DC2, DC3, DC5 Construction Schedule				Classic Schedule Layout					2022								2023				2024	
#	Activity ID	Activity Name		Original Duration	Remaining Duration	Start	Finish		Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2			
3111	2nd Floor Sector 2G1&G2 Back of House	FRME.D5.372 2nd Floor 2G1/G2 - Layout and Frame Walls		9	9	21-Mar-23	31-Mar-23													12-May-23, 2nd Floor Sector 2G1&G2 Back of House		
3112		MEP.D5.3380 2nd Floor 2G1/G2 - Rough-in Plumbing		8	8	21-Mar-23	30-Mar-23													2nd Floor 2G1/G2 - Layout and Frame Walls		
3113		MEP.D5.3390 2nd Floor 2G1/G2 - Rough-in HVAC		7	7	21-Mar-23	29-Mar-23													2nd Floor 2G1/G2 - Rough-in Plumbing		
3114		MEP.D5.3400 2nd Floor 2G1/G2 - Rough-in Fire		7	7	21-Mar-23	29-Mar-23													2nd Floor 2G1/G2 - Rough-in HVAC		
3115		MEP.D5.3410 2nd Floor 2G1/G2 - Rough-in Electric		8	8	21-Mar-23	30-Mar-23													2nd Floor 2G1/G2 - Rough-in Fire		
3116		MEP.D5.3420 2nd Floor 2G1/G2 - Rough-in Low Volt		8	8	21-Mar-23	30-Mar-23													2nd Floor 2G1/G2 - Rough-in Electric		
3117		FRME.D5.377 2nd Floor 2G1/G2 - Install HM Door Frame		5	5	21-Mar-23	27-Mar-23													2nd Floor 2G1/G2 - Rough-in Low Volt		
3118		MEP.D5.3430 2nd Floor 2G1/G2 - Fire caulk		2	2	31-Mar-23	03-Apr-23													2nd Floor 2G1/G2 - Install HM Door Frame		
3119		FRME.D5.373 2nd Floor 2G1/G2 - Insulate		2	2	04-Apr-23	05-Apr-23													2nd Floor 2G1/G2 - Fire caulk		
3120		FRME.D5.374 2nd Floor 2G1/G2 - Install Drywall Upper		5	5	06-Apr-23	12-Apr-23													2nd Floor 2G1/G2 - Insulate		
3121		FRME.D5.375 2nd Floor 2G1/G2 - Hang and Tape Drywall		7	7	13-Apr-23	21-Apr-23													2nd Floor 2G1/G2 - Install Drywall Upper		
3122		FNSH.D5.3110 2nd Floor 2G1/G2 - Tile in Restroom		3	3	13-Apr-23	17-Apr-23													2nd Floor 2G1/G2 - Hang and Tape Drywall		
3123		FNSH.D5.3090 2nd Floor 2G1/G2 - Paint		3	3	24-Apr-23	26-Apr-23													2nd Floor 2G1/G2 - Tile in Restroom		
3124		FRME.D5.376 2nd Floor 2G1/G2 - Wood Ceiling		3	3	27-Apr-23	01-May-23													2nd Floor 2G1/G2 - Paint		
3125		FNSH.D5.3100 2nd Floor 2G1/G2 - Doors & Hardware		5	5	27-Apr-23	03-May-23													2nd Floor 2G1/G2 - Wood Ceiling		
3126		FNSH.D5.3120 2nd Floor 2G1/G2 - Finish Electric		5	5	27-Apr-23	03-May-23													2nd Floor 2G1/G2 - Doors & Hardware		
3127		FNSH.D5.3130 2nd Floor 2G1/G2 - Finish Plumbing		4	4	04-May-23	09-May-23													2nd Floor 2G1/G2 - Finish Electric		
3128		FNSH.D5.3140 2nd Floor 2G1/G2 - Finish HVAC		3	3	10-May-23	12-May-23													2nd Floor 2G1/G2 - Finish Plumbing		
3129		Site Finishes		67	67	07-Apr-23	12-Jul-23													2nd Floor 2G1/G2 - Finish HVAC		
3130		Site Finishes		67	67	07-Apr-23	12-Jul-23													12-Jul-23, Site Finishes		
3131	Trash Enclosure	FOND.D5.257 Trash Encl - Dig Footings		1	1	07-Apr-23	07-Apr-23													19-Apr-23, Trash Enclosure		
3132		FOND.D5.258 Trash Encl - Form Footings		1	1	07-Apr-23	07-Apr-23													Trash Encl - Dig Footings		
3133		FOND.D5.259 Trash Encl - Install Rebar & Bollards		1	1	10-Apr-23	10-Apr-23													Trash Encl - Form Footings		
3134		FOND.D5.260 Trash Encl - Inspect & Pour		1	1	10-Apr-23	10-Apr-23													Trash Encl - Install Rebar & Bollards		
3135		CONC.D5.232 Trash Encl - Embeds for Gate		3	3	10-Apr-23	12-Apr-23													Trash Encl - Inspect & Pour		
3136		CONC.D5.23 SOG.D5.2280 Trash Encl - SOG		2	2	11-Apr-23	12-Apr-23													19-Apr-23, Trash Enclosure		
3137		CONC.D5.233 Trash Encl - CMU - Trash Enc.		3	3	13-Apr-23	17-Apr-23													Trash Encl - Embeds for Gate		
3138		CONC.D5.234 Trash Encl - Grout CMU		1	1	18-Apr-23	18-Apr-23													Trash Encl - SOG		
3139		FNSH.D5.3150 Trash Encl - Install Gate		1	1	19-Apr-23	19-Apr-23													Trash Encl - CMU - Trash Enc.		
3140		FNSH.D5.3160 Trash Encl - Install Steel Coping		1	1	19-Apr-23	19-Apr-23													Trash Encl - Grout CMU		
3141		FNSH.D5.3170 Trash Encl - Paint		1	1	19-Apr-23	19-Apr-23													Trash Encl - Install Gate		
3142		FNSH.D5.3180 Trash Encl - Install Steel Coping		1	1	19-Apr-23	19-Apr-23													Trash Encl - Paint		
3143		Parking Lot		24	24	25-May-23	28-Jun-23													28-Jun-23, Parking Lot		
3144		UTIL.D5.1160 Park. Lot - Install/Adjust Manhole Covers		3	3	25-May-23	30-May-23													Park. Lot - Install/Adjust Manhole Covers		
3145		FOND.D5.261 Park. Lot - Rough Grade Parking Lot		2	2	25-May-23	26-May-23													Park. Lot - Rough Grade Parking Lot		
3146		FNSH.D5.3190 Park. Lot - Landscape Sleeves		3	3	25-May-23	30-May-23													Park. Lot - Landscape Sleeves		
3147		CONC.D5.234 Park. Lot - Cut Curbs		2	2	30-May-23	31-May-23													Park. Lot - Cut Curbs		
3148		UTIL.D5.1170 Park. Lot - Install Catch Basins		3	3	01-Jun-23	05-Jun-23													Park. Lot - Install Catch Basins		
3149		MEP.D5.3440 Park. Lot - Street Light Conduits		2	2																	

QTS HIL2 DC2, DC3, DC5 Construction Schedule			Classic Schedule Layout						12-Jul-22 15:37							
#	Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish		2022					2023			
					Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	
3206	MEP.D5.26	1st Floor MPOE 1/2 - Install Sprinkler Drops	5	5	11-May-23	17-May-23							1st Floor MPOE 1/2 - Install Sprinkler Drops			
3207	FNSH.D5.2	1st Floor MPOE 1/2 - Paint MPOE	2	2	18-May-23	19-May-23							1st Floor MPOE 1/2 - Paint MPOE			
3208	FRME.D5.1	1st Floor MPOE 1/2 - Install Overhead Doors	5	5	18-May-23	24-May-23							1st Floor MPOE 1/2 - Install Overhead Doors			
3209	FNSH.D5.2	1st Floor MPOE 1/2 - Install Finishes	5	5	22-May-23	26-May-23							1st Floor MPOE 1/2 - Install Finishes			
3210	FNSH.D5.2	1st Floor MPOE 1/2 - Trim Out Electrical Devices	5	5	22-May-23	26-May-23							1st Floor MPOE 1/2 - Trim Out Electrical Devices			
3211	Equipment		29	29	22-May-23	30-Jun-23							30-Jun-23; Equipment			
3212	EQPT.D5.3	1st Floor MPOE 1/2 - Install HDP Panels	10	10	22-May-23	05-Jun-23							1st Floor MPOE 1/2 - Install HDP Panels			
3213	EQPT.D5.3	1st Floor MPOE 1/2 - Install Network COD 2000AMP	10	10	22-May-23	05-Jun-23							1st Floor MPOE 1/2 - Install Network COD 2000AMP			
3214	EQPT.D5.3	1st Floor MPOE 1/2 - Install PDU	5	5	06-Jun-23	12-Jun-23							1st Floor MPOE 1/2 - Install PDU			
3215	EQPT.D5.3	1st Floor MPOE 1/2 - Set CRAC Units	5	5	08-Jun-23	14-Jun-23							1st Floor MPOE 1/2 - Set CRAC Units			
3216	EQPT.D5.3	1st Floor MPOE 1/2 - Install COD Boards	5	5	08-Jun-23	14-Jun-23							1st Floor MPOE 1/2 - Install COD Boards			
3217	EQPT.D5.3	1st Floor MPOE 1/2 - Final Connections CRAC Units	15	15	12-Jun-23	30-Jun-23							1st Floor MPOE 1/2 - Final Connections CRAC Units			
3218	EQPT.D5.3	1st Floor MPOE 1/2 - Set HUM	5	5	15-Jun-23	21-Jun-23							1st Floor MPOE 1/2 - Set HUM			
3219	Systems Gallery 1001 and 1010 DH A		106	106	06-Feb-23	06-Jul-23							06-Jul-23; Systems Gallery 1001 and 1010 DH A			
3220	Rough-In		68	68	06-Feb-23	11-May-23							11-May-23; Rough-In			
3221	MEP.D5.28	1st Floor DHA SG1001/1010 - Install Fire Protection	15	15	06-Feb-23	27-Feb-23							1st Floor DHA SG1001/1010 - Install Fire Protection			
3222	MEP.D5.28	1st Floor DHA SG1001/1010 - Install OH Mechanical (Plumbing and HVAC)	15	15	28-Feb-23	20-Mar-23							1st Floor DHA SG1001/1010 - Install OH Mechanical (Plumbing and HVAC)			
3223	MEP.D5.28	1st Floor DHA SG1001/1010 - Install OH Electrical	20	20	28-Feb-23	27-Mar-23							1st Floor DHA SG1001/1010 - Install OH Electrical			
3224	FRME.D5.1	1st Floor DHA SG1001/1010 - Layout and Frame Walls	6	6	11-Apr-23	18-Apr-23							1st Floor DHA SG1001/1010 - Layout and Frame Walls			
3225	FRME.D5.1	1st Floor DHA SG1001/1010 - Install Drywall Upper	6	6	13-Apr-23	20-Apr-23							1st Floor DHA SG1001/1010 - Install Drywall Upper			
3226	MEP.D5.28	1st Floor DHA SG1001/1010 - In-wall Rough-in Electrical	5	5	13-Apr-23	19-Apr-23							1st Floor DHA SG1001/1010 - In-wall Rough-in Electrical			
3227	FRME.D5.1	1st Floor DHA SG1001/1010 - Insulate and Inspect	5	5	20-Apr-23	26-Apr-23							1st Floor DHA SG1001/1010 - Insulate and Inspect			
3228	FRME.D5.1	1st Floor DHA SG1001/1010 - Hang and Tape Drywall	6	6	27-Apr-23	04-May-23							1st Floor DHA SG1001/1010 - Hang and Tape Drywall			
3229	FNSH.D5.2	1st Floor DHA SG1001/1010 - Paint - DHA SG	2	2	05-May-23	08-May-23							1st Floor DHA SG1001/1010 - Paint - DHA SG			
3230	FNSH.D5.2	1st Floor DHA SG1001/1010 - Install Finishes	3	3	09-May-23	11-May-23							1st Floor DHA SG1001/1010 - Install Finishes			
3231	Equipment		43	43	05-May-23	06-Jul-23							06-Jul-23; Equipment			
3232	EQPT.D5.3	1st Floor DHA SG1001/1010 - Install Switch Gear	5	5	05-May-23	11-May-23							1st Floor DHA SG1001/1010 - Install Switch Gear			
3233	EQPT.D5.3	1st Floor DHA SG1001/1010 - Install ATS	5	5	05-May-23	11-May-23							1st Floor DHA SG1001/1010 - Install ATS			
3234	EQPT.D5.3	1st Floor DHA SG1001/1010 - Install PDU	5	5	05-May-23	11-May-23							1st Floor DHA SG1001/1010 - Install PDU			
3235	EQPT.D5.3	1st Floor DHA SG1001/1010 - Install Reserve Busway	5	5	05-May-23	11-May-23							1st Floor DHA SG1001/1010 - Install Reserve Busway			
3236	EQPT.D5.3	1st Floor DHA SG1001/1010 - Install HDP	5	5	09-May-23	15-May-23							1st Floor DHA SG1001/1010 - Install HDP			
3237	EQPT.D5.3	1st Floor DHA SG1001/1010 - Install COD Boards	5	5	08-Jun-23	14-Jun-23							1st Floor DHA SG1001/1010 - Install COD Boards			
3238	EQPT.D5.3	1st Floor DHA SG1001/1010 - Install CRAC Units	5	5	08-Jun-23	14-Jun-23							1st Floor DHA SG1001/1010 - Install CRAC Units			
3239	EQPT.D5.3	1st Floor DHA SG1001/1010 - Final Connections CRAC Units	15	15	15-Jun-23	06-Jul-23							1st Floor DHA SG1001/1010 - Final Connections CRAC Units			
3240	EQPT.D5.3	1st Floor DHA SG1001/1010 - Pull and Terminate Feeders	15	15	15-Jun-23	06-Jul-23							1st Floor DHA SG1001/1010 - Pull and Terminate Feeders			
3241	Mechanical Gallery 1002 DH A		103	103	09-Feb-23	06-Jul-23							06-Jul-23; Mechanical Gallery 1002 DH A			
3242	Rough-In		23	23	09-Feb-23	14-Mar-23							14-Mar-23; Rough-In			
3243	FRME.D5.1	1st Floor DHA MG1002 - Layout and Frame Walls	6	6	09-Feb-23	16-Feb-23							1st Floor DHA MG1002 - Layout and Frame Walls			
3244	MEP.D5.27	1st Floor DHA MG1002 - Install Fire Protection	1	1	09-Feb-23	09-Feb-23							1st Floor DHA MG1002 - Install Fire Protection			
3245	MEP.D5.28	1st Floor DHA MG1002 - Install OH Mechanical (Plumbing and HVAC)	3	3	09-Feb-23	13-Feb-23							1st Floor DHA MG1002 - Install OH Mechanical (Plumbing and HVAC)			
3246	MEP.D5.28	1st Floor DHA MG1002 - Install OH Electrical	5	5	09-Feb-23	15-Feb-23							1st Floor DHA MG1002 - Install OH Electrical			
3247	MEP.D5.27	1st Floor DHA MG1002 - In-wall Rough-in Electrical	3	3	10-Feb-23	14-Feb-23							1st Floor DHA MG1002 - In-wall Rough-in Electrical			
3248	FRME.D5.1	1st Floor DHA MG1002 - Insulate and Inspect	5	5	15-Feb-23	22-Feb-23							1st Floor DHA MG1002 - Insulate and Inspect			
3249	FRME.D5.1	1st Floor DHA MG1002 - Install Drywall Upper	6	6	17-Feb-23	27-Feb-23							1st Floor DHA MG1002 - Install Drywall Upper			
3250	FRME.D5.1	1st Floor DHA MG1002 - Hang and Tape Drywall	6	6	28-Feb-23	07-Mar-23							1st Floor DHA MG1002 - Hang and Tape Drywall			
3251	FNSH.D5.2	1st Floor DHA MG1002 - Paint	2	2	08-Mar-23	09-Mar-23							1st Floor DHA MG1002 - Paint			
3252	FNSH.D5.2	1st Floor DHA MG1002 - Install Finishes	3	3	10-Mar-23	14-Mar-23							1st Floor DHA MG1002 - Install Finishes			
3253	Equipment		61	61	11-Apr-23	06-Jul-23							06-Jul-23; Equipment			



QTS HIL2 DC2, DC3, DC5 Construction Schedule				Classic Schedule Layout							12-Jul-22 15:37							
#	Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	2022					2023					2024	
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	
3254	DH A ROOM 1100	EQPT.D5.3 1st Floor DHA MG1002 - Install HDP Boards	5	5	11-Apr-23	17-Apr-23											1st Floor DHA MG1002 - Install HDP Boards	
3255		EQPT.D5.3 1st Floor DHA MG1002 - Pull and Terminate Feeders	15	15	18-Apr-23	08-May-23											1st Floor DHA MG1002 -Pull and Terminate Feeders	
3256		EQPT.D5.3 1st Floor DHA MG1002 - Install CRAC Units	5	5	08-Jun-23	14-Jun-23											1st Floor DHA MG1002 - Install CRAC Units	
3257		EQPT.D5.3 1st Floor DHA MG1002 - Final Connections CRAC Units	15	15	15-Jun-23	06-Jul-23											1st Floor DHA MG1002 - Final Connections	
3258		DH A ROOM 1100		41	41	17-Feb-23	17-Apr-23										17-Apr-23, DH A ROOM 1100	
3259		Rough-In		41	41	17-Feb-23	17-Apr-23										17-Apr-23, Rough-In	
3260		FRME.D5.1 1st Floor DHA R1100 - Layout and Frame Walls	10	10	17-Feb-23	03-Mar-23											1st Floor DHA R1100 - Layout and Frame Walls	
3261		FRME.D5.1 1st Floor DHA R1100 - Install Drywall Upper	4	4	06-Mar-23	09-Mar-23											1st Floor DHA R1100 - Install Drywall Upper	
3262		MEP.D5.27 1st Floor DHA R1100 - Rough-In Fire Protection	3	3	10-Mar-23	14-Mar-23											1st Floor DHA R1100 - Rough-In Fire Protection	
3263		MEP.D5.27 1st Floor DHA R1100 - In-wall Rough-in Electrical	4	4	10-Mar-23	15-Mar-23											1st Floor DHA R1100 - In-wall Rough-in Electrical	
3264	Systems Gallery 1003 and 1020 DH D	MEP.D5.27 1st Floor DHA R1100 - Install OH Mechanical (Plumbing and HVAC)	5	5	16-Mar-23	22-Mar-23											1st Floor DHA R1100 - Install OH Mechanical (Plumbing and HVAC)	
3265		FRME.D5.1 1st Floor DHA R1100 - Insulate and Inspect	5	5	16-Mar-23	22-Mar-23											1st Floor DHA R1100 - Insulate and Inspect	
3266		MEP.D5.27 1st Floor DHA R1100 - Install OH Electrical	7	7	23-Mar-23	31-Mar-23											1st Floor DHA R1100 - Install OH Electrical	
3267		FRME.D5.1 1st Floor DHA R1100 - Hang and Tape Drywall	6	6	03-Apr-23	10-Apr-23											1st Floor DHA R1100 - Hang and Tape Drywall	
3268		FRME.D5.1 1st Floor DHA R1100 - Install Structural Grid	10	10	03-Apr-23	14-Apr-23											1st Floor DHA R1100 - Install Structural Grid	
3269		FNSH.D5.2 1st Floor DHA R1100 - Paint DHA R	2	2	11-Apr-23	12-Apr-23											1st Floor DHA R1100 - Paint DHA R	
3270		FNSH.D5.2 1st Floor DHA R1100 - Install Finishes	3	3	13-Apr-23	17-Apr-23											1st Floor DHA R1100 - Install Finishes	
3271		Systems Gallery 1003 and 1020 DH D		81	81	21-Mar-23	13-Jul-23										13-Jul-23, Systems Gallery 1003 and 1020	
3272		Rough-In		49	49	21-Mar-23	26-May-23										26-May-23, Rough-In	
3273		MEP.D5.29 1st Floor DHD SG1003/1020 - Install Fire Protection	5	5	21-Mar-23	27-Mar-23											1st Floor DHD SG1003/1020 -Install Fire Protection	
3274		MEP.D5.29 1st Floor DHD SG1003/1020 - Install OH Mechanical (Plumbing and HVAC)	15	15	28-Mar-23	17-Apr-23											1st Floor DHD SG1003/1020 - Install OH Mechanical (Plumbing and HVAC)	
3275		MEP.D5.29 1st Floor DHD SG1003/1020 - Install OH Electrical	20	20	28-Mar-23	24-Apr-23											1st Floor DHD SG1003/1020 - Install OH Electrical	
3276	Equipment	FRME.D5.1 1st Floor DHD SG1003/1020 - Layout and Frame Walls	6	6	28-Apr-23	05-May-23											1st Floor DHD SG1003/1020 - Layout and Frame Walls	
3277		FRME.D5.1 1st Floor DHD SG1003/1020 - Install Drywall Upper	6	6	02-May-23	09-May-23											1st Floor DHD SG1003/1020 - Install Drywall Upper	
3278		MEP.D5.29 1st Floor DHD SG1003/1020 - In-wall Rough-in Electrical	3	3	02-May-23	04-May-23											1st Floor DHD SG1003/1020 - In-wall Rough-in Electrical	
3279		FRME.D5.1 1st Floor DHD SG1003/1020 - Insulate and Inspect	5	5	05-May-23	11-May-23											1st Floor DHD SG1003/1020 - Insulate and Inspect	
3280		FRME.D5.1 1st Floor DHD SG1003/1020 - Hang and Tape Drywall	6	6	12-May-23	19-May-23											1st Floor DHD SG1003/1020 - Hang and Tape Drywall	
3281		FNSH.D5.2 1st Floor DHD SG1003/1020 - Paint	2	2	22-May-23	23-May-23											1st Floor DHD SG1003/1020 - Paint	
3282		FNSH.D5.2 1st Floor DHD SG1003/1020 - Install Finishes	3	3	24-May-23	26-May-23											1st Floor DHD SG1003/1020 - Install Finishes	
3283		Equipment		37	37	22-May-23	13-Jul-23										13-Jul-23, Equipment	
3284		EQPT.D5.3 1st Floor DHD SG1003/1020 - Install Switch Gear	5	5	22-May-23	26-May-23											1st Floor DHD SG1003/1020 - Install Switch Gear	
3285		EQPT.D5.3 1st Floor DHD SG1003/1020 - Install Reserve Busway	5	5	22-May-23	26-May-23											1st Floor DHD SG1003/1020 - Install Reserve Busway	
3286	Mechanical Gallery 1004 DH D	EQPT.D5.3 1st Floor DHD SG1003/1020 - Install ATS	5	5	30-May-23	05-Jun-23											1st Floor DHD SG1003/1020 - Install ATS	
3287		EQPT.D5.3 1st Floor DHD SG1003/1020 - Install COD Boards	5	5	08-Jun-23	14-Jun-23											1st Floor DHD SG1003/1020 - Install COD Boards	
3288		EQPT.D5.3 1st Floor DHD SG1003/1020 - Install CRAC Units	5	5	08-Jun-23	14-Jun-23											1st Floor DHD SG1003/1020 - Install CRAC Units	
3289		EQPT.D5.3 1st Floor DHD SG1003/1020 - Install HDP	5	5	15-Jun-23	21-Jun-23											1st Floor DHD SG1003/1020 - Install HDP	
3290		EQPT.D5.3 1st Floor DHD SG1003/1020 - Install PDU	5	5	15-Jun-23	21-Jun-23											1st Floor DHD SG1003/1020 - Install PDU	
3291		EQPT.D5.3 1st Floor DHD SG1003/1020 - Final Connections CRAC Units	15	15	15-Jun-23	06-Jul-23											1st Floor DHD SG1003/1020 - Final Connections CRAC Units	
3292		EQPT.D5.3 1st Floor DHD SG1003/1020 - Pull and Terminate Feeders	15	15	22-Jun-23	13-Jul-23											1st Floor DHD SG1003/1020 - Pull and Terminate Feeders	
3293		Mechanical Gallery 1004 DH D		76	76	21-Mar-23	06-Jul-23										06-Jul-23, Mechanical Gallery 1004 DH D	
3294		Rough-In		57	57	21-Mar-23	08-Jun-23										08-Jun-23, Rough-In	
3295		MEP.D5.28 1st Floor DHD MG1004 - Install Fire Protection	5	5	21-Mar-23	27-Mar-23											1st Floor DHD MG1004 - Install Fire Protection	
3296		MEP.D5.28 1st Floor DHD MG1004 - In-wall Rough-in Electrical	3	3	28-Mar-23	30-Mar-23											1st Floor DHD MG1004 - In-wall Rough-in Electrical	
3297		MEP.D5.28 1st Floor DHD MG1004 - Install OH Mechanical (Plumbing and HVAC)	5	5	28-Mar-23	03-Apr-23											1st Floor DHD MG1004 - Install OH Mechanical (Plumbing and HVAC)	
3298	DH D MG 1004	FRME.D5.1 1st Floor DHD MG1004 - Insulate and Inspect	5	5	31-Mar-23	06-Apr-23											1st Floor DHD MG1004 - Insulate and Inspect	

QTS HIL2 DC2, DC3, DC5 Construction Schedule				Classic Schedule Layout						Timeline View									
#	Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	2022					2023					2024		
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2		
3302	FRME.D5.1	1st Floor DHD MG1004 - Hang and Tape Drywall	6	6	24-May-23	01-Jun-23											1st Floor DHD MG1004 - Hang and Tape Drywall		
3303		1st Floor DHD MG1004 - Paint		2	2	02-Jun-23											1st Floor DHD MG1004 - Paint		
3304		1st Floor DHD MG1004 - Install Finishes		3	3	06-Jun-23											1st Floor DHD MG1004 - Install Finishes		
3305		Equipment	24	24	02-Jun-23	06-Jul-23											06-Jul-23; Equipment		
3306		EQPT.D5.3	1st Floor DHD MG1004 - Install HDP Boards	5	5	02-Jun-23	08-Jun-23										1st Floor DHD MG1004 - Install HDP Boards		
3307		EQPT.D5.3	1st Floor DHD MG1004 - Install CRAC Units	5	5	08-Jun-23	14-Jun-23										1st Floor DHD MG1004 - Install CRAC Units		
3308		EQPT.D5.3	1st Floor DHD MG1004 - Pull and Terminate Feeders	15	15	09-Jun-23	29-Jun-23										1st Floor DHD MG1004 - Pull and Terminate Feeders		
3309		EQPT.D5.3	1st Floor DHD MG1004 - Final Connections CRAC Units	15	15	15-Jun-23	06-Jul-23										1st Floor DHD MG1004 - Final Connections CRAC Units		
3310	DH D ROOM 1200			41	41	16-May-23	13-Jul-23										13-Jul-23; DH D ROOM 1200		
3311	Rough-In			41	41	16-May-23	13-Jul-23										13-Jul-23; Rough-In		
3312	FRME.D5.1	1st Floor DHD R1200 - Layout and Frame Walls	10	10	16-May-23	30-May-23											1st Floor DHD R1200 - Layout and Frame Walls		
3313	FRME.D5.1	1st Floor DHD R1200 - Install Drywall Upper	4	4	31-May-23	05-Jun-23											1st Floor DHD R1200 - Install Drywall Upper		
3314	MEP.D5.27	1st Floor DHD R1200 - Install Fire Protection		3	3	06-Jun-23	08-Jun-23										1st Floor DHD R1200 - Install Fire Protection		
3315	MEP.D5.27	1st Floor DHD R1200 - In-wall Rough-in Electrical		4	4	06-Jun-23	09-Jun-23										1st Floor DHD R1200 - In-wall Rough-in Electrical		
3316	MEP.D5.27	1st Floor DHD R1200 - Install OH Mechanical (Plumbing and HVAC)	5	5	12-Jun-23	16-Jun-23											1st Floor DHD R1200 - Install OH Mechanical (Plumbing and HVAC)		
3317	FRME.D5.1	1st Floor DHD R1200 - Insulate and Inspect		5	5	12-Jun-23	16-Jun-23										1st Floor DHD R1200 - Insulate and Inspect		
3318	MEP.D5.27	1st Floor DHD R1200 - Install OH Electrical		7	7	19-Jun-23	27-Jun-23										1st Floor DHD R1200 - Install OH Electrical		
3319	FRME.D5.1	1st Floor DHD R1200 - Hang and Tape Drywall		6	6	28-Jun-23	06-Jul-23										1st Floor DHD R1200 - Hang and Tape Drywall		
3320	FRME.D5.1	1st Floor DHD R1200 - Install Structural Grid		10	10	28-Jun-23	12-Jul-23										1st Floor DHD R1200 - Install Structural Grid		
3321	FNSH.D5.2	1st Floor DHD R1200 - Paint		2	2	07-Jul-23	10-Jul-23										1st Floor DHD R1200 - Paint		
3322	FNSH.D5.2	1st Floor DHD R1200 - Install Finishes		3	3	11-Jul-23	13-Jul-23										1st Floor DHD R1200 - Install Finishes		
3323	2nd Floor Data Hall			101	101	21-Feb-23	13-Jul-23										13-Jul-23; 2nd Floor Data Hall		
3324	BDF 1 and 2			93	93	03-Mar-23	13-Jul-23										13-Jul-23; BDF 1 and 2		
3325	Rough-In			40	40	03-Mar-23	27-Apr-23										27-Apr-23; Rough-In		
3326	MEP.D5.29	2nd Floor BDF1/2 - Install Fire Protection		3	3	03-Mar-23	07-Mar-23										2nd Floor BDF1/2 - Install Fire Protection		
3327	MEP.D5.29	2nd Floor BDF1/2 - Install OH Mechanical (Plumbing and HVAC)		5	5	08-Mar-23	14-Mar-23										2nd Floor BDF1/2 - Install OH Mechanical (Plumbing and HVAC)		
3328	MEP.D5.29	2nd Floor BDF1/2 - Install OH Electrical		7	7	08-Mar-23	16-Mar-23										2nd Floor BDF1/2 - Install OH Electrical		
3329	FRME.D5.1	2nd Floor BDF1/2 - Layout and Frame Walls		10	10	17-Mar-23	30-Mar-23										2nd Floor BDF1/2 - Layout and Frame Walls		
3330	FRME.D5.1	2nd Floor BDF1/2 - Install Drywall Upper		4	4	31-Mar-23	05-Apr-23										2nd Floor BDF1/2 - Install Drywall Upper		
3331	MEP.D5.29	2nd Floor BDF1/2 - In-wall Rough-in Electrical		4	4	31-Mar-23	05-Apr-23										2nd Floor BDF1/2 - In-wall Rough-in Electrical		
3332	FRME.D5.1	2nd Floor BDF1/2 - Install Structural Grid		10	10	06-Apr-23	19-Apr-23										2nd Floor BDF1/2 - Install Structural Grid		
3333	FRME.D5.1	2nd Floor BDF1/2 - Insulate and Inspect		5	5	06-Apr-23	12-Apr-23										2nd Floor BDF1/2 - Insulate and Inspect		
3334	FRME.D5.1	2nd Floor BDF1/2 - Hang and Tape Drywall		6	6	13-Apr-23	20-Apr-23										2nd Floor BDF1/2 - Hang and Tape Drywall		
3335	FNSH.D5.2	2nd Floor BDF1/2 - Paint		2	2	21-Apr-23	24-Apr-23										2nd Floor BDF1/2 - Paint		
3336	FNSH.D5.2	2nd Floor BDF1/2 - Install Finishes		3	3	25-Apr-23	27-Apr-23										2nd Floor BDF1/2 - Install Finishes		
3337	Equipment			56	56	25-Apr-23	13-Jul-23										13-Jul-23; Equipment		
3338	EQPT.D5.3	2nd Floor BDF1/2 - Install HDP Panels		10	10	25-Apr-23	08-May-23										2nd Floor BDF1/2 - Install HDP Panels		
3339	EQPT.D5.3	2nd Floor BDF1/2 - Set CRAC's		5	5	08-Jun-23	14-Jun-23										2nd Floor BDF1/2 - Set CRAC's		
3340	EQPT.D5.3	2nd Floor BDF1/2 - Set HUM		5	5	15-Jun-23	21-Jun-23										2nd Floor BDF1/2 - Set HUM		
3341	EQPT.D5.3	2nd Floor BDF1/2 - Final Connections CRAC Units		15	15	15-Jun-23	06-Jul-23										2nd Floor BDF1/2 - Final Connections CRAC Units		
3342	EQPT.D5.3	2nd Floor BDF1/2 - Pull and Terminate Feeders		15	15	22-Jun-23	13-Jul-23										2nd Floor BDF1/2 - Pull and Terminate Feeders		
3343	Systems Gallery 2001 and 2010 DH B			96	96	21-Feb-23	06-Jul-23										06-Jul-23; Systems Gallery 2001 and 2010 DH B		
3344	Rough-In			58	58	21-Feb-23	11-May-23										11-May-23; Rough-In		
3345	MEP.D5.31	2nd Floor DHB SG 2001/2010 - Install Fire Protection		5	5	21-Feb-23	27-Feb-23										2nd Floor DHB SG 2001/2010 - Install Fire Protection		
3346	MEP.D5.31	2nd Floor DHB SG 2001/2010 - Install OH Mechanical (Plumbing and HVAC)		15	15	28-Feb-23	20-Mar-23										2nd Floor DHB SG 2001/2010 - Install OH Mechanical (Plumbing and HVAC)		
3347	MEP.D5.31	2nd Floor DHB SG 2001/2010 - Install OH Electrical		20	20	28-Feb-23	27-Mar-23										2nd Floor DHB SG 2001/2010 - Install OH Electrical		
3348	FRME.D5.1	2nd Floor DHB SG 2001/2010 - Layout and Frame Walls		6	6	11-Apr-23	18-Apr-23										2nd Floor DHB SG 2001/2010 - Layout and Frame Walls		
3349	MEP.D5.31	2nd Floor DHB SG 2001/2010 - In-wall Rough-in Electrical		3	3	13-Apr-23	17-Apr-23										2nd Floor DHB SG 2001/2010 - In-wall Rough-in Electrical		

QTS HIL2 DC2, DC3, DC5 Construction Schedule				Classic Schedule Layout					Timeline View									
#	Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	2022					2023				2024		
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	
3350		FRME.D5.1 2nd Floor DHB SG 2001/2010 - Insulate and Inspect	5	5	18-Apr-23	24-Apr-23												2nd Floor DHB SG 2001/2010 - Insulate and Inspect
3351		FRME.D5.1 2nd Floor DHB SG 2001/2010 - Install Drywall Upper	6	6	19-Apr-23	26-Apr-23												2nd Floor DHB SG 2001/2010 - Install Drywall Upper
3352		FRME.D5.1 2nd Floor DHB SG 2001/2010 - Hang and Tape Drywall	6	6	27-Apr-23	04-May-23												2nd Floor DHB SG 2001/2010 - Hang and Tape Drywall
3353		FNSH.D5.2 2nd Floor DHB SG 2001/2010 - Paint	2	2	05-May-23	08-May-23												2nd Floor DHB SG 2001/2010 - Paint
3354		FNSH.D5.2 2nd Floor DHB SG 2001/2010 - Install Finishes	3	3	09-May-23	11-May-23												2nd Floor DHB SG 2001/2010 - Install Finishes
3355	Equipment			58	58	14-Apr-23	06-Jul-23											06-Jul-23; Equipment
3356		EQPT.D5.3 2nd Floor DHB SG 2001/2010 - Install Switch Gear	5	5	14-Apr-23	20-Apr-23												2nd Floor DHB SG 2001/2010 - Install Switch Gear
3357		EQPT.D5.3 2nd Floor DHB SG 2001/2010 - Install ATS	5	5	14-Apr-23	20-Apr-23												2nd Floor DHB SG 2001/2010 - Install ATS
3358		EQPT.D5.3 2nd Floor DHB SG 2001/2010 - Install HDP	5	5	14-Apr-23	20-Apr-23												2nd Floor DHB SG 2001/2010 - Install HDP
3359		EQPT.D5.3 2nd Floor DHB SG 2001/2010 - Install PDU	5	5	14-Apr-23	20-Apr-23												2nd Floor DHB SG 2001/2010 - Install PDU
3360		EQPT.D5.3 2nd Floor DHB SG 2001/2010 - Install Reserve Busway	5	5	14-Apr-23	20-Apr-23												2nd Floor DHB SG 2001/2010 - Install Reserve Busway
3361		EQPT.D5.3 2nd Floor DHB SG 2001/2010 - Install COD Boards	5	5	08-Jun-23	14-Jun-23												2nd Floor DHB SG 2001/2010 - Install COD Boards
3362		EQPT.D5.3 2nd Floor DHB SG 2001/2010 - Install CRAC Units	5	5	08-Jun-23	14-Jun-23												2nd Floor DHB SG 2001/2010 - Install CRAC Units
3363		EQPT.D5.3 2nd Floor DHB SG 2001/2010 - Final Connections CRAC Units	15	15	15-Jun-23	06-Jul-23												2nd Floor DHB SG 2001/2010 - Final Connections CRAC Units
3364		EQPT.D5.3 2nd Floor DHB SG 2001/2010 - Pull and Terminate Feeders	15	15	15-Jun-23	06-Jul-23												2nd Floor DHB SG 2001/2010 - Pull and Terminate Feeders
3365	Mechanical Gallery 2002 DH B			96	96	21-Feb-23	06-Jul-23											06-Jul-23; Mechanical Gallery 2002 DH B
3366	Rough-In			64	64	21-Feb-23	19-May-23											19-May-23; Rough-In
3367		FRME.D5.1 2nd Floor DHB MG 2002 - Layout and Frame Walls	6	6	21-Feb-23	28-Feb-23												2nd Floor DHB MG 2002 - Layout and Frame Walls
3368		MEP.D5.3C 2nd Floor DHB MG 2002 - Install Fire Protection	1	1	21-Feb-23	21-Feb-23												2nd Floor DHB MG 2002 - Install Fire Protection
3369		MEP.D5.3C 2nd Floor DHB MG 2002 - Install OH Mechanical (Plumbing and HVAC)	3	3	21-Feb-23	23-Feb-23												2nd Floor DHB MG 2002 - Install OH Mechanical (Plumbing and HVAC)
3370		MEP.D5.3C 2nd Floor DHB MG 2002 - Install OH Electrical	5	5	21-Feb-23	27-Feb-23												2nd Floor DHB MG 2002 - Install OH Electrical
3371		MEP.D5.3C 2nd Floor DHB MG 2002 - In-wall Rough-in Electrical	3	3	22-Feb-23	24-Feb-23												2nd Floor DHB MG 2002 - In-wall Rough-in Electrical
3372		FRME.D5.1 2nd Floor DHB MG 2002 - Insulate and Inspect	5	5	27-Feb-23	03-Mar-23												2nd Floor DHB MG 2002 - Insulate and Inspect
3373		FRME.D5.1 2nd Floor DHB MG 2002 - Install Drywall Upper	6	6	01-Mar-23	08-Mar-23												2nd Floor DHB MG 2002 - Install Drywall Upper
3374		FRME.D5.1 2nd Floor DHB MG 2002 - Hang and Tape Drywall	6	6	05-May-23	12-May-23												2nd Floor DHB MG 2002 - Hang and Tape Drywall
3375		FNSH.D5.2 2nd Floor DHB MG 2002 - Paint	2	2	15-May-23	16-May-23												2nd Floor DHB MG 2002 - Paint
3376		FNSH.D5.2 2nd Floor DHB MG 2002 - Install Finishes	3	3	17-May-23	19-May-23												2nd Floor DHB MG 2002 - Install Finishes
3377	Equipment			37	37	15-May-23	06-Jul-23											06-Jul-23; Equipment
3378		EQPT.D5.3 2nd Floor DHB MG 2002 - Install HDP Boards	5	5	15-May-23	19-May-23												2nd Floor DHB MG 2002 - Install HDP Boards
3379		EQPT.D5.3 2nd Floor DHB MG 2002 - Pull and Terminate Feeders	15	15	22-May-23	12-Jun-23												2nd Floor DHB MG 2002 - Pull and Terminate Feeders
3380		EQPT.D5.3 2nd Floor DHB MG 2002 - Install CRAC Units	5	5	08-Jun-23	14-Jun-23												2nd Floor DHB MG 2002 - Install CRAC Units
3381		EQPT.D5.3 2nd Floor DHB MG 2002 - Final Connections CRAC Units	15	15	15-Jun-23	06-Jul-23												2nd Floor DHB MG 2002 - Final Connections CRAC Units
3382	DH B ROOM 2100			64	64	01-Mar-23	30-May-23											30-May-23; DH B ROOM 2100
3383	Rough-In			64	64	01-Mar-23	30-May-23											30-May-23; Rough-In
3384		FRME.D5.1 2nd Floor DHB R2100 - Layout and Frame Walls	10	10	01-Mar-23	14-Mar-23												2nd Floor DHB R2100 - Layout and Frame Walls
3385		MEP.D5.29 2nd Floor DHB R2100 - Install Fire Protection	3	3	01-Mar-23	03-Mar-23												2nd Floor DHB R2100 - Install Fire Protection
3386		MEP.D5.30 2nd Floor DHB R2100 - Install OH Electrical	7	7	01-Mar-23	09-Mar-23												2nd Floor DHB R2100 - Install OH Electrical
3387		FRME.D5.1 2nd Floor DHB R2100 - Install Structural Grid	10	10	10-Mar-23	23-Mar-23												2nd Floor DHB R2100 - Install Structural Grid
3388		FRME.D5.1 2nd Floor DHB R2100 - Install Drywall Upper	4	4	15-Mar-23	20-Mar-23												2nd Floor DHB R2100 - Install Drywall Upper
3389		MEP.D5.29 2nd Floor DHB R2100 - In-wall Rough-in Electrical	4	4	21-Mar-23	24-Mar-23												2nd Floor DHB R2100 - In-wall Rough-in Electrical
3390		FRME.D5.1 2nd Floor DHB R2100 - Insulate and Inspect	5	5	27-Mar-23	31-Mar-23												2nd Floor DHB R2100 - Insulate and Inspect
3391		FRME.D5.1 2nd Floor DHB R2100 - Hang and Tape Drywall	6	6	15-May-23	22-May-23												2nd Floor DHB R2100 - Hang and Tape Drywall
3392		FNSH.D5.2 2nd Floor DHB R2100 - Paint	2	2	23-May-23	24-May-23												2nd Floor DHB R2100 - Paint
3393		FNSH.D5.2 2nd Floor DHB R2100 - Install Finishes	3	3	25-May-23	30-May-23												2nd Floor DHB R2100 - Install Finishes
3394	Systems Gallery 2020 and 2003 DH C			81	81	21-Mar-23	13-Jul-23											13-Jul-23; Systems Gallery 2020 and 2003 DH C
3395	Rough-In			59	59	21-Mar-23	12-Jun-23											12-Jun-23; Rough-In
3396		MEP.D5.31 2nd Floor DHC 2020/2003 - Install Fire Protection	5	5	21-Mar-23	27-Mar-23												2nd Floor DHC 2020/2003 - Install Fire Protection
3397		MEP.D5.31 2nd Floor DHC 2020/2003 - Install OH Mechanical (Plumbing and HVAC)	15	15	28-Mar-23	17-Apr-23												2nd Floor DHC 2020/2003 - Install OH Mechanical (Plumbing and HVAC)
█ Remaining Level of Effort █ Remaining Work ◆ Milestone ◆ Critical Remaining Work █ Summary			Page 71 of 74															

QTS HIL2 DC2, DC3, DC5 Construction Schedule				Classic Schedule Layout					12-Jul-22 15:37									
#	Activity ID	Activity Name		Original Duration	Remaining Duration	Start	Finish	2022					2023				2024	
								Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2
3446		Closeout and Final Inspections		73	73	29-Jun-23	09-Oct-23										09-Oct-23, Closeout and Final I	
3447		PNCH.D5.1370	Punch House	15	15	29-Jun-23	19-Jul-23										Punch House	
3448		PNCH.D5.1320	Punch MPOE/BDF	15	15	07-Jul-23	27-Jul-23									Punch MPOE/BDF		
3449		PNCH.D5.1330	Punch - DH A	15	15	07-Jul-23	27-Jul-23									Punch - DH A		
3450		PNCH.D5.1340	Punch DH B	15	15	07-Jul-23	27-Jul-23									Punch DH B		
3451		PNCH.D5.1350	Punch DH C	15	15	07-Jul-23	27-Jul-23									Punch DH C		
3452		PNCH.D5.1280	Elevators Final Inspections	5	5	11-Jul-23	17-Jul-23									Elevators Final Inspections		
3453		PNCH.D5.1360	Punch DH D	15	15	14-Jul-23	03-Aug-23									Punch DH D		
3454		PNCH.D5.1260	Electrical Final Inspections - DC2	5	5	14-Sep-23	20-Sep-23									Electrical Final Inspections -DC2		
3455		PNCH.D5.1290	Fire and Life Safety Final Inspections	5	5	14-Sep-23	20-Sep-23									Fire and Life Safety Final Inspections		
3456		PNCH.D5.1310	Low Voltage Final Inspections	5	5	14-Sep-23	20-Sep-23									Low Voltage Final Inspections		
3457		PNCH.D5.1270	Mechanical Final Inspections	5	5	19-Sep-23	25-Sep-23									Mechanical Final Inspections		
3458		PNCH.D5.1300	Building Final Inspections	5	5	26-Sep-23	02-Oct-23									Building Final Inspections		
3459		PNCH.D5.1380	Receive Certificate of Occupancy	5	5	03-Oct-23	09-Oct-23									Receive Certificate of Occupan		
3460		Startup Commissioning and Turnover		365	365	13-Sep-22	01-Mar-24										01-Mar-24, S	
3461		Startup Level 3 CX		254	254	13-Sep-22	18-Sep-23										18-Sep-23, Startup Level 3 CX	
3462		Energize Utility Circuits		205	205	13-Sep-22	10-Jul-23										10-Jul-23, Energize Utility Circuits	
3463		STUP.D5.1	Utility Power Available (DC5 NUF Power Available)	0	0		13-Sep-22										Utility Power Available (DC5 NUF Power Available)	
3464		STUP.D5.1	Utility Power Available (DC5 SUF Power Available)	0	0		05-Oct-22										Utility Power Available (DC5 SUF Power Available)	
3465		STUP.D5.1	Energize MV A & B	10	10	20-Jun-23	03-Jul-23										Energize MV A & B	
3466		STUP.D5.1	Energize MV C & D	10	10	26-Jun-23	10-Jul-23										Energize MV C & D	
3467		Energize MPOD/BDF		54	54	22-Jun-23	07-Sep-23										07-Sep-23, Energize MPOD/BDF	
3468		STUP.D5.1	MPOE/BDF - Startup HUM	5	5	22-Jun-23	28-Jun-23										MPOE/BDF - Startup HUM	
3469		STUP.D5.1	MPOE/BDF - Startup Transformers	15	15	05-Jul-23	25-Jul-23										MPOE/BDF - Startup Transformers	
3470		STUP.D5.1	MPOE/BDF - Energize UPS Pods	15	15	26-Jul-23	15-Aug-23										MPOE/BDF - Energize UPS/Pods	
3471		STUP.D5.1	MPOE/BDF - Startup MPOE Generators	10	10	26-Jul-23	08-Aug-23										MPOE/BDF - Startup MPOE Generators	
3472		STUP.D5.1	MPOE/BDF - Energize ATS/PDU	15	15	16-Aug-23	05-Sep-23										MPOE/BDF - Energize ATS/PDU	
3473		STUP.D5.1	MPOE/BDF - Startup CRAC Units	15	15	17-Aug-23	07-Sep-23										MPOE/BDF - Startup CRAC Units	
3474		Energize Data Hall A-B		33	33	26-Jul-23	11-Sep-23										11-Sep-23, Energize Data Hall A-B	
3475		STUP.D5.1	DHA/B - Startup Transformers	5	5	26-Jul-23	01-Aug-23										DHA/B - Startup Transformers	
3476		STUP.D5.1	DHA/B - Energize SWGR	5	5	02-Aug-23	08-Aug-23										DHA/B - Energize SWGR	
3477		STUP.D5.1	DHA/B - Startup Generators	20	20	09-Aug-23	06-Sep-23										DHA/B - Startup Generators	
3478		STUP.D5.1	DHA/B - Energize COD/ATS/PDU	10	10	09-Aug-23	22-Aug-23										DHA/B - Energize COD/ATS/PDU	
3479		STUP.D5.1	DHA/B - Startup CRAC Units	20	20	14-Aug-23	11-Sep-23										DHA/B - Startup CRAC Units	
3480		Energize Data Hall C-D		33	33	02-Aug-23	18-Sep-23										18-Sep-23, Energize Data Hall C-D	
3481		STUP.D5.1	DHC/D - Startup Transformers	5	5	02-Aug-23	08-Aug-23										DHC/D - Startup Transformers	
3482		STUP.D5.1	DHC/D - Energize SWGR	5	5	09-Aug-23	15-Aug-23										DHC/D - Energize SWGR	
3483		STUP.D5.1	DHC/D - Startup Generators	20	20	16-Aug-23	13-Sep-23										DHC/D - Startup Generators	
3484		STUP.D5.1	DHC/D - Energize COD/ATS/PDU	10	10	16-Aug-23	29-Aug-23										DHC/D - Energize COD/ATS/PDU	
3485		STUP.D5.1	DHC/D - Startup CRAC Units	20	20	21-Aug-23	18-Sep-23										DHC/D - Startup CRAC Units	
3486		Energize House		28	28	04-Jul-23	10-Aug-23										10-Aug-23, Energize House	
3487		STUP.D5.1	House - Energize Transformer	1	1	04-Jul-23	04-Jul-23										House - Energize Transformer	
3488		STUP.D5.1	House - Energize Switchboard/HDP	5	5	05-Jul-23	11-Jul-23										House - Energize Switchboard/HDP	
3489		STUP.D5.1	House - Energize Rooftop RTU Units	5	5	12-Jul-23	18-Jul-23										House - Energize Rooftop RTU Units	
3490		STUP.D5.1	House - Startup VAVs	20	20	14-Jul-23	10-Aug-23										House - Startup VAVs	
3491		Electrical Level 4 CX		137	137	12-Jul-23	30-Jan-24										30-Jan-24, Elect	
3492		COMS.D5.13	Level 4 Electrical CX - House	10	10	12-Jul-23	25-Jul-23										Level 4 Electrical CX - House	
3493		COMS.D5.12	Level 4 Electrical CX - Network Rooms	10	10	16-Aug-23	29-Aug-23										Level 4 Electrical CX -Network Roon	

█ Remaining Level of Effort █ Remaining Work ◆ Milestone
█ Actual Work █ Critical Remaining Work ▼ Summary

QTS HIL2 DC2, DC3, DC5 Construction Schedule				Classic Schedule Layout					12-Jul-22 15:37								
#	Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	2022				2023				2024		
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2
3494	COMS.D5.12t	Level 4 Electrical CX - Data Halls A & B	20	20	07-Sep-23	04-Oct-23										Level 4 Electrical CX - Data Hall	
3495	COMS.D5.12t	Level 4 Electrical CX - Data Halls C & D	20	20	02-Jan-24	30-Jan-24										Level 4 Electrical CX - Data Hall	
3496	Mechanical Level 4 CX			110	110	08-Sep-23	20-Feb-24									20-Feb-24, M	
3497	COMS.D5.13t	Level 4 Mechanical CX - Network Rooms	17	17	08-Sep-23	02-Oct-23										Level 4 Mechanical CX - Network	
3498	COMS.D5.13t	Level 4 Mechanical CX - House	20	20	03-Oct-23	31-Oct-23										Level 4 Mechanical CX - House	
3499	COMS.D5.13t	Level 4 Mechanical CX - Data Halls A & B	16	16	01-Nov-23	27-Nov-23										Level 4 Mechanical CX - Data Halls A & B	
3500	COMS.D5.13t	Level 4 Mechanical CX - Data Halls C & D	34	34	02-Jan-24	20-Feb-24										Level 4 Mechanical CX - Data Halls C & D	
3501	Integrated Level 5 CX			101	101	03-Oct-23	01-Mar-24									01-Mar-24, I	
3502	COMS.D5.13t	Level 5 CX - Network	5	5	03-Oct-23	10-Oct-23										Level 5 CX - Network	
3503	COMS.D5.13t	Level 5 CX - House	5	5	01-Nov-23	07-Nov-23										Level 5 CX - House	
3504	COMS.D5.13t	Level 5 CX - Data Halls A & B	5	5	26-Dec-23	01-Jan-24										Level 5 CX - Data Halls A & B	
3505	COMS.D5.13t	Level 5 CX - Data halls C & D	5	5	26-Feb-24	01-Mar-24										Level 5 CX - Data halls C & D	
3506	Weather Days			64	64	28-Nov-23	23-Feb-24									23-Feb-24, W	
3507	WEATHER.D5t	Weather Days DC5 DH A & B (40-0=40)	19	19	28-Nov-23	22-Dec-23										Weather Days DC5 DH A & B (40-0=40)	
3508	WEATHER.D5t	Weather Days DC5 DH C&D (41-0=41)	3	3	21-Feb-24	23-Feb-24										Weather Days DC5 DH C&D (41-0=41)	
3509	Deleted activities			48	48	07-Jul-22	13-Sep-22									13-Sep-22, Deleted activities	
