




QTS HIL2 DC2, DC3, DC5 Construction Schedule				Classic Schedule Layout					12-Jul-22 15:36								
#	Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	2022					2023				2024	
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2
336		PROC.PW. OFCI Procure - RTUs House	0	0		14-Sep-22					◆ OFCI Procure - RTUs House						
337		PROC.PW. OFCI Procure - Transformer House (XFMR-H)	0	0		09-Jan-23					◆ OFCI Procure - Transformer House (XFMR-H)						
338		PROC.PW. OFCI Procure - HDP Boards House	0	0		07-Feb-23					◆ OFCI Procure - HDP Boards House						
339		PROC.PW. OFCI Procure - Medium Voltage - Service Entry Switch Gear	0	0		10-Feb-23					◆ OFCI Procure - Medium Voltage - Service Entry Switch Gear						
340		PROC.PW. OFCI Procure - Medium Voltage - Vista Switch	0	0		10-Feb-23					◆ OFCI Procure - Medium Voltage - Vista Switch						
341		MPOE/BDF		71	71	24-Oct-22 A	07-Feb-23										
342		PROC.PW. OFCI Procure - ACCU MPOE/BDF	0	0		24-Oct-22					◆ OFCI Procure - ACCU MPOE/BDF						
343		PROC.PW. OFCI Procure - UPS Pods MPOE/BDF	0	0	23-Dec-22 A						◆ OFCI Procure - UPS Pods MPOE/BDF						
344		PROC.PW. OFCI Procure - Transformers MPOE/BDF	0	0		23-Dec-22					◆ OFCI Procure - Transformers MPOE/BDF						
345		PROC.PW. OFCI Procure - Generators MPOE/BDF	0	0		30-Dec-22					◆ OFCI Procure - Generators MPOE/BDF						
346		PROC.PW. OFCI Procure - Network COD 2000AMP	0	0		09-Jan-23					◆ OFCI Procure - Network COD 2000AMP						
347		PROC.PW. OFCI Procure - COD boards MPOE/BDF	0	0		13-Jan-23					◆ OFCI Procure - COD boards MPOE/BDF						
348		PROC.PW. OFCI Procure - CRAC Units MPOE/BDF	0	0		03-Feb-23					◆ OFCI Procure - CRAC Units MPOE/BDF						
349		PROC.PW. OFCI Procure - HDP Boards MPOE/BDF	0	0		07-Feb-23					◆ OFCI Procure - HDP Boards MPOE/BDF						
350		DH A and B		82	82	29-Sep-22	31-Jan-23										
351		PROC.PW. OFCI Procure - ACCU DH A	0	0		29-Sep-22					◆ OFCI Procure - ACCU DH A						
352		PROC.PW. OFCI Procure - ACCU DH B	0	0		29-Sep-22					◆ OFCI Procure - ACCU DH B						
353		PROC.PW. OFCI Procure - Transformers DH A and B	0	0		09-Jan-23					◆ OFCI Procure - Transformers DH A and B						
354		PROC.PW. OFCI Procure - COD boards DH A	0	0		13-Jan-23					◆ OFCI Procure - COD boards DH A						
355		PROC.PW. OFCI Procure - COD boards DH B	0	0		13-Jan-23					◆ OFCI Procure - COD boards DH B						
356		PROC.PW. OFCI Procure - Generators DH A and B	0	0		17-Jan-23					◆ OFCI Procure - Generators DH A and B						
357		PROC.PW. OFCI Procure - CRAC Units DH A	0	0		23-Jan-23					◆ OFCI Procure - CRAC Units DH A						
358		PROC.PW. OFCI Procure - HDP Boards DH A & B	0	0		25-Jan-23					◆ OFCI Procure - HDP Boards DH A & B						
359		PROC.PW. OFCI Procure - CRAC Units DH B	0	0		31-Jan-23					◆ OFCI Procure - CRAC Units DH B						
360		DH C and D		71	71	07-Nov-22	22-Feb-23										
361		PROC.PW. OFCI Procure - ACCU DH C	0	0		07-Nov-22					◆ OFCI Procure - ACCU DH C						
362		PROC.PW. OFCI Procure - ACCU DH D	0	0		07-Nov-22					◆ OFCI Procure - ACCU DH D						
363		PROC.PW. OFCI Procure - Transformers DH C and D	0	0		30-Jan-23					◆ OFCI Procure - Transformers DH C and D						
364		PROC.PW. OFCI Procure - Generators DH C and D	0	0		07-Feb-23					◆ OFCI Procure - Generators DH C and D						
365		PROC.PW. OFCI Procure - COD boards DH D	0	0		07-Feb-23					◆ OFCI Procure - COD boards DH D						
366		PROC.PW. OFCI Procure - HDP Boards DH C & D	0	0		09-Feb-23					◆ OFCI Procure - HDP Boards DH C & D						
367		PROC.PW. OFCI Procure - CRAC Units DH D	0	0		17-Feb-23					◆ OFCI Procure - CRAC Units DH D						
368		PROC.PW. OFCI Procure - CRAC Units DH C	0	0		22-Feb-23					◆ OFCI Procure - CRAC Units DH C						
369		PROC.PW. OFCI Procure - COD boards DH C	0	0		22-Feb-23					◆ OFCI Procure - COD boards DH C						
370		DC3		41	41	02-Feb-23	03-Apr-23										
371		House		28	28	16-Feb-23	29-Mar-23										
372		PROC.PW. OFCI Procure - Transformer House (XFMR-H)	0	0		16-Feb-23					◆ OFCI Procure - Transformer House (XFMR-H)						
373		PROC.PW. OFCI Procure - HDP Boards House	0	0		20-Mar-23					◆ OFCI Procure - HDP Boards House						
374		PROC.PW. OFCI Procure - Medium Voltage - Service Entry Switch Gear	0	0		23-Mar-23					◆ OFCI Procure - Medium Voltage - Service Entry Switch Gear						
375		PROC.PW. OFCI Procure - Medium Voltage - Vista Switch	0	0		23-Mar-23					◆ OFCI Procure - Medium Voltage - Vista Switch						
376		PROC.PW. OFCI Procure - RTUs House	0	0		29-Mar-23					◆ OFCI Procure - RTUs House						
377		MPOE/BDF		38	38	02-Feb-23	29-Mar-23										
378		PROC.PW. OFCI Procure - UPS Pods MPOE/BDF	0	0		02-Feb-23					◆ OFCI Procure - UPS Pods MPOE/BDF						
379		PROC.PW. OFCI Procure - Transformers MPOE/BDF	0	0		03-Feb-23					◆ OFCI Procure - Transformers MPOE/BDF						
380		PROC.PW. OFCI Procure - Generators MPOE/BDF	0	0		09-Feb-23					◆ OFCI Procure - Generators MPOE/BDF						
381		PROC.PW. OFCI Procure - Network COD 2000AMP	5	5	15-Feb-23	22-Feb-23					◆ OFCI Procure - Network COD 2000AMP						
382		PROC.PW. OFCI Procure - HDP Boards MPOE/BDF	0	0		20-Mar-23					◆ OFCI Procure - HDP Boards MPOE/BDF						
383		PROC.PW. OFCI Procure - COD boards MPOE/BDF	0	0		29-Mar-23					◆ OFCI Procure - COD boards MPOE/BDF						

Remaining Level of Effort Remaining Work ◆ Milestone
 Actual Work Critical Remaining Work Summary

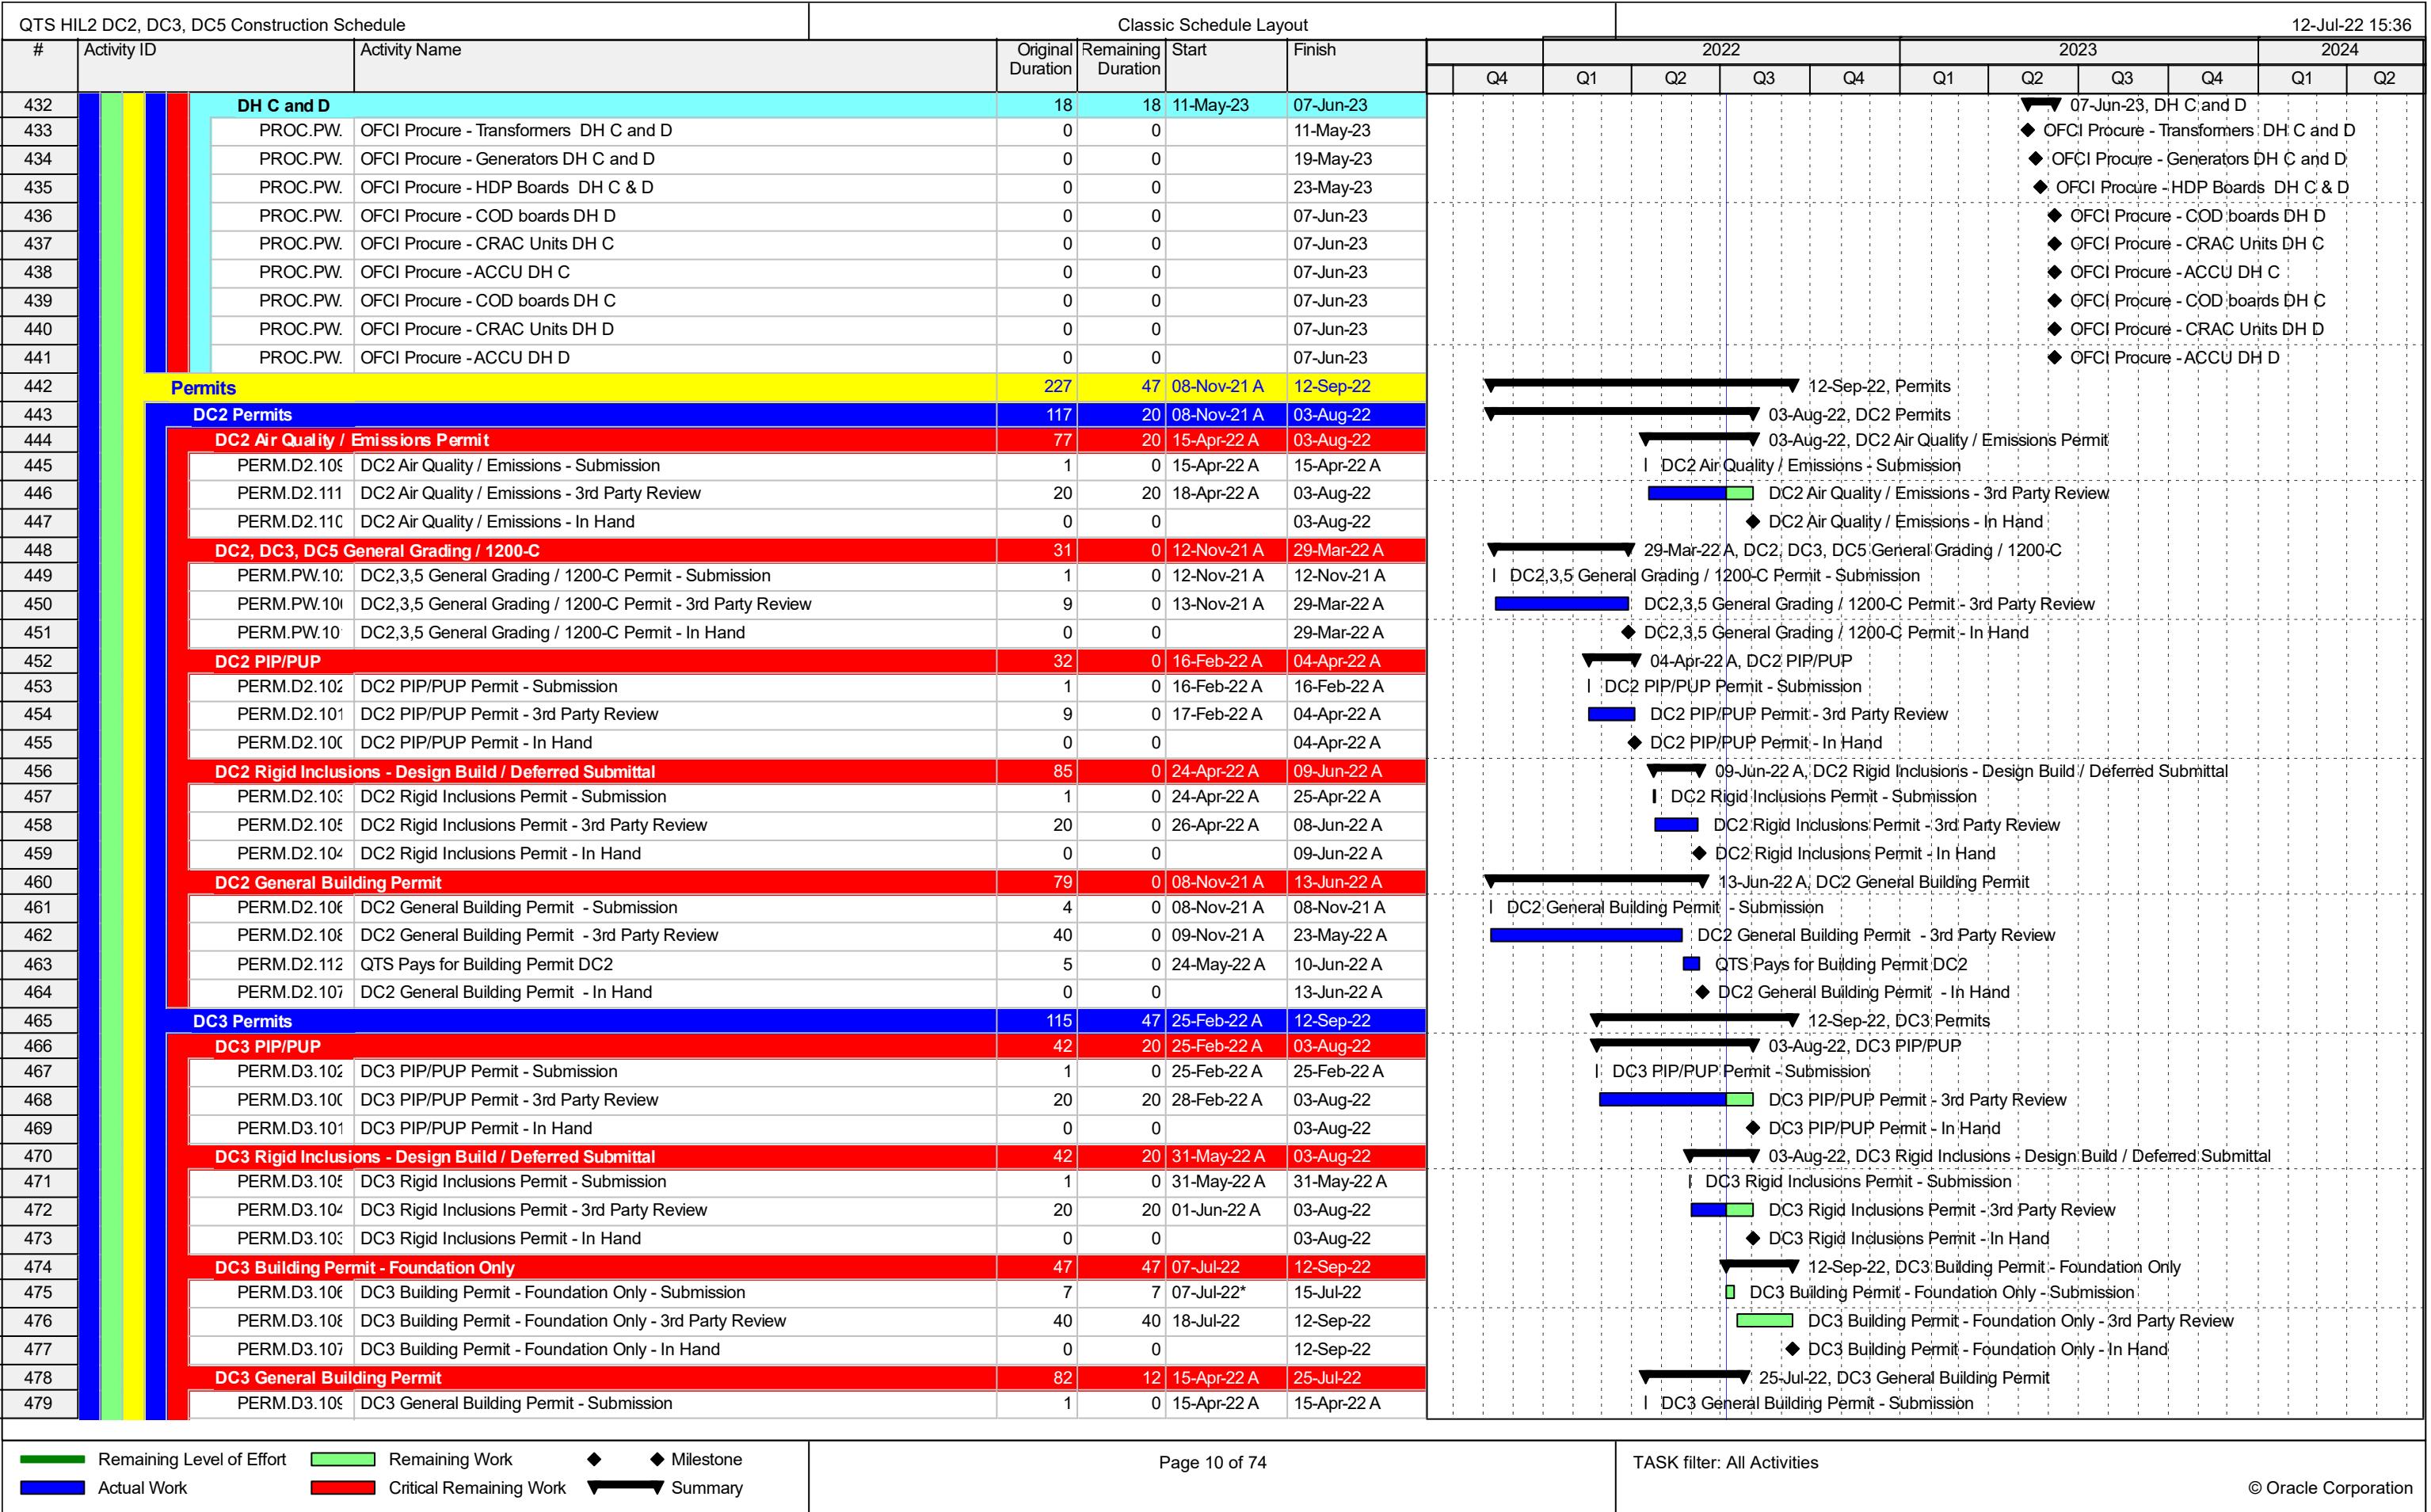

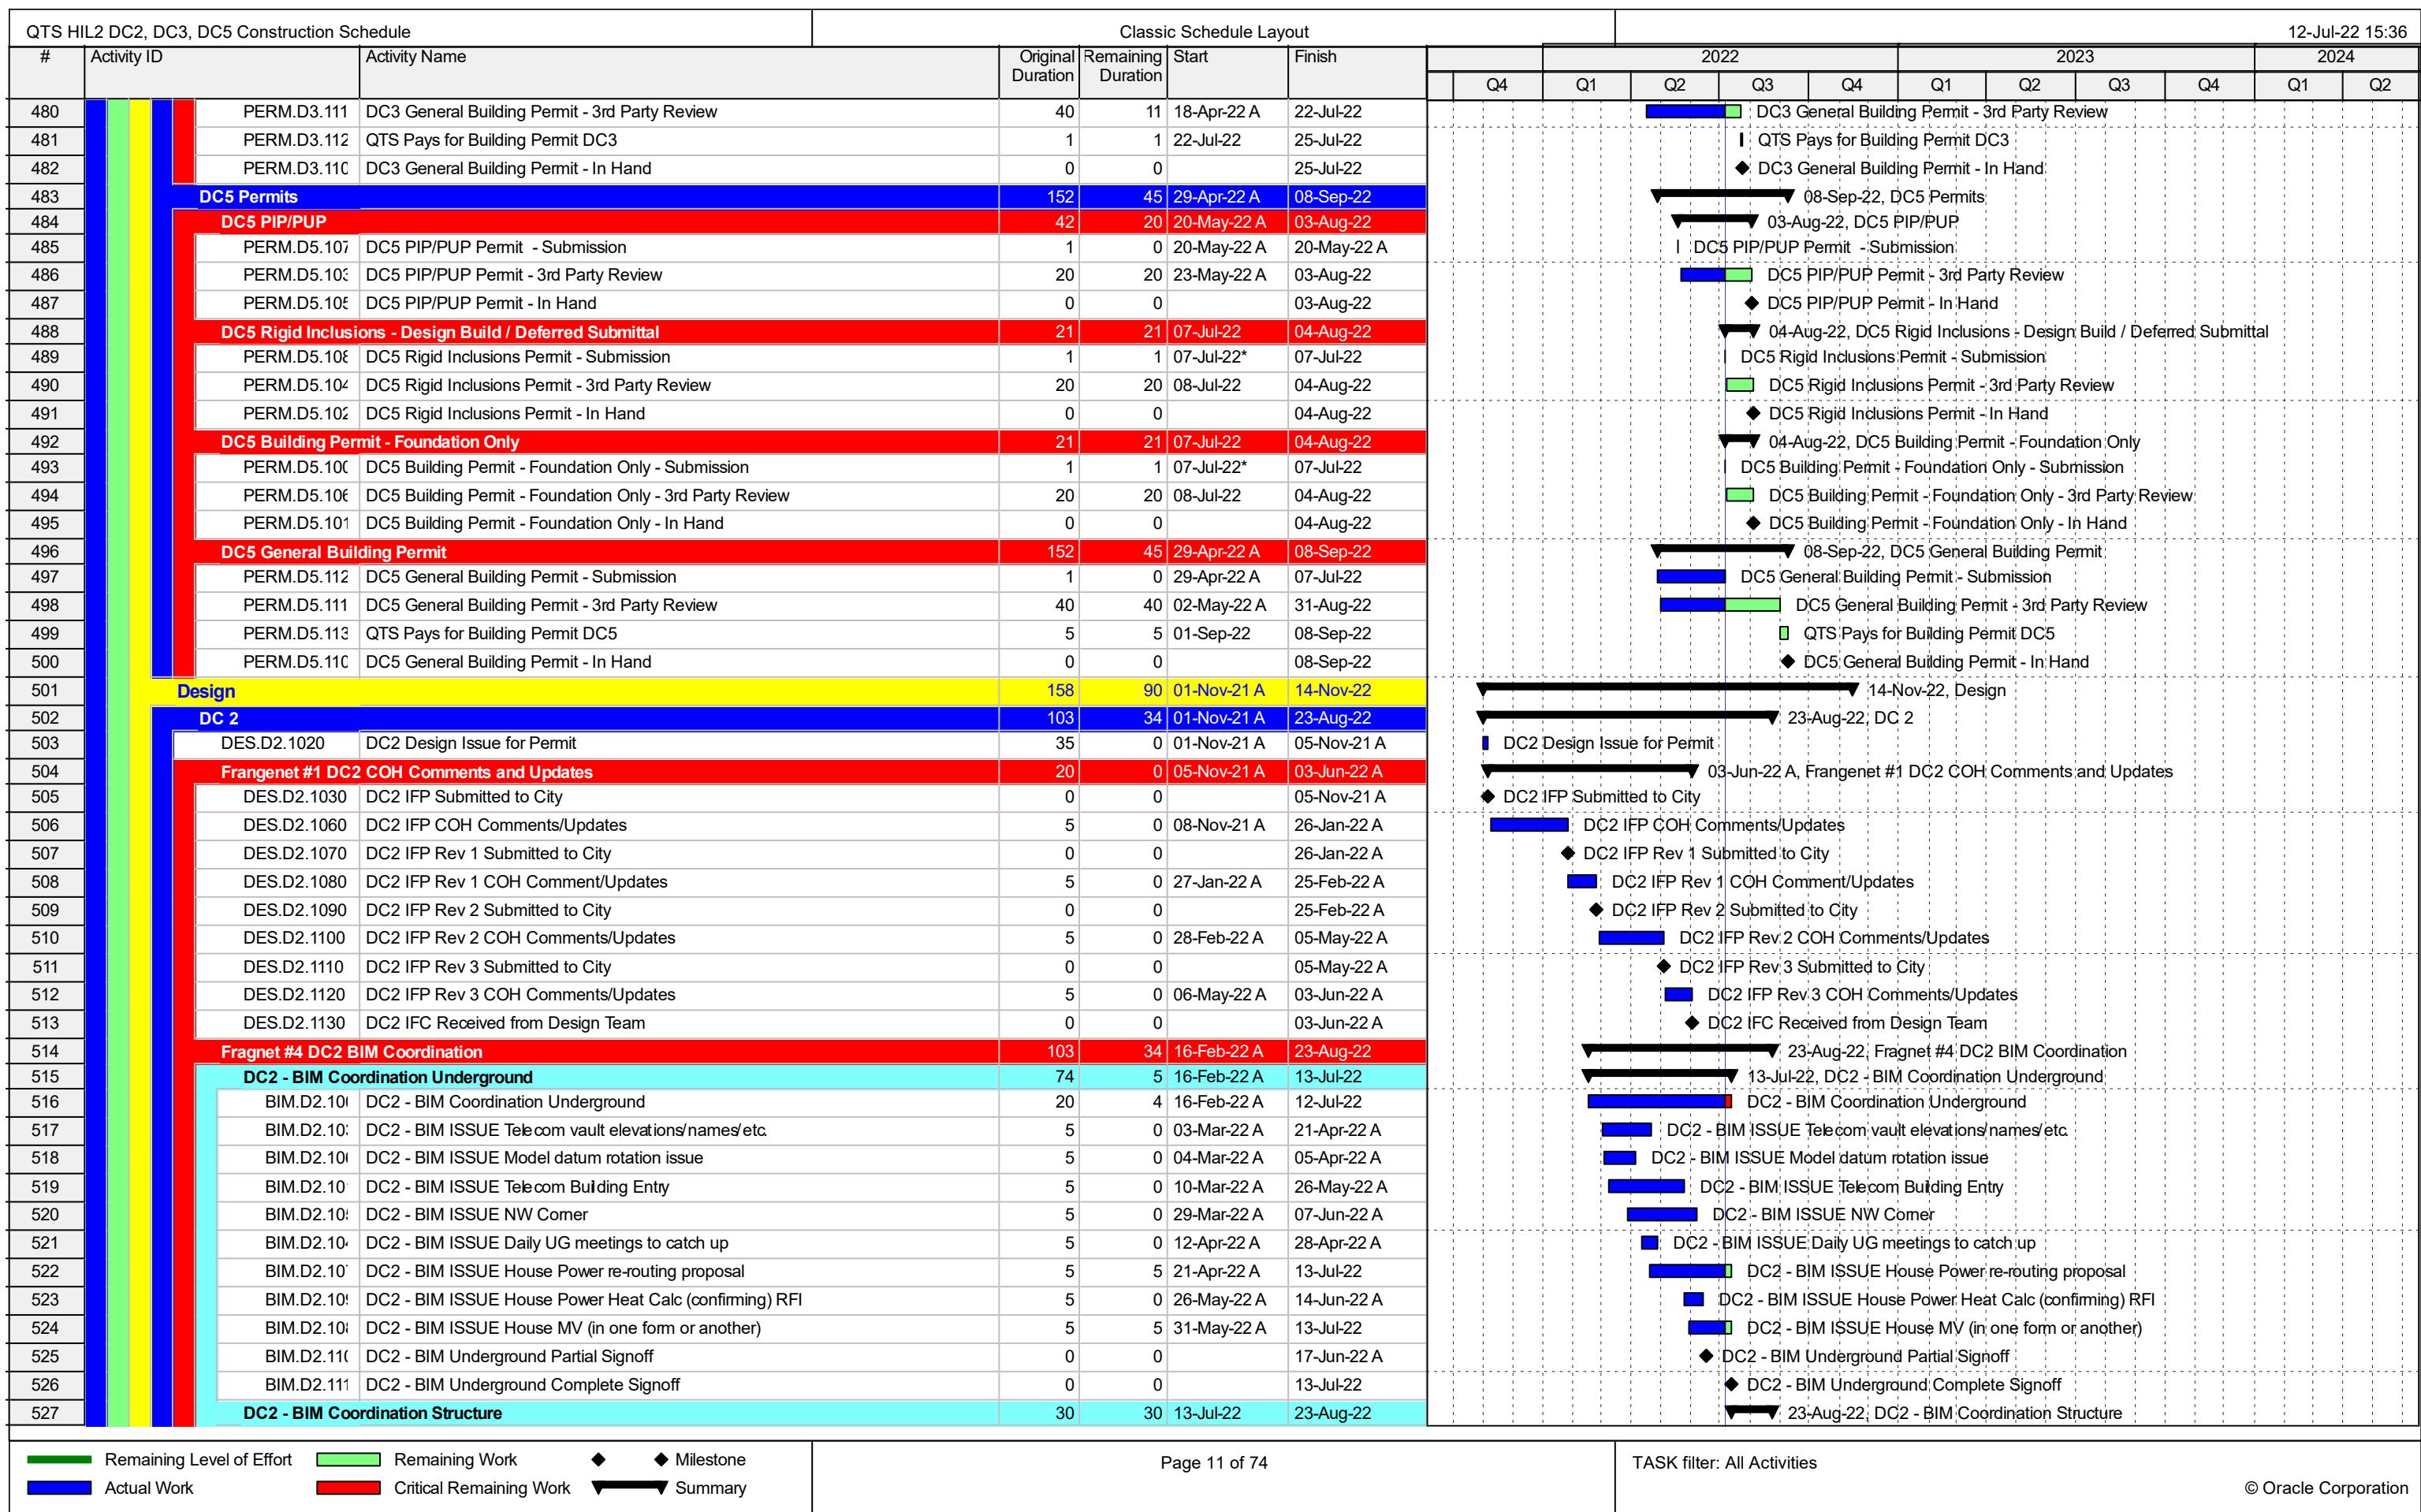

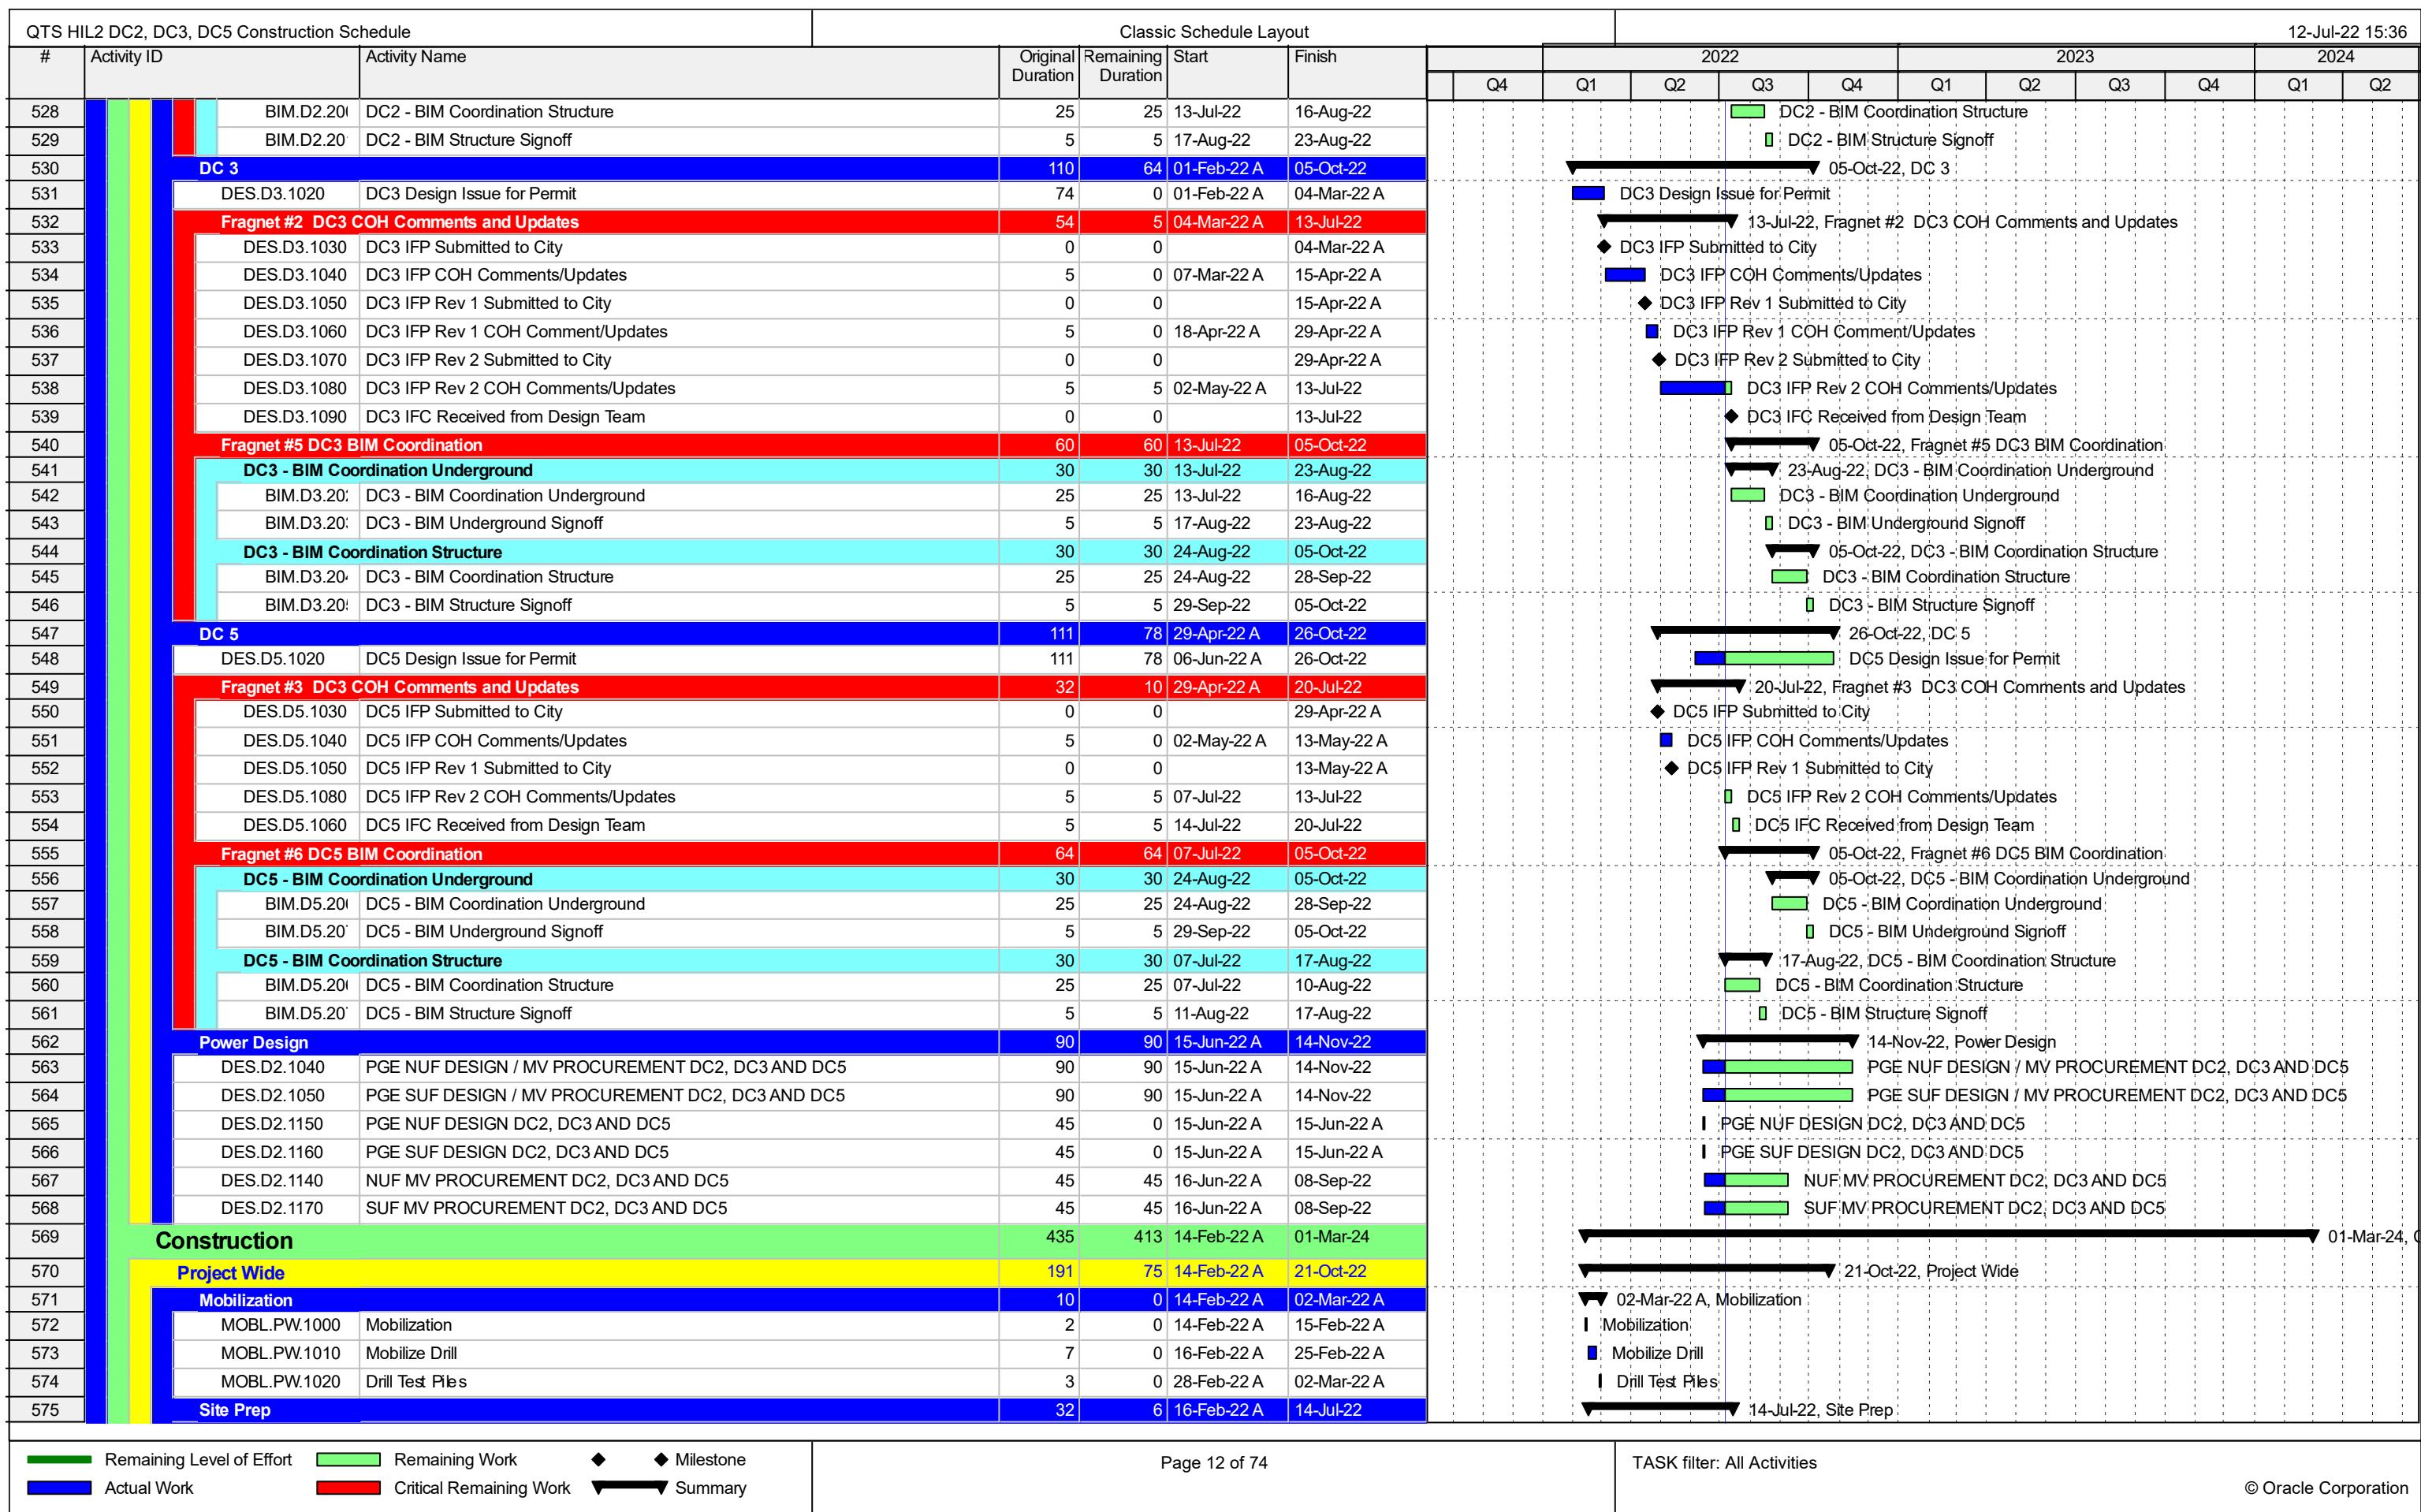

QTS HIL2 DC2, DC3, DC5 Construction Schedule				Classic Schedule Layout					12-Jul-22 15:36										
#	Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish		2022					2023					2024	
					Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2				
576	PREP.PW.1030	Install Tree Protection Fence	1	0	16-Feb-22 A	16-Feb-22 A													
577	PREP.PW.1160	Cut Trees		3	0	21-Feb-22 A	04-Mar-22 A												
578	PREP.PW.1070	Install Construction Entrances		3	0	31-Mar-22 A	02-Apr-22 A												
579	PREP.PW.1080	Install Haul Roads		10	0	31-Mar-22 A	22-Apr-22 A												
580	PREP.PW.1130	Strip and Rock Tailor Park		5	0	31-Mar-22 A	09-Apr-22 A												
581	PREP.PW.1110	Strip Organics to Stockpile		17	3	01-Apr-22 A	11-Jul-22												
582	PREP.PW.1060	Install Security fence		5	0	04-Apr-22 A	07-Apr-22 A												
583	PREP.PW.1100	Tree Removal / Site Clearing		20	0	08-Apr-22 A	28-May-22 A												
584	PREP.PW.1170	Foundation Start		0	0	31-May-22 A													
585	PREP.PW.1120	Install Conduits for Temp Power		5	1	22-Jun-22 A	07-Jul-22												
586	PREP.PW.1140	Strip and Rock Trade Parking		6	6	07-Jul-22	14-Jul-22												
587	PREP.PW.1150	Install walk/Cart Paths		4	4	07-Jul-22	12-Jul-22												
588	Erosion Control			5	0	30-Mar-22 A	01-Apr-22 A												
589	PREP.PW.1040	Install Inlet Protection		1	0	30-Mar-22 A	30-Mar-22 A												
590	PREP.PW.1050	Install Silt Fence		5	0	30-Mar-22 A	01-Apr-22 A												
591	Site Improvements			169	75	21-Apr-22 A	21-Oct-22												
592	Dry Utilities			152	75	14-Jun-22 A	21-Oct-22												
593	Telecommunications			118	38	20-Jun-22 A	02-Sep-22												
594	Excavation			114	36	20-Jun-22 A	31-Aug-22												
595	EXCV.P	Telecom Excavation - TMH-6 TO THM-35		4	0	20-Jun-22 A	21-Jun-22 A												
596	EXCV.P	Telecom Excavation - TMH-7 TO TMH-34		4	0	21-Jun-22 A	22-Jun-22 A												
597	EXCV.P	Telecom Excavation - BUILDING TO BEV-05		4	0	01-Jul-22 A	06-Jul-22 A												
598	EXCV.P	Telecom Excavation - BEV-08 TO BUILDING		4	1	05-Jul-22 A	01-Aug-22												
599	EXCV.P	Telecom Excavation - BUILDING TO BEV-06		4	3	07-Jul-22 A	25-Jul-22												
600	EXCV.P	Telecom Excavation - TMH-7, TMH-34		2	2	13-Jul-22	14-Jul-22												
601	EXCV.P	Telecom Excavation - TMH-34 TO TMH-35		2	2	13-Jul-22	14-Jul-22												
602	EXCV.P	Telecom Excavation - BEV-07,BEV-09		3	3	13-Jul-22	15-Jul-22												
603	EXCV.P	Telecom Excavation - BEV-09 TO BEV-10		3	3	13-Jul-22	15-Jul-22												
604	EXCV.P	Telecom Excavation - BEV-08 TO TMH-14		3	3	13-Jul-22	15-Jul-22												
605	EXCV.P	Telecom Excavation - TMH-17,TMH-14,TMH-15,TMH-16		3	3	13-Jul-22	15-Jul-22												
606	EXCV.P	Telecom Excavation - BEV-10, BEV-08		3	3	14-Jul-22	18-Jul-22												
607	EXCV.P	Telecom Excavation - TMH-32 TO TMH-33		2	2	15-Jul-22	18-Jul-22												
608	EXCV.P	Telecom Excavation - TMH-15 TO MMV-03 existing		3	3	18-Jul-22	20-Jul-22												
609	EXCV.P	Telecom Excavation - TMH-33, TMH-34		2	2	19-Jul-22	20-Jul-22												
610	EXCV.P	Telecom Excavation - TMH-14 TO TMH-08 existing		2	2	21-Jul-22	22-Jul-22												
611	EXCV.P	Telecom Excavation - TMH-15 TO TMH-16		2	2	25-Jul-22	26-Jul-22												
612	EXCV.P	Telecom Excavation - BEV-07 TO BUILDING		4	4	26-Jul-22	29-Jul-22												
613	EXCV.P	Telecom Excavation - TMH-17 TO TMH-16		2	2	27-Jul-22	28-Jul-22												
614	EXCV.P	Telecom Excavation - TMH-14 TO TMH-15		2	2	29-Jul-22	01-Aug-22												
615	EXCV.P	Telecom Excavation - BEV-09 TO TMH-33		3	3	02-Aug-22	04-Aug-22												
616	EXCV.P	Telecom Excavation - TMH-17 TO TMH-14		2	2	02-Aug-22	03-Aug-22												
617	EXCV.P	Telecom Excavation - BEV-07 TO TMH-34		3	3	05-Aug-22	09-Aug-22												
618	EXCV.P	Telecom Excavation - BEV-10 TO TMH-17		3	3	10-Aug-22	12-Aug-22												
619	EXCV.P	Telecom Excavation - BEV-112 TO BUILDING		2	2	15-Aug-22	16-Aug-22												
620	EXCV.P	Telecom Excavation - BEV-112		2	2	16-Aug-22	17-Aug-22												
621	EXCV.P	Telecom Excavation - BEV-112 TO Future		2	2	18-Aug-22	19-Aug-22												
622	EXCV.P	Telecom Excavation - BEV-112 TO TMH-120		2	2	19-Aug-22	22-Aug-22												

Remaining Level of Effort Remaining Work Milestone
 Actual Work Critical Remaining Work Summary

QTS HIL2 DC2, DC3, DC5 Construction Schedule				Classic Schedule Layout					12-Jul-22 15:36									
#	Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish			2022				2023				2024	
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	
623		EXCV.P Telecom Excavation - TMH-16 TO Future	1	1	24-Aug-22	24-Aug-22						I Telecom Excavation - TMH-16 TO Future						
624		EXCV.P Telecom Excavation - TMH-17 TO Future	1	1	25-Aug-22	25-Aug-22						I Telecom Excavation - TMH-17 TO Future						
625		EXCV.P Telecom Excavation - TMH-32 TO Future	1	1	25-Aug-22	25-Aug-22						I Telecom Excavation - TMH-32 TO Future						
626		EXCV.P Telecom Excavation - TMH-33 TO Future	1	1	25-Aug-22	25-Aug-22						I Telecom Excavation - TMH-33 TO Future						
627		EXCV.P Telecom Excavation - TMH-120 TO TMH-116 existing	2	2	26-Aug-22	29-Aug-22						I Telecom Excavation - TMH-120 TO TMH-116 existing						
628		EXCV.P Telecom Excavation - TMH-120 TO Future	2	2	30-Aug-22	31-Aug-22						I Telecom Excavation - TMH-120 TO Future						
629		Ductbank Install	118	38	21-Jun-22 A	02-Sep-22												
630	DUCT.P	Telecom Ductbank - TMH-6 TO THM-35	3	1	21-Jun-22 A	14-Jul-22						I Telecom Ductbank -TMH-6 TO THM-35						
631	DUCT.P	Telecom Ductbank - Vault Install TMH-35, TMH-32	1	0	21-Jun-22 A	23-Jun-22 A						I Telecom Ductbank- Vault Install TMH-35, TMH-32						
632	DUCT.P	Telecom Ductbank - Vault Install TMH-33, TMH-34	1	0	21-Jun-22 A	23-Jun-22 A						I Telecom Ductbank- Vault Install TMH-33, TMH-34						
633	DUCT.P	Telecom Ductbank - BUILDING TO BEV-05	5	3	06-Jul-22 A	25-Jul-22						I Telecom Ductbank- BUILDING TO BEV-05						
634	DUCT.P	Telecom Ductbank - BEV-08 TO BUILDING	5	5	07-Jul-22 A	08-Aug-22						I Telecom Ductbank - BEV-08 TO BUILDING						
635	DUCT.P	Telecom Ductbank - TMH-7 TO TMH-34	3	3	13-Jul-22	15-Jul-22						I Telecom Ductbank - TMH-7 TO TMH-34						
636	DUCT.P	Telecom Ductbank - THM-35 TO TMH-32	1	1	15-Jul-22	15-Jul-22						I Telecom Ductbank - THM-35 TO TMH-32						
637	DUCT.P	Telecom Ductbank - Vault Install BEV-07,BEV-09	1	1	18-Jul-22	18-Jul-22						I Telecom Ductbank - Vault Install BEV-07,BEV-09						
638	DUCT.P	Telecom Ductbank - BEV-09 TO BEV-10	5	5	18-Jul-22	22-Jul-22						I Telecom Ductbank - BEV-09 TO BEV-10						
639	DUCT.P	Telecom Ductbank - BEV-08 TO TMH-14	4	4	18-Jul-22	21-Jul-22						I Telecom Ductbank - BEV-08 TO TMH-14						
640	DUCT.P	Telecom Ductbank - TMH-17,TMH-14,TMH-15,TMH-16	1	1	18-Jul-22	18-Jul-22						I Telecom Ductbank - TMH-17,TMH-14,TMH-15,TMH-16						
641	DUCT.P	Telecom Ductbank - TMH-32 TO Future	1	1	18-Jul-22	18-Jul-22						I Telecom Ductbank - TMH-32 TO Future						
642	DUCT.P	Telecom Ductbank - TMH-33 TO Future	1	1	18-Jul-22	18-Jul-22						I Telecom Ductbank - TMH-33 TO Future						
643	DUCT.P	Telecom Ductbank - Vault Install BEV-10, BEV-08	1	1	19-Jul-22	19-Jul-22						I Telecom Ductbank - Vault Install BEV-10, BEV-08						
644	DUCT.P	Telecom Ductbank - TMH-34 TO TMH-33	1	1	21-Jul-22	21-Jul-22						I Telecom Ductbank - TMH-34 TO TMH-33						
645	DUCT.P	Telecom Ductbank - TMH-32 TO TMH-33	1	1	21-Jul-22	21-Jul-22						I Telecom Ductbank - TMH-32 TO TMH-33						
646	DUCT.P	Telecom Ductbank - TMH-34 TO TMH-35	1	1	21-Jul-22	21-Jul-22						I Telecom Ductbank - TMH-34 TO TMH-35						
647	DUCT.P	Telecom Ductbank - TMH-15 TO MMV-03 existing	3	3	21-Jul-22	25-Jul-22						I Telecom Ductbank - TMH-15 TO MMV-03 existing						
648	DUCT.P	Telecom Ductbank - TMH-14 TO TMH-08 existing	3	3	25-Jul-22	27-Jul-22						I Telecom Ductbank - TMH-14 TO TMH-08 existing						
649	DUCT.P	Telecom Ductbank - BUILDING TO BEV-06	5	5	26-Jul-22	01-Aug-22						I Telecom Ductbank - BUILDING TO BEV-06						
650	DUCT.P	Telecom Ductbank - TMH-15 TO TMH-16	2	2	27-Jul-22	28-Jul-22						I Telecom Ductbank - TMH-15 TO TMH-16						
651	DUCT.P	Telecom Ductbank - TMH-17 TO TMH-16	1	1	29-Jul-22	29-Jul-22						I Telecom Ductbank - TMH-17 TO TMH-16						
652	DUCT.P	Telecom Ductbank - BEV-07 TO BUILDING	5	5	01-Aug-22	05-Aug-22						I Telecom Ductbank - BEV-07 TO BUILDING						
653	DUCT.P	Telecom Ductbank - BEV-07 TO BEV-08	2	2	02-Aug-22	03-Aug-22						I Telecom Ductbank - BEV-07 TO BEV-08						
654	DUCT.P	Telecom Ductbank - TMH-14 TO TMH-15	1	1	02-Aug-22	02-Aug-22						I Telecom Ductbank - TMH-14 TO TMH-15						
655	DUCT.P	Telecom Ductbank - TMH-17 TO TMH-14	2	2	04-Aug-22	05-Aug-22						I Telecom Ductbank - TMH-17 TO TMH-14						
656	DUCT.P	Telecom Ductbank - BEV-09 TO TMH-33	3	3	05-Aug-22	09-Aug-22						I Telecom Ductbank - BEV-09 TO TMH-33						
657	DUCT.P	Telecom Ductbank - BEV-07 TO TMH-34	3	3	10-Aug-22	12-Aug-22						I Telecom Ductbank - BEV-07 TO TMH-34						
658	DUCT.P	Telecom Ductbank - BEV-10 TO TMH-17	4	4	15-Aug-22	18-Aug-22						I Telecom Ductbank - BEV-10 TO TMH-17						
659	DUCT.P	Telecom Ductbank - BEV-112 TO BUILDING	1	1	17-Aug-22	17-Aug-22						I Telecom Ductbank - BEV-112 TO BUILDING						
660	DUCT.P	Telecom Ductbank - Vault Install BEV-112	1	1	18-Aug-22	18-Aug-22						I Telecom Ductbank - Vault Install BEV-112						
661	DUCT.P	Telecom Ductbank - BEV-112 TO Future	1	1	22-Aug-22	22-Aug-22						I Telecom Ductbank - BEV-112 TO Future						
662	DUCT.P	Telecom Ductbank - BEV-112 TO TMH-120	2	2	23-Aug-22	24-Aug-22						I Telecom Ductbank - BEV-112 TO TMH-120						
663	DUCT.P	Telecom Ductbank - TMH-16 TO Future	1	1	25-Aug-22	25-Aug-22						I Telecom Ductbank - TMH-16 TO Future						
664	DUCT.P	Telecom Ductbank - TMH-32 To Future	1	1	26-Aug-22	26-Aug-22						I Telecom Ductbank - TMH-32 To Future						
665	DUCT.P	Telecom Ductbank - TMH-33 To Future	1	1	26-Aug-22	26-Aug-22						I Telecom Ductbank - TMH-33 To Future						
666	DUCT.P	Telecom Ductbank - TMH-17 TO Future	1	1	26-Aug-22	26-Aug-22						I Telecom Ductbank - TMH-17 TO Future						
667	DUCT.P	Telecom Ductbank - TMH-120 TO TMH-116 existing	2	2	30-Aug-22	31-Aug-22						I Telecom Ductbank - TMH-120 TO TMH-116 existing						
668	DUCT.P	Telecom Ductbank - TMH-120 TO Future	2	2	01-Sep-22	02-Sep-22						I Telecom Ductbank - TMH-120 TO Future						
669	PGE Utility Feeders			152	75	14-Jun-22 A	21-Oct-22											

QTS HIL2 DC2, DC3, DC5 Construction Schedule				Classic Schedule Layout					Timeline & Resource Allocation								
#	Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	2022				2023				2024		
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2
670	PGE MV SUF Underground Installation	PGE MV SUF - VT-52 TO VT-53	19	19	09-Sep-22	05-Oct-22										05-Oct-22, PGE MV SUF Underground Installation	
671		SUF.PW	4	4	09-Sep-22	14-Sep-22										PGE MV SUF - VT-52 TO VT-53	
672		SUF.PW	PGE MV SUF - VT-53	1	1	15-Sep-22	15-Sep-22									PGE MV SUF - VT-53	
673		SUF.PW	PGE MV SUF - VT-53 TO VT-54	4	4	16-Sep-22	21-Sep-22									PGE MV SUF - VT-53 TO VT-54	
674		SUF.PW	PGE MV SUF - VT-54	1	1	22-Sep-22	22-Sep-22									PGE MV SUF - VT-54	
675		SUF.PW	PGE MV SUF - VT-54 TO VT-55	4	4	23-Sep-22	28-Sep-22									PGE MV SUF - VT-54 TO VT-55	
676		SUF.PW	PGE MV SUF - VT-55	2	2	29-Sep-22	30-Sep-22									PGE MV SUF - VT-55	
677		SUF.PW	PGE MV SUF - VT-56	2	2	03-Oct-22	04-Oct-22									PGE MV SUF - VT-56	
678		SUF.PW	PGE MV SUF - Conduit Bore under Starr Blvd	1	1	05-Oct-22	05-Oct-22									PGE MV SUF - Conduit Bore under Starr Blvd	
679		PGE MV NUF Underground Installation		107	75	14-Jun-22 A	21-Oct-22									21-Oct-22, PGE MV NUF Underground Installation	
680	PGE MV NUF Underground Installation	NUF.PW	PGE MV NUF - Conduit Bore under Starr Blvd	1	0	14-Jun-22 A	07-Jul-22									PGE MV NUF - Conduit Bore under Starr Blvd	
681		NUF.PW	PGE MV NUF - VT-63 TO VT-64	3	3	09-Sep-22	13-Sep-22									PGE MV NUF - VT-63 TO VT-64	
682		NUF.PW	PGE MV NUF - VT-64	2	2	14-Sep-22	15-Sep-22									PGE MV NUF - VT-64	
683		NUF.PW	PGE MV NUF - VT-64 TO VT-65	4	4	16-Sep-22	21-Sep-22									PGE MV NUF - VT-64 TO VT-65	
684		NUF.PW	PGE MV NUF - VT-65	2	2	22-Sep-22	23-Sep-22									PGE MV NUF - VT-65	
685		NUF.PW	PGE MV NUF - VT-65 TO VT-66	4	4	26-Sep-22	29-Sep-22									PGE MV NUF - VT-65 TO VT-66	
686		NUF.PW	PGE MV NUF - VT-66	2	2	30-Sep-22	03-Oct-22									PGE MV NUF - VT-66	
687		NUF.PW	PGE MV NUF - VT-66 TO VT-67	4	4	04-Oct-22	07-Oct-22									PGE MV NUF - VT-66 TO VT-67	
688		NUF.PW	PGE MV NUF - VT-67	2	2	11-Oct-22	12-Oct-22									PGE MV NUF - VT-67	
689		NUF.PW	PGE MV NUF - VT-67 TO VT-68	3	3	13-Oct-22	17-Oct-22									PGE MV NUF - VT-67 TO VT-68	
690	PGE MV NUF Underground Installation	NUF.PW	PGE MV NUF - VT-68	2	2	18-Oct-22	19-Oct-22									PGE MV NUF - VT-68	
691		NUF.PW	PGE MV NUF - VT-81	2	2	20-Oct-22	21-Oct-22									PGE MV NUF - VT-81	
692		PGE MV DC2 NUF		6	6	06-Sep-22	13-Sep-22									13-Sep-22, PGE MV DC2 NUF	
693		NUF.PW	PGE MV DC2 NUF - Pull Feeders	5	5	06-Sep-22	12-Sep-22									PGE MV DC2 NUF - Pull Feeders	
694		NUF.PW	PGE MV DC2 NUF - Terminate	1	1	13-Sep-22	13-Sep-22									PGE MV DC2 NUF - Terminate	
695		PGE MV DC2 SUF		6	6	06-Sep-22	13-Sep-22									13-Sep-22, PGE MV DC2 SUF	
696		NUF.PW	PGE MV DC2 SUF - Pull Feeders	5	5	06-Sep-22	12-Sep-22									PGE MV DC2 SUF - Pull Feeders	
697		NUF.PW	PGE MV DC2 SUF - Terminate	1	1	13-Sep-22	13-Sep-22									PGE MV DC2 SUF - Terminate	
698		PGE MV DC3 NUF		43	43	07-Jul-22	06-Sep-22									06-Sep-22, PGE MV DC3 NUF	
699		NUF.PW	PGE MV DC3 NUF - Pull Feeders	5	5	07-Jul-22	14-Jul-22									PGE MV DC3 NUF - Pull Feeders	
700		NUF.PW	PGE MV DC3 NUF - Terminate	1	1	06-Sep-22	06-Sep-22									PGE MV DC3 NUF - Terminate	
701	PGE MV DC3 NUF	PGE MV DC3 SUF		6	6	06-Sep-22	13-Sep-22									13-Sep-22, PGE MV DC3 SUF	
702		NUF.PW	PGE MV DC3 SUF - Pull Feeders	5	5	06-Sep-22	12-Sep-22									PGE MV DC3 SUF - Pull Feeders	
703		NUF.PW	PGE MV DC3 SUF - Terminate	1	1	13-Sep-22	13-Sep-22									PGE MV DC3 SUF - Terminate	
704		PGE MV DC5 SUF		6	6	06-Sep-22	13-Sep-22									13-Sep-22, PGE MV DC5 SUF	
705		NUF.PW	PGE MV DC5 SUF - Pull Feeders	5	5	06-Sep-22	12-Sep-22									PGE MV DC5 SUF - Pull Feeders	
706		NUF.PW	PGE MV DC5 SUF - Terminate	1	1	13-Sep-22	13-Sep-22									PGE MV DC5 SUF - Terminate	
707		PGE MV DC5 NUF		6	6	06-Sep-22	13-Sep-22									13-Sep-22, PGE MV DC5 NUF	
708		NUF.PW	PGE MV DC5 NUF - Pull Feeders	5	5	06-Sep-22	12-Sep-22									PGE MV DC5 NUF - Pull Feeders	
709		NUF.PW	PGE MV DC5 NUF - Terminate	1	1	13-Sep-22	13-Sep-22									PGE MV DC5 NUF - Terminate	
710		Wet Utilities		165	41	21-Apr-22 A	09-Sep-22									09-Sep-22, Wet Utilities	
711	Storm Utilities	Storm Utilities		165	41	18-May-22 A	09-Sep-22									09-Sep-22, Storm Utilities	
712		UTIL.PW.1i	Install Storm Underground Piping	24	19	18-May-22 A	09-Aug-22									Install Storm Underground Piping	
713		UTIL.PW.1i	Install DC2 Detention System	6	2	25-May-22 A	15-Jul-22									Install DC2 Detention System	
714		UTIL.PW.1i	Install DC3 Detention System	7	7	13-Jul-22	21-Jul-22									Install DC3 Detention System	
715		UTIL.PW.1i	Install Storm Runoff Surface Structures	22	22	09-Aug-22	09-Sep-22									Install Storm Runoff Surface Structures	
716	Sanitary Sewer		UTIL.PW.1i	Install Sanitary - Private Underground	118	29	21-Apr-22 A	22-Aug-22								22-Aug-22, Sanitary Sewer	
717		UTIL.PW.1i	Install Sanitary - Private Underground	15	3	21-Apr-22 A	15-Jul-22									Install Sanitary - Private Underground	
Remaining Level of Effort				Remaining Work				◆	◆	Milestone					TASK filter: All Activities		
Actual Work				Critical Remaining Work				▼	▼	Summary					© Oracle Corporation		

QTS HIL2 DC2, DC3, DC5 Construction Schedule				Classic Schedule Layout					12-Jul-22 15:36									
#	Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish		2022				2023				2024		
					Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2			
718	UTIL.PW.11	Install Sanitary - Public Underground	6	6	15-Aug-22*	22-Aug-22												
719	Fresh Water Utilities			20	20	18-Jul-22	12-Aug-22											
720	UTIL.PW.11	Fire - Private Underground	13	13	18-Jul-22	03-Aug-22												
721	UTIL.PW.11	Fire - Public Underground	3	3	04-Aug-22	08-Aug-22												
722	UTIL.PW.11	Domestic - Public Underground	1	1	09-Aug-22	09-Aug-22												
723	UTIL.PW.11	Domestic - Private Underground	3	3	10-Aug-22	12-Aug-22												
724	DC2			284	274	14-Apr-22 A	08-Aug-23											
725	DC2 Milestones			0	0	15-Feb-23	15-Feb-23											
726	MILE.D2.1000	Substantially Weather-tight	0	0		15-Feb-23												
727	Earthwork			44	6	14-Apr-22 A	14-Jul-22											
728	Site Development			32	6	14-Apr-22 A	14-Jul-22											
729	SITE.D2.1020	Place Imported Fill Materials	26	0	14-Apr-22 A	16-May-22 A												
730	SITE.D2.1080	Fragnet ## DC2 Over Excavation of Organic Soil and Additional Fills	27	0	21-Apr-22 A	27-May-22 A												
731	SITE.D2.1000	Earthwork Onsite Cut to Fill	6	0	25-Apr-22 A	03-May-22 A												
732	SITE.D2.1010	Earthwork Onsite CTS Site Fills	4	0	28-Apr-22 A	31-May-22 A												
733	SITE.D2.1030	Place Surcharge	6	0	16-May-22 A	06-Jun-22 A												
734	SITE.D2.1040	Surcharge Waiting Period	30	6	18-May-22 A	14-Jul-22												
735	SITE.D2.1050	DC2 Surcharge Waiting Period zone1	10	0	18-May-22 A	27-Jun-22 A												
736	SITE.D2.1060	DC2 Surcharge Waiting Period Zone 2	10	6	25-May-22 A	14-Jul-22												
737	SITE.D2.1070	DC2 Surcharge Waiting Period Zone 3	10	4	04-Jun-22 A	12-Jul-22												
738	Rigid Inclusions			37	0	29-Apr-22 A	22-Jun-22 A											
739	RIGD.D2.1020	Drill / Pour RI-CL L2 to CL Q	10	0	29-Apr-22 A	07-Jun-22 A												
740	RIGD.D2.1010	Drill / Pour RI-CL C to CL L.2	10	0	03-May-22 A	03-Jun-22 A												
741	RIGD.D2.1000	Drill / Pour RI-CL A to C	7	0	11-May-22 A	19-May-22 A												
742	RIGD.D2.1030	Drill / Pour RI-CL Q to CL Z	10	0	06-Jun-22 A	22-Jun-22 A												
743	Foundation			119	111	28-May-22 A	15-Dec-22											
744	Building Pad Prep			27	27	07-Jul-22	12-Aug-22											
745	Area Wide			21	21	15-Jul-22	12-Aug-22											
746	FOND.D2.1	Move Surcharge to DC3	5	5	15-Jul-22	21-Jul-22												
747	FOND.D2.1	Compact Subgrade And Place Stone	5	5	08-Aug-22	12-Aug-22												
748	Grid A - C			11	11	07-Jul-22	21-Jul-22											
749	UTIL.D2.1C	Under-slab Utilities CL A to C	12	5	25-JUL-22	5-AUG-22												
750	UTIL.D2.1C	Deep Underground Utilities	10	10	08-Jul-22	21-Jul-22												
751	FOND.D2.1	Backfill/Compact CL A to C	5	5	14-Jul-22	20-Jul-22												
752	Grid C - L			10	10	14-Jul-22	27-Jul-22											
753	UTIL.D2.1C	Under-slab Utilities CL C to L.2	After Line 929 FS	12	5	12-SEP-22	20-Jul-22											
754	FOND.D2.1	Backfill/Compact CL C to L.2	5	5	21-Jul-22	27-Jul-22												
755	Grid L - Q.1			10	10	21-Jul-22	03-Aug-22											
756	UTIL.D2.1C	Under-slab Utilities CL L.2 to Q	After Line 786 FS	5	5	8-AUG-22	15-AUG-22											
757	FOND.D2.1	Backfill/Compact CL L.2 to Q	5	5	28-Jul-22	03-Aug-22												
758	Grid Q.1 - Z			10	10	28-Jul-22	10-Aug-22											
759	UTIL.D2.1C	Under-slab Utilities CL Q to Z	After Line 940 FS	18	5	18-OCT-22	03-Aug-22											
760	FOND.D2.1	Backfill/Compact CL Q to Z	5	5	04-Aug-22	10-Aug-22												
761	DC2 Foundations			41	33	28-May-22 A	22-Aug-22											
762	Grid A-C			18	11	28-May-22 A	21-Jul-22											
763	FOND.D2.1	Found A-C - Survey Footing Excavation	1	0	28-May-22 A	30-May-22 A												
764	FOND.D2.1	Found A-C - Dig Footings	3	0	31-May-22 A	07-Jun-22 A												
765	FOND.D2.1	Found A-C - Form Foundations (#1 Formwork Delivery)	5	0	08-Jun-22 A	22-Jun-22 A												

Remaining Level of Effort Remaining Work ◆ Milestone
 Actual Work Critical Remaining Work ▶ Summary

QTS HIL2 DC2, DC3, DC5 Construction Schedule				Classic Schedule Layout					12-Jul-22 15:36										
#	Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish		2022					2023					2024	
								Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	
766	FOND.D2.1	Found A-C - Survey Formwork	1	0	08-Jun-22 A	22-Jun-22 A													
767	FOND.D2.1	Found A-C - Install Anchor Bolts		5	0	13-Jun-22 A	29-Jun-22 A												
768	FOND.D2.1	Found A-C - Install Reinforcement		5	0	14-Jun-22 A	29-Jun-22 A												
769	FOND.D2.1	Found A-C - Place Foundations		1	0	23-Jun-22 A	30-Jun-22 A												
770	FOND.D2.1	Found A-C - Strip Foundations		4	1	24-Jun-22 A	07-Jul-22												
771	FOND.D2.1	Found A-C - Install Elevator Pit		5	5	07-Jul-22	13-Jul-22												
772	FOND.D2.1	Found A-C - Plinths and Grade Beams		5	5	07-Jul-22	13-Jul-22												
773	FOND.D2.1	Found A-C - Waterproof/Insulate		3	3	14-Jul-22	18-Jul-22												
774	FOND.D2.1	Found A-C - Backfill Foundations		3	3	19-Jul-22	21-Jul-22												
775	Grid C-L			30	22	24-Jun-22 A	05-Aug-22												
776	FOND.D2.1	Found C-L - Survey Footing Excavation		1	0	24-Jun-22 A	07-Jul-22												
777	FOND.D2.1	Found C-L - Dig Footings		1	0	24-Jun-22 A	07-Jul-22												
778	FOND.D2.1	Found C-L - Form Foundations (#2 Formwork Delivery)		6	2	06-Jul-22 A	08-Jul-22												
779	FOND.D2.1	Found C-L - Install Reinforcement		6	5	06-Jul-22 A	13-Jul-22												
780	FOND.D2.1	Found C-L - Survey Formwork		1	1	06-Jul-22 A	07-Jul-22												
781	FOND.D2.1	Found C-L - Install Anchor Bolts		6	6	07-Jul-22	14-Jul-22												
782	FOND.D2.1	Found C-L - Place Foundations		2	2	15-Jul-22	18-Jul-22												
783	FOND.D2.1	Found C-L - Strip Foundations		6	6	19-Jul-22	26-Jul-22												
784	FOND.D2.1	Found C-L - Plinths and Grade Beams		6	6	19-Jul-22	26-Jul-22												
785	FOND.D2.1	Found C-L - Waterproof/Insulate		3	3	27-Jul-22	29-Jul-22												
786	FOND.D2.1	Found C-L - Backfill Foundations		5	5	01-Aug-22	05-Aug-22												
787	Grid L-Q.1			21	21	15-Jul-22	12-Aug-22												
788	FOND.D2.1	Found L-Q.1 - Survey Footing Excavation		1	1	15-Jul-22	15-Jul-22												
789	FOND.D2.1	Found L-Q.1 - Dig Footings		3	3	18-Jul-22	20-Jul-22												
790	FOND.D2.1	Found L-Q.1 - Survey Formwork		1	1	21-Jul-22	21-Jul-22												
791	FOND.D2.1	Found L-Q.1 - Form Foundations (Formwork From A-C)		6	6	22-Jul-22	29-Jul-22												
792	FOND.D2.1	Found L-Q.1 - Install Anchor Bolts		5	5	22-Jul-22	28-Jul-22												
793	FOND.D2.1	Found L-Q.1 - Install Reinforcement		5	5	25-Jul-22	29-Jul-22												
794	FOND.D2.1	Found L-Q.1 - Place Foundations		1	1	01-Aug-22	01-Aug-22												
795	FOND.D2.1	Found L-Q.1 - Strip Foundations		3	3	02-Aug-22	04-Aug-22												
796	FOND.D2.1	Found L-Q.1 - Plinths and Grade Beams		5	5	02-Aug-22	08-Aug-22												
797	FOND.D2.1	Found L-Q.1 - Waterproof/Insulate		3	3	05-Aug-22	09-Aug-22												
798	FOND.D2.1	Found L-Q.1 - Backfill Foundations		3	3	10-Aug-22	12-Aug-22												
799	Grid Q.1-Z			29	29	13-Jul-22	22-Aug-22												
800	FOND.D2.1	Grid Q.1-Z - Survey Footing Excavation		1	1	13-Jul-22	13-Jul-22												
801	FOND.D2.1	Grid Q.1-Z - Dig Footings		3	3	22-Jul-22	26-Jul-22												
802	FOND.D2.1	Grid Q.1-Z - Survey Formwork		1	1	27-Jul-22	27-Jul-22												
803	FOND.D2.1	Grid Q.1-Z - Form Foundations (Formwork From C-L)		6	6	01-Aug-22	08-Aug-22												
804	FOND.D2.1	Grid Q.1-Z - Install Anchor Bolts		5	5	01-Aug-22	05-Aug-22												
805	FOND.D2.1	Grid Q.1-Z - Install Reinforcement		5	5	02-Aug-22	08-Aug-22												
806	FOND.D2.1	Grid Q.1-Z - Place Foundations		1	1	09-Aug-22	09-Aug-22												
807	FOND.D2.1	Grid Q.1-Z - Strip Foundations		3	3	10-Aug-22	12-Aug-22												
808	FOND.D2.1	Grid Q.1-Z - Plinths and Grade Beams		5	5	10-Aug-22	16-Aug-22												
809	FOND.D2.1	Grid Q.1-Z - Waterproof/Insulate		3	3	15-Aug-22	17-Aug-22												
810	FOND.D2.1	Grid Q.1-Z - Backfill Foundations		3	3	18-Aug-22	22-Aug-22												
811	DC2 Slab On Grade			100	100	22-Jul-22	15-Dec-22												
812	Grid A-C			50	50	22-Jul-22	30-Sep-22												
813	Pour 1			50	50	22-Jul-22	30-Sep-22												

Remaining Level of Effort Remaining Work Milestone Critical Remaining Work Summary

QTS HIL2 DC2, DC3, DC5 Construction Schedule				Classic Schedule Layout					12-Jul-22 15:36									
#	Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish			2022				2023				2024	
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	
814	SOG.D2	SOG A-C P1 - Fine Grade CL A to C	3	3	22-Jul-22	26-Jul-22						I SOG A-C P1 - Fine Grade CL A to C						
815	SOG.D2	SOG A-C P1 - Edgeforms/Diamonds		2	2	13-Sep-22	14-Sep-22					I SOG A-C P1 - Edgeforms/Diamonds						
816	SOG.D2	SOG A-C P1 - Vapor Barrier		1	1	15-Sep-22	15-Sep-22					I SOG A-C P1 - Vapor Barrier						
817	SOG.D2	SOG A-C P1 - Install reinforcement		3	3	19-Sep-22	21-Sep-22					I SOG A-C P1 - Install reinforcement						
818	SOG.D2	SOG A-C P1 - MEP Final Set		1	1	22-Sep-22	22-Sep-22	Need 2 days if not using blockouts				C P1 - MEP Final Set						
819	SOG.D2	SOG A-C P1 - Place SOG		1	1	23-Sep-22	23-Sep-22					I SOG A-C P1 - Place SOG						
820	SOG.D2	SOG A-C P1 - Cure SOG		5	5	26-Sep-22	30-Sep-22					I SOG A-C P1 - Cure SOG						
821	Grid C-L			54	54	08-Aug-22	24-Oct-22											
822	Pour 2			48	48	08-Aug-22	14-Oct-22											
823	SOG.D2	SOG C-L P2 - Fine Grade		3	3	08-Aug-22	10-Aug-22					I SOG C-L P2 - Fine Grade						
824	SOG.D2	SOG C-L P2 - Edgeforms/Diamonds		2	2	27-Sep-22	28-Sep-22					I SOG C-L P2 - Edgeforms/Diamonds						
825	SOG.D2	SOG C-L P2 - Vapor Barrier		1	1	29-Sep-22	29-Sep-22					I SOG C-L P2 - Vapor Barrier						
826	SOG.D2	SOG C-L P2 - Install reinforcement		3	3	30-Sep-22	04-Oct-22					I SOG C-L P2 - Install reinforcement						
827	SOG.D2	SOG C-L P2 - MEP Final Set		1	1	05-Oct-22	05-Oct-22					I SOG C-L P2 - MEP Final Set						
828	SOG.D2	SOG C-L P2 - Place SOG		1	1	06-Oct-22	06-Oct-22					I SOG C-L P2 - Place SOG						
829	SOG.D2	SOG C-L P2 - Cure SOG		5	5	07-Oct-22	14-Oct-22					I SOG C-L P2 - Cure SOG						
830	Pour 3			54	54	08-Aug-22	24-Oct-22											
831	SOG.D2	SOG C-L P3 - Fine Grade		3	3	08-Aug-22	10-Aug-22					I SOG C-L P3 - Fine Grade						
832	SOG.D2	SOG C-L P3 - Edgeforms/Diamonds		2	2	05-Oct-22	06-Oct-22					I SOG C-L P3 - Edgeforms/Diamonds						
833	SOG.D2	SOG C-L P3 - Vapor Barrier		1	1	07-Oct-22	07-Oct-22					I SOG C-L P3 - Vapor Barrier						
834	SOG.D2	SOG C-L P3 - Install reinforcement		3	3	11-Oct-22	13-Oct-22					I SOG C-L P3 - Install reinforcement						
835	SOG.D2	SOG C-L P3 - MEP Final Set		1	1	14-Oct-22	14-Oct-22					I SOG C-L P3 - MEP Final Set						
836	SOG.D2	SOG C-L P3 - Place SOG		1	1	17-Oct-22	17-Oct-22					I SOG C-L P3 - Place SOG						
837	SOG.D2	SOG C-L P3 - Cure SOG		5	5	18-Oct-22	24-Oct-22					I SOG C-L P3 - Cure SOG						
838	Grid L-Q.1			58	58	15-Aug-22	04-Nov-22											
839	Pour 4			58	58	15-Aug-22	04-Nov-22											
840	SOG.D2	SOG L-Q.1 P4 - Fine Grade		3	3	15-Aug-22	17-Aug-22					I SOG L-Q.1 P4 - Fine Grade						
841	SOG.D2	SOG L-Q.1 P4 - Edgeforms/Diamonds		2	2	19-Oct-22	20-Oct-22					I SOG L-Q.1 P4 - Edgeforms/Diamonds						
842	SOG.D2	SOG L-Q.1 P4 - Vapor Barrier		1	1	21-Oct-22	21-Oct-22					I SOG L-Q.1 P4 - Vapor Barrier						
843	SOG.D2	SOG L-Q.1 P4 - Install reinforcement		3	3	24-Oct-22	26-Oct-22					I SOG L-Q.1 P4 - Install reinforcement						
844	SOG.D2	SOG L-Q.1 P4 - MEP Final Set		1	1	27-Oct-22	27-Oct-22					I SOG L-Q.1 P4 - MEP Final Set						
845	SOG.D2	SOG L-Q.1 P4 - Place SOG		1	1	28-Oct-22	28-Oct-22					I SOG L-Q.1 P4 - Place SOG						
846	SOG.D2	SOG L-Q.1 P4 - Cure SOG		5	5	31-Oct-22	04-Nov-22					I SOG L-Q.1 P4 - Cure SOG						
847	Grid Q.1-Z			78	78	23-Aug-22	15-Dec-22											
848	Pour 5			28	28	26-Oct-22	07-Dec-22											
849	SOG.D2	SOG Q.1-Z P5 - Fine Grade		3	3	26-Oct-22	28-Oct-22					I SOG Q.1-Z P5 - Fine Grade						
850	SOG.D2	SOG Q.1-Z P5 - Edgeforms/Diamonds		2	2	17-Nov-22	18-Nov-22					I SOG Q.1-Z P5 - Edgeforms/Diamonds						
851	SOG.D2	SOG Q.1-Z P5 - Vapor Barrier		1	1	21-Nov-22	21-Nov-22					I SOG Q.1-Z P5 - Vapor Barrier						
852	SOG.D2	SOG Q.1-Z P5 - Install reinforcement		3	3	22-Nov-22	28-Nov-22					I SOG Q.1-Z P5 - Install reinforcement						
853	SOG.D2	SOG Q.1-Z P5 - MEP Final Set		1	1	29-Nov-22	29-Nov-22					I SOG Q.1-Z P5 - MEP Final Set						
854	SOG.D2	SOG Q.1-Z P5 - Place SOG		1	1	30-Nov-22	30-Nov-22					I SOG Q.1-Z P5 - Place SOG						
855	SOG.D2	SOG Q.1-Z P5 - Cure SOG		5	5	01-Dec-22	07-Dec-22					I SOG Q.1-Z P5 - Cure SOG						
856	Pour 6			78	78	23-Aug-22	15-Dec-22											
857	SOG.D2	SOG Q.1-Z P6 - Fine Grade		3	3	23-Aug-22	25-Aug-22					I SOG Q.1-Z P6 - Fine Grade						
858	SOG.D2	SOG Q.1-Z P6 - Edgeforms/Diamonds		2	2	23-Nov-22	28-Nov-22					I SOG Q.1-Z P6 - Edgeforms/Diamonds						
859	SOG.D2	SOG Q.1-Z P6 - Vapor Barrier		1	1	29-Nov-22	29-Nov-22					I SOG Q.1-Z P6 - Vapor Barrier						
860	SOG.D2	SOG Q.1-Z P6 - Install reinforcement		3	3	02-Dec-22	06-Dec-22					I SOG Q.1-Z P6 - Install reinforcement						
861	SOG.D2	SOG Q.1-Z P6 - MEP Final Set		1	1	07-Dec-22	07-Dec-22	Need 2 days if not using blockouts				I SOG Q.1-Z P6 - MEP Final Set						
				Page 18 of 74							TASK filter: All Activities						© Oracle Corporation	

QTS HIL2 DC2, DC3, DC5 Construction Schedule				Classic Schedule Layout					12-Jul-22 15:36									
#	Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish		Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2
862	SOG.D2	SOG Q.1-Z P6 - Place SOG	1	1	08-Dec-22	08-Dec-22							I	SOG Q.1-Z P6 - Place SOG				
863	SOG.D2	SOG Q.1-Z P6 - Cure SOG		5	5	09-Dec-22	15-Dec-22						I	SOG Q.1-Z P6 - Cure SOG				
864	DC2 SOMD			66	66	29-Aug-22	05-Dec-22						▼	05-Dec-22, DC2 SOMD				
865	A-Z			66	66	29-Aug-22	05-Dec-22						▼	05-Dec-22, A-Z				
866	Grid A - C			9	9	29-Aug-22	09-Sep-22						▼	09-Sep-22, Grid A - C				
867	Pour 1 A - C			9	9	29-Aug-22	09-Sep-22						▼	09-Sep-22, Pour 1 A - C				
868	SOM	SOMD A-C P1 - As-Built Structure	1	1	29-Aug-22	29-Aug-22							I	SOMD A-C P1 - As-Built Structure				
869	SOM	SOMD A-C P1 - MEP		3	3	30-Aug-22	01-Sep-22						I	SOMD A-C P1 - MEP				
870	SOM	SOMD A-C P1 - Edgeforms/Embeds		3	3	30-Aug-22	01-Sep-22						I	SOMD A-C P1 - Edgeforms/Embeds				
871	SOM	SOMD A-C P1 - Install Reinforcement		3	3	02-Sep-22	07-Sep-22						I	SOMD A-C P1 - Install Reinforcement				
872	SOM	SOMD A-C P1 - MEP Final		1	1	08-Sep-22	08-Sep-22						I	SOMD A-C P1 - MEP Final				
873	SOM	SOMD A-C P1 - Place Slab		1	1	09-Sep-22	09-Sep-22						I	SOMD A-C P1 - Place Slab				
874	Grid C - L			21	21	02-Sep-22	03-Oct-22						▼	03-Oct-22, Grid C - L				
875	Pour 2 C - F.4			9	9	02-Sep-22	15-Sep-22						▼	15-Sep-22, Pour 2 C - F.4				
876	SOM	SOMD C-F.4 P2 - MEP		2	2	02-Sep-22	06-Sep-22						I	SOMD C-F.4 P2 - MEP				
877	SOM	SOMD C-F.4 P2 - Edgeforms/Embeds		2	2	07-Sep-22	08-Sep-22						I	SOMD C-F.4 P2 - Edgeforms/Embeds				
878	SOM	SOMD C-F.4 P2 - Install Reinforcement		3	3	09-Sep-22	13-Sep-22						I	SOMD C-F.4 P2 - Install Reinforcement				
879	SOM	SOMD C-F.4 P2 - MEP Final		1	1	14-Sep-22	14-Sep-22						I	SOMD C-F.4 P2 - MEP Final				
880	SOM	SOMD C-F.4 P2 - Place Slab		1	1	15-Sep-22	15-Sep-22						I	SOMD C-F.4 P2 - Place Slab				
881	Pour 3 F.4 - J.8			8	8	09-Sep-22	20-Sep-22						▼	20-Sep-22, Pour 3 F.4 - J.8				
882	SOM	SOMD F.4-J.8 P3 - Edgeforms/Embeds		2	2	09-Sep-22	12-Sep-22						I	SOMD F.4-J.8 P3 - Edgeforms/Embeds				
883	SOM	SOMD F.4-J.8 P3 - Install Reinforcement		3	3	14-Sep-22	16-Sep-22						I	SOMD F.4-J.8 P3 - Install Reinforcement				
884	SOM	SOMD F.4-J.8 P3 - MEP		2	2	19-Sep-22	20-Sep-22						I	SOMD F.4-J.8 P3 - MEP				
885	SOM	SOMD F.4-J.8 P3 - MEP Final		1	1	19-Sep-22	19-Sep-22						I	SOMD F.4-J.8 P3 - MEP Final				
886	SOM	SOMD F.4-J.8 P3 - Place Slab		1	1	20-Sep-22	20-Sep-22						I	SOMD F.4-J.8 P3 - Place Slab				
887	Pour 4 J.8 - M.5			7	7	23-Sep-22	03-Oct-22						▼	03-Oct-22, Pour 4 J.8 - M.5				
888	SOM	SOMD J.8-M.5 P4 - MEP		2	2	23-Sep-22	26-Sep-22						I	SOMD J.8-M.5 P4 - MEP				
889	SOM	SOMD J.8-M.5 P4 - Edgeforms/Embeds		2	2	23-Sep-22	26-Sep-22						I	SOMD J.8-M.5 P4 - Edgeforms/Embeds				
890	SOM	SOMD J.8-M.5 P4 - Install Reinforcement		3	3	27-Sep-22	29-Sep-22						I	SOMD J.8-M.5 P4 - Install Reinforcement				
891	SOM	SOMD J.8-M.5 P4 - MEP Final		1	1	30-Sep-22	30-Sep-22						I	SOMD J.8-M.5 P4 - MEP Final				
892	SOM	SOMD J.8-M.5 P4 - Place Slab		1	1	03-Oct-22	03-Oct-22						I	SOMD J.8-M.5 P4 - Place Slab				
893	Grid L - Q.1			7	7	03-Oct-22	12-Oct-22						▼	12-Oct-22, Grid L - Q.1				
894	Pour 5 M.5 - Q			7	7	03-Oct-22	12-Oct-22						▼	12-Oct-22, Pour 5 M.5 - Q				
895	SOM	SOMD M.5-Q P5 - MEP		2	2	03-Oct-22	04-Oct-22						I	SOMD M.5-Q P5 - MEP				
896	SOM	SOMD M.5-Q P5 - Edgeforms/Embeds		2	2	03-Oct-22	04-Oct-22						I	SOMD M.5-Q P5 - Edgeforms/Embeds				
897	SOM	SOMD M.5-Q P5 - Install Reinforcement		3	3	05-Oct-22	07-Oct-22						I	SOMD M.5-Q P5 - Install Reinforcement				
898	SOM	SOMD M.5-Q P5 - MEP Final		1	1	11-Oct-22	11-Oct-22						I	SOMD M.5-Q P5 - MEP Final				
899	SOM	SOMD M.5-Q P5 - Place Slab		1	1	12-Oct-22	12-Oct-22						I	SOMD M.5-Q P5 - Place Slab				
900	Grid Q.1 - Z			34	34	14-Oct-22	05-Dec-22						▼	05-Dec-22, Grid Q.1 - Z				
901	Pour 6 Q - T.3			8	8	14-Oct-22	25-Oct-22						▼	25-Oct-22, Pour 6 Q - T.3				
902	SOM	SOMD Q-T.3 P6 - As-Built Structure		1	1	14-Oct-22	14-Oct-22						I	SOMD Q-T.3 P6 - As-Built Structure				
903	SOM	SOMD Q-T.3 P6 - MEP		2	2	17-Oct-22	18-Oct-22						I	SOMD Q-T.3 P6 - MEP				
904	SOM	SOMD Q-T.3 P6 - Edgeforms/Embeds		2	2	17-Oct-22	18-Oct-22						I	SOMD Q-T.3 P6 - Edgeforms/Embeds				
905	SOM	SOMD Q-T.3 P6 - Install Reinforcement		3	3	19-Oct-22	21-Oct-22						I	SOMD Q-T.3 P6 - Install Reinforcement				
906	SOM	SOMD Q-T.3 P6 - MEP Final		1	1	24-Oct-22	24-Oct-22						I	SOMD Q-T.3 P6 - MEP Final				
907	SOM	SOMD Q-T.3 P6 - Place Slab		1	1	25-Oct-22	25-Oct-22						I	SOMD Q-T.3 P6 - Place Slab				
908	Pour 7 T.3 - W.3			20	20	19-Oct-22	16-Nov-22						▼	16-Nov-22, Pour 7 T.3 - W.3				
909	SOM	SOMD T.3-W.3 P7 - MEP		2	2	19-Oct-22	20-Oct-22						I	SOMD T.3-W.3 P7 - MEP				



QTS HIL2 DC2, DC3, DC5 Construction Schedule				Classic Schedule Layout					12-Jul-22 15:36									
#	Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	2022					2023					2024	
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	
910	Pour 8 W.3 - Z	SOMD T.3-W.3 P7 - Edgeforms/Embeds	2	2	07-Nov-22	08-Nov-22						I SOMD T.3-W.3 P7 - Edgeforms/Embeds						
911		SOMD T.3-W.3 P7 - Install Reinforcement		3	3	09-Nov-22	14-Nov-22					I SOMD T.3-W.3 P7 - Install Reinforcement						
912		SOMD T.3-W.3 P7 - MEP Final		1	1	15-Nov-22	15-Nov-22					I SOMD T.3-W.3 P7 - MEP Final						
913		SOMD T.3-W.3 P7 - Place Slab		1	1	16-Nov-22	16-Nov-22					I SOMD T.3-W.3 P7 - Place Slab						
914		Pour 8 W.3 - Z		29	29	21-Oct-22	05-Dec-22					▼ 05-Dec-22, Pour 8 W.3 - Z						
915		SOMD W.3-Z P8 - MEP		2	2	21-Oct-22	24-Oct-22					I SOMD W.3-Z P8 - MEP						
916		SOMD W.3-Z P8 - Edgeforms/Embeds		2	2	21-Nov-22	22-Nov-22					I SOMD W.3-Z P8 - Edgeforms/Embeds						
917		SOMD W.3-Z P8 - Install Reinforcement		3	3	29-Nov-22	01-Dec-22					I SOMD W.3-Z P8 - Install Reinforcement						
918		SOMD W.3-Z P8 - MEP Final		1	1	02-Dec-22	02-Dec-22					I SOMD W.3-Z P8 - MEP Final						
919		SOMD W.3-Z P8 - Place Slab		1	1	05-Dec-22	05-Dec-22					I SOMD W.3-Z P8 - Place Slab						
920	Steel		103	103	15-Aug-22	13-Jan-23						▼ 13-Jan-23, Steel						
921	Steel Erection		44	44	15-Aug-22	17-Oct-22						▼ 17-Oct-22, Steel Erection						
922	ERCT.D2.1000	Erect Steel - Sequence 11		3	3	15-Aug-22	17-Aug-22					I Erect Steel - Sequence 11						
923	ERCT.D2.1070	Erect Steel - Sequence 12		3	3	18-Aug-22	22-Aug-22					I Erect Steel - Sequence 12						
924	ERCT.D2.1010	Erect Steel - Sequence 21		2	2	23-Aug-22	24-Aug-22					I Erect Steel - Sequence 21						
925	ERCT.D2.1110	Erect Steel - Sequence 31		2	2	25-Aug-22	26-Aug-22					I Erect Steel - Sequence 31						
926	ERCT.D2.1080	Erect Steel - Sequence 22		2	2	29-Aug-22	30-Aug-22					I Erect Steel - Sequence 22						
927	ERCT.D2.1120	Erect Steel - Sequence 32		2	2	31-Aug-22	01-Sep-22					I Erect Steel - Sequence 32						
928	ERCT.D2.1090	Erect Steel - Sequence 23		2	2	02-Sep-22	06-Sep-22					I Erect Steel - Sequence 23						
929	ERCT.D2.1130	Erect Steel - Sequence 33		2	2	07-Sep-22	08-Sep-22					I Erect Steel - Sequence 33						
930	ERCT.D2.1100	Erect Steel - Sequence 24		3	3	09-Sep-22	13-Sep-22					I Erect Steel - Sequence 24						
931	ERCT.D2.1140	Erect Steel - Sequence 34		3	3	14-Sep-22	16-Sep-22					I Erect Steel - Sequence 34						
932	ERCT.D2.1150	Erect Steel - Sequence 25		2	2	19-Sep-22	20-Sep-22					I Erect Steel - Sequence 25						
933	ERCT.D2.1190	Erect Steel - Sequence 35		2	2	21-Sep-22	22-Sep-22					I Erect Steel - Sequence 35						
934	ERCT.D2.1160	Erect Steel - Sequence 26		3	3	23-Sep-22	27-Sep-22					I Erect Steel - Sequence 26						
935	ERCT.D2.1200	Erect Steel - Sequence 36		3	3	28-Sep-22	30-Sep-22					I Erect Steel - Sequence 36						
936	ERCT.D2.1170	Erect Steel - Sequence 27		2	2	03-Oct-22	04-Oct-22					I Erect Steel - Sequence 27						
937	ERCT.D2.1210	Erect Steel - Sequence 37		2	2	05-Oct-22	06-Oct-22					I Erect Steel - Sequence 37						
938	ERCT.D2.1180	Erect Steel - Sequence 28		2	2	07-Oct-22	11-Oct-22					I Erect Steel - Sequence 28						
939	ERCT.D2.1220	Erect Steel - Sequence 38		2	2	12-Oct-22	13-Oct-22					I Erect Steel - Sequence 38						
940	ERCT.D2.1230	Erect Steel - Sequence 40		2	2	14-Oct-22	17-Oct-22					I Erect Steel - Sequence 40						
941	Stairs		100	100	18-Aug-22	13-Jan-23						▼ 13-Jan-23, Stairs						
942	ERCT.D2.1020	Stair 1 (S Loading Dock)		2	2	18-Aug-22	19-Aug-22					I Stair 1 (S Loading Dock)						
943	ERCT.D2.1030	Stair 2 (Admin)		2	2	23-Aug-22	24-Aug-22					I Stair 2 (Admin)						
944	ERCT.D2.1060	Stair 3 (Back of House)		2	2	18-Oct-22	19-Oct-22					I Stair 3 (Back of House)						
945	ERCT.D2.1040	Exterior Equipment Yard (2 Sets)		10	10	06-Dec-22	19-Dec-22					■ Exterior Equipment Yard (2 Sets)						
946	ERCT.D2.1050	Exterior Exit Stair (2 Sets)		10	10	30-Dec-22	13-Jan-23					■ Exterior Exit Stair (2 Sets)						
947	Precast		30	30	01-Dec-22	13-Jan-23						▼ 13-Jan-23, Precast						
948	PCST.D2.1000	Precast - CL Q to L 2 - East Elevation		3	3	01-Dec-22	05-Dec-22					■ Precast - CL Q to L 2 - East Elevation						
949	PCST.D2.1010	Precast - CL L 2 to C.1 - East Elevation		3	3	06-Dec-22	08-Dec-22					■ Precast - CL L 2 to C.1 - East Elevation						
950	PCST.D2.1020	Precast - CL C.1 to A - East Elevation		2	2	09-Dec-22	12-Dec-22					■ Precast - CL C.1 to A - East Elevation						
951	PCST.D2.1030	Precast - CL 8 to 1 - South Elevation		4	4	13-Dec-22	16-Dec-22					■ Precast - CL 8 to 1 - South Elevation						
952	PCST.D2.1040	Precast - CL A to C.1 - West Elevation		2	2	19-Dec-22	20-Dec-22					I Precast - CL A to C.1 - West Elevation						
953	PCST.D2.1050	Precast - CL C.1 to L 2 - West Elevation		3	3	21-Dec-22	23-Dec-22					I Precast - CL C.1 to L 2 - West Elevation						
954	PCST.D2.1060	Precast - CL L 2 to Q - West Elevation		3	3	27-Dec-22	29-Dec-22					I Precast - CL L 2 to Q - West Elevation						
955	PCST.D2.1070	Precast - CL Q to Z - West Elevation		3	3	30-Dec-22	04-Jan-23					I Precast - CL Q to Z - West Elevation						
956	PCST.D2.1080	Precast - CL 1 to 8 - True North		4	4	05-Jan-23	10-Jan-23					I Precast - CL 1 to 8 - True North						
Remaining Level of Effort				Remaining Work		◆◆ Milestone	Page 20 of 74					TASK filter: All Activities					© Oracle Corporation	
Actual Work				Critical Remaining Work		▼ Summary												

QTS HIL2 DC2, DC3, DC5 Construction Schedule				Classic Schedule Layout					12-Jul-22 15:36											
#	Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish		Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2		
957	PCST.D2.1090	Precast - CL Z to Q- East Elevation	3	3	11-Jan-23	13-Jan-23							I	Precast - CL Z to Q- East Elevation						
958	Glazing and Metal Paneling			41	41	19-Dec-22	15-Feb-23							▼	15-Feb-23, Glazing and Metal Paneling					
959	GZMP.D2.1010	Metal Paneling - S Elevation	15	15	19-Dec-22	10-Jan-23									Metal Paneling - S Elevation					
960	GZMP.D2.1030	Precast Field Verification for Glazing	1	1	19-Dec-22	19-Dec-22							I	Precast Field Verification for Glazing						
961	GZMP.D2.1000	Install Glazing - S Elevation CL-8 to CL-1	15	15	19-Jan-23	08-Feb-23									Install Glazing - S Elevation CL-8 to CL-1					
962	GZMP.D2.1020	Install Glazing - W Elevation CL-C to CL-A	5	5	09-Feb-23	15-Feb-23									Install Glazing - W Elevation CL-C to CL-A					
963	Roof			99	99	29-Aug-22	23-Jan-23								▼	23-Jan-23, Roof				
964	CL A to CL C			83	83	29-Aug-22	29-Dec-22								▼	29-Dec-22, CL A to CL C				
965	ROOF.D2.103	Roof A-C - Temp Roof	2	2	29-Aug-22	30-Aug-22							I	Roof A-C - Temp Roof						
966	ROOF.D2.104	Roof A-C - Foam Insulation	5	5	31-Aug-22	07-Sep-22									Roof A-C - Foam Insulation					
967	ROOF.D2.105	Roof A-C - Install Roofing Material	5	5	08-Sep-22	14-Sep-22							I	Install Roofing Material						
968	ROOF.D2.100	Roof A-C - Install Curbs	3	3	21-Nov-22	23-Nov-22									Roof A-C - Install Curbs					
969	ROOF.D2.101	Roof A-C - Roof Penetrations	3	3	28-Nov-22	30-Nov-22							I	Roof A-C - Roof Penetrations						
970	ROOF.D2.102	Roof A-C - Inspect/Punch/QAQC	1	1	30-Nov-22	30-Nov-22							I	Roof A-C - Inspect/Punch/QAQC						
971	ROOF.D2.106	Roof A-C - Interior Wall Covering	5	5	15-Dec-22	21-Dec-22									Roof A-C - Interior Wall Covering					
972	ROOF.D2.107	Roof A-C - Wall Cap	5	5	22-Dec-22	29-Dec-22									Roof A-C - Wall Cap					
973	CL C to CL L			82	82	02-Sep-22	04-Jan-23								▼	04-Jan-23, CL C to CL L				
974	ROOF.D2.108	Roof C-L - Install Curbs	3	3	02-Sep-22	07-Sep-22							I	Roof C-L - Install Curbs						
975	ROOF.D2.109	Roof C-L - Roof Penetrations	3	3	08-Sep-22	12-Sep-22									Roof C-L - Roof Penetrations					
976	ROOF.D2.111	Roof C-L - Temp Roof	5	5	09-Sep-22	15-Sep-22									Roof C-L - Temp Roof					
977	ROOF.D2.110	Roof C-L - Inspect/Punch/QAQC	1	1	12-Sep-22	12-Sep-22							I	Roof C-L - Inspect/Punch/QAQC						
978	ROOF.D2.112	Roof C-L - Foam Insulation	5	5	16-Sep-22	22-Sep-22									Roof C-L - Foam Insulation					
979	ROOF.D2.113	Roof C-L - Roofing Material	5	5	23-Sep-22	29-Sep-22									Roof C-L - Roofing Material					
980	ROOF.D2.114	Roof C-L - Interior Wall Covering	5	5	20-Dec-22	27-Dec-22									Roof C-L - Interior Wall Covering					
981	ROOF.D2.115	Roof C-L - Wall Cap	5	5	28-Dec-22	04-Jan-23									Roof C-L - Wall Cap					
982	CL L to CL Q			71	71	23-Sep-22	09-Jan-23								▼	09-Jan-23, CL L to CL Q				
983	ROOF.D2.116	Roof L-Q - Install Curbs	3	3	23-Sep-22	27-Sep-22							I	Roof L-Q - Install Curbs						
984	ROOF.D2.117	Roof L-Q - Roof Penetrations	3	3	28-Sep-22	30-Sep-22							I	Roof L-Q - Roof Penetrations						
985	ROOF.D2.118	Roof L-Q - Inspect/Punch/QAQC	1	1	30-Sep-22	30-Sep-22							I	Roof L-Q - Inspect/Punch/QAQC						
986	ROOF.D2.119	Roof L-Q - Temp Roof	5	5	03-Oct-22	07-Oct-22							I	Roof L-Q - Temp Roof						
987	ROOF.D2.120	Roof L-Q - Foam Insulation	5	5	11-Oct-22	17-Oct-22									Roof L-Q - Foam Insulation					
988	ROOF.D2.121	Roof L-Q - Roofing Material	5	5	18-Oct-22	24-Oct-22									Roof L-Q - Roofing Material					
989	ROOF.D2.122	Roof L-Q - Interior Wall Covering	5	5	23-Dec-22	30-Dec-22									Roof L-Q - Interior Wall Covering					
990	ROOF.D2.123	Roof L-Q - Wall Cap	5	5	03-Jan-23	09-Jan-23									Roof L-Q - Wall Cap					
991	CL Q to CL Z			67	67	14-Oct-22	23-Jan-23								▼	23-Jan-23, CL Q to CL Z				
992	ROOF.D2.124	Roof Q-Z - Install Curbs	3	3	14-Oct-22	18-Oct-22							I	Roof Q-Z - Install Curbs						
993	ROOF.D2.127	Roof Q-Z - Temp Roof	5	5	18-Oct-22	24-Oct-22									Roof Q-Z - Temp Roof					
994	ROOF.D2.125	Roof Q-Z - Roof Penetrations	3	3	19-Oct-22	21-Oct-22							I	Roof Q-Z - Roof Penetrations						
995	ROOF.D2.126	Roof Q-Z - Inspect/Punch/QAQC	1	1	21-Oct-22	21-Oct-22							I	Roof Q-Z - Inspect/Punch/QAQC						
996	ROOF.D2.128	Roof Q-Z - Foam Insulation	5	5	25-Oct-22	31-Oct-22									Roof Q-Z - Foam Insulation					
997	ROOF.D2.129	Roof Q-Z - Roofing Material	5	5	01-Nov-22	07-Nov-22									Roof Q-Z - Roofing Material					
998	ROOF.D2.130	Roof Q-Z - Interior Wall Covering	5	5	10-Jan-23	16-Jan-23									Roof Q-Z - Interior Wall Covering					
999	ROOF.D2.131	Roof Q-Z - Wall Cap	5	5	17-Jan-23	23-Jan-23									Roof Q-Z - Wall Cap					
1000	Rooftop Equipment			89	89	15-Sep-22	25-Jan-23								▼	25-Jan-23, Rooftop Equipment				
1001	House			66	66	15-Sep-22	21-Dec-22								▼	21-Dec-22, House				
1002	MEP1	House - Rough In Roof MEP	5	5	15-Sep-22	21-Sep-22										House - Rough In Roof MEP				
1003	EQPT.D2.1990	House - Set Rooftop RTU Equipment	5	5	01-Dec-22	07-Dec-22										House - Set Rooftop RTU Equipment				
1004	EQPT.D2.1980	House - Pull and Terminate RTU Feeders	5	5	08-Dec-22	14-Dec-22											House - Pull and Terminate RTU Feeders			

█ Remaining Level of Effort █ Remaining Work ◆ Milestone
█ Actual Work █ Critical Remaining Work ▼ Summary

Is this Admin or Back of house?

House - Rough In Roof MEP

House - Set Rooftop RTU Equipment


House - Pull and Terminate RTU Feeders


QTS HIL2 DC2, DC3, DC5 Construction Schedule				Classic Schedule Layout					12-Jul-22 15:36									
#	Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	2022					2023					2024	
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	
1005		EQPT.D2.1970 House - Mechanical RTU Final Connections	5	5	15-Dec-22	21-Dec-22												
1006		MPOE/BDF		20	20	25-Oct-22	22-Nov-22											
1007		MEP2 MPOE/BDF - Rough In Roof MEP		5	5	25-Oct-22	31-Oct-22											
1008		EQPT.D2.2000 MPOE/BDF - Set Rooftop ACCU Equipment		5	5	01-Nov-22	07-Nov-22											
1009		EQPT.D2.2010 MPOE/BDF - Pull and Terminate ACCU Feeders		5	5	08-Nov-22	15-Nov-22											
1010		EQPT.D2.2020 MPOE/BDF - Mechanical ACCU Final Connections		5	5	16-Nov-22	22-Nov-22											
1011		DH A - B		78	78	30-Sep-22	25-Jan-23											
1012		MEP3 DH A/B - Rough In Roof MEP		5	5	30-Sep-22	06-Oct-22											
1013		EQPT.D2.2080 DH A/B - Set Rooftop ACCU Equipment		5	5	05-Jan-23	11-Jan-23											
1014		EQPT.D2.2070 DH A/B - Pull and Terminate ACCU Feeders		5	5	12-Jan-23	18-Jan-23											
1015		EQPT.D2.2060 Mechanical ACCU Final Connections DH AB		5	5	19-Jan-23	25-Jan-23											
1016		DH C - D		20	20	08-Nov-22	08-Dec-22											
1017		MEP4 DH C/D - Rough In Roof MEP		5	5	08-Nov-22	15-Nov-22											
1018		EQPT.D2.2030 DH C/D - Set Rooftop ACCU Equipment		5	5	16-Nov-22	22-Nov-22											
1019		EQPT.D2.2040 DH C/D - Pull and Terminate ACCU Feeders		5	5	23-Nov-22	01-Dec-22											
1020		EQPT.D2.2050 DH C/D - Mechanical ACCU Final Connections		5	5	02-Dec-22	08-Dec-22											
1021		Equipment Yard		164	164	19-Jul-22	15-Mar-23											
1022		Medium Voltage Ductbank		57	57	19-Jul-22	06-Oct-22											
1023		EXCV.D2.1000 Excavate Medium Voltage Underground - Sequence 1		3	3	19-Jul-22	21-Jul-22											
1024		EXCV.D2.1010 Excavate Medium Voltage Underground - Sequence 2		9	9	22-Jul-22	03-Aug-22											
1025		MVDP.D2.100 Install Medium Voltage Underground - Sequence 1		2	2	22-Jul-22	25-Jul-22											
1026		EXCV.D2.1020 Excavate Medium Voltage Underground - Sequence 3		7	7	04-Aug-22	12-Aug-22											
1027		MVDP.D2.101 Install Medium Voltage Underground - Sequence 2		8	8	04-Aug-22	15-Aug-22											
1028		EXCV.D2.1030 Excavate Medium Voltage Underground - Sequence 4		8	8	15-Aug-22	24-Aug-22											
1029		MVDP.D2.102 Install Medium Voltage Underground - Sequence 3		7	7	15-Aug-22	23-Aug-22											
1030		EXCV.D2.1040 Excavate Medium Voltage Underground - Sequence 5		16	16	25-Aug-22	16-Sep-22											
1031		MVDP.D2.103 Install Medium Voltage Underground - Sequence 4		8	8	25-Aug-22	06-Sep-22											
1032		EXCV.D2.1050 Excavate Medium Voltage Underground - North Vault Group 1		5	5	19-Sep-22	23-Sep-22											
1033		MVDP.D2.104 Install Medium Voltage Underground - Sequence 5		14	14	19-Sep-22	06-Oct-22											
1034		EXCV.D2.1060 Excavate Medium Voltage Underground - North Vault Group 2		5	5	26-Sep-22	30-Sep-22											
1035		MVDP.D2.105 Install Medium Voltage Underground - North Vault Group 1		4	4	26-Sep-22	29-Sep-22											
1036		MVDP.D2.106 Install Medium Voltage Underground - North Vault Group 2		4	4	03-Oct-22	06-Oct-22											
1037		Equipment Yard Pads and Set Equipment		69	69	06-Dec-22	15-Mar-23											
1038		MPOE/BDF Pads and Set Equipment		28	28	06-Dec-22	16-Jan-23											
1039		SURV.D2.1 Survey MPOE/BDF Equipment Foundations		1	1	06-Dec-22	06-Dec-22											
1040		Pod Pads and Set Equipment		25	25	07-Dec-22	12-Jan-23											
1041		EXCV.D Yard MPOE/BDF - Excavate UPS Pod Foundations		2	2	07-Dec-22	08-Dec-22											
1042		CONC.I Yard MPOE/BDF - Form UPS Pod Foundations MPOE BDF		2	2	08-Dec-22	09-Dec-22											
1043		CONC.I Yard MPOE/BDF - Rebar UPS Pod Foundations		2	2	09-Dec-22	12-Dec-22											
1044		CONC.I Yard MPOE/BDF - Pour UPS Pod Foundations		3	3	13-Dec-22	15-Dec-22											
1045		CONC.I Yard MPOE/BDF - Cure UPS Pod Foundations		5	5	16-Dec-22	22-Dec-22											
1046		CONC.I Yard MPOE/BDF - Install Steel Rails UPS Pod Foundations		3	3	23-Dec-22	28-Dec-22											
1047		EQPT.D Yard MPOE/BDF - Set UPS Pods		5	5	29-Dec-22	05-Jan-23											
1048		EQPT.D Yard MPOE/BDF - Pull and Terminate UPS Pods		5	5	06-Jan-23	12-Jan-23											
1049		Transformer Pads and Set Equipment		23	23	07-Dec-22	10-Jan-23											
1050		EXCV.D Yard MPOE/BDF - Excavation Transformer Foundations		2	2	07-Dec-22	08-Dec-22											
1051		CONC.I Yard MPOE/BDF - Form Transformer Foundations		2	2	08-Dec-22	09-Dec-22											
1052		CONC.I Yard MPOE/BDF - Rebar Transformer Foundations		2	2	09-Dec-22	12-Dec-22											

█ Remaining Level of Effort █ Remaining Work ◆ Milestone
█ Actual Work █ Critical Remaining Work ▼ Summary

QTS HIL2 DC2, DC3, DC5 Construction Schedule				Classic Schedule Layout						12-Jul-22 15:36									
#	Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	2022					2023					2024		
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2		
1053		CONC.I Yard MPOE/BDF - Pour Transformer Foundations	1	1	16-Dec-22	16-Dec-22						I	Yard MPOE/BDF - Pour Transformer Foundations						
1054		CONC.I Yard MPOE/BDF - Cure Transformer Foundations		5	5	19-Dec-22	23-Dec-22					I	Yard MPOE/BDF - Cure Transformer Foundations						
1055		EQPT.D Yard MPOE/BDF - Set Transformers		5	5	27-Dec-22	03-Jan-23					■	Yard MPOE/BDF - Set Transformers						
1056		EQPT.D Yard MPOE/BDF - Pull and Terminate Transformers		5	5	04-Jan-23	10-Jan-23					■	Yard MPOE/BDF - Pull and Terminate Transformers						
1057		Generator Pads and Set Equipment		25	25	09-Dec-22	16-Jan-23					▼	16-Jan-23, Generator Pads and Set Equipment						
1058		EXCV.D Yard MPOE/BDF - Excavation Generator Foundations		2	2	09-Dec-22	12-Dec-22					I	Yard MPOE/BDF - Excavation Generator Foundations						
1059		CONC.I Yard MPOE/BDF - Form Generator Foundations		2	2	12-Dec-22	13-Dec-22					I	Yard MPOE/BDF - Form Generator Foundations						
1060		CONC.I Yard MPOE/BDF - Rebar Generator Foundations		3	3	13-Dec-22	15-Dec-22					I	Yard MPOE/BDF - Rebar Generator Foundations						
1061		CONC.I Yard MPOE/BDF - Pour Generator Foundations		4	4	19-Dec-22	22-Dec-22					I	Yard MPOE/BDF - Pour Generator Foundations						
1062		CONC.I Yard MPOE/BDF - Cure Generator Foundations		5	5	23-Dec-22	30-Dec-22					■	Yard MPOE/BDF - Cure Generator Foundations						
1063		EQPT.D Yard MPOE/BDF - Set Generators		5	5	03-Jan-23	09-Jan-23					■	Yard MPOE/BDF - Set Generators						
1064		EQPT.D Yard MPOE/BDF - Pull and Terminate Generators		5	5	10-Jan-23	16-Jan-23					▼	31-Jan-23, Data Hall A and B Pads and Set Equipment						
1065		Data Hall A and B Pads and Set Equipment		36	36	09-Dec-22	31-Jan-23					I	Survey DH A/B - Equipment Foundations						
1066		SURV.D2.1 Survey DH A/B - Equipment Foundations		1	1	09-Dec-22	09-Dec-22					▼	23-Jan-23, Transformer Pads and Set Equipment						
1067		Transformer Pads and Set Equipment		20	20	23-Dec-22	23-Jan-23					■	Yard DH A/B - Excavation Transformer Foundations						
1068		EXCV.D Yard DH A/B - Excavation Transformer Foundations		2	2	23-Dec-22	27-Dec-22					I	Yard DH A/B - Form Transformer Foundations DH AB						
1069		CONC.I Yard DH A/B - Form Transformer Foundations DH AB		2	2	27-Dec-22	28-Dec-22					I	Yard DH A/B - Rebar Transformer Foundations						
1070		CONC.I Yard DH A/B - Rebar Transformer Foundations		2	2	28-Dec-22	29-Dec-22					I	Yard DH A/B - Pour Transformer Foundations						
1071		CONC.I Yard DH A/B - Pour Transformer Foundations		1	1	30-Dec-22	30-Dec-22					■	Yard DH A/B - Cure Transformer Foundations						
1072		CONC.I Yard DH A/B - Cure Transformer Foundations		5	5	03-Jan-23	09-Jan-23					■	Yard DH A/B - Set Transformers						
1073		EQPT.D Yard DH A/B - Set Transformers		5	5	10-Jan-23	16-Jan-23					■	Yard DH A/B - Pull and Terminate Transformers						
1074		EQPT.D Yard DH A/B - Pull and Terminate Transformers		5	5	17-Jan-23	23-Jan-23					▼	31-Jan-23, Generator Pads and Set Equipment						
1075		Generator Pads and Set Equipment		24	24	28-Dec-22	31-Jan-23					I	Yard DH A/B - Excavation Generator Foundations						
1076		EXCV.D Yard DH A/B - Excavation Generator Foundations		2	2	28-Dec-22	29-Dec-22					I	Yard DH A/B - Form Generator Foundations						
1077		CONC.I Yard DH A/B - Rebar Generator Foundations		2	2	29-Dec-22	30-Dec-22					■	Yard DH A/B - Pour Generator Foundations						
1078		CONC.I Yard DH A/B - Pour Generator Foundations		3	3	30-Dec-22	04-Jan-23					I	Yard DH A/B - Cure Generator Foundations						
1079		CONC.I Yard DH A/B - Cure Generator Foundations		4	4	05-Jan-23	10-Jan-23					■	Yard DH A/B - Set Generators						
1080		CONC.I Yard DH A/B - Set Generators		5	5	11-Jan-23	17-Jan-23					■	Yard DH A/B - Pull and Terminate Generators						
1081		EQPT.D Yard DH A/B - Pull and Terminate Generators		5	5	18-Jan-23	24-Jan-23					▼	31-Jan-23, Medium Voltage Pads and Set Equipment						
1082		Medium Voltage Pads and Set Equipment		22	22	30-Dec-22	31-Jan-23					■	Yard DH A/B - Excavation MV Pads						
1083		EXCV.D Yard DH A/B - Excavation MV Pads		2	2	30-Dec-22	03-Jan-23					I	Yard DH A/B - Form MV Pads						
1084		CONC.I Yard DH A/B - Form MV Pads		2	2	04-Jan-23	05-Jan-23					■	Yard DH A/B - Rebar MV Foundations						
1085		CONC.I Yard DH A/B - Rebar MV Foundations		3	3	06-Jan-23	10-Jan-23					I	Yard DH A/B - Pour MV Pads						
1086		CONC.I Yard DH A/B - Pour MV Pads		4	4	11-Jan-23	16-Jan-23					■	Yard DH A/B - Cure MV Pads						
1087		CONC.I Yard DH A/B - Cure MV Pads		5	5	17-Jan-23	23-Jan-23					I	Yard DH A/B - Set MV Equipment						
1088		EQPT.D Yard DH A/B - Set MV Equipment		5	5	24-Jan-23	30-Jan-23					■	Yard DH A/B - Pull and Terminate MV Feeders						
1089		EQPT.D Yard DH A/B - Pull and Terminate MV Feeders		5	5	25-Jan-23	31-Jan-23					▼	15-Mar-23, Data Hall C and D Pads and Set Equipment						
1090		Data Hall C and D Pads and Set Equipment		42	42	16-Jan-23	15-Mar-23					I	Survey DH C/D Equipment Foundations						
1091		SURV.D2.1 Survey DH C/D Equipment Foundations		1	1	16-Jan-23	16-Jan-23					▼	13-Feb-23, Transformer Pads and Set Equipment						
1092		Transformer Pads and Set Equipment		20	20	17-Jan-23	13-Feb-23					I	Yard DH C/D - Excavation Transformer Foundations						
1093		EXCV.D Yard DH C/D - Excavation Transformer Foundations		2	2	17-Jan-23	18-Jan-23					I	Yard DH C/D - Form Transformer Foundations						
1094		CONC.I Yard DH C/D - Form Transformer Foundations		2	2	18-Jan-23	19-Jan-23					I	Yard DH C/D - Rebar Transformer Foundations						
1095		CONC.I Yard DH C/D - Rebar Transformer Foundations		2	2	19-Jan-23	20-Jan-23					I	Yard DH C/D - Pour Transformer Foundations						
1096		CONC.I Yard DH C/D - Pour Transformer Foundations		1	1	23-Jan-23	23-Jan-23					I	Yard DH C/D - Cure Transformer Foundations						
1097		CONC.I Yard DH C/D - Cure Transformer Foundations		5	5	24-Jan-23	30-Jan-23					■	Yard DH C/D - Set Transformers						
1098		EQPT.D Yard DH C/D - Set Transformers		5	5	31-Jan-23	06-Feb-23					■	Yard DH C/D - Pull and Terminate Transformers						
1099		EQPT.D Yard DH C/D - Pull and Terminate Transformers		5	5	07-Feb-23	13-Feb-23												
1100																			

QTS HIL2 DC2, DC3, DC5 Construction Schedule				Classic Schedule Layout					12-Jul-22 15:36									
#	Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	2022					2023					2024	
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	
1101		Generator Pads and Set Equipment	39	39	19-Jan-23	15-Mar-23												15-Mar-23, Generator Pads and Set Equipment
1102		EXCV.D Yard DH C/D - Excavation Generator Foundations	2	2	19-Jan-23	20-Jan-23												Yard DH C/D - Excavation Generator Foundations
1103		CONC.I Yard DH C/D - Form Generator Foundations	2	2	20-Jan-23	23-Jan-23												Yard DH C/D - Form Generator Foundations
1104		CONC.I Yard DH C/D - Rebar Generator Foundations	3	3	23-Jan-23	25-Jan-23												Yard DH C/D - Rebar Generator Foundations
1105		CONC.I Yard DH C/D - Pour Generator Foundations	4	4	26-Jan-23	31-Jan-23												Yard DH C/D - Pour Generator Foundations
1106		CONC.I Yard DH C/D - Cure Generator Foundations	5	5	01-Feb-23	07-Feb-23												Yard DH C/D - Cure Generator Foundations
1107		EQPT.D Yard DH C/D - Set Generators	5	5	08-Feb-23	14-Feb-23												Yard DH C/D - Set Generators
1108		EQPT.D Yard DH C/D - Pull and Terminate Generators	20	20	15-Feb-23	15-Mar-23												Yard DH C/D - Pull and Terminate Generators
1109		Medium Voltage Pads and Set Equipment	21	21	23-Jan-23	21-Feb-23												21-Feb-23, Medium Voltage Pads and Set Equipment
1110		EXCV.D Yard DH C/D - Excavation MV Pads	2	2	23-Jan-23	24-Jan-23												Yard DH C/D - Excavation MV Pads
1111		CONC.I Yard DH C/D - Form MV Pads	2	2	25-Jan-23	26-Jan-23												Yard DH C/D - Form MV Pads
1112		CONC.I Yard DH C/D - Rebar MV Foundations	2	2	27-Jan-23	30-Jan-23												Yard DH C/D - Rebar MV Foundations
1113		CONC.I Yard DH C/D - Pour MV Pads	4	4	31-Jan-23	03-Feb-23												Yard DH C/D - Pour MV Pads
1114		CONC.I Yard DH C/D - Cure MV Pads	5	5	06-Feb-23	10-Feb-23												Yard DH C/D - Cure MV Pads
1115		EQPT.D Yard DH C/D - Set MV Equipment	5	5	13-Feb-23	17-Feb-23												Yard DH C/D - Set MV Equipment
1116		EQPT.D Yard DH C/D - Pull and Terminate MV Feeders	5	5	14-Feb-23	21-Feb-23												Yard DH C/D - Pull and Terminate MV Feeders
1117		House	20	20	23-Dec-22	23-Jan-23												23-Jan-23, House
1118		EXCV.D.1 Yard House - Excavation Transformer Foundations	2	2	23-Dec-22	27-Dec-22												Yard House - Excavation Transformer Foundations
1119		CONC.D.2. Yard House - Form Transformer Foundations DH AB	2	2	27-Dec-22	28-Dec-22												Yard House - Form Transformer Foundations DH AB
1120		CONC.D.2. Yard House - Rebar Transformer Foundations	2	2	28-Dec-22	29-Dec-22												Yard House - Rebar Transformer Foundations
1121		CONC.D.2. Yard House - Pour Transformer Foundations	1	1	30-Dec-22	30-Dec-22												Yard House - Pour Transformer Foundations
1122		CONC.D.2. Yard House - Cure Transformer Foundations	5	5	03-Jan-23	09-Jan-23												Yard House - Cure Transformer Foundations
1123		EQPT.D.2.2 Yard House - Set Transformers	5	5	10-Jan-23	16-Jan-23												Yard House - Set Transformers
1124		EQPT.D.2.2 Yard House - Pull and Terminate Transformers	5	5	17-Jan-23	23-Jan-23												Yard House - Pull and Terminate Transformers
1125		Elevators	85	85	01-Dec-22	03-Apr-23												03-Apr-23, Elevators
1126		Freight Elevator E03	61	61	30-Dec-22	28-Mar-23												28-Mar-23, Freight Elevator E03
1127		ELVT.D.2.1000 Freight Elev. 3 - Hoisting Equipment	7	7	30-Dec-22	10-Jan-23												Freight Elev. 3 - Hoisting Equipment
1128		ELVT.D.2.1010 Freight Elev. 3 - Pit Rails/Frame/Cab	5	5	11-Jan-23	17-Jan-23												Freight Elev. 3 - Pit Rails/Frame/Cab
1129		ELVT.D.2.1020 Freight Elev. 3 - Tirak & Governor Rope	5	5	18-Jan-23	24-Jan-23												Freight Elev. 3 - Tirak & Governor Rope
1130		ELVT.D.2.1030 Freight Elev. 3 - Rails	8	8	25-Jan-23	03-Feb-23												Freight Elev. 3 - Rails
1131		ELVT.D.2.1040 Freight Elev. 3 - Door entrances	4	4	06-Feb-23	09-Feb-23												Freight Elev. 3 - Door entrances
1132		ELVT.D.2.1050 Freight Elev. 3 - Duct/Wire Machine/Startup	7	7	10-Feb-23	21-Feb-23												Freight Elev. 3 - Duct/Wire Machine/Startup
1133		ELVT.D.2.1060 Freight Elev. 3 - Rope Elevator/Remove Tirak	4	4	22-Feb-23	27-Feb-23												Freight Elev. 3 - Rope Elevator/Remove Tirak
1134		ELVT.D.2.1070 Freight Elev. 3 - Pipe and Wire Hatch Devices	6	6	28-Feb-23	07-Mar-23												Freight Elev. 3 - Pipe and Wire Hatch Devices
1135		ELVT.D.2.1080 Freight Elev. 3 - Terminate Devices	8	8	08-Mar-23	17-Mar-23												Freight Elev. 3 - Terminate Devices
1136		ELVT.D.2.1090 Freight Elev. 3 - Clean Rails	2	2	20-Mar-23	21-Mar-23												Freight Elev. 3 - Clean Rails
1137		ELVT.D.2.1100 Freight Elev. 3 - Inspect	5	5	22-Mar-23	28-Mar-23												Freight Elev. 3 - Inspect
1138		Freight Elevator E02A and E02B	85	85	01-Dec-22	03-Apr-23												03-Apr-23, Freight Elevator E02A and E02B
1139		ELVT.D.2.1110 Freight Elev. E02A/E02B - Hoisting Equipment	10	10	01-Dec-22	14-Dec-22												Freight Elev. E02A/E02B - Hoisting Equipment
1140		ELVT.D.2.1120 Freight Elev. E02A/E02B - Pit Rails/Frame/Cab	7	7	15-Dec-22	23-Dec-22												Freight Elev. E02A/E02B - Pit Rails/Frame/Cab
1141		ELVT.D.2.1130 Freight Elev. E02A/E02B - Tirak & Governor Rope	7	7	27-Dec-22	05-Jan-23												Freight Elev. E02A/E02B - Tirak & Governor Rope
1142		ELVT.D.2.1140 Freight Elev. E02A/E02B - Rails	10	10	06-Jan-23	19-Jan-23												Freight Elev. E02A/E02B - Rails
1143		ELVT.D.2.1150 Freight Elev. E02A/E02B - Door entrances	6	6	20-Jan-23	27-Jan-23												Freight Elev. E02A/E02B - Door entrances
1144		ELVT.D.2.1160 Freight Elev. E02A/E02B - Duct/Wire Machine/Startup	9	9	30-Jan-23	09-Feb-23												Freight Elev. E02A/E02B - Duct/Wire Machine/Startup
1145		ELVT.D.2.1170 Freight Elev. E02A/E02B - Rope Elevator/Remove Tirak	6	6	10-Feb-23	17-Feb-23												Freight Elev. E02A/E02B - Rope Elevator/Remove Tirak
1146		ELVT.D.2.1180 Freight Elev. E02A/E02B - Pipe and Wire Hatch Devices	8	8	21-Feb-23	02-Mar-23												Freight Elev. E02A/E02B - Pipe and Wire Hatch Devices
1147		ELVT.D.2.1190 Freight Elev. E02A/E02B - Terminate Devices	10	10	03-Mar-23	16-Mar-23												Freight Elev. E02A/E02B - Terminate Devices
1148		ELVT.D.2.1200 Freight Elev. E02A/E02B - Clean Rails	4	4	17-Mar-23	22-Mar-23												Freight Elev. E02A/E02B - Clean Rails



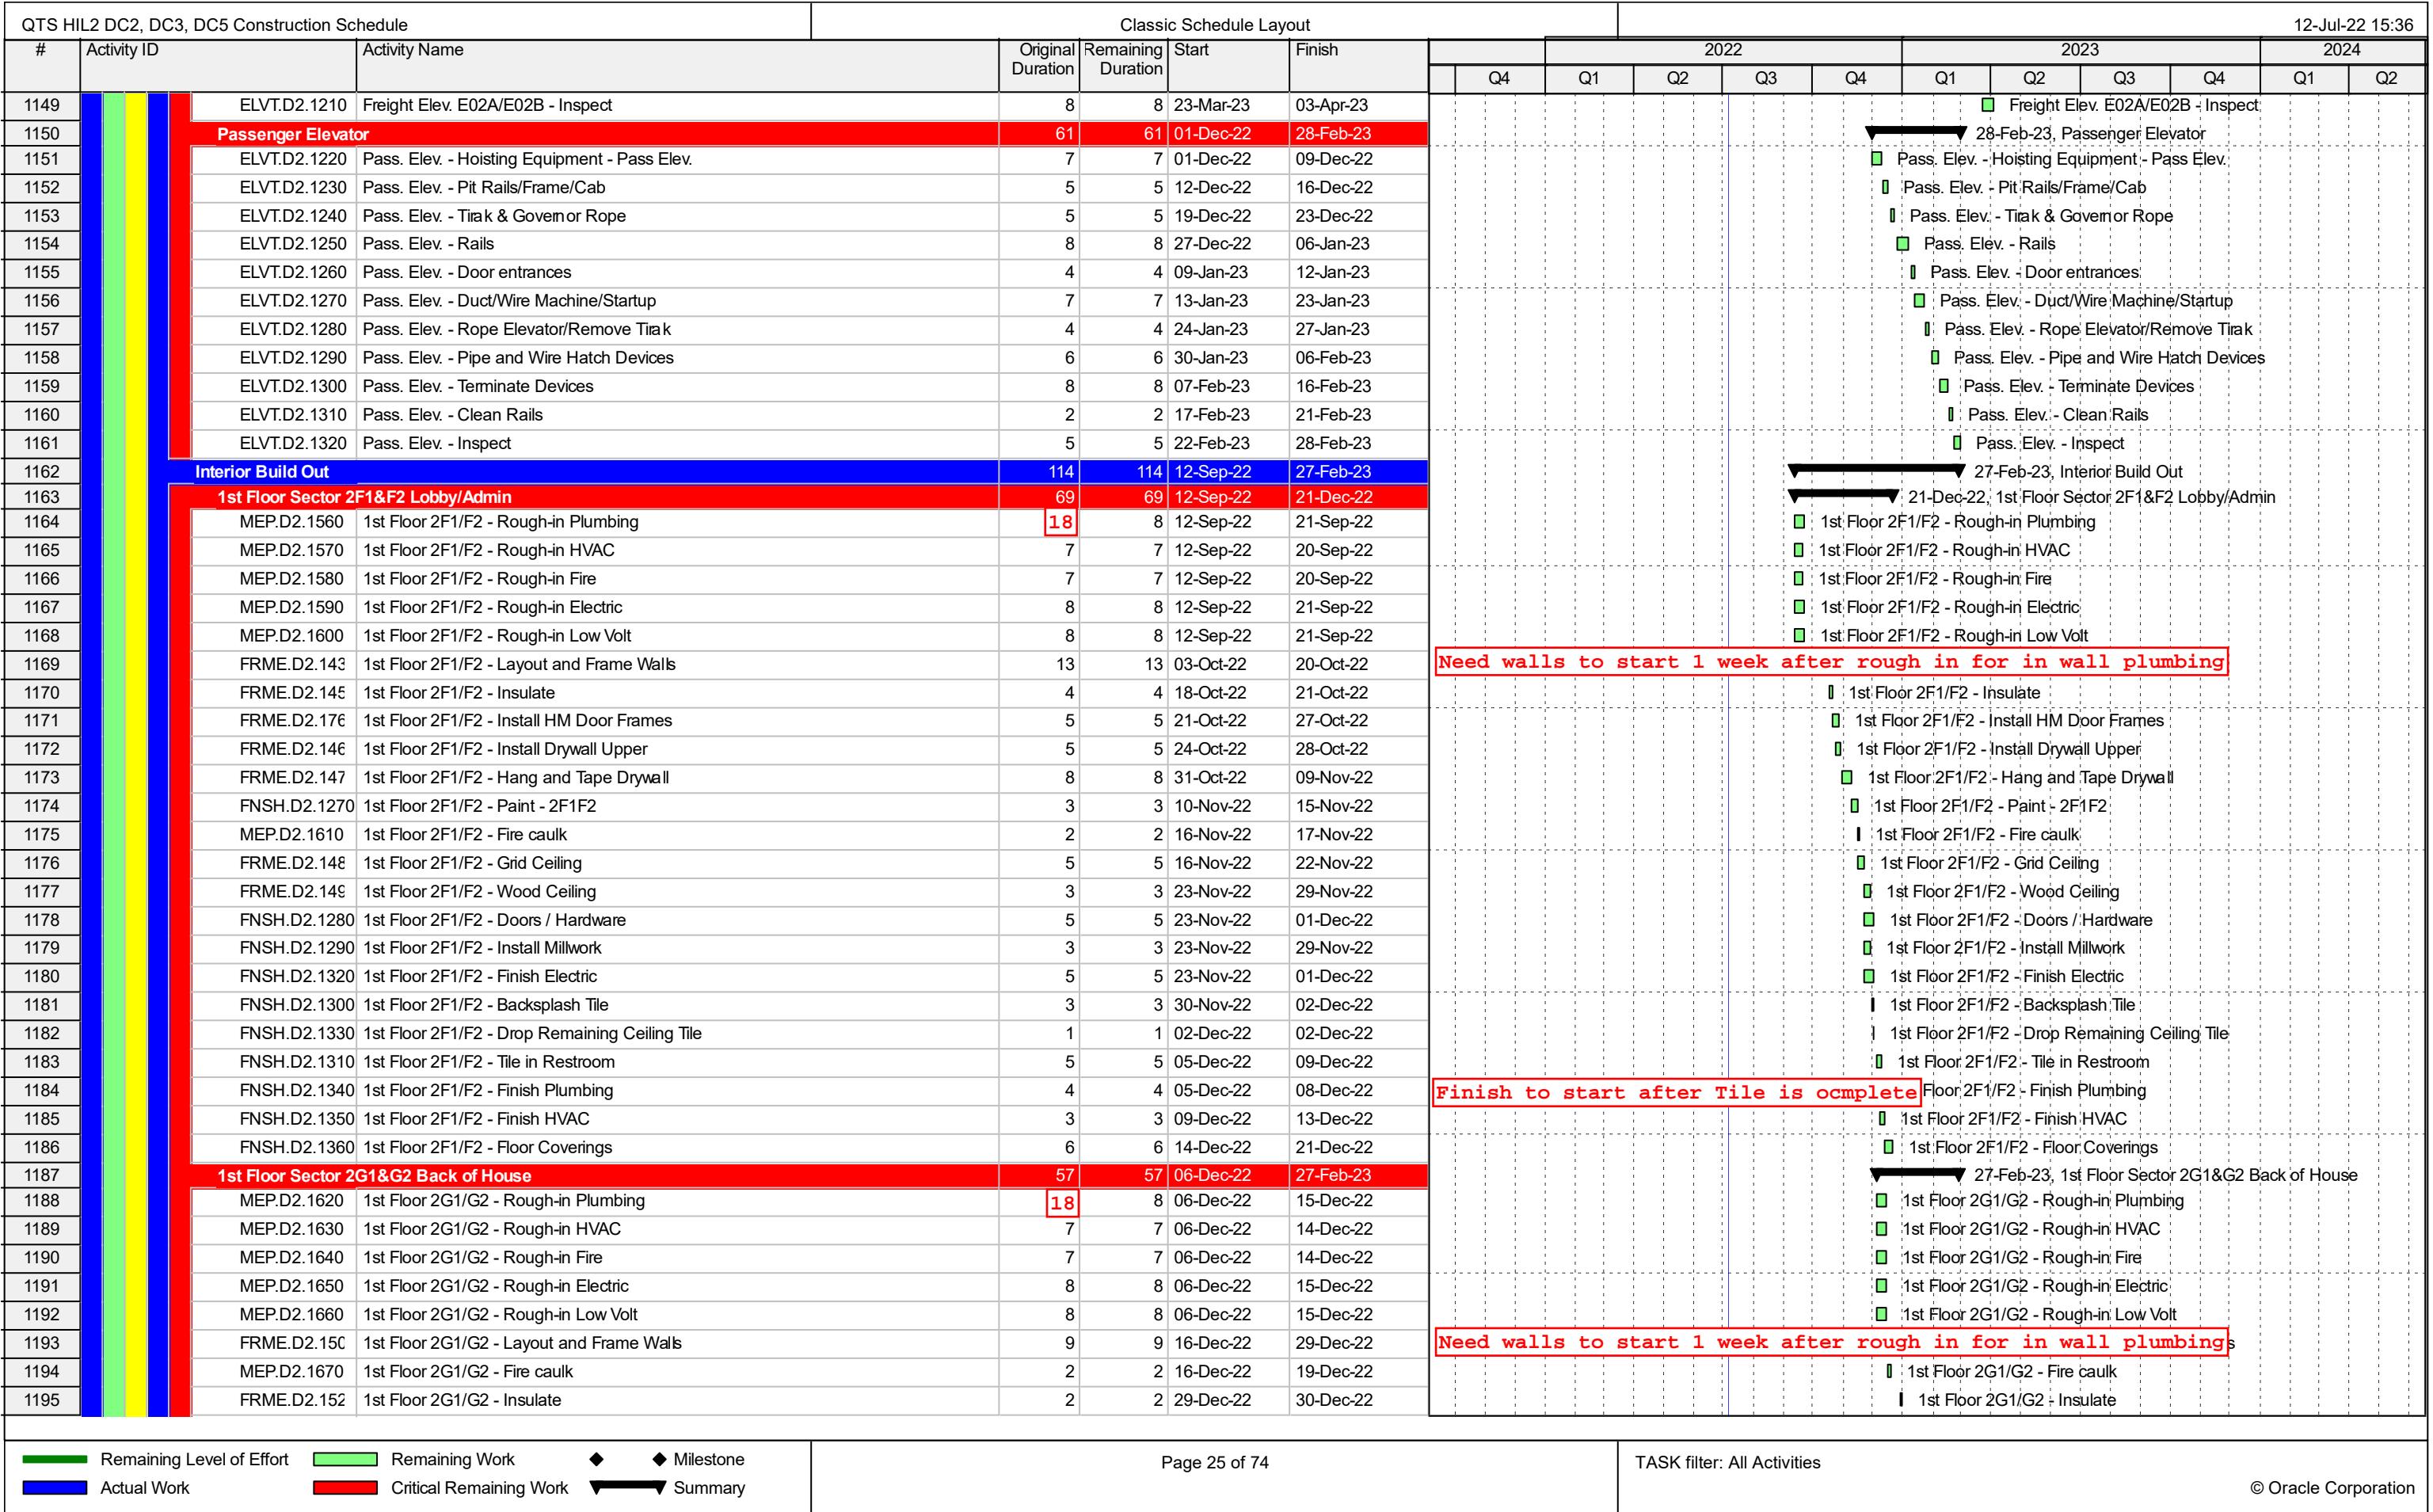



QTS HIL2 DC2, DC3, DC5 Construction Schedule				Classic Schedule Layout					12-Jul-22 15:36									
#	Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	2022					2023				2024		
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	
1196	FRME.D2.153	1st Floor 2G1/G2 - Install Drywall Upper	5	5	03-Jan-23	09-Jan-23						1st Floor 2G1/G2 - Install Drywall Upper						
1197	FRME.D2.154	1st Floor 2G1/G2 - Hang and Tape Drywall	7	7	10-Jan-23	18-Jan-23						1st Floor 2G1/G2 - Hang and Tape Drywall						
1198	FNSH.D2.1390	1st Floor 2G1/G2 - Tile in Restroom	3	3	10-Jan-23	12-Jan-23						1st Floor 2G1/G2 - Tile in Restroom						
1199	FNSH.D2.1400	1st Floor 2G1/G2 - Backsplash Tile	5	5	13-Jan-23	19-Jan-23						1st Floor 2G1/G2 - Backsplash Tile						
1200	FNSH.D2.1370	1st Floor 2G1/G2 - Paint	3	3	19-Jan-23	23-Jan-23						1st Floor 2G1/G2 - Paint						
1201	FRME.D2.155	1st Floor 2G1/G2 - Grid Ceiling	5	5	24-Jan-23	30-Jan-23						1st Floor 2G1/G2 - Grid Ceiling						
1202	FRME.D2.156	1st Floor 2G1/G2 - Wood Ceiling	3	3	31-Jan-23	02-Feb-23						1st Floor 2G1/G2 - Wood Ceiling						
1203	FNSH.D2.1380	1st Floor 2G1/G2 - Doors & Hardware	5	5	31-Jan-23	06-Feb-23						1st Floor 2G1/G2 - Doors & Hardware						
1204	FRME.D2.157	1st Floor 2G1/G2 - Install Millwork	3	3	31-Jan-23	02-Feb-23						1st Floor 2G1/G2 - Install Millwork						
1205	FNSH.D2.1410	1st Floor 2G1/G2 - Finish Electric	5	5	31-Jan-23	06-Feb-23						1st Floor 2G1/G2 - Finish Electric						
1206	FNSH.D2.1420	1st Floor 2G1/G2 - Drop Remaining Ceiling Tile	1	1	07-Feb-23	07-Feb-23						1st Floor 2G1/G2 - Drop Remaining Ceiling Tile						
1207	FNSH.D2.1430	1st Floor 2G1/G2 - Finish Plumbing	4	4	08-Feb-23	13-Feb-23						1st Floor 2G1/G2 - Finish Plumbing						
1208	FNSH.D2.1440	1st Floor 2G1/G2 - Finish HVAC	3	3	14-Feb-23	16-Feb-23						1st Floor 2G1/G2 - Finish HVAC						
1209	FNSH.D2.1450	1st Floor 2G1/G2 - Floor Coverings	6	6	17-Feb-23	27-Feb-23						1st Floor 2G1/G2 - Floor Coverings						
1210	2nd Floor Sector 2F1&F2 Admin			54	54	19-Sep-22	07-Dec-22						07-Dec-22, 2nd Floor Sector 2F1&F2 Admin					
1211	FRME.D2.158	2nd Floor 2F1/F2 - Layout and Frame Walls	13	13	19-Sep-22	05-Oct-22						2nd Floor 2F1/F2 - Layout and Frame Walls						
1212	MEP.D2.1680	2nd Floor 2F1/F2 - Rough-in Plumbing	18	18	19-Sep-22	28-Sep-22						2nd Floor 2F1/F2 - Rough-in Plumbing						
1213	MEP.D2.1690	2nd Floor 2F1/F2 - Rough-in HVAC	18	18	19-Sep-22	27-Sep-22						2nd Floor 2F1/F2 - Rough-in HVAC						
1214	MEP.D2.1700	2nd Floor 2F1/F2 - Rough-in Fire	7	7	19-Sep-22	27-Sep-22						2nd Floor 2F1/F2 - Rough-in Fire						
1215	MEP.D2.1710	2nd Floor 2F1/F2 - Rough-in Electric	8	8	19-Sep-22	28-Sep-22						2nd Floor 2F1/F2 - Rough-in Electric						
1216	MEP.D2.1720	2nd Floor 2F1/F2 - Rough-in Low Volt	8	8	19-Sep-22	28-Sep-22						2nd Floor 2F1/F2 - Rough-in Low Volt						
1217	FRME.D2.182	2nd Floor 2F1/F2 - Install HM Door Frames	5	5	19-Sep-22	23-Sep-22						2nd Floor 2F1/F2 - Install HM Door Frames						
1218	MEP.D2.1730	2nd Floor 2F1/F2 - Fire caulk	2	2	29-Sep-22	30-Sep-22						2nd Floor 2F1/F2 - Fire caulk						
1219	FRME.D2.160	2nd Floor 2F1/F2 - Insulate	4	4	03-Oct-22	06-Oct-22						2nd Floor 2F1/F2 - Insulate						
1220	FRME.D2.161	2nd Floor 2F1/F2 - Install Drywall Upper	5	5	07-Oct-22	14-Oct-22						2nd Floor 2F1/F2 - Install Drywall Upper						
1221	FRME.D2.162	2nd Floor 2F1/F2 - Hang and Tape Drywall	8	8	17-Oct-22	26-Oct-22						2nd Floor 2F1/F2 - Hang and Tape Drywall						
1222	FNSH.D2.1460	2nd Floor 2F1/F2 - Paint	3	3	27-Oct-22	31-Oct-22						2nd Floor 2F1/F2 - Paint						
1223	FRME.D2.163	2nd Floor 2F1/F2 - Grid Ceiling	5	5	01-Nov-22	07-Nov-22						2nd Floor 2F1/F2 - Grid Ceiling						
1224	FNSH.D2.1470	2nd Floor 2F1/F2 - Doors & Hardware	5	5	08-Nov-22	15-Nov-22						2nd Floor 2F1/F2 - Doors & Hardware						
1225	FNSH.D2.1490	2nd Floor 2F1/F2 - Tile in Restroom	5	5	08-Nov-22	15-Nov-22						2nd Floor 2F1/F2 - Tile in Restroom						
1226	FNSH.D2.1500	2nd Floor 2F1/F2 - Finish Electric	5	5	08-Nov-22	15-Nov-22						2nd Floor 2F1/F2 - Finish Electric						
1227	FNSH.D2.1510	2nd Floor 2F1/F2 - Drop Remaining Ceiling Tile	1	1	16-Nov-22	16-Nov-22						2nd Floor 2F1/F2 - Drop Remaining Ceiling Tile						
1228	FNSH.D2.1520	2nd Floor 2F1/F2 - Finish Plumbing	4	4	17-Nov-22	22-Nov-22						2nd Floor 2F1/F2 - Finish Plumbing						
1229	FNSH.D2.1530	2nd Floor 2F1/F2 - Finish HVAC	3	3	23-Nov-22	29-Nov-22						2nd Floor 2F1/F2 - Finish HVAC						
1230	FNSH.D2.1540	2nd Floor 2F1/F2 - Floor Coverings	6	6	30-Nov-22	07-Dec-22						2nd Floor 2F1/F2 - Floor Coverings						
1231	2nd Floor Sector 2G1&G2 Back of House			39	39	06-Dec-22	31-Jan-23						31-Jan-23, 2nd Floor Sector 2G1&G2 Back of House					
1232	FRME.D2.166	2nd Floor 2G1/G2 - Layout and Frame Walls	9	9	06-Dec-22	16-Dec-22						2nd Floor 2G1/G2 - Layout and Frame Walls						
1233	MEP.D2.1740	2nd Floor 2G1/G2 - Rough-in Plumbing	18	18	06-Dec-22	15-Dec-22						2nd Floor 2G1/G2 - Rough-in Plumbing						
1234	MEP.D2.1750	2nd Floor 2G1/G2 - Rough-in HVAC	18	18	06-Dec-22	14-Dec-22						2nd Floor 2G1/G2 - Rough-in HVAC						
1235	MEP.D2.1760	2nd Floor 2G1/G2 - Rough-in Fire	7	7	06-Dec-22	14-Dec-22						2nd Floor 2G1/G2 - Rough-in Fire						
1236	MEP.D2.1770	2nd Floor 2G1/G2 - Rough-in Electric	8	8	06-Dec-22	15-Dec-22						2nd Floor 2G1/G2 - Rough-in Electric						
1237	MEP.D2.1780	2nd Floor 2G1/G2 - Rough-in Low Volt	8	8	06-Dec-22	15-Dec-22						2nd Floor 2G1/G2 - Rough-in Low Volt						
1238	FRME.D2.183	2nd Floor 2G1/G2 - Install HM Door Frame	5	5	06-Dec-22	12-Dec-22						2nd Floor 2G1/G2 - Install HM Door Frame						
1239	MEP.D2.1790	2nd Floor 2G1/G2 - Fire caulk	2	2	16-Dec-22	19-Dec-22						2nd Floor 2G1/G2 - Fire caulk						
1240	FRME.D2.168	2nd Floor 2G1/G2 - Insulate	2	2	20-Dec-22	21-Dec-22						2nd Floor 2G1/G2 - Insulate						
1241	FRME.D2.169	2nd Floor 2G1/G2 - Install Drywall Upper	5	5	22-Dec-22	29-Dec-22						2nd Floor 2G1/G2 - Install Drywall Upper						
1242	FRME.D2.170	2nd Floor 2G1/G2 - Hang and Tape Drywall	7	7	30-Dec-22	10-Jan-23						2nd Floor 2G1/G2 - Hang and Tape Drywall						



QTS HIL2 DC2, DC3, DC5 Construction Schedule				Classic Schedule Layout					12-Jul-22 15:36										
#	Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	2022					2023					2024		
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2		
1243		FNSH.D2.1570 2nd Floor 2G1/G2 - Tile in Restroom	3	3	30-Dec-22	04-Jan-23						2nd Floor 2G1/G2 - Tile in Restroom							
1244		FNSH.D2.1550 2nd Floor 2G1/G2 - Paint	3	3	11-Jan-23	13-Jan-23						2nd Floor 2G1/G2 - Paint							
1245		FRME.D2.172 2nd Floor 2G1/G2 - Wood Ceiling	3	3	16-Jan-23	18-Jan-23						2nd Floor 2G1/G2 - Wood Ceiling							
1246		FNSH.D2.1560 2nd Floor 2G1/G2 - Doors & Hardware	5	5	16-Jan-23	20-Jan-23						2nd Floor 2G1/G2 - Doors & Hardware							
1247		FNSH.D2.1590 2nd Floor 2G1/G2 - Finish Electric	5	5	16-Jan-23	20-Jan-23						2nd Floor 2G1/G2 - Finish Electric							
1248		FNSH.D2.1610 2nd Floor 2G1/G2 - Finish Plumbing	4	4	23-Jan-23	26-Jan-23						2nd Floor 2G1/G2 - Finish Plumbing							
1249		FNSH.D2.1620 2nd Floor 2G1/G2 - Finish HVAC	3	3	27-Jan-23	31-Jan-23						2nd Floor 2G1/G2 - Finish HVAC							
1250	Site Finishes			67	67	23-Dec-22	30-Mar-23						30-Mar-23, Site Finishes						
1251	Trash Enclosure			9	9	23-Dec-22	06-Jan-23						06-Jan-23, Trash Enclosure						
1252	FOND.D2.152	Trash Encl - Dig Footings	1	1	23-Dec-22	23-Dec-22						Trash Encl - Dig Footings							
1253	FOND.D2.153	Trash Encl - Form Footings	1	1	23-Dec-22	23-Dec-22						Trash Encl - Form Footings							
1254	FOND.D2.154	Trash Encl - Install Rebar & Bollards	1	1	27-Dec-22	27-Dec-22						Trash Encl - Install Rebar & Bollards							
1255	FOND.D2.155	Trash Encl - Inspect & Pour	1	1	27-Dec-22	27-Dec-22						Trash Encl - Inspect & Pour							
1256	CONC.D2.134	Trash Encl - Embeds for Gate	3	3	27-Dec-22	29-Dec-22						Trash Encl - Embeds for Gate							
1257	SOG.D2.1420	Trash Encl - SOG	2	2	28-Dec-22	29-Dec-22						Trash Encl - SOG							
1258	CONC.D2.135	Trash Encl - CMU - Trash Enc.	3	3	30-Dec-22	04-Jan-23						Trash Encl - CMU - Trash Enc.							
1259	CONC.D2.136	Trash Encl - Grout CMU	1	1	05-Jan-23	05-Jan-23						Trash Encl - Grout CMU							
1260	FNSH.D2.1640	Trash Encl - Install Gate	1	1	06-Jan-23	06-Jan-23						Trash Encl - Install Gate							
1261	FNSH.D2.1650	Trash Encl - Install Steel Coping	1	1	06-Jan-23	06-Jan-23						Trash Encl - Install Steel Coping							
1262	FNSH.D2.1660	Trash Encl - Paint	1	1	06-Jan-23	06-Jan-23						Trash Encl - Paint							
1263	Parking Lot			23	23	13-Feb-23	16-Mar-23						16-Mar-23, Parking Lot						
1264	UTIL.D2.1040	Park. Lot - Install/Adjust Manhole Covers	3	3	13-Feb-23	15-Feb-23						Park. Lot - Install/Adjust Manhole Covers							
1265	FOND.D2.156	Park. Lot - Rough Grade Parking Lot	2	2	13-Feb-23	14-Feb-23						Park. Lot - Rough Grade Parking Lot							
1266	FNSH.D2.1680	Park. Lot - Landscape Sleeves	3	3	13-Feb-23	15-Feb-23						Park. Lot - Landscape Sleeves							
1267	CONC.D2.136	Park. Lot - Cut Curbs	2	2	15-Feb-23	16-Feb-23						Park. Lot - Cut Curbs							
1268	UTIL.D2.1050	Park. Lot - Install Catch Basins	3	3	17-Feb-23	22-Feb-23						Park. Lot - Install Catch Basins							
1269	MEP.D2.1800	Park. Lot - Street Light Conduits	2	2	23-Feb-23	24-Feb-23						Park. Lot - Street Light Conduits							
1270	CONC.D2.137	Park. Lot - Install Curbs & Inlets	3	3	23-Feb-23	27-Feb-23						Park. Lot - Install Curbs & Inlets							
1271	CONC.D2.138	Park. Lot - Street Light Bases	5	5	27-Feb-23	03-Mar-23						Park. Lot - Street Light Bases							
1272	FOND.D2.157	Park. Lot - Fine Grade Parking Lot	2	2	06-Mar-23	07-Mar-23						Park. Lot - Fine Grade Parking Lot							
1273	ASPV.D2.1000	Park. Lot - 1st Lift Asphalt - DC2	2	2	08-Mar-23	09-Mar-23						Park. Lot - 1st Lift Asphalt - DC2							
1274	CONC.D2.139	Park. Lot - Sidewalks	3	3	10-Mar-23	14-Mar-23						Park. Lot - Sidewalks							
1275	ASPV.D2.1010	Park. Lot - 2nd Lift Asphalt	1	1	15-Mar-23	15-Mar-23						Park. Lot - 2nd Lift Asphalt							
1276	CONC.D2.140	Park. Lot - Wheel Stops	1	1	16-Mar-23	16-Mar-23						Park. Lot - Wheel Stops							
1277	CONC.D2.141	Park. Lot - Strip	1	1	16-Mar-23	16-Mar-23						Park. Lot - Strip							
1278	FNSH.D2.1670	Park. Lot - Signage	1	1	16-Mar-23	16-Mar-23						Park. Lot - Signage							
1279	Landscape and Fencing			15	15	10-Mar-23	30-Mar-23						30-Mar-23, Landscape and Fencing						
1280	CONC.D2.142	Land Scp. - Site Concrete for Fence - DC2	3	3	10-Mar-23	14-Mar-23						Land Scp. - Site Concrete for Fence - DC2							
1281	FNSH.D2.1690	Land Scp. - Landscape Power and Irrigation	10	10	15-Mar-23	28-Mar-23						Land Scp. - Landscape Power and Irrigation							
1282	FNSH.D2.1700	Land Scp. - Fill Planters	2	2	15-Mar-23	16-Mar-23						Land Scp. - Fill Planters							
1283	FNSH.D2.1720	Land Scp. - Ground Cover	5	5	15-Mar-23	21-Mar-23						Land Scp. - Ground Cover							
1284	FNSH.D2.1780	Land Scp. - Install Fence	7	7	15-Mar-23	23-Mar-23						Land Scp. - Install Fence							
1285	FNSH.D2.1710	Land Scp. - Plantings	5	5	17-Mar-23	23-Mar-23						Land Scp. - Plantings							
1286	FNSH.D2.1790	Land Scp. - Gates and Access Control	5	5	24-Mar-23	30-Mar-23						Land Scp. - Gates and Access Control							
1287	1st Floor Data Hall			139	139	14-Sep-22	05-Apr-23						05-Apr-23, 1st Floor Data Hall						
1288	House			124	124	14-Sep-22	15-Mar-23						15-Mar-23, House						
1289	Rough-In			104	104	14-Sep-22	14-Feb-23						14-Feb-23, Rough-In						
1290	FRME.D2.1	1st Floor House - Layout and Frame Walls	10	10	14-Sep-22	27-Sep-22						1st Floor House - Layout and Frame Walls							

What is house?

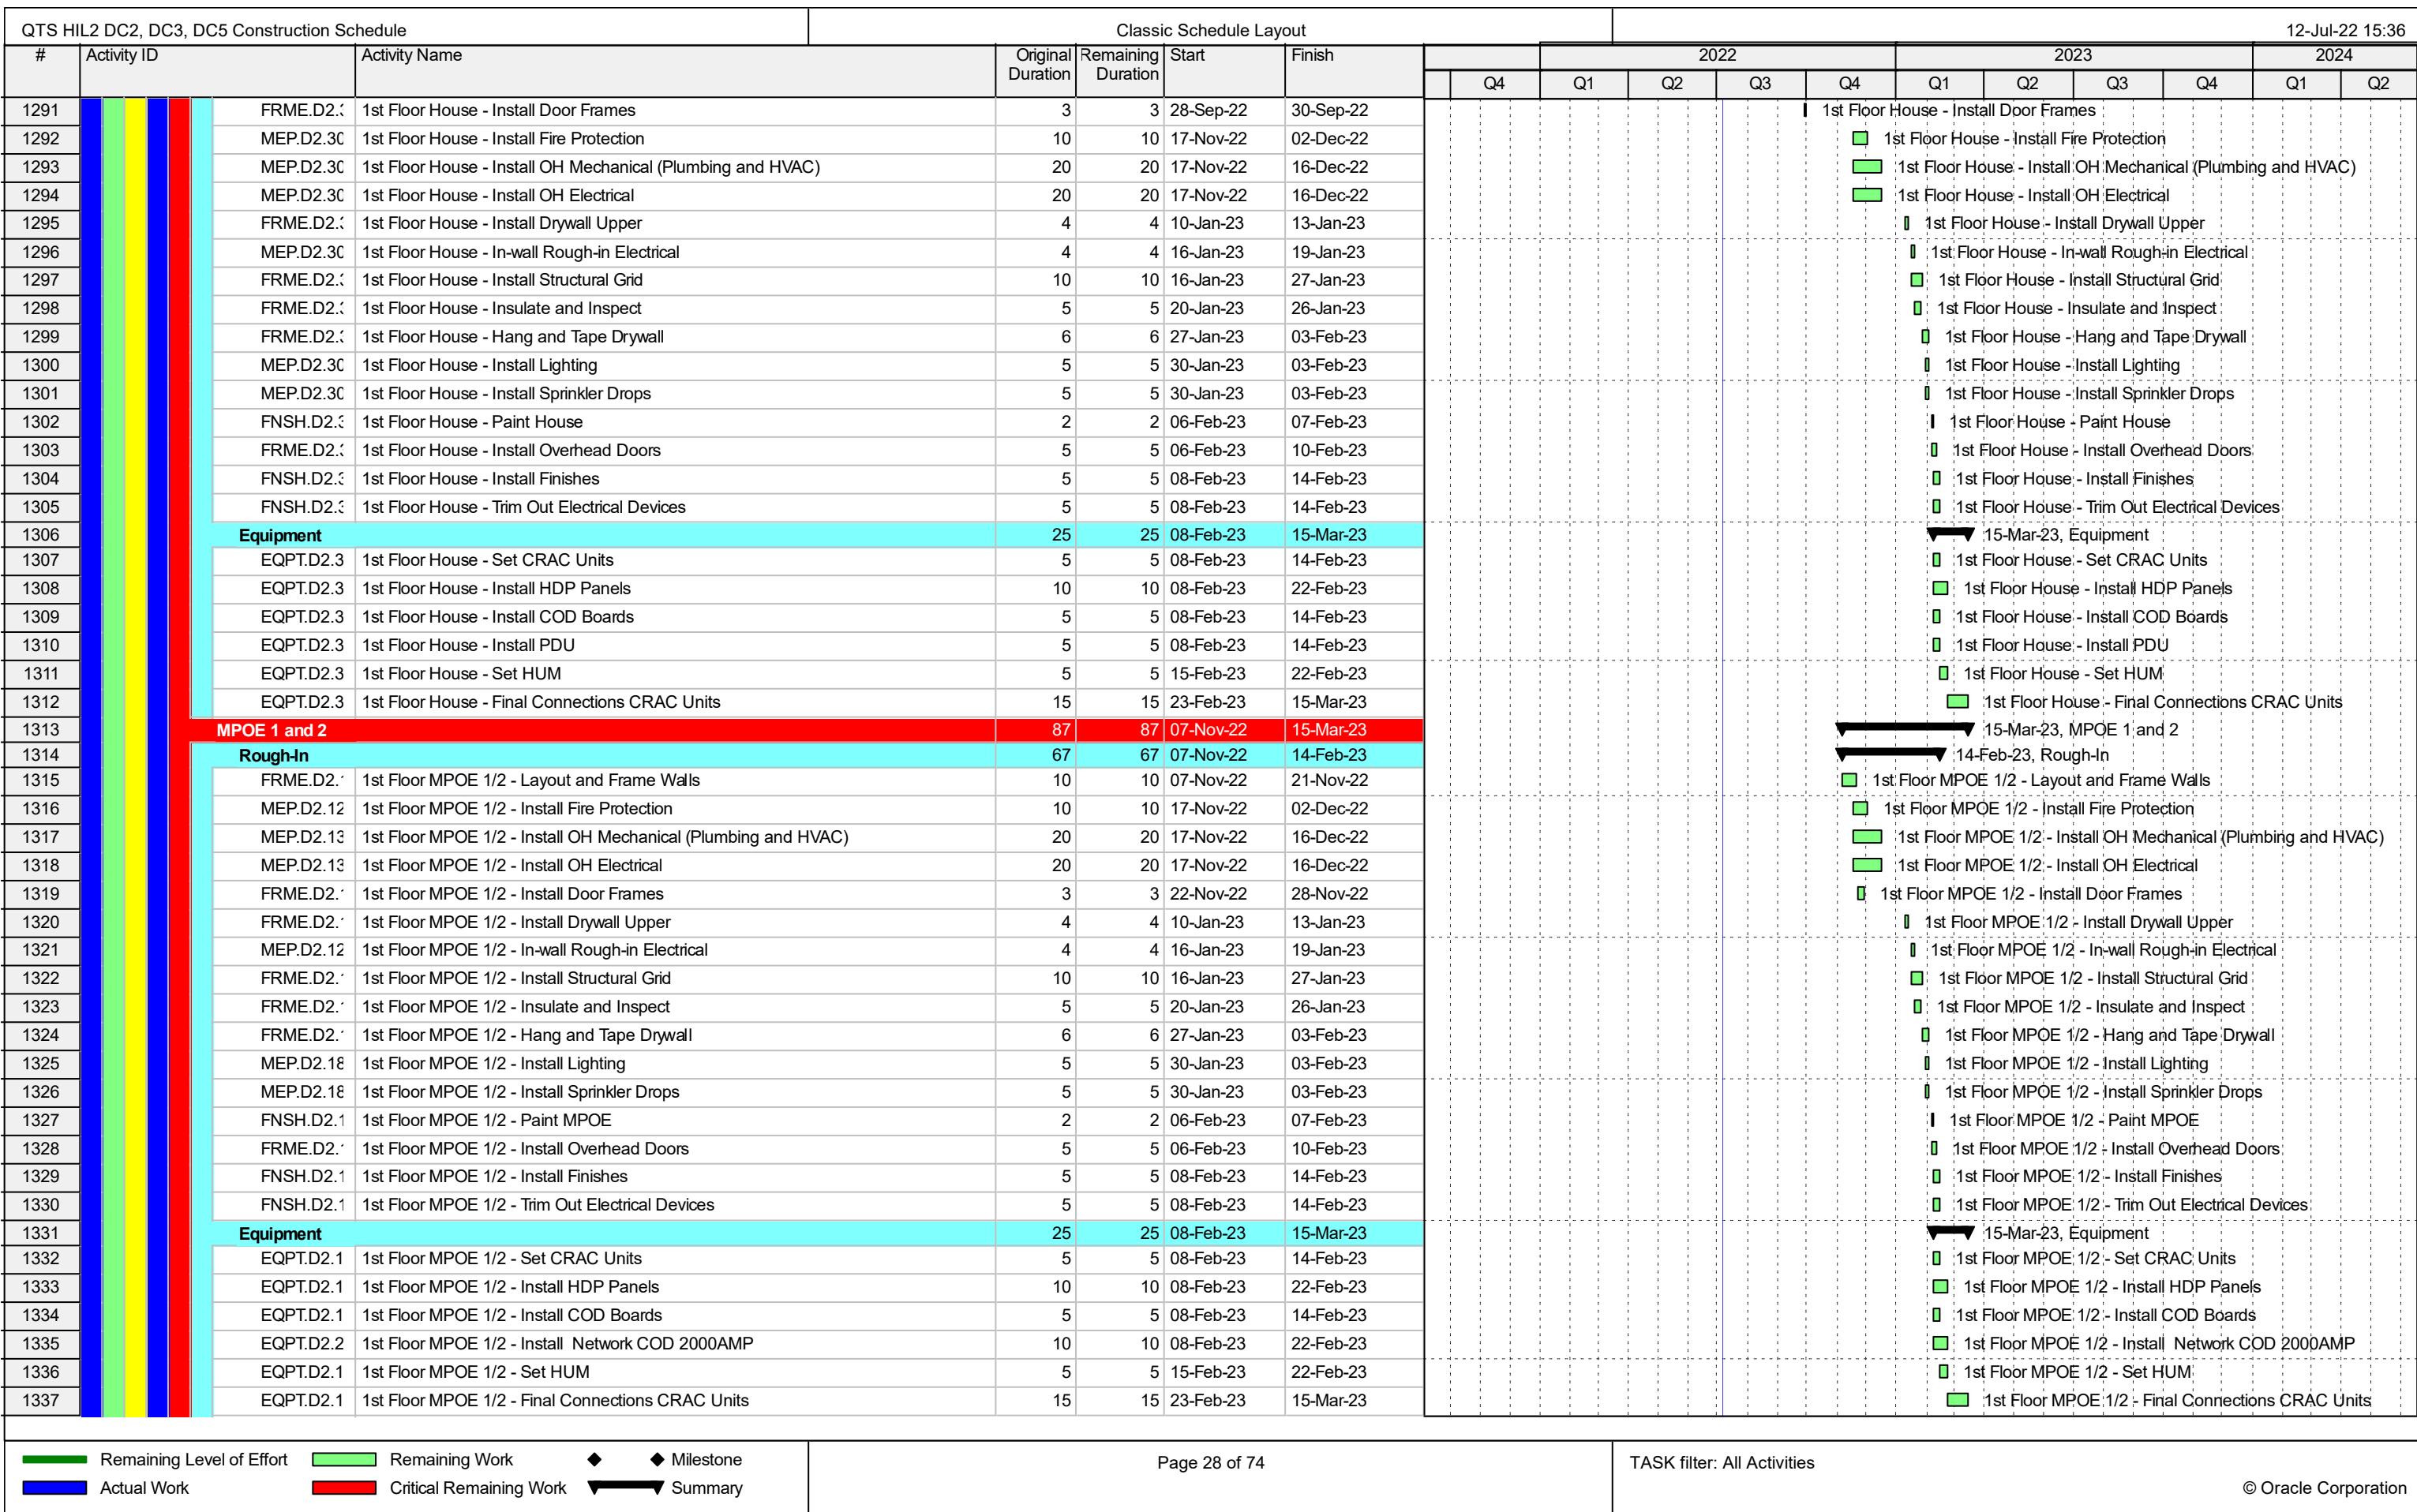

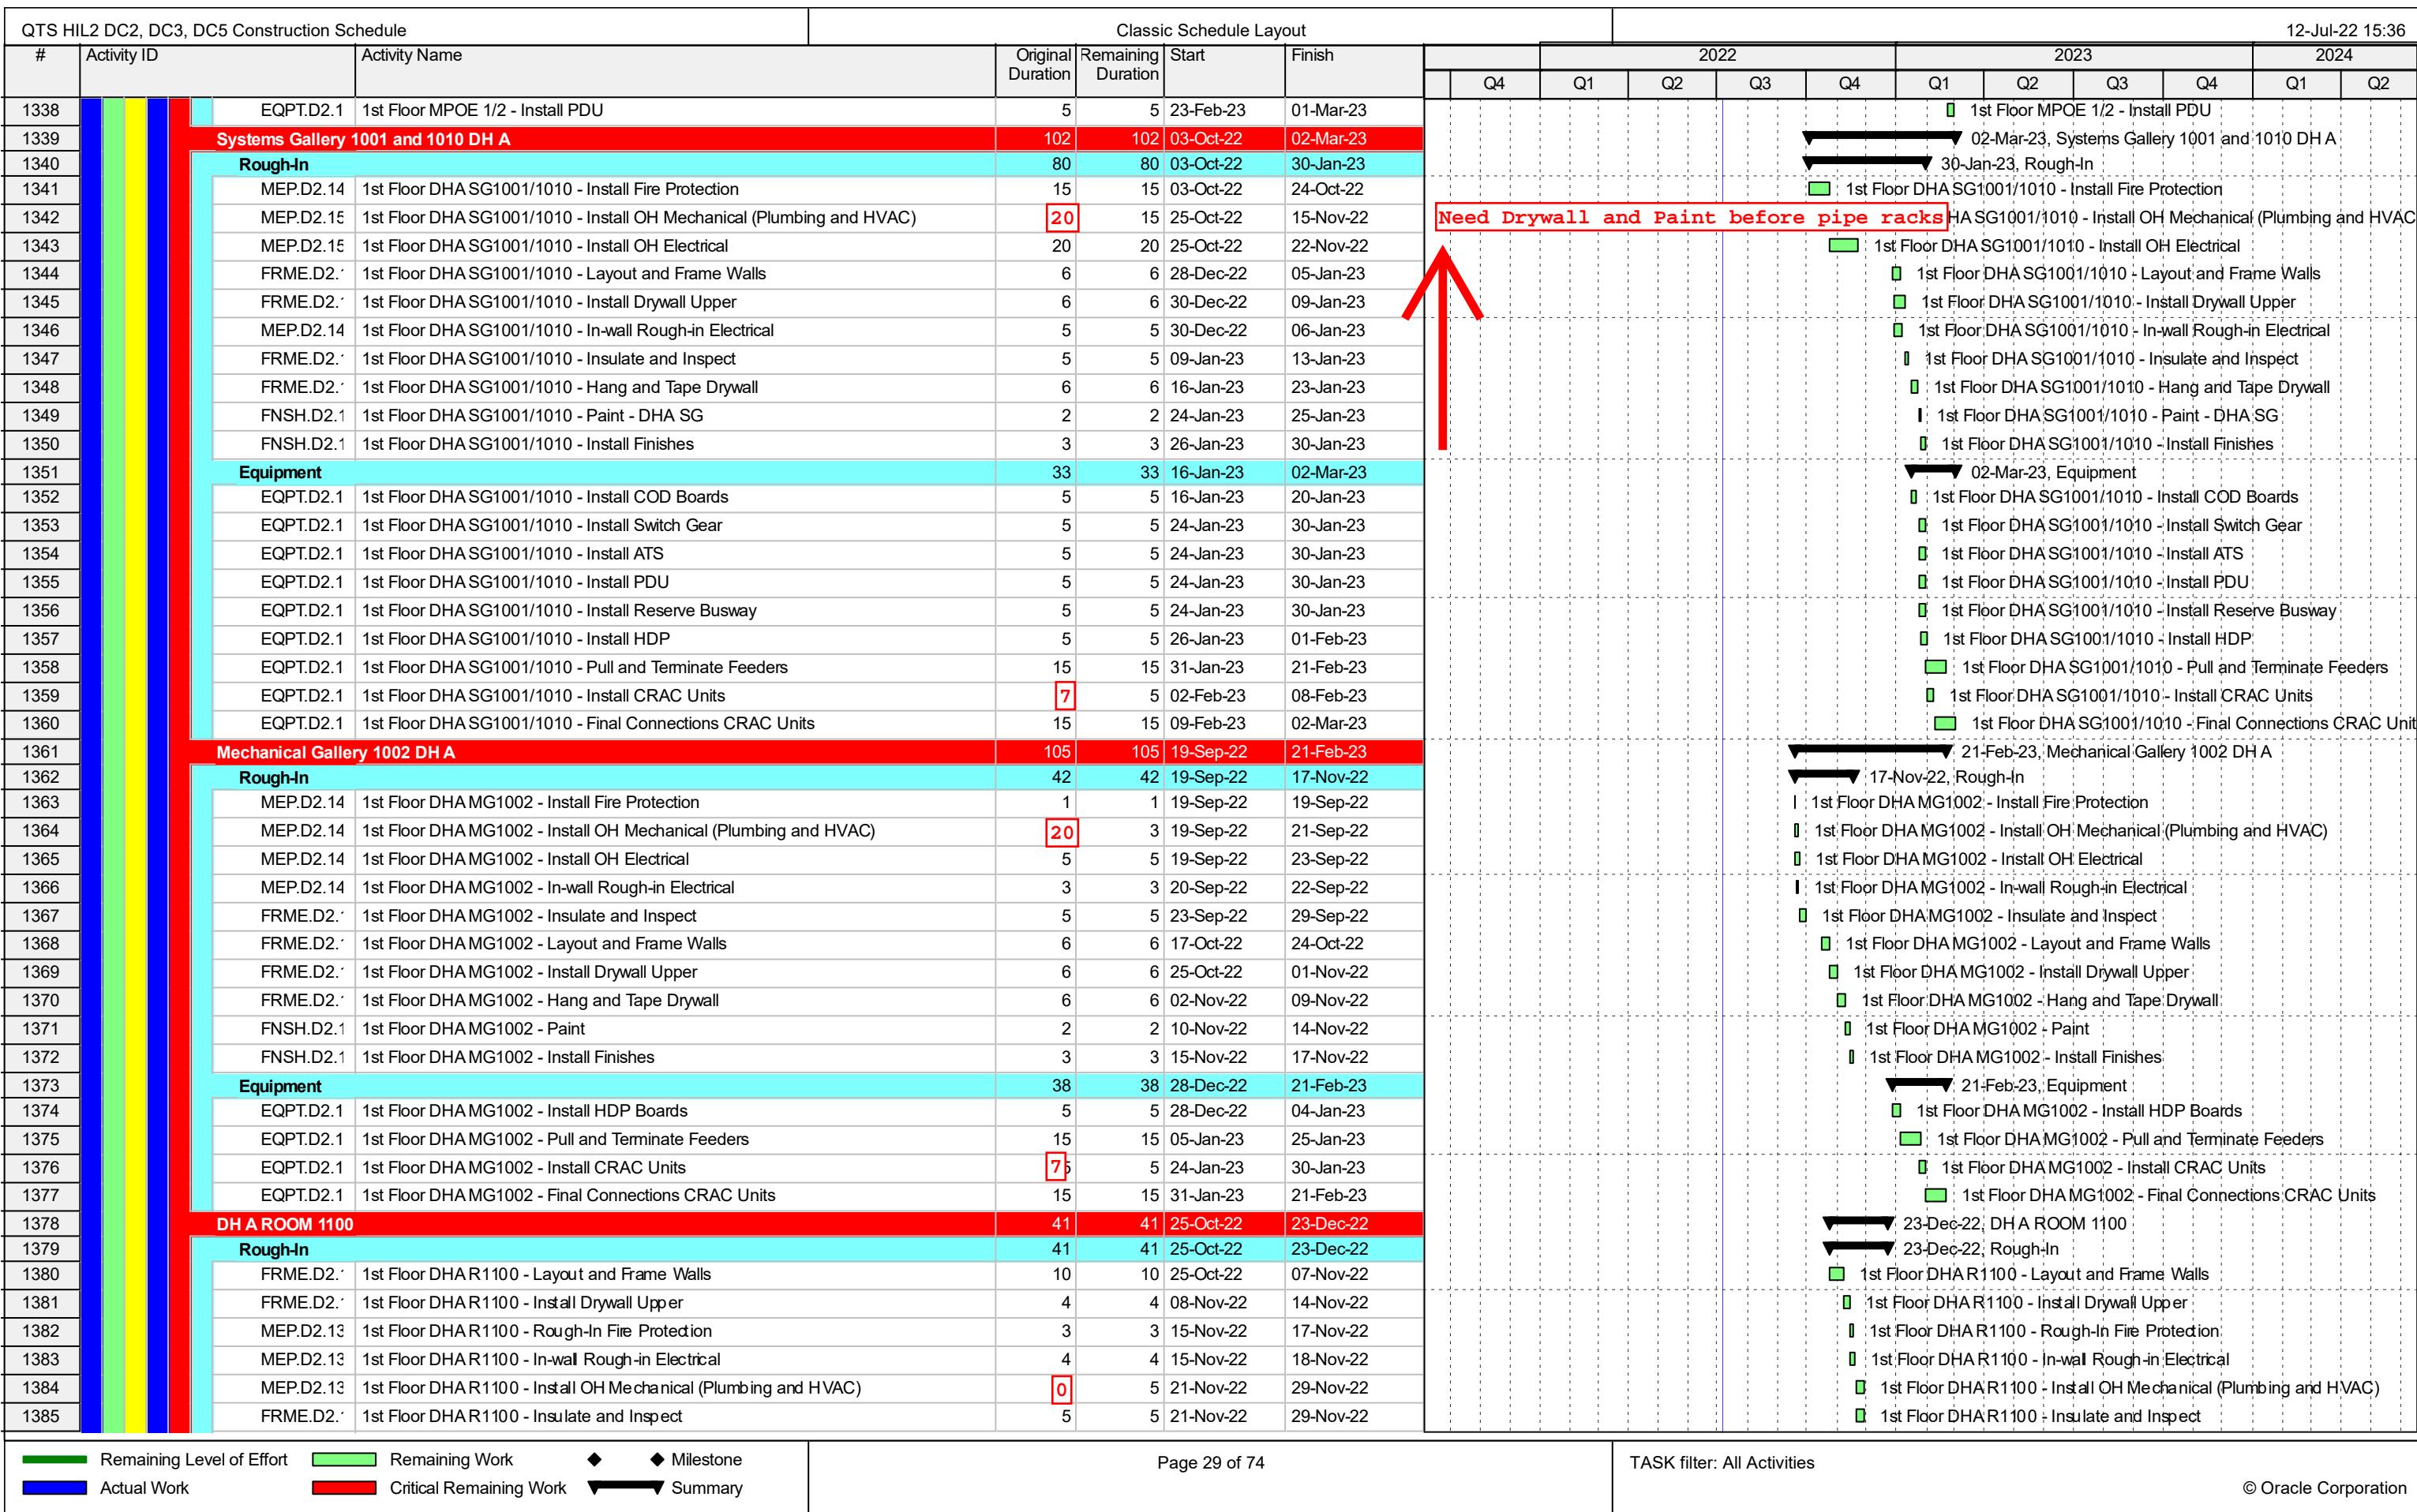

QTS HIL2 DC2, DC3, DC5 Construction Schedule				Classic Schedule Layout					12-Jul-22 15:36								
#	Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish		2022				2023				2024	
					Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2		
1386	MEP.D2.13	1st Floor DHA R1100 - Install OH Electrical	7	7	30-Nov-22	08-Dec-22											
1387	FRME.D2.1	1st Floor DHA R1100 - Hang and Tape Drywall	6	6	09-Dec-22	16-Dec-22											
1388	FRME.D2.1	1st Floor DHA R1100 - Install Structural Grid	10	10	09-Dec-22	22-Dec-22											
1389	FNSH.D2.1	1st Floor DHA R1100 - Paint DHA R	2	2	19-Dec-22	20-Dec-22											
1390	FNSH.D2.1	1st Floor DHA R1100 - Install Finishes	3	3	21-Dec-22	23-Dec-22											
1391	Systems Gallery 1003 and 1020 DH D			84	84	06-Dec-22	05-Apr-23										
1392	Rough-In			49	49	06-Dec-22	14-Feb-23										
1393	MEP.D2.15	1st Floor DHD SG1003/1020 - Install Fire Protection	5	5	06-Dec-22	12-Dec-22											
1394	MEP.D2.15	1st Floor DHD SG1003/1020 - Install OH Mechanical (Plumbing and HVAC)	20	15	13-Dec-22	04-Jan-23											
1395	MEP.D2.15	1st Floor DHD SG1003/1020 - Install OH Electrical	20	20	13-Dec-22	11-Jan-23											
1396	FRME.D2.1	1st Floor DHD SG1003/1020 - Layout and Frame Walls	6	6	17-Jan-23	24-Jan-23											
1397	FRME.D2.1	1st Floor DHD SG1003/1020 - Install Drywall Upper	6	6	19-Jan-23	26-Jan-23											
1398	MEP.D2.15	1st Floor DHD SG1003/1020 - In-wall Rough-in Electrical	3	3	19-Jan-23	23-Jan-23											
1399	FRME.D2.1	1st Floor DHD SG1003/1020 - Insulate and Inspect	5	5	24-Jan-23	30-Jan-23											
1400	FRME.D2.1	1st Floor DHD SG1003/1020 - Hang and Tape Drywall	6	6	31-Jan-23	07-Feb-23											
1401	FNSH.D2.1	1st Floor DHD SG1003/1020 - Paint	2	2	08-Feb-23	09-Feb-23											
1402	FNSH.D2.1	1st Floor DHD SG1003/1020 - Install Finishes	3	3	10-Feb-23	14-Feb-23											
1403	Equipment			40	40	08-Feb-23	05-Apr-23										
1404	EQPT.D2.1	1st Floor DHD SG1003/1020 - Install Switch Gear	5	5	08-Feb-23	14-Feb-23											
1405	EQPT.D2.1	1st Floor DHD SG1003/1020 - Install Reserve Busway	5	5	08-Feb-23	14-Feb-23											
1406	EQPT.D2.1	1st Floor DHD SG1003/1020 - Install COD Boards	5	5	15-Feb-23	22-Feb-23											
1407	EQPT.D2.1	1st Floor DHD SG1003/1020 - Install ATS	5	5	15-Feb-23	22-Feb-23											
1408	EQPT.D2.1	1st Floor DHD SG1003/1020 - Install CRAC Units	7	5	21-Feb-23	27-Feb-23											
1409	EQPT.D2.1	1st Floor DHD SG1003/1020 - Install HDP	5	5	23-Feb-23	01-Mar-23											
1410	EQPT.D2.1	1st Floor DHD SG1003/1020 - Install PDU	5	5	23-Feb-23	01-Mar-23											
1411	EQPT.D2.1	1st Floor DHD SG1003/1020 - Final Connections CRAC Units	15	15	28-Feb-23	20-Mar-23											
1412	EQPT.D2.1	1st Floor DHD SG1003/1020 - Pull and Terminate Feeders	25	25	02-Mar-23	05-Apr-23											
1413	Mechanical Gallery 1004 DH D			72	72	06-Dec-22	20-Mar-23										
1414	Rough-In			57	57	06-Dec-22	27-Feb-23										
1415	MEP.D2.14	1st Floor DHD MG1004 - Install Fire Protection	5	5	06-Dec-22	12-Dec-22											
1416	MEP.D2.14	1st Floor DHD MG1004 - In-wall Rough-in Electrical	3	3	13-Dec-22	15-Dec-22											
1417	MEP.D2.14	1st Floor DHD MG1004 - Install OH Mechanical (Plumbing and HVAC)	20	5	13-Dec-22	19-Dec-22											
1418	FRME.D2.1	1st Floor DHD MG1004 - Insulate and Inspect	5	5	16-Dec-22	22-Dec-22											
1419	MEP.D2.14	1st Floor DHD MG1004 - Install OH Electrical	5	5	20-Dec-22	27-Dec-22											
1420	FRME.D2.1	1st Floor DHD MG1004 - Layout and Frame Walls	6	6	25-Jan-23	01-Feb-23											
1421	FRME.D2.1	1st Floor DHD MG1004 - Install Drywall Upper	6	6	02-Feb-23	09-Feb-23											
1422	FRME.D2.1	1st Floor DHD MG1004 - Hang and Tape Drywall	6	6	10-Feb-23	17-Feb-23											
1423	FNSH.D2.1	1st Floor DHD MG1004 - Paint	2	2	21-Feb-23	22-Feb-23											
1424	FNSH.D2.1	1st Floor DHD MG1004 - Install Finishes	3	3	23-Feb-23	27-Feb-23											
1425	Equipment			20	20	21-Feb-23	20-Mar-23										
1426	EQPT.D2.1	1st Floor DHD MG1004 - Install CRAC Units	7	5	21-Feb-23	27-Feb-23											
1427	EQPT.D2.1	1st Floor DHD MG1004 - Install HDP Boards	5	5	21-Feb-23	27-Feb-23											
1428	EQPT.D2.1	1st Floor DHD MG1004 - Final Connections CRAC Units	15	15	28-Feb-23	20-Mar-23											
1429	EQPT.D2.1	1st Floor DHD MG1004 - Pull and Terminate Feeders	15	15	28-Feb-23	20-Mar-23											
1430	DH D ROOM 1200			41	41	02-Feb-23	31-Mar-23										
1431	Rough-In			41	41	02-Feb-23	31-Mar-23										
1432	FRME.D2.1	1st Floor DHD R1200 - Layout and Frame Walls	10	10	02-Feb-23	15-Feb-23											
1433	FRME.D2.1	1st Floor DHD R1200 - Install Drywall Upper	4	4	16-Feb-23	22-Feb-23											

The legend consists of six items arranged horizontally. From left to right: a green bar labeled 'Remaining Level of Effort'; a light green bar labeled 'Remaining Work'; a black diamond symbol labeled 'Milestone'; a blue bar labeled 'Actual Work'; a red bar labeled 'Critical Remaining Work'; and a black arrow symbol labeled 'Summary'.

Page 31 of 74


TASK filter: All Activities

© Oracle Corporation

QTS HIL2 DC2, DC3, DC5 Construction Schedule				Classic Schedule Layout					12-Jul-22 15:37									
#	Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	2022					2023				2024		
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	
1482		EQPT.D2.1 2nd Floor DHB SG 2001/2010 - Pull and Terminate Feeders	15	15	23-Jan-23	10-Feb-23												2nd Floor DHB SG 2001/2010 - Pull and Terminate Feeders
1483		EQPT.D2.1 2nd Floor DHB SG 2001/2010 - Install CRAC Units		7	5	01-Feb-23	07-Feb-23											2nd Floor DHB SG 2001/2010 - Install CRAC Units
1484		EQPT.D2.1 2nd Floor DHB SG 2001/2010 - Final Connections CRAC Units		15	15	08-Feb-23	01-Mar-23											2nd Floor DHB SG 2001/2010 - Final Connections CRAC Units
1485		Mechanical Gallery 2002 DH B	100	100	04-Oct-22	01-Mar-23												Cant energize until equipment is connected
1486		Rough-In		85	85	04-Oct-22	07-Feb-23											01-Mar-23, Mechanical Gallery 2002 DH B
1487		FRME.D2.1 2nd Floor DHB MG 2002 - Layout and Frame Walls		6	6	04-Oct-22	12-Oct-22											07-Feb-23, Rough-In
1488		MEP.D2.11 2nd Floor DHB MG 2002 - Install Fire Protection		1	1	04-Oct-22	04-Oct-22											2nd Floor DHB MG 2002 - Layout and Frame Walls
1489		MEP.D2.11 2nd Floor DHB MG 2002 - Install OH Mechanical (Plumbing and HVAC)		20	3	04-Oct-22	06-Oct-22											2nd Floor DHB MG 2002 - Install Fire Protection
1490		MEP.D2.11 2nd Floor DHB MG 2002 - Install OH Electrical		5	5	04-Oct-22	11-Oct-22											2nd Floor DHB MG 2002 - Install OH Mechanical (Plumbing and HVAC)
1491		MEP.D2.11 2nd Floor DHB MG 2002 - In-wall Rough-in Electrical		3	3	05-Oct-22	07-Oct-22											2nd Floor DHB MG 2002 - Install OH Electrical
1492		FRME.D2.1 2nd Floor DHB MG 2002 - Insulate and Inspect		5	5	11-Oct-22	17-Oct-22											2nd Floor DHB MG 2002 - In-wall Rough-in Electrical
1493		FRME.D2.1 2nd Floor DHB MG 2002 - Install Drywall Upper		6	6	13-Oct-22	20-Oct-22											2nd Floor DHB MG 2002 - Insulate and Inspect
1494		FRME.D2.1 2nd Floor DHB MG 2002 - Hang and Tape Drywall		6	6	24-Jan-23	31-Jan-23											2nd Floor DHB MG 2002 - Install Drywall Upper
1495		FNSH.D2.1 2nd Floor DHB MG 2002 - Paint		2	2	01-Feb-23	02-Feb-23											2nd Floor DHB MG 2002 - Hang and Tape Drywall
1496		FNSH.D2.1 2nd Floor DHB MG 2002 - Install Finishes		3	3	03-Feb-23	07-Feb-23											2nd Floor DHB MG 2002 - Paint
1497		Equipment		20	20	01-Feb-23	01-Mar-23											2nd Floor DHB MG 2002 - Install Finishes
1498		EQPT.D2.1 2nd Floor DHB MG 2002 - Install CRAC Units		7	5	01-Feb-23	07-Feb-23											01-Mar-23, Equipment
1499		EQPT.D2.1 2nd Floor DHB MG 2002 - Install HDP Boards		5	5	01-Feb-23	07-Feb-23											2nd Floor DHB MG 2002 - Install CRAC Units
1500		EQPT.D2.1 2nd Floor DHB MG 2002 - Final Connections CRAC Units		15	15	08-Feb-23	01-Mar-23											2nd Floor DHB MG 2002 - Install HDP Boards
1501		EQPT.D2.1 2nd Floor DHB MG 2002 - Pull and Terminate Feeders		15	15	08-Feb-23	01-Mar-23											2nd Floor DHB MG 2002 - Final Connections CRAC Units
1502		DH B ROOM 2100		85	85	13-Oct-22	15-Feb-23											2nd Floor DHB MG 2002 - Pull and Terminate Feeders
1503		Rough-In		85	85	13-Oct-22	15-Feb-23											15-Feb-23, DH B ROOM 2100
1504		FRME.D2.1 2nd Floor DHB R2100 - Layout and Frame Walls		10	10	13-Oct-22	26-Oct-22											15-Feb-23, Rough-In
1505		MEP.D2.10 2nd Floor DHB R2100 - Install Fire Protection		3	3	13-Oct-22	17-Oct-22											2nd Floor DHB R2100 - Layout and Frame Walls
1506		MEP.D2.10 2nd Floor DHB R2100 - Install OH Electrical		7	7	13-Oct-22	21-Oct-22											2nd Floor DHB R2100 - Install Fire Protection
1507		FRME.D2.1 2nd Floor DHB R2100 - Install Structural Grid		10	10	24-Oct-22	04-Nov-22											2nd Floor DHB R2100 - Install OH Electrical
1508		FRME.D2.1 2nd Floor DHB R2100 - Install Drywall Upper		4	4	27-Oct-22	01-Nov-22											2nd Floor DHB R2100 - Install Structural Grid
1509		MEP.D2.10 2nd Floor DHB R2100 - In-wall Rough-in Electrical		4	4	02-Nov-22	07-Nov-22											2nd Floor DHB R2100 - Install Drywall Upper
1510		FRME.D2.1 2nd Floor DHB R2100 - Insulate and Inspect		5	5	08-Nov-22	15-Nov-22											2nd Floor DHB R2100 - In-wall Rough-in Electrical
1511		FRME.D2.1 2nd Floor DHB R2100 - Hang and Tape Drywall		6	6	01-Feb-23	08-Feb-23											2nd Floor DHB R2100 - Insulate and Inspect
1512		FNSH.D2.1 2nd Floor DHB R2100 - Paint		2	2	09-Feb-23	10-Feb-23											2nd Floor DHB R2100 - Hang and Tape Drywall
1513		FNSH.D2.1 2nd Floor DHB R2100 - Install Finishes		3	3	13-Feb-23	15-Feb-23											2nd Floor DHB R2100 - Paint
1514		Systems Gallery 2020 and 2003 DH C		94	94	06-Dec-22	19-Apr-23											2nd Floor DHB R2100 - Install Finishes
1515		Rough-In		59	59	06-Dec-22	01-Mar-23											19-Apr-23, Systems Gallery 2020 and 2003 DH C
1516		MEP.D2.12 2nd Floor DHC 2020/2003 - Install Fire Protection		5	5	06-Dec-22	12-Dec-22											01-Mar-23, Rough-In
1517		MEP.D2.12 2nd Floor DHC 2020/2003 - Install OH Mechanical (Plumbing and HVAC)		20	15	13-Dec-22	04-Jan-23											2nd Floor DHC 2020/2003 - Install Fire Protection
1518		MEP.D2.12 2nd Floor DHC 2020/2003 - Install OH Electrical		20	20	13-Dec-22	11-Jan-23											2nd Floor DHC 2020/2003 - Install OH Mechanical (Plumbing and HVAC)
1519		FRME.D2.1 2nd Floor DHC 2020/2003 - Layout and Frame Walls		6	6	17-Jan-23	24-Jan-23											2nd Floor DHC 2020/2003 - Install OH Electrical
1520		FRME.D2.1 2nd Floor DHC 2020/2003 - Install Drywall Upper		6	6	25-Jan-23	01-Feb-23											2nd Floor DHC 2020/2003 - Layout and Frame Walls
1521		MEP.D2.12 2nd Floor DHC 2020/2003 - In-wall Rough-in Electrical		3	3	02-Feb-23	06-Feb-23											2nd Floor DHC 2020/2003 - Install Drywall Upper
1522		FRME.D2.1 2nd Floor DHC 2020/2003 - Insulate and Inspect		5	5	07-Feb-23	13-Feb-23											2nd Floor DHC 2020/2003 - In-wall Rough-in Electrical
1523		FRME.D2.1 2nd Floor DHC 2020/2003 - Hang and Tape Drywall		6	6	14-Feb-23	22-Feb-23											2nd Floor DHC 2020/2003 - Insulate and Inspect
1524		FNSH.D2.1 2nd Floor DHC 2020/2003 - Paint		2	2	23-Feb-23	24-Feb-23											2nd Floor DHC 2020/2003 - Hang and Tape Drywall
1525		FNSH.D2.1 2nd Floor DHC 2020/2003 - Install Finishes		3	3	27-Feb-23	01-Mar-23											2nd Floor DHC 2020/2003 - Paint
1526		Equipment		66	66	17-Jan-23	19-Apr-23											2nd Floor DHC 2020/2003 - Install Finishes
1527		EQPT.D2.1 2nd Floor DHC 2020/2003 - Install ATS		5	5	17-Jan-23	23-Jan-23											19-Apr-23, Equipment
1528		EQPT.D2.1 2nd Floor DHC 2020/2003 - Install HDP		5	5	17-Jan-23	23-Jan-23											2nd Floor DHC 2020/2003 - Install ATS
1529																		

QTS HIL2 DC2, DC3, DC5 Construction Schedule				Classic Schedule Layout					12-Jul-22 15:37									
#	Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	2022					2023					2024	
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	
1530		EQPT.D2.1	5	5	17-Jan-23	23-Jan-23												
1531		EQPT.D2.1 2nd Floor DHC 2020/2003 - Install COD Boards	10	10	23-Feb-23	08-Mar-23												
1532		EQPT.D2.1 2nd Floor DHC 2020/2003 - Install CRAC Units	7	5	23-Feb-23	01-Mar-23												
1533		EQPT.D2.1 2nd Floor DHC 2020/2003 - Final Connections CRAC Units	15	15	02-Mar-23	22-Mar-23												
1534		EQPT.D2.1 2nd Floor DHC 2020/2003 - Install Switch Gear	5	5	09-Mar-23	15-Mar-23												
1535		EQPT.D2.1 2nd Floor DHC 2020/2003 - Pull and Terminate Feeders	25	25	16-Mar-23	19-Apr-23												
1536		Mechanical Gallery 2003 DH C	74	74	06-Dec-22	22-Mar-23												
1537		Rough-In	30	30	06-Dec-22	18-Jan-23												
1538		FRME.D2.1 2nd Floor DHC MG 2003 - Layout and Frame Walls	5	5	06-Dec-22	12-Dec-22												
1539		MEP.D2.11 2nd Floor DHC MG 2003 - Install Fire Protection	1	1	06-Dec-22	06-Dec-22												
1540		MEP.D2.11 2nd Floor DHC MG 2003 - Install OH Mechanical (Plumbing and HVAC)	20	3	06-Dec-22	08-Dec-22												
1541		MEP.D2.11 2nd Floor DHC MG 2003 - Install OH Electrical	5	5	06-Dec-22	12-Dec-22												
1542		MEP.D2.11 2nd Floor DHC MG 2003 - In-wall Rough-in Electrical	3	3	07-Dec-22	09-Dec-22												
1543		FRME.D2.1 2nd Floor DHC MG 2003 - Insulate and Inspect	5	5	12-Dec-22	16-Dec-22												
1544		FRME.D2.1 2nd Floor DHC MG 2003 - Install Drywall Upper	6	6	13-Dec-22	20-Dec-22												
1545		FRME.D2.1 2nd Floor DHC MG 2003 - Hang and Tape Drywall	6	6	21-Dec-22	29-Dec-22												
1546		FNSH.D2.1 2nd Floor DHC MG 2003 - Paint	2	2	30-Dec-22	03-Jan-23												
1547		FNSH.D2.1 2nd Floor DHC MG 2003 - Install Finishes	3	3	16-Jan-23	18-Jan-23												
1548		Equipment	55	55	04-Jan-23	22-Mar-23												
1549		EQPT.D2.1 2nd Floor DHC MG 2003 - Ducting	4	4	04-Jan-23	09-Jan-23												
1550		EQPT.D2.1 2nd Floor DHC MG 2003 - Install HDP Boards	5	5	17-Jan-23	23-Jan-23												
1551		EQPT.D2.1 2nd Floor DHC MG 2003 - Pull and Terminate Feeders	15	15	24-Jan-23	13-Feb-23												
1552		EQPT.D2.1 2nd Floor DHC MG 2003 - Install CRAC Units	7	5	23-Feb-23	01-Mar-23												
1553		EQPT.D2.1 2nd Floor DHC MG 2003 - Final Connections CRAC Units	15	15	02-Mar-23	22-Mar-23												
1554		DH C ROOM 2200	34	34	13-Dec-22	31-Jan-23												
1555		Rough-In	34	34	13-Dec-22	31-Jan-23												
1556		FRME.D2.1 2nd Floor DHC R2200 - Layout and Frame Walls	10	10	13-Dec-22	27-Dec-22												
1557		MEP.D2.1C 2nd Floor DHC R2200 - Install Fire Protection	3	3	13-Dec-22	15-Dec-22												
1558		MEP.D2.11 2nd Floor DHC R2200 - Install OH Electrical	7	7	13-Dec-22	21-Dec-22												
1559		FRME.D2.1 2nd Floor DHC R2200 - Install Structural Grid	10	10	22-Dec-22	06-Jan-23												
1560		FRME.D2.1 2nd Floor DHC R2200 - Install Drywall Upper	4	4	28-Dec-22	03-Jan-23												
1561		MEP.D2.1C 2nd Floor DHC R2200 - In-wall Rough-in Electrical	4	4	04-Jan-23	09-Jan-23												
1562		FRME.D2.1 2nd Floor DHC R2200 - Insulate and Inspect	5	5	10-Jan-23	16-Jan-23												
1563		FRME.D2.1 2nd Floor DHC R2200 - Hang and Tape Drywall	6	6	17-Jan-23	24-Jan-23												
1564		FNSH.D2.1 2nd Floor DHC R2200 - Paint	2	2	25-Jan-23	26-Jan-23												
1565		FNSH.D2.1 2nd Floor DHC R2200 - Install Finishes	3	3	27-Jan-23	31-Jan-23												
1566		Closeout and Final Inspections	78	78	02-Mar-23	20-Jun-23												
1567		PNCH.D2.1080 Punch DH B	15	15	02-Mar-23	22-Mar-23												
1568		PNCH.D2.1070 Punch - DH A	15	15	03-Mar-23	23-Mar-23												
1569		PNCH.D2.1110 Punch House	15	15	17-Mar-23	06-Apr-23												
1570		PNCH.D2.1090 Punch DH C	15	15	23-Mar-23	12-Apr-23												
1571		PNCH.D2.1100 Punch DH D	15	15	03-Apr-23	21-Apr-23												
1572		PNCH.D2.1020 Elevators Final Inspections	5	5	04-Apr-23	10-Apr-23												
1573		PNCH.D2.1060 Punch MPOE/BDF	15	15	25-Apr-23	15-May-23												
1574		PNCH.D2.1000 Electrical Final Inspections - DC2	5	5	25-May-23	01-Jun-23												
1575		PNCH.D2.1030 Fire and Life Safety Final Inspections	5	5	25-May-23	01-Jun-23												
1576		PNCH.D2.1050 Low Voltage Final Inspections	5	5	25-May-23	01-Jun-23												
1577		PNCH.D2.1010 Mechanical Final Inspections	5	5	31-May-23	06-Jun-23												

█ Remaining Level of Effort █ Remaining Work ◆ Milestone
█ Actual Work █ Critical Remaining Work ▼ Summary

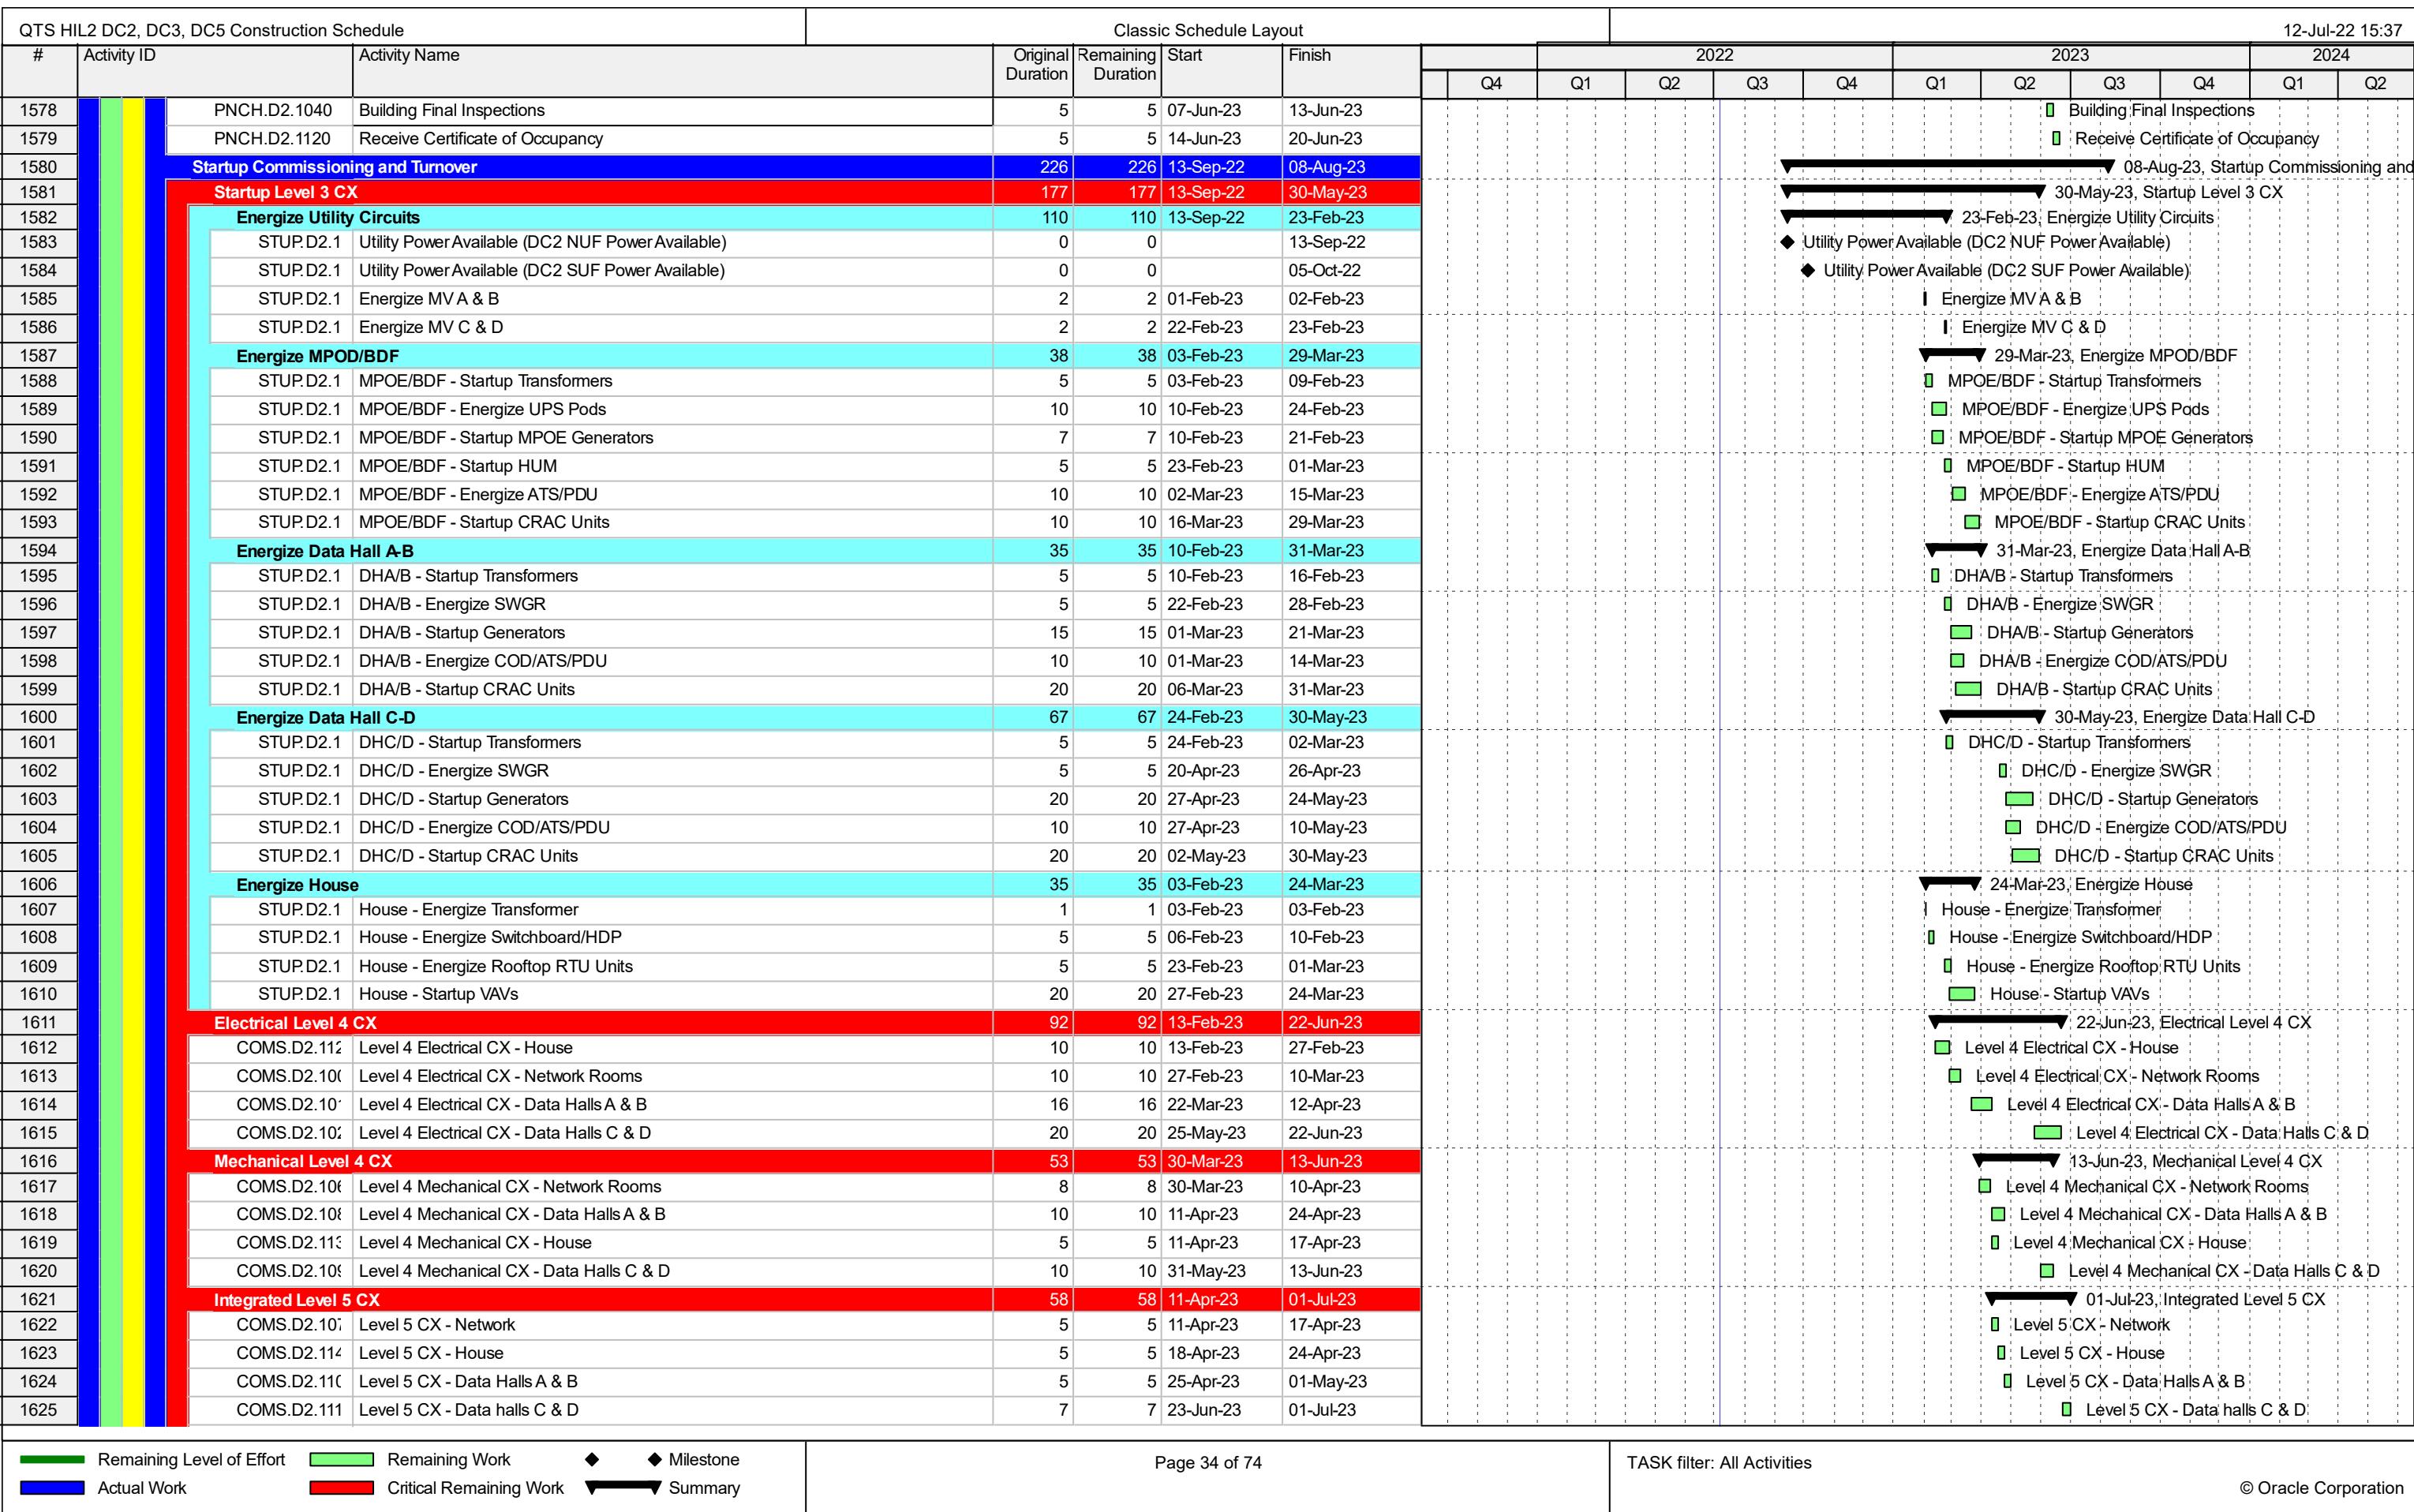

QTS HIL2 DC2, DC3, DC5 Construction Schedule				Classic Schedule Layout					12-Jul-22 15:37								
#	Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish		Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	2024
1626		Weather Days	99	99	02-May-23	08-Aug-23											08-Aug-23, Weather Days
1627	WEATHER.D2	Weather Days DC2 DH A & B (36-0=36)	36	36	02-May-23	06-Jun-23											Weather Days DC2 DH A& B (36-0=36)
1628	WEATHER.D2	Weather Days DC2 DH C & D (38-0=38)	38	38	01-Jul-23	08-Aug-23											Weather Days DC2 DH C & D (38-0=38)
1629		DC3	343	339	14-Apr-22 A	09-Nov-23											09-Nov-23, DC3
1630		DC3 Milestones	0	0	29-Mar-23	29-Mar-23											29-Mar-23, DC3 Milestones
1631	MILE.D3.1010	Substantially Weathertight	0	0		29-Mar-23											Substantially Weathertight
1632		Earthwork	61	40	14-Apr-22 A	31-Aug-22											31-Aug-22, Earthwork
1633		Site Development	44	40	14-Apr-22 A	31-Aug-22											31-Aug-22, Site Development
1634	SITE.D3.1000	Place Imported Fill Materials	20	4	14-Apr-22 A	12-Jul-22											Place Imported Fill Materials
1635	SITE.D3.1010	Earthwork Onsite CTS Site Fills	21	6	18-Apr-22 A	15-Jul-22											Earthwork Onsite CTS Site Fills
1636	SITE.D3.1020	Place Surcharge	10	10	07-Jul-22	20-Jul-22											Place Surcharge
1637	SITE.D3.1030	Surcharge Waiting Period	30	30	21-Jul-22	31-Aug-22											Surcharge Waiting Period
1638		Rigid Inclusions	51	29	28-Jun-22 A	22-Aug-22											22-Aug-22, Rigid Inclusions
1639	RIGD.D3.1030	RI-CL Q to CL Z	10	2	28-Jun-22 A	14-Jul-22											RI-CL Q to CL Z
1640	RIGD.D3.1020	RI-CL L2 to CL Q	10	10	15-Jul-22	28-Jul-22											RI-CL L2 to CL Q
1641	RIGD.D3.1010	RI-CL C to CL L.2	10	10	29-Jul-22	11-Aug-22											RI-CL C to CL L.2
1642	RIGD.D3.1000	RI-CL A to C	7	7	12-Aug-22	22-Aug-22											RI-CL A to C
1643		Foundation	139	139	15-Jul-22	03-Feb-23											03-Feb-23, Foundation
1644		Building Pad Prep	32	32	01-Sep-22	18-Oct-22											18-Oct-22, Building Pad Prep
1645		Area Wide	10	10	01-Sep-22	15-Sep-22											15-Sep-22, Area Wide
1646	FOND.D3.1	Move Surcharge to DC5	5	5	01-Sep-22	08-Sep-22											Move Surcharge to DC5
1647	FOND.D3.1	Rock and Compact Slab	5	5	09-Sep-22	15-Sep-22											Rock and Compact Slab
1648		Grid A - C	10	10	13-Sep-22	26-Sep-22											26-Sep-22, Grid A - C
1649	UTIL.D3.1C	Under-slab Utilities CL A to C	5	5	13-Sep-22	19-Sep-22											Under-slab Utilities CL A to C
1650	FOND.D3.1	Backfill/Compact CL A to C	5	5	20-Sep-22	26-Sep-22											Backfill/Compact CL A to C
1651		Grid C - L	10	10	20-Sep-22	03-Oct-22											03-Oct-22, Grid C - L
1652	UTIL.D3.1C	Under-slab Utilities CL C to L.2	5	5	20-Sep-22	26-Sep-22											Under-slab Utilities CL C to L.2
1653	FOND.D3.1	Backfill/Compact CL C to L.2	5	5	27-Sep-22	03-Oct-22											Backfill/Compact CL C to L.2
1654		Grid L - Q.1	10	10	27-Sep-22	11-Oct-22											11-Oct-22, Grid L - Q.1
1655	UTIL.D3.1C	Under-slab Utilities CL L.2 to Q	5	5	27-Sep-22	03-Oct-22											Under-slab Utilities CL L.2 to Q
1656	FOND.D3.1	Backfill/Compact CL L.2 to Q	5	5	04-Oct-22	11-Oct-22											Backfill/Compact CL L.2 to Q
1657		Grid Q.1 - Z	10	10	04-Oct-22	18-Oct-22											18-Oct-22, Grid Q.1 - Z
1658	UTIL.D3.1C	Under-slab Utilities CL Q to Z	5	5	04-Oct-22	11-Oct-22											Under-slab Utilities CL Q to Z
1659	FOND.D3.1	Backfill/Compact CL Q to Z	5	5	12-Oct-22	18-Oct-22											Backfill/Compact CL Q to Z
1660		DC3 Foundations	66	66	15-Jul-22	18-Oct-22											18-Oct-22, DC3 Foundations
1661		Grid A-C	48	48	15-Jul-22	21-Sep-22											21-Sep-22, Grid A-C
1662	FOND.D3.1	Found A-C - Survey Footing Excavation	1	1	15-Jul-22	18-Jul-22											Found A-C - Survey Footing Excavation
1663	FOND.D3.1	Found A-C - Dig Footings	3	3	23-Aug-22	25-Aug-22											Found A-C - Dig Footings
1664	FOND.D3.1	Found A-C - Survey Formwork	1	1	26-Aug-22	26-Aug-22											Found A-C - Survey Formwork
1665	FOND.D3.1	Found A-C - Form Foundations (#1 Formwork Delivery)	5	5	29-Aug-22	02-Sep-22											Found A-C - Form Foundations (#1 Formwork Delivery)
1666	FOND.D3.1	Found A-C - Install Anchor Bolts	5	5	29-Aug-22	02-Sep-22											Found A-C - Install Anchor Bolts
1667	FOND.D3.1	Found A-C - Install Reinforcement	5	5	30-Aug-22	06-Sep-22											Found A-C - Install Reinforcement
1668	FOND.D3.1	Found A-C - Install Elevator Pit	5	5	07-Sep-22	13-Sep-22											Found A-C - Install Elevator Pit
1669	FOND.D3.1	Found A-C - Place Foundations	1	1	07-Sep-22	07-Sep-22											Found A-C - Place Foundations
1670	FOND.D3.1	Found A-C - Strip Foundations	3	3	08-Sep-22	12-Sep-22											Found A-C - Strip Foundations
1671	FOND.D3.1	Found A-C - Plinths and Grade Beams	5	5	08-Sep-22	14-Sep-22											Found A-C - Plinths and Grade Beams
1672	FOND.D3.1	Found A-C - Waterproof/Insulate	3	3	14-Sep-22	16-Sep-22											Found A-C - Waterproof/Insulate
1673	FOND.D3.1	Found A-C - Backfill Foundations	3	3	19-Sep-22	21-Sep-22											Found A-C - Backfill Foundations
1674		Grid C-L	38	38	12-Aug-22	05-Oct-22											05-Oct-22, Grid C-L

Remaining Level of Effort Remaining Work ◆ Milestone
 Actual Work Critical Remaining Work ▶ Summary

The legend consists of six items arranged horizontally. From left to right: a green bar labeled 'Remaining Level of Effort'; a light green bar labeled 'Remaining Work'; a black diamond symbol labeled 'Milestone'; a blue bar labeled 'Actual Work'; a red bar labeled 'Critical Remaining Work'; and a black arrow symbol labeled 'Summary'.

Page 36 of 74

TASK filter: All Activities


© Oracle Corporation

QTS HIL2 DC2, DC3, DC5 Construction Schedule				Classic Schedule Layout					12-Jul-22 15:37									
#	Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish			2022				2023				2024	
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	
1723	SOG.D3	SOG C-L P2 - Edgeforms/Diamonds	2	2	12-Oct-22	13-Oct-22					I	SOG C-L P2 - Edgeforms/Diamonds						
1724	SOG.D3	SOG C-L P2 - Vapor Barrier		1	1	14-Oct-22	14-Oct-22				I	SOG C-L P2 - Vapor Barrier						
1725	SOG.D3	SOG C-L P2 - Install reinforcement		3	3	17-Oct-22	19-Oct-22				I	SOG C-L P2 - Install reinforcement						
1726	SOG.D3	SOG C-L P2 - MEP Final Set		1	1	20-Oct-22	20-Oct-22				I	SOG C-L P2 - MEP Final Set						
1727	SOG.D3	SOG C-L P2 - Place SOG		1	1	21-Oct-22	21-Oct-22				I	SOG C-L P2 - Place SOG						
1728	SOG.D3	SOG C-L P2 - Cure SOG		5	5	24-Oct-22	28-Oct-22				I	SOG C-L P2 - Cure SOG						
1729	Pour 3			16	16	06-Oct-22	28-Oct-22											
1730	SOG.D3	SOG C-L P3 - Fine Grade		3	3	06-Oct-22	11-Oct-22				I	SOG C-L P3 - Fine Grade						
1731	SOG.D3	SOG C-L P3 - Edgeforms/Diamonds		2	2	12-Oct-22	13-Oct-22				I	SOG C-L P3 - Edgeforms/Diamonds						
1732	SOG.D3	SOG C-L P3 - Vapor Barrier		1	1	14-Oct-22	14-Oct-22				I	SOG C-L P3 - Vapor Barrier						
1733	SOG.D3	SOG C-L P3 - Install reinforcement		3	3	17-Oct-22	19-Oct-22				I	SOG C-L P3 - Install reinforcement						
1734	SOG.D3	SOG C-L P3 - MEP Final Set		1	1	20-Oct-22	20-Oct-22				I	SOG C-L P3 - MEP Final Set						
1735	SOG.D3	SOG C-L P3 - Place SOG		1	1	21-Oct-22	21-Oct-22				I	SOG C-L P3 - Place SOG						
1736	SOG.D3	SOG C-L P3 - Cure SOG		5	5	24-Oct-22	28-Oct-22				I	SOG C-L P3 - Cure SOG						
1737	Grid L-Q.1			16	16	12-Oct-22	02-Nov-22											
1738	Pour 4			16	16	12-Oct-22	02-Nov-22											
1739	SOG.D3	SOG L-Q.1 P4 - Fine Grade		3	3	12-Oct-22	14-Oct-22				I	SOG L-Q.1 P4 - Fine Grade						
1740	SOG.D3	SOG L-Q.1 P4 - Edgeforms/Diamonds		2	2	17-Oct-22	18-Oct-22				I	SOG L-Q.1 P4 - Edgeforms/Diamonds						
1741	SOG.D3	SOG L-Q.1 P4 - Vapor Barrier		1	1	19-Oct-22	19-Oct-22				I	SOG L-Q.1 P4 - Vapor Barrier						
1742	SOG.D3	SOG L-Q.1 P4 - Install reinforcement		3	3	20-Oct-22	24-Oct-22				I	SOG L-Q.1 P4 - Install reinforcement						
1743	SOG.D3	SOG L-Q.1 P4 - MEP Final Set		1	1	25-Oct-22	25-Oct-22				I	SOG L-Q.1 P4 - MEP Final Set						
1744	SOG.D3	SOG L-Q.1 P4 - Place SOG		1	1	26-Oct-22	26-Oct-22				I	SOG L-Q.1 P4 - Place SOG						
1745	SOG.D3	SOG L-Q.1 P4 - Cure SOG		5	5	27-Oct-22	02-Nov-22				I	SOG L-Q.1 P4 - Cure SOG						
1746	Grid Q.1-Z			16	16	19-Oct-22	09-Nov-22											
1747	Pour 5			16	16	19-Oct-22	09-Nov-22											
1748	SOG.D3	SOG Q.1-Z P5 - Fine Grade		3	3	19-Oct-22	21-Oct-22				I	SOG Q.1-Z P5 - Fine Grade						
1749	SOG.D3	SOG Q.1-Z P5 - Edgeforms/Diamonds		2	2	24-Oct-22	25-Oct-22				I	SOG Q.1-Z P5 - Edgeforms/Diamonds						
1750	SOG.D3	SOG Q.1-Z P5 - Vapor Barrier		1	1	26-Oct-22	26-Oct-22				I	SOG Q.1-Z P5 - Vapor Barrier						
1751	SOG.D3	SOG Q.1-Z P5 - Install reinforcement		3	3	27-Oct-22	31-Oct-22				I	SOG Q.1-Z P5 - Install reinforcement						
1752	SOG.D3	SOG Q.1-Z P5 - MEP Final Set		1	1	01-Nov-22	01-Nov-22				I	SOG Q.1-Z P5 - MEP Final Set						
1753	SOG.D3	SOG Q.1-Z P5 - Place SOG		1	1	02-Nov-22	02-Nov-22				I	SOG Q.1-Z P5 - Place SOG						
1754	SOG.D3	SOG Q.1-Z P5 - Cure SOG		5	5	03-Nov-22	09-Nov-22				I	SOG Q.1-Z P5 - Cure SOG						
1755	Pour 6			16	16	19-Oct-22	09-Nov-22											
1756	SOG.D3	SOG Q.1-Z P6 - Fine Grade		3	3	19-Oct-22	21-Oct-22				I	SOG Q.1-Z P6 - Fine Grade						
1757	SOG.D3	SOG Q.1-Z P6 - Edgeforms/Diamonds		2	2	24-Oct-22	25-Oct-22				I	SOG Q.1-Z P6 - Edgeforms/Diamonds						
1758	SOG.D3	SOG Q.1-Z P6 - Vapor Barrier		1	1	26-Oct-22	26-Oct-22				I	SOG Q.1-Z P6 - Vapor Barrier						
1759	SOG.D3	SOG Q.1-Z P6 - Install reinforcement		3	3	27-Oct-22	31-Oct-22				I	SOG Q.1-Z P6 - Install reinforcement						
1760	SOG.D3	SOG Q.1-Z P6 - MEP Final Set		1	1	01-Nov-22	01-Nov-22				I	SOG Q.1-Z P6 - MEP Final Set						
1761	SOG.D3	SOG Q.1-Z P6 - Place SOG		1	1	02-Nov-22	02-Nov-22				I	SOG Q.1-Z P6 - Place SOG						
1762	SOG.D3	SOG Q.1-Z P6 - Cure SOG		5	5	03-Nov-22	09-Nov-22				I	SOG Q.1-Z P6 - Cure SOG						
1763	Leave Out			49	49	23-Nov-22	03-Feb-23											
1764	Leave Out Pour 1 C-F.4			16	16	23-Nov-22	16-Dec-22											
1765	SOG.D3	SOG Leave Out P2 - Fine Grade CL C-F.4		3	3	23-Nov-22	29-Nov-22				I	SOG Leave Out P2 - Fine Grade CL C-F.4						
1766	SOG.D3	SOG Leave Out P2 - Edgeforms/Diamonds		2	2	30-Nov-22	01-Dec-22				I	SOG Leave Out P2 - Edgeforms/Diamonds						
1767	SOG.D3	SOG Leave Out P2 - Vapor Barrier		1	1	02-Dec-22	02-Dec-22				I	SOG Leave Out P2 - Vapor Barrier						
1768	SOG.D3	SOG Leave Out P2 - Install reinforcement		3	3	05-Dec-22	07-Dec-22				I	SOG Leave Out P2 - Install reinforcement						
1769	SOG.D3	SOG Leave Out P2 - MEP Final Set		1	1	08-Dec-22	08-Dec-22				I	SOG Leave Out P2 - MEP Final Set						
1770	SOG.D3	SOG Leave Out P2 - Place SOG		1	1	09-Dec-22	09-Dec-22				I	SOG Leave Out P2 - Place SOG						
Remaining Level of Effort				Remaining Work		Milestone												
Actual Work				Critical Remaining Work		Summary												
Page 37 of 74										TASK filter: All Activities							© Oracle Corporation	

QTS HIL2 DC2, DC3, DC5 Construction Schedule				Classic Schedule Layout					12-Jul-22 15:37										
#	Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	2022					2023					2024		
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2		
1819	SOM	SOMD C-F.4 P2 - MEP Final	1	1	30-Nov-22	30-Nov-22						I	SOMD C-F.4 P2 -MEP Final						
1820	SOM	SOMD C-F.4 P2 - Place Slab	1	1	01-Dec-22	01-Dec-22						I	SOMD C-F.4 P2 -Place Slab						
1821	Pour 3 F.4 - J.8						7	7	29-Nov-22	07-Dec-22						▼	07-Dec-22, Pour 3 F.4 - J.8		
1822	SOM	SOMD F.4-J.8 P3 - MEP	2	2	29-Nov-22	30-Nov-22						I	SOMD F.4-J.8 P3 - MEP						
1823	SOM	SOMD F.4-J.8 P3 - Edgeforms/Embeds	2	2	29-Nov-22	30-Nov-22						I	SOMD F.4-J.8 P3 - Edgeforms/Embeds						
1824	SOM	SOMD F.4-J.8 P3 - Install Reinforcement	3	3	01-Dec-22	05-Dec-22						I	SOMD F.4-J.8 P3 - Install Reinforcement						
1825	SOM	SOMD F.4-J.8 P3 - MEP Final	1	06-Dec-22	06-Dec-22							I	SOMD F.4-J.8 P3 - MEP Final						
1826	SOM	SOMD F.4-J.8 P3 - Place Slab	1	1	07-Dec-22	07-Dec-22						I	SOMD F.4-J.8 P3 - Place Slab						
1827	Pour 4 J.8 - M.5						7	7	07-Dec-22	15-Dec-22						▼	15-Dec-22, Pour 4 J.8 - M.5		
1828	SOM	SOMD J.8-M.5 P4 - MEP	2	2	07-Dec-22	08-Dec-22						I	SOMD J.8-M.5 P4 - MEP						
1829	SOM	SOMD J.8-M.5 P4 - Edgeforms/Embeds	2	2	07-Dec-22	08-Dec-22						I	SOMD J.8-M.5 P4 - Edgeforms/Embeds						
1830	SOM	SOMD J.8-M.5 P4 - Install Reinforcement	3	3	09-Dec-22	13-Dec-22						I	SOMD J.8-M.5 P4 - Install Reinforcement						
1831	SOM	SOMD J.8-M.5 P4 - MEP Final	1	1	14-Dec-22	14-Dec-22						I	SOMD J.8-M.5 P4 - MEP Final						
1832	SOM	SOMD J.8-M.5 P4 - Place Slab	1	1	15-Dec-22	15-Dec-22						I	SOMD J.8-M.5 P4 -Place Slab						
1833	Grid L - Q.1						7	7	13-Dec-22	21-Dec-22						▼	21-Dec-22, Grid L - Q.1		
1834	Pour 5 M.5 - Q						7	7	13-Dec-22	21-Dec-22						▼	21-Dec-22, Pour 5 M.5 - Q		
1835	SOM	SOMD M.5-Q P5 - MEP	2	2	13-Dec-22	14-Dec-22						I	SOMD M.5-Q P5 - MEP						
1836	SOM	SOMD M.5-Q P5 - Edgeforms/Embeds	2	2	13-Dec-22	14-Dec-22						I	SOMD M.5-Q P5 - Edgeforms/Embeds						
1837	SOM	SOMD M.5-Q P5 - Install Reinforcement	3	3	15-Dec-22	19-Dec-22						I	SOMD M.5-Q P5 - Install Reinforcement						
1838	SOM	SOMD M.5-Q P5 - MEP Final	1	1	20-Dec-22	20-Dec-22						I	SOMD M.5-Q P5 - MEP Final						
1839	SOM	SOMD M.5-Q P5 - Place Slab	1	1	21-Dec-22	21-Dec-22						I	SOMD M.5-Q P5 - Place Slab						
1840	Grid Q.1 - Z						13	13	28-Dec-22	16-Jan-23						▼	16-Jan-23, Grid Q.1 - Z		
1841	Pour 6 Q - T.3						8	8	28-Dec-22	09-Jan-23						▼	09-Jan-23, Pour 6 Q - T.3		
1842	SOM	SOMD Q-T.3 P6 - As-Built Structure	1	1	28-Dec-22	28-Dec-22						I	SOMD Q-T.3 P6 - As-Built Structure						
1843	SOM	SOMD Q-T.3 P6 - MEP	2	2	29-Dec-22	30-Dec-22						I	SOMD Q-T.3 P6 - MEP						
1844	SOM	SOMD Q-T.3 P6 - Edgeforms/Embeds	2	2	29-Dec-22	30-Dec-22						I	SOMD Q-T.3 P6 - Edgeforms/Embeds						
1845	SOM	SOMD Q-T.3 P6 - Install Reinforcement	3	3	03-Jan-23	05-Jan-23						I	SOMD Q-T.3 P6 - Install Reinforcement						
1846	SOM	SOMD Q-T.3 P6 - MEP Final	1	1	06-Jan-23	06-Jan-23						I	SOMD Q-T.3 P6 - MEP Final						
1847	SOM	SOMD Q-T.3 P6 - Place Slab	1	1	09-Jan-23	09-Jan-23						I	SOMD Q-T.3 P6- Place Slab						
1848	Pour 7 T.3 - W.3						7	7	04-Jan-23	12-Jan-23						▼	12-Jan-23, Pour 7 T.3 - W.3		
1849	SOM	SOMD T.3-W.3 P7 - MEP	2	2	04-Jan-23	05-Jan-23						I	SOMD T.3-W.3 P7 - MEP						
1850	SOM	SOMD T.3-W.3 P7 - Edgeforms/Embeds	2	2	04-Jan-23	05-Jan-23						I	SOMD T.3-W.3 P7 - Edgeforms/Embeds						
1851	SOM	SOMD T.3-W.3 P7 - Install Reinforcement	3	3	06-Jan-23	10-Jan-23						I	SOMD T.3-W.3 P7 - Install Reinforcement						
1852	SOM	SOMD T.3-W.3 P7 - MEP Final	1	1	11-Jan-23	11-Jan-23						I	SOMD T.3-W.3 P7 - MEP Final						
1853	SOM	SOMD T.3-W.3 P7 - Place Slab	1	1	12-Jan-23	12-Jan-23						I	SOMD T.3-W.3 P7 - Place Slab						
1854	Pour 8 W.3 - Z						7	7	06-Jan-23	16-Jan-23						▼	16-Jan-23, Pour 8 W.3 -Z		
1855	SOM	SOMD W.3-Z P8 - MEP	2	2	06-Jan-23	09-Jan-23						I	SOMD W.3-Z P8 - MEP						
1856	SOM	SOMD W.3-Z P8 - Edgeforms/Embeds	2	2	06-Jan-23	09-Jan-23						I	SOMD W.3-Z P8 - Edgeforms/Embeds						
1857	SOM	SOMD W.3-Z P8 - Install Reinforcement	3	3	10-Jan-23	12-Jan-23						I	SOMD W.3-Z P8 - Install Reinforcement						
1858	SOM	SOMD W.3-Z P8 - MEP Final	1	1	13-Jan-23	13-Jan-23						I	SOMD W.3-Z P8 - MEP Final						
1859	SOM	SOMD W.3-Z P8 - Place Slab	1	1	16-Jan-23	16-Jan-23						I	SOMD W.3-Z P8 - Place Slab						
1860	Steel						78	78	31-Oct-22	23-Feb-23						►	23-Feb-23, Steel		
1861	Steel Erection						44	44	31-Oct-22	05-Jan-23						►	05-Jan-23, Steel Erection		
1862	ERCT.D3.1290	Erect Steel - Sequence 11		3	3	31-Oct-22	02-Nov-22						I	Erect Steel - Sequence 11					
1863	ERCT.D3.1310	Erect Steel - Sequence 12		3	3	03-Nov-22	07-Nov-22						I	Erect Steel - Sequence 12					
1864	ERCT.D3.1300	Erect Steel - Sequence 21		2	2	08-Nov-22	09-Nov-22						I	Erect Steel - Sequence 21					
1865	ERCT.D3.1350	Erect Steel - Sequence 31		2	2	10-Nov-22	14-Nov-22						I	Erect Steel - Sequence 31					
1866	ERCT.D3.1320	Erect Steel - Sequence 22		2	2	15-Nov-22	16-Nov-22						I	Erect Steel - Sequence 22	</td				

QTS HIL2 DC2, DC3, DC5 Construction Schedule				Classic Schedule Layout					12-Jul-22 15:37										
#	Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	2022					2023					2024		
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2		
1867	ERCT.D3.1360	Erect Steel - Sequence 32	2	2	17-Nov-22	18-Nov-22						I	Erect Steel - Sequence 32						
1868	ERCT.D3.1330	Erect Steel - Sequence 23	2	2	21-Nov-22	22-Nov-22						I	Erect Steel - Sequence 23						
1869	ERCT.D3.1370	Erect Steel - Sequence 33	2	2	23-Nov-22	28-Nov-22						■	Erect Steel - Sequence 33						
1870	ERCT.D3.1340	Erect Steel - Sequence 24	3	3	29-Nov-22	01-Dec-22						■	Erect Steel - Sequence 24						
1871	ERCT.D3.1380	Erect Steel - Sequence 34	3	3	02-Dec-22	06-Dec-22						■	Erect Steel - Sequence 34						
1872	ERCT.D3.1390	Erect Steel - Sequence 25	2	2	07-Dec-22	08-Dec-22						I	Erect Steel - Sequence 25						
1873	ERCT.D3.1430	Erect Steel - Sequence 35	2	2	09-Dec-22	12-Dec-22						■	Erect Steel - Sequence 35						
1874	ERCT.D3.1400	Erect Steel - Sequence 26	3	3	13-Dec-22	15-Dec-22						I	Erect Steel - Sequence 26						
1875	ERCT.D3.1440	Erect Steel - Sequence 36	3	3	16-Dec-22	20-Dec-22						■	Erect Steel - Sequence 36						
1876	ERCT.D3.1410	Erect Steel - Sequence 27	2	2	21-Dec-22	22-Dec-22						I	Erect Steel - Sequence 27						
1877	ERCT.D3.1450	Erect Steel - Sequence 37	2	2	23-Dec-22	27-Dec-22						■	Erect Steel - Sequence 37						
1878	ERCT.D3.1420	Erect Steel - Sequence 28	2	2	28-Dec-22	29-Dec-22						I	Erect Steel - Sequence 28						
1879	ERCT.D3.1460	Erect Steel - Sequence 38	2	2	30-Dec-22	03-Jan-23						■	Erect Steel - Sequence 38						
1880	ERCT.D3.1470	Erect Steel - Sequence 40	2	2	04-Jan-23	05-Jan-23						I	Erect Steel - Sequence 40						
1881	Stairs			75	75	03-Nov-22	23-Feb-23						23-Feb-23	Stairs					
1882	ERCT.D3.1240	Stair 1 (S Loading Dock)	2	2	03-Nov-22	04-Nov-22						I	Stair 1 (S Loading Dock)						
1883	ERCT.D3.1250	Stair 2 (Admin)	2	2	08-Nov-22	09-Nov-22						I	Stair 2 (Admin)						
1884	ERCT.D3.1280	Stair 3 (Back of House)	2	2	06-Jan-23	09-Jan-23						■	Stair 3 (Back of House)						
1885	ERCT.D3.1260	Exterior Equipment Yard (2 Sets)	10	10	17-Jan-23	30-Jan-23						■	Exterior Equipment Yard (2 Sets)						
1886	ERCT.D3.1270	Exterior Exit Stair (2 Sets)	10	10	09-Feb-23	23-Feb-23						■	Exterior Exit Stair (2 Sets)						
1887	Precast			30	30	12-Jan-23	23-Feb-23						23-Feb-23	Precast					
1888	PCST.D3.1100	Precast - CL Q to L.2 - East Elevation	3	3	12-Jan-23	16-Jan-23						■	Precast - CL Q to L.2 - East Elevation						
1889	PCST.D3.1110	Precast - CL L.2 to C.1 - East Elevation	3	3	17-Jan-23	19-Jan-23						■	Precast - CL L.2 to C.1 - East Elevation						
1890	PCST.D3.1120	Precast - CL C.1 to A - East Elevation	2	2	20-Jan-23	23-Jan-23						■	Precast - CL C.1 to A - East Elevation						
1891	PCST.D3.1130	Precast - CL 8 to 1 - South Elevation	4	4	24-Jan-23	27-Jan-23						■	Precast - CL 8 to 1 - South Elevation						
1892	PCST.D3.1140	Precast - CL A to C.1 - West Elevation	2	2	30-Jan-23	31-Jan-23						■	Precast - CL A to C.1 - West Elevation						
1893	PCST.D3.1150	Precast - CL C.1 to L.2 - West Elevation	3	3	01-Feb-23	03-Feb-23						■	Precast - CL C.1 to L.2 - West Elevation						
1894	PCST.D3.1160	Precast - CL L.2 to Q - West Elevation	3	3	06-Feb-23	08-Feb-23						■	Precast - CL L.2 to Q - West Elevation						
1895	PCST.D3.1170	Precast - CL Q to Z - West Elevation	3	3	09-Feb-23	13-Feb-23						■	Precast - CL Q to Z - West Elevation						
1896	PCST.D3.1180	Precast - CL 1 to 8 - True North	4	4	14-Feb-23	17-Feb-23						■	Precast - CL 1 to 8 - True North						
1897	PCST.D3.1190	Precast - CL Z to Q - East Elevation	3	3	21-Feb-23	23-Feb-23						■	Precast - CL Z to Q - East Elevation						
1898	Glazing and Metal Paneling			42	42	30-Jan-23	29-Mar-23						29-Mar-23	Glazing and Metal Paneling					
1899	GZMP.D3.1040	Metal Paneling - S Elevation	15	15	30-Jan-23	17-Feb-23						■	Metal Paneling - S Elevation						
1900	GZMP.D3.1060	Precast Field Verification for Glazing	2	2	30-Jan-23	31-Jan-23						I	Precast Field Verification for Glazing						
1901	GZMP.D3.1030	Install Glazing - S Elevation CL-8 to CL-1	15	15	02-Mar-23	22-Mar-23						■	Install Glazing - S Elevation CL-8 to CL-1						
1902	GZMP.D3.1050	Install Glazing - W Elevation CL-C to CL-A	5	5	23-Mar-23	29-Mar-23						■	Install Glazing - W Elevation CL-C to CL-A						
1903	Roof			78	78	08-Nov-22	03-Mar-23						03-Mar-23	Roof					
1904	CL A to CL C			62	62	08-Nov-22	08-Feb-23						08-Feb-23	CL A to CL C					
1905	ROOF.D3.132	Roof A-C - Install Curbs	5	5	08-Nov-22	15-Nov-22						■	Roof A-C - Install Curbs						
1906	ROOF.D3.135	Roof A-C - Temp Roof	2	2	15-Nov-22	16-Nov-22						■	Roof A-C - Temp Roof						
1907	ROOF.D3.133	Roof A-C - Roof Penetrations	3	3	16-Nov-22	18-Nov-22						■	Roof A-C - Roof Penetrations						
1908	ROOF.D3.136	Roof A-C - Foam Insulation	5	5	17-Nov-22	23-Nov-22						■	Roof A-C - Foam Insulation						
1909	ROOF.D3.134	Roof A-C - Inspect/Punch/QAAC	1	1	18-Nov-22	18-Nov-22						■	Roof A-C - Inspect/Punch/QAAC						
1910	ROOF.D3.137	Roof A-C - Install Roofing Material	5	5	28-Nov-22	02-Dec-22						■	Roof A-C - Install Roofing Material						
1911	ROOF.D3.138	Roof A-C - Interior Wall Covering	5	5	26-Jan-23	01-Feb-23						■	Roof A-C - Interior Wall Covering						
1912	ROOF.D3.139	Roof A-C - Wall Cap	5	5	02-Feb-23	08-Feb-23						■	Roof A-C - Wall Cap						
1913	CL C to CL L			57	57	21-Nov-22	13-Feb-23						13-Feb-23	CL C to CL L					
1914	ROOF.D3.140	Roof C-L - Install Curbs	5	5	21-Nov-22	29-Nov-22						■	Roof C-L - Install Curbs						

█ Remaining Level of Effort █ Remaining Work ◆ Milestone
█ Actual Work █ Critical Remaining Work ▼ Summary

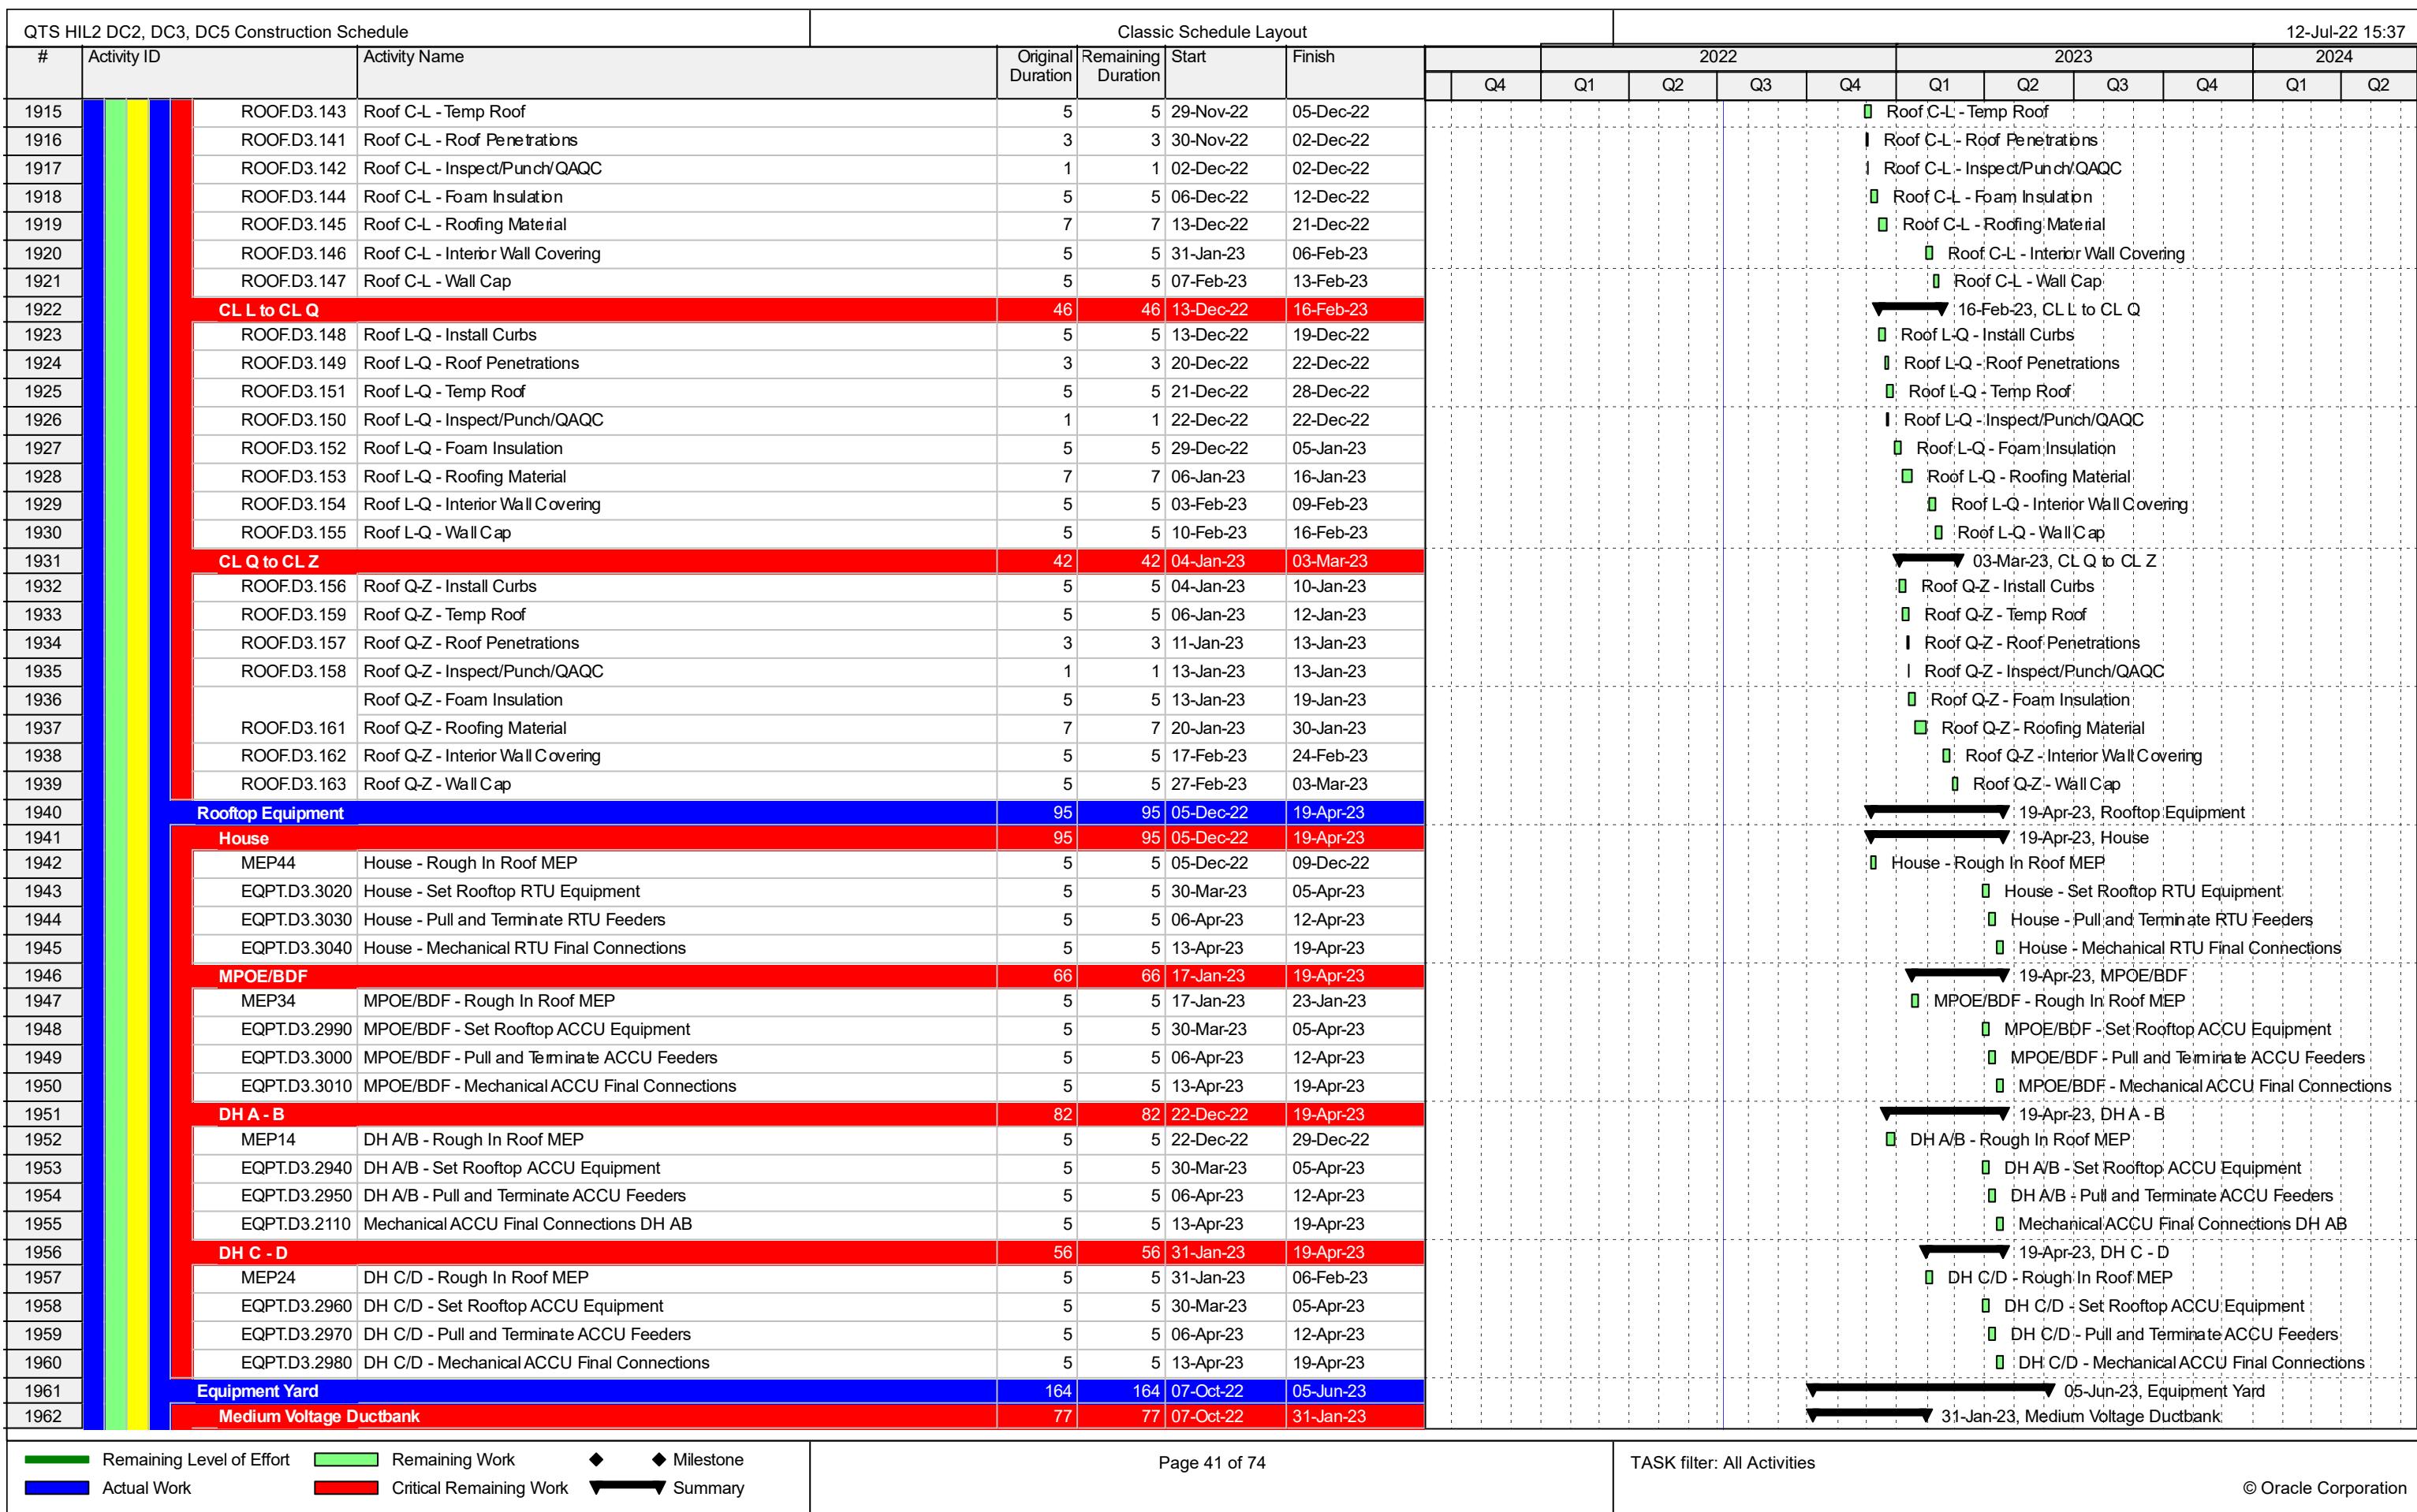


QTS HIL2 DC2, DC3, DC5 Construction Schedule				Classic Schedule Layout					12-Jul-22 15:37									
#	Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	2022					2023					2024	
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	
1963		EXCV.D3.1250 Excavate Medium Voltage Underground - Sequence 1	6	6	07-Oct-22	17-Oct-22												
1964		EXCV.D3.1260 Excavate Medium Voltage Underground - Sequence 2	14	14	18-Oct-22	04-Nov-22												
1965		MVDP.D3.107 Install Medium Voltage Underground - Sequence 1	2	2	18-Oct-22	19-Oct-22												
1966		EXCV.D3.1270 Excavate Medium Voltage Underground - Sequence 3	13	13	07-Nov-22	28-Nov-22												
1967		MVDP.D3.108 Install Medium Voltage Underground - Sequence 2	8	8	07-Nov-22	17-Nov-22												
1968		EXCV.D3.1280 Excavate Medium Voltage Underground - Sequence 4	13	13	29-Nov-22	15-Dec-22												
1969		MVDP.D3.109 Install Medium Voltage Underground - Sequence 3	7	7	29-Nov-22	07-Dec-22												
1970		EXCV.D3.1290 Excavate Medium Voltage Underground - Sequence 5	17	17	16-Dec-22	11-Jan-23												
1971		MVDP.D3.110 Install Medium Voltage Underground - Sequence 4	8	8	16-Dec-22	28-Dec-22												
1972		EXCV.D3.1300 Excavate Medium Voltage Underground - North Vault Group 1	5	5	12-Jan-23	18-Jan-23												
1973		MVDP.D3.111 Install Medium Voltage Underground - Sequence 5	14	14	12-Jan-23	31-Jan-23												
1974		Excavate Medium Voltage Underground - North Vault Group 2	5	5	19-Jan-23	25-Jan-23												
1975		MVDP.D3.112 Install Medium Voltage Underground - North Vault Group 1	4	4	19-Jan-23	24-Jan-23												
1976		MVDP.D3.113 Install Medium Voltage Underground - North Vault Group 2	4	4	26-Jan-23	31-Jan-23												
1977		Equipment Yard Pads and Set Equipment	98	98	17-Jan-23	05-Jun-23												
1978		House	20	20	03-Feb-23	03-Mar-23												
1979		EXCV.D3.4 Yard House - Excavation Transformer Foundations	2	2	03-Feb-23	06-Feb-23												
1980		CONC.D3. Yard House - Form Transformer Foundations DH AB	2	2	06-Feb-23	07-Feb-23												
1981		CONC.D3. Yard House - Rebar Transformer Foundations	2	2	07-Feb-23	08-Feb-23												
1982		CONC.D3. Yard House - Pour Transformer Foundations	1	1	09-Feb-23	09-Feb-23												
1983		CONC.D3. Yard House - Cure Transformer Foundations	5	5	10-Feb-23	16-Feb-23												
1984		EQPT.D3.4 Yard House - Set Transformers	5	5	17-Feb-23	24-Feb-23												
1985		EQPT.D3.4 Yard House - Pull and Terminate Transformers	5	5	27-Feb-23	03-Mar-23												
1986		MPOE/BDF Pads and Set Equipment	38	38	17-Jan-23	10-Mar-23												
1987		SURV.D3.1 Survey MPOE/BDF Equipment Foundations	1	1	17-Jan-23	17-Jan-23												
1988		Pod Pads and Set Equipment	35	35	18-Jan-23	08-Mar-23												
1989		EXCV.D Yard MPOE/BDF - Excavate UPS Pod Foundations	2	2	18-Jan-23	19-Jan-23												
1990		CONC.I Yard MPOE/BDF - Form UPS Pod Foundations MPOE BDF	2	2	19-Jan-23	20-Jan-23												
1991		CONC.I Yard MPOE/BDF - Rebar UPS Pod Foundations	2	2	20-Jan-23	23-Jan-23												
1992		CONC.I Yard MPOE/BDF - Pour UPS Pod Foundations	3	3	24-Jan-23	26-Jan-23												
1993		CONC.I Yard MPOE/BDF - Cure UPS Pod Foundations	5	5	27-Jan-23	02-Feb-23												
1994		CONC.I Yard MPOE/BDF - Install Steel Rails UPS Pod Foundations	3	3	03-Feb-23	07-Feb-23												
1995		EQPT.D Yard MPOE/BDF - Set UPS Pods	5	5	08-Feb-23	14-Feb-23												
1996		EQPT.D Yard MPOE/BDF - Pull and Terminate UPS Pods	15	15	15-Feb-23	08-Mar-23												
1997		Transformer Pads and Set Equipment	28	28	18-Jan-23	27-Feb-23												
1998		EXCV.D Yard MPOE/BDF - Excavation Transformer Foundations	2	2	18-Jan-23	19-Jan-23												
1999		CONC.I Yard MPOE/BDF - Form Transformer Foundations	2	2	19-Jan-23	20-Jan-23												
2000		CONC.I Yard MPOE/BDF - Rebar Transformer Foundations	2	2	20-Jan-23	23-Jan-23												
2001		CONC.I Yard MPOE/BDF - Pour Transformer Foundations	1	1	27-Jan-23	27-Jan-23												
2002		CONC.I Yard MPOE/BDF - Cure Transformer Foundations	5	5	30-Jan-23	03-Feb-23												
2003		EQPT.D Yard MPOE/BDF - Set Transformers	5	5	06-Feb-23	10-Feb-23												
2004		EQPT.D Yard MPOE/BDF - Pull and Terminate Transformers	10	10	13-Feb-23	27-Feb-23												
2005		Generator Pads and Set Equipment	35	35	20-Jan-23	10-Mar-23												
2006		EXCV.D Yard MPOE/BDF - Excavation Generator Foundations	2	2	20-Jan-23	23-Jan-23												
2007		CONC.I Yard MPOE/BDF - Form Generator Foundations	2	2	23-Jan-23	24-Jan-23												
2008		CONC.I Yard MPOE/BDF - Rebar Generator Foundations	3	3	24-Jan-23	26-Jan-23												
2009		CONC.I Yard MPOE/BDF - Pour Generator Foundations	4	4	30-Jan-23	02-Feb-23												
2010		CONC.I Yard MPOE/BDF - Cure Generator Foundations	5	5	03-Feb-23	09-Feb-23												







QTS HIL2 DC2, DC3, DC5 Construction Schedule				Classic Schedule Layout						12-Jul-22 15:37							
#	Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	2022					2023				2024	
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2
2011		EQPT.D Yard MPOE/BDF - Set Generators	5	5	10-Feb-23	16-Feb-23											
2012		EQPT.D Yard MPOE/BDF - Pull and Terminate Generators	15	15	17-Feb-23	10-Mar-23											
2013		Data Hall A and B Pads and Set Equipment			51	51	20-Jan-23	03-Apr-23									
2014		SURV.D3.1 Survey DH A/B - Equipment Foundations	1	1	20-Jan-23	20-Jan-23											
2015		Transformer Pads and Set Equipment			30	30	03-Feb-23	17-Mar-23									
2016		EXCV.D Yard DH A/B - Excavation Transformer Foundations	2	2	03-Feb-23	06-Feb-23											
2017		CONC.I Yard DH A/B - Form Transformer Foundations DH AB	2	2	06-Feb-23	07-Feb-23											
2018		CONC.I Yard DH A/B - Rebar Transformer Foundations	2	2	07-Feb-23	08-Feb-23											
2019		CONC.I Yard DH A/B - Pour Transformer Foundations	1	1	09-Feb-23	09-Feb-23											
2020		CONC.I Yard DH A/B - Cure Transformer Foundations	5	5	10-Feb-23	16-Feb-23											
2021		EQPT.D Yard DH A/B - Set Transformers	5	5	17-Feb-23	24-Feb-23											
2022		EQPT.D Yard DH A/B - Pull and Terminate Transformers	15	15	27-Feb-23	17-Mar-23											
2023		Generator Pads and Set Equipment			39	39	07-Feb-23	03-Apr-23									
2024		EXCV.D Yard DH A/B - Excavation Generator Foundations	2	2	07-Feb-23	08-Feb-23											
2025		CONC.I Yard DH A/B - Form Generator Foundations	2	2	08-Feb-23	09-Feb-23											
2026		CONC.I Yard DH A/B - Rebar Generator Foundations	3	3	09-Feb-23	13-Feb-23											
2027		CONC.I Yard DH A/B - Pour Generator Foundations	4	4	14-Feb-23	17-Feb-23											
2028		CONC.I Yard DH A/B - Cure Generator Foundations	5	5	21-Feb-23	27-Feb-23											
2029		EQPT.D Yard DH A/B - Set Generators	5	5	28-Feb-23	06-Mar-23											
2030		EQPT.D Yard DH A/B - Pull and Terminate Generators	20	20	07-Mar-23	03-Apr-23											
2031		Medium Voltage Pads and Set Equipment			32	32	09-Feb-23	27-Mar-23									
2032		EXCV.D Yard DH A/B - Excavation MV Pads	2	2	09-Feb-23	10-Feb-23											
2033		CONC.I Yard DH A/B - Form MV Pads	2	2	13-Feb-23	14-Feb-23											
2034		CONC.I Yard DH A/B - Rebar MV Foundations	3	3	15-Feb-23	17-Feb-23											
2035		CONC.I Yard DH A/B - Pour MV Pads	4	4	21-Feb-23	24-Feb-23											
2036		CONC.I Yard DH A/B - Cure MV Pads	5	5	27-Feb-23	03-Mar-23											
2037		EQPT.D Yard DH A/B - Set MV Equipment	5	5	06-Mar-23	10-Mar-23											
2038		EQPT.D Yard DH A/B - Pull and Terminate MV Feeders	15	15	07-Mar-23	27-Mar-23											
2039		Data Hall C and D Pads and Set Equipment			71	71	24-Feb-23	05-Jun-23									
2040		SURV.D3.1 Survey DH C/D Equipment Foundations	1	1	24-Feb-23	24-Feb-23											
2041		Transformer Pads and Set Equipment			30	30	27-Feb-23	07-Apr-23									
2042		EXCV.D Yard DH C/D - Excavation Transformer Foundations	2	2	27-Feb-23	28-Feb-23											
2043		CONC.I Yard DH C/D - Form Transformer Foundations	2	2	28-Feb-23	01-Mar-23											
2044		CONC.I Yard DH C/D - Rebar Transformer Foundations	2	2	01-Mar-23	02-Mar-23											
2045		CONC.I Yard DH C/D - Pour Transformer Foundations	1	1	03-Mar-23	03-Mar-23											
2046		CONC.I Yard DH C/D - Cure Transformer Foundations	5	5	06-Mar-23	10-Mar-23											
2047		EQPT.D Yard DH C/D - Set Transformers	5	5	13-Mar-23	17-Mar-23											
2048		EQPT.D Yard DH C/D - Pull and Terminate Transformers	15	15	20-Mar-23	07-Apr-23											
2049		Generator Pads and Set Equipment			48	48	01-Mar-23	05-May-23									
2050		EXCV.D Yard DH C/D - Excavation Generator Foundations	2	2	01-Mar-23	02-Mar-23											
2051		CONC.I Yard DH C/D - Form Generator Foundations	2	2	02-Mar-23	03-Mar-23											
2052		CONC.I Yard DH C/D - Rebar Generator Foundations	3	3	03-Mar-23	07-Mar-23											
2053		CONC.I Yard DH C/D - Pour Generator Foundations	4	4	08-Mar-23	13-Mar-23											
2054		CONC.I Yard DH C/D - Cure Generator Foundations	5	5	14-Mar-23	20-Mar-23											
2055		EQPT.D Yard DH C/D - Set Generators	5	5	21-Mar-23	27-Mar-23											
2056		EQPT.D Yard DH C/D - Pull and Terminate Generators	20	20	10-Apr-23	05-May-23											
2057		Medium Voltage Pads and Set Equipment			66	66	03-Mar-23	05-Jun-23									
2058		EXCV.D Yard DH C/D - Excavation MV Pads	2	2	03-Mar-23	06-Mar-23											

 Remaining Level of Effort
  Remaining Work
  Milestone
  Actual Work
  Critical Remaining Work
  Summary

QTS HIL2 DC2, DC3, DC5 Construction Schedule				Classic Schedule Layout						12-Jul-22 15:37							
#	Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	2022					2023				2024	
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2
2059	CONC.I	Yard DH C/D - Form MV Pads	2	2	07-Mar-23	08-Mar-23						I	Yard DH C/D - Form MV Pads				
2060		Yard DH C/D - Rebar MV Foundations	2	2	09-Mar-23	10-Mar-23						I	Yard DH C/D - Rebar MV Foundations				
2061		Yard DH C/D - Pour MV Pads	4	4	13-Mar-23	16-Mar-23						I	Yard DH C/D - Pour MV Pads				
2062		Yard DH C/D - Cure MV Pads	5	5	17-Mar-23	23-Mar-23						I	Yard DH C/D - Cure MV Pads				
2063		EQPT.D	Yard DH C/D - Set MV Equipment	5	5	24-Mar-23	30-Mar-23					I	Yard DH C/D - Set MV Equipment				
2064		EQPT.D	Yard DH C/D - Pull and Terminate MV Feeders	20	20	08-May-23	05-Jun-23					I	Yard DH C/D - Pull and Terminate MV Feeders				
2065	Elevators			85	85	23-Feb-23	22-Jun-23										
2066	Freight Elevator E03			61	61	23-Feb-23	18-May-23										
2067	ELVT.D3.1330	Freight Elev. 3 - Hoisting Equipment	7	7	23-Feb-23	03-Mar-23						I	Freight Elev. 3 - Hoisting Equipment				
2068	ELVT.D3.1340	Freight Elev. 3 - Pit Rails/Frame/Cab	5	5	06-Mar-23	10-Mar-23						I	Freight Elev. 3 - Pit Rails/Frame/Cab				
2069	ELVT.D3.1350	Freight Elev. 3 - Tirak & Governor Rope	5	5	13-Mar-23	17-Mar-23						I	Freight Elev. 3 - Tirak & Governor Rope				
2070	ELVT.D3.1360	Freight Elev. 3 - Rails	8	8	20-Mar-23	29-Mar-23						I	Freight Elev. 3 - Rails				
2071	ELVT.D3.1370	Freight Elev. 3 - Door entrances	4	4	30-Mar-23	04-Apr-23						I	Freight Elev. 3 - Door entrances				
2072	ELVT.D3.1380	Freight Elev. 3 - Duct/Wire Machine/Startup	7	7	05-Apr-23	13-Apr-23						I	Freight Elev. 3 - Duct/Wire Machine/Startup				
2073	ELVT.D3.1390	Freight Elev. 3 - Rope Elevator/Remove Tirak	4	4	14-Apr-23	19-Apr-23						I	Freight Elev. 3 - Rope Elevator/Remove Tirak				
2074	ELVT.D3.1400	Freight Elev. 3 - Pipe and Wire Hatch Devices	6	6	20-Apr-23	27-Apr-23						I	Freight Elev. 3 - Pipe and Wire Hatch Devices				
2075	ELVT.D3.1410	Freight Elev. 3 - Terminate Devices	8	8	28-Apr-23	09-May-23						I	Freight Elev. 3 - Terminate Devices				
2076	ELVT.D3.1420	Freight Elev. 3 - Clean Rails	2	2	10-May-23	11-May-23						I	Freight Elev. 3 - Clean Rails				
2077	ELVT.D3.1430	Freight Elev. 3 - Inspect	5	5	12-May-23	18-May-23						I	Freight Elev. 3 - Inspect				
2078	Freight Elevator E02A and E02B			85	85	23-Feb-23	22-Jun-23										
2079	ELVT.D3.1440	Freight Elev. E02A/E02B - Hoisting Equipment	10	10	23-Feb-23	08-Mar-23						I	Freight Elev. E02A/E02B - Hoisting Equipment				
2080	ELVT.D3.1450	Freight Elev. E02A/E02B - Pit Rails/Frame/Cab	7	7	09-Mar-23	17-Mar-23						I	Freight Elev. E02A/E02B - Pit Rails/Frame/Cab				
2081	ELVT.D3.1460	Freight Elev. E02A/E02B - Tirak & Governor Rope	7	7	20-Mar-23	28-Mar-23						I	Freight Elev. E02A/E02B - Tirak & Governor Rope				
2082	ELVT.D3.1470	Freight Elev. E02A/E02B - Rails	10	10	29-Mar-23	11-Apr-23						I	Freight Elev. E02A/E02B - Rails				
2083	ELVT.D3.1480	Freight Elev. E02A/E02B - Door entrances	6	6	12-Apr-23	19-Apr-23						I	Freight Elev. E02A/E02B - Door entrances				
2084	ELVT.D3.1490	Freight Elev. E02A/E02B - Duct/Wire Machine/Startup	9	9	20-Apr-23	02-May-23						I	Freight Elev. E02A/E02B - Duct/Wire Machine/Startup				
2085	ELVT.D3.1500	Freight Elev. E02A/E02B - Rope Elevator/Remove Tirak	6	6	03-May-23	10-May-23						I	Freight Elev. E02A/E02B - Rope Elevator/Remove Tirak				
2086	ELVT.D3.1510	Freight Elev. E02A/E02B - Pipe and Wire Hatch Devices	8	8	11-May-23	22-May-23						I	Freight Elev. E02A/E02B - Pipe and Wire Hatch Devices				
2087	ELVT.D3.1520	Freight Elev. E02A/E02B - Terminate Devices	10	10	23-May-23	06-Jun-23						I	Freight Elev. E02A/E02B - Terminate Devices				
2088	ELVT.D3.1530	Freight Elev. E02A/E02B - Clean Rails	4	4	07-Jun-23	12-Jun-23						I	Freight Elev. E02A/E02B - Clean Rails				
2089	ELVT.D3.1540	Freight Elev. E02A/E02B - Inspect	8	8	13-Jun-23	22-Jun-23						I	Freight Elev. E02A/E02B - Inspect				
2090	Passenger Elevator			61	61	23-Feb-23	18-May-23										
2091	ELVT.D3.1550	Pass. Elev. - Hoisting Equipment - Pass Elev.	7	7	23-Feb-23	03-Mar-23						I	Pass. Elev. - Hoisting Equipment - Pass Elev.				
2092	ELVT.D3.1560	Pass. Elev. - Pit Rails/Frame/Cab	5	5	06-Mar-23	10-Mar-23						I	Pass. Elev. - Pit Rails/Frame/Cab				
2093	ELVT.D3.1570	Pass. Elev. - Tirak & Governor Rope	5	5	13-Mar-23	17-Mar-23						I	Pass. Elev. - Tirak & Governor Rope				
2094	ELVT.D3.1580	Pass. Elev. - Rails	8	8	20-Mar-23	29-Mar-23						I	Pass. Elev. - Rails				
2095	ELVT.D3.1590	Pass. Elev. - Door entrances	4	4	30-Mar-23	04-Apr-23						I	Pass. Elev. - Door entrances				
2096	ELVT.D3.1600	Pass. Elev. - Duct/Wire Machine/Startup	7	7	05-Apr-23	13-Apr-23						I	Pass. Elev. - Duct/Wire Machine/Startup				
2097	ELVT.D3.1610	Pass. Elev. - Rope Elevator/Remove Tirak	4	4	14-Apr-23	19-Apr-23						I	Pass. Elev. - Rope Elevator/Remove Tirak				
2098	ELVT.D3.1620	Pass. Elev. - Pipe and Wire Hatch Devices	6	6	20-Apr-23	27-Apr-23						I	Pass. Elev. - Pipe and Wire Hatch Devices				
2099	ELVT.D3.1630	Pass. Elev. - Terminate Devices	8	8	28-Apr-23	09-May-23						I	Pass. Elev. - Terminate Devices				
2100	ELVT.D3.1640	Pass. Elev. - Clean Rails	2	2	10-May-23	11-May-23						I	Pass. Elev. - Clean Rails				
2101	ELVT.D3.1650	Pass. Elev. - Inspect	5	5	12-May-23	18-May-23						I	Pass. Elev. - Inspect				
2102	Interior Buildout			85	85	22-Nov-22	27-Mar-23										
2103	1st Floor Sector 2F1&F2 Lobby/Admin			54	54	22-Nov-22	09-Feb-23										
2104	FRME.D3.262	1st Floor 2F1/F2 - Layout and Frame Walls	13	13	22-Nov-22	12-Dec-22						I	1st Floor 2F1/F2 - Layout and Frame Walls				
2105	MEP.D3.2390	1st Floor 2F1/F2 - Rough-in Plumbing	8	8	22-Nov-22	05-Dec-22						I	1st Floor 2F1/F2 - Rough-in Plumbing				
2106	MEP.D3.2400	1st Floor 2F1/F2 - Rough-in HVAC	7	7	22-Nov-22	02-Dec-22						I	1st Floor 2F1/F2 - Rough-in HVAC				



QTS HIL2 DC2, DC3, DC5 Construction Schedule				Classic Schedule Layout					12-Jul-22 15:37											
#	Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	2022					2023					2024			
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2			
2154	MEP.D3.2530	2nd Floor 2F1/F2 - Rough-in Fire	7	7	07-Dec-22	15-Dec-22														
2155		2nd Floor 2F1/F2 - Rough-in Electric	8	8	07-Dec-22	16-Dec-22														
2156		MEP.D3.2550	2nd Floor 2F1/F2 - Rough-in Low Volt	8	8	07-Dec-22	16-Dec-22													
2157		FRME.D3.281	2nd Floor 2F1/F2 - Install HM Door Frames	5	5	07-Dec-22	13-Dec-22													
2158		MEP.D3.2560	2nd Floor 2F1/F2 - Fire caulk	2	2	19-Dec-22	20-Dec-22													
2159		FRME.D3.277	2nd Floor 2F1/F2 - Insulate	4	4	21-Dec-22	27-Dec-22													
2160		FRME.D3.278	2nd Floor 2F1/F2 - Install Drywall Upper	5	5	28-Dec-22	04-Jan-23													
2161		FRME.D3.279	2nd Floor 2F1/F2 - Hang and Tape Drywall	8	8	05-Jan-23	16-Jan-23													
2162		FNSH.D3.2280	2nd Floor 2F1/F2 - Paint	3	3	17-Jan-23	19-Jan-23													
2163		FRME.D3.280	2nd Floor 2F1/F2 - Grid Ceiling	5	5	20-Jan-23	26-Jan-23													
2164		FNSH.D3.2290	2nd Floor 2F1/F2 - Doors & Hardware	5	5	27-Jan-23	02-Feb-23													
2165		FNSH.D3.2300	2nd Floor 2F1/F2 - Tile in Restroom	5	5	27-Jan-23	02-Feb-23													
2166		FNSH.D3.2310	2nd Floor 2F1/F2 - Finish Electric	5	5	27-Jan-23	02-Feb-23													
2167		FNSH.D3.2320	2nd Floor 2F1/F2 - Drop Remaining Ceiling Tile	1	1	03-Feb-23	03-Feb-23													
2168		FNSH.D3.2330	2nd Floor 2F1/F2 - Finish Plumbing	4	4	06-Feb-23	09-Feb-23													
2169		FNSH.D3.2340	2nd Floor 2F1/F2 - Finish HVAC	3	3	10-Feb-23	14-Feb-23													
2170		2nd Floor 2F1/F2 - Floor Coverings		6	6	15-Feb-23	23-Feb-23													
2171	2nd Floor Sector 2G1&G2 Back of House				39	39	17-Jan-23	13-Mar-23												
2172	FRME.D3.282	2nd Floor 2G1/G2 - Layout and Frame Walls	9	9	17-Jan-23	27-Jan-23														
2173	MEP.D3.2570	2nd Floor 2G1/G2 - Rough-in Plumbing	8	8	17-Jan-23	26-Jan-23														
2174	MEP.D3.2580	2nd Floor 2G1/G2 - Rough-in HVAC	7	7	17-Jan-23	25-Jan-23														
2175	MEP.D3.2590	2nd Floor 2G1/G2 - Rough-in Fire	7	7	17-Jan-23	25-Jan-23														
2176	MEP.D3.2600	2nd Floor 2G1/G2 - Rough-in Electric	8	8	17-Jan-23	26-Jan-23														
2177	MEP.D3.2610	2nd Floor 2G1/G2 - Rough-in Low Volt	8	8	17-Jan-23	26-Jan-23														
2178	FRME.D3.287	2nd Floor 2G1/G2 - Install HM Door Frame	5	5	17-Jan-23	23-Jan-23														
2179	MEP.D3.2620	2nd Floor 2G1/G2 - Fire caulk	2	2	27-Jan-23	30-Jan-23														
2180	FRME.D3.283	2nd Floor 2G1/G2 - Insulate	2	2	31-Jan-23	01-Feb-23														
2181	FRME.D3.284	2nd Floor 2G1/G2 - Install Drywall Upper	5	5	02-Feb-23	08-Feb-23														
2182	FRME.D3.285	2nd Floor 2G1/G2 - Hang and Tape Drywall	7	7	09-Feb-23	17-Feb-23														
2183	FNSH.D3.2380	2nd Floor 2G1/G2 - Tile in Restroom	3	3	09-Feb-23	13-Feb-23														
2184	FNSH.D3.2360	2nd Floor 2G1/G2 - Paint	3	3	21-Feb-23	23-Feb-23														
2185	FRME.D3.286	2nd Floor 2G1/G2 - Wood Ceiling	3	3	24-Feb-23	28-Feb-23														
2186	FNSH.D3.2370	2nd Floor 2G1/G2 - Doors & Hardware	5	5	24-Feb-23	02-Mar-23														
2187	FNSH.D3.2390	2nd Floor 2G1/G2 - Finish Electric	5	5	24-Feb-23	02-Mar-23														
2188	FNSH.D3.2400	2nd Floor 2G1/G2 - Finish Plumbing	4	4	03-Mar-23	08-Mar-23														
2189	FNSH.D3.2410	2nd Floor 2G1/G2 - Finish HVAC	3	3	09-Mar-23	13-Mar-23														
2190	Site Finishes				68	68	03-Feb-23	10-May-23												
2191	Trash Enclosure	15-Feb-23, Trash Enclosure				9	9	03-Feb-23	15-Feb-23											
2192		FOND.D3.205	Trash Encl - Dig Footings	1	1	03-Feb-23	03-Feb-23													
2193		FOND.D3.206	Trash Encl - Form Footings	1	1	03-Feb-23	03-Feb-23													
2194		FOND.D3.207	Trash Encl - Install Rebar & Bolards	1	1	06-Feb-23	06-Feb-23													
2195		FOND.D3.208	Trash Encl - Inspect & Pour	1	1	06-Feb-23	06-Feb-23													
2196		CONC.D3.18t	Trash Encl - Embeds for Gate	3	3	06-Feb-23	08-Feb-23													
2197		SOG.D3.1850	Trash Encl - SOG	2	2	07-Feb-23	08-Feb-23													
2198		CONC.D3.18t	Trash Encl - CMU - Trash Enc.	3	3	09-Feb-23	13-Feb-23													
2199		CONC.D3.18t	Trash Encl - Grout CMU	1	1	14-Feb-23	14-Feb-23													
2200		FNSH.D3.2420	Trash Encl - Install Gate	1	1	15-Feb-23	15-Feb-23													
Remaining Level of Effort				Remaining Work				Milestone				Page 46 of 74					TASK filter: All Activities			
Actual Work				Critical Remaining Work				Summary									© Oracle Corporation			


QTS HIL2 DC2, DC3, DC5 Construction Schedule				Classic Schedule Layout					Timeline View									
#	Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	2022					2023				2024		
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	
2201	  	FNSH.D3.2430	Trash Encl - Install Steel Coping	1	1	15-Feb-23	15-Feb-23									 Trash Encl - Install Steel Coping		
2202		FNSH.D3.2440	Trash Encl - Paint	1	1	15-Feb-23	15-Feb-23									 Trash Encl - Paint		
2203		Parking Lot		24	24	24-Mar-23	26-Apr-23									 26-Apr-23, Parking Lot		
2204		UTIL.D3.1100	Park. Lot - Install/Adjust Manhole Covers	3	3	24-Mar-23	28-Mar-23									 Park. Lot - Install/Adjust Manhole Covers		
2205		FOND.D3.209	Park. Lot - Rough Grade Parking Lot	2	2	24-Mar-23	27-Mar-23									 Park. Lot - Rough Grade Parking Lot		
2206		FNSH.D3.2460	Park. Lot - Landscape Sleeves	3	3	24-Mar-23	28-Mar-23									 Park. Lot - Landscape Sleeves		
2207		CONC.D3.187	Park. Lot - Cut Curbs	2	2	28-Mar-23	29-Mar-23									 Park. Lot - Cut Curbs		
2208		UTIL.D3.1110	Park. Lot - Install Catch Basins	3	3	30-Mar-23	03-Apr-23									 Park. Lot - Install Catch Basins		
2209		MEP.D3.2630	Park. Lot - Street Light Conduits	2	2	04-Apr-23	05-Apr-23									 Park. Lot - Street Light Conduits		
2210		CONC.D3.188	Park. Lot - Install Curbs & Inlets	3	3	04-Apr-23	06-Apr-23									 Park. Lot - Install Curbs & Inlets		
2211		CONC.D3.190	Park. Lot - Street Light Bases	5	5	07-Apr-23	13-Apr-23									 Park. Lot - Street Light Bases		
2212		FOND.D3.210	Park. Lot - Fine Grade Parking Lot	2	2	14-Apr-23	17-Apr-23									 Park. Lot - Fine Grade Parking Lot		
2213		ASPV.D3.1020	Park. Lot - 1st Lift Asphalt - DC2	2	2	18-Apr-23	19-Apr-23									 Park. Lot - 1st Lift Asphalt - DC2		
2214		CONC.D3.189	Park. Lot - Sidewalks	3	3	20-Apr-23	24-Apr-23									 Park. Lot - Sidewalks		
2215		ASPV.D3.1030	Park. Lot - 2nd Lift Asphalt	1	1	25-Apr-23	25-Apr-23									 Park. Lot - 2nd Lift Asphalt		
2216		CONC.D3.191	Park. Lot - Wheel Stops	1	1	26-Apr-23	26-Apr-23									 Park. Lot - Wheel Stops		
2217		CONC.D3.192	Park. Lot - Strip	1	1	26-Apr-23	26-Apr-23									 Park. Lot - Strip		
2218		FNSH.D3.2450	Park. Lot - Signage	1	1	26-Apr-23	26-Apr-23									 Park. Lot - Signage		
2219	Landscape and Fencing		15	15	20-Apr-23	10-May-23										 10-May-23, Landscape and Fencing		
2220	CONC.D3.193	Land Scp. - Site Concrete for Fence - DC2	3	3	20-Apr-23	24-Apr-23									 Land Scp. - Site Concrete for Fence - DC2			
2221	FNSH.D3.2470	Land Scp. - Landscape Power and Irrigation	10	10	25-Apr-23	08-May-23									 Land Scp. - Landscape Power and Irrigation			
2222	FNSH.D3.2480	Land Scp. - Fill Planters	2	2	25-Apr-23	26-Apr-23									 Land Scp. - Fill Planters			
2223	FNSH.D3.2500	Land Scp. - Ground Cover	5	5	25-Apr-23	01-May-23									 Land Scp. - Ground Cover			
2224	FNSH.D3.2510	Land Scp. - Install Fence	7	7	25-Apr-23	03-May-23									 Land Scp. - Install Fence			
2225	FNSH.D3.2490	Land Scp. - Plantings	5	5	27-Apr-23	03-May-23									 Land Scp. - Plantings			
2226	FNSH.D3.2520	Land Scp. - Gates and Access Control	5	5	04-May-23	10-May-23									 Land Scp. - Gates and Access Control			
2227	1st Floor Data Hall		117	117	22-Nov-22	10-May-23										 10-May-23, 1st Floor Data Hall		
2228	House		105	105	22-Nov-22	24-Apr-23									 24-Apr-23, House			
2229	Rough-In		85	85	22-Nov-22	27-Mar-23									 27-Mar-23, Rough-In			
2230	FRME.D3.3	1st Floor House - Layout and Frame Walls	10	10	22-Nov-22	07-Dec-22									 1st Floor House - Layout and Frame Walls			
2231	FRME.D3.3	1st Floor House - Install Door Frames	3	3	08-Dec-22	12-Dec-22									 1st Floor House - Install Door Frames			
2232	MEP.D3.30	1st Floor House - Install Fire Protection	10	10	13-Jan-23	26-Jan-23									 1st Floor House - Install Fire Protection			
2233	MEP.D3.30	1st Floor House - Install OH Mechanical (Plumbing and HVAC)	20	20	13-Jan-23	09-Feb-23									 1st Floor House - Install OH Mechanical (Plumbing and HVAC)			
2234	MEP.D3.30	1st Floor House - Install OH Electrical	20	20	13-Jan-23	09-Feb-23									 1st Floor House - Install OH Electrical			
2235	FRME.D3.3	1st Floor House - Install Drywall Upper	4	4	17-Feb-23	23-Feb-23									 1st Floor House - Install Drywall Upper			
2236	MEP.D3.30	1st Floor House - In-wall Rough-in Electrical	4	4	24-Feb-23	01-Mar-23									 1st Floor House - In-wall Rough-in Electrical			
2237	FRME.D3.3	1st Floor House - Install Structural Grid	10	10	24-Feb-23	09-Mar-23									 1st Floor House - Install Structural Grid			
2238	FRME.D3.3	1st Floor House - Insulate and Inspect	5	5	02-Mar-23	08-Mar-23									 1st Floor House - Insulate and Inspect			
2239	FRME.D3.3	1st Floor House - Hang and Tape Drywall	6	6	09-Mar-23	16-Mar-23									 1st Floor House - Hang and Tape Drywall			
2240	MEP.D3.30	1st Floor House - Install Lighting	5	5	10-Mar-23	16-Mar-23									 1st Floor House - Install Lighting			
2241	MEP.D3.30	1st Floor House - Install Sprinkler Drops	5	5	10-Mar-23	16-Mar-23									 1st Floor House - Install Sprinkler Drops			
2242	FNSH.D3.3	1st Floor House - Paint House	2	2	17-Mar-23	20-Mar-23									 1st Floor House - Paint House			
2243	FRME.D3.3	1st Floor House - Install Overhead Doors	5	5	17-Mar-23	23-Mar-23									 1st Floor House - Install Overhead Doors			
2244	FNSH.D3.3	1st Floor House - Install Finishes	5	5	21-Mar-23	27-Mar-23									 1st Floor House - Install Finishes			
2245	FNSH.D3.3	1st Floor House - Trim Out Electrical Devices	5	5	21-Mar-23	27-Mar-23									 1st Floor House - Trim Out Electrical Devices			
2246	Equipment		25	25	21-Mar-23	24-Apr-23										 24-Apr-23		

QTS HIL2 DC2, DC3, DC5 Construction Schedule				Classic Schedule Layout					12-Jul-22 15:37									
#	Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	2022					2023					2024	
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	
2249		EQPT.D3.5 1st Floor House - Set CRAC Units	5	5	30-Mar-23	05-Apr-23										1st Floor House - Set CRAC Units		
2250		EQPT.D3.5 1st Floor House - Install COD Boards	5	5	30-Mar-23	05-Apr-23										1st Floor House - Install COD Boards		
2251		EQPT.D3.5 1st Floor House - Final Connections CRAC Units	15	15	04-Apr-23	24-Apr-23										1st Floor House - Final Connections CRAC Units		
2252		EQPT.D3.5 1st Floor House - Set HUM	5	5	06-Apr-23	12-Apr-23										1st Floor House - Set HUM		
2253		MPOE 1 and 2	78	78	04-Jan-23	24-Apr-23										24-Apr-23, MPOE 1 and 2		
2254		Rough-In	58	58	04-Jan-23	27-Mar-23										27-Mar-23, Rough-In		
2255	FRME.D3.1	1st Floor MPOE 1/2 - Layout and Frame Walls	10	10	04-Jan-23	17-Jan-23										1st Floor MPOE 1/2 - Layout and Frame Walls		
2256	MEP.D3.18	1st Floor MPOE 1/2 - Install Fire Protection	10	10	13-Jan-23	26-Jan-23										1st Floor MPOE 1/2 - Install Fire Protection		
2257	MEP.D3.18	1st Floor MPOE 1/2 - Install OH Mechanical (Plumbing and HVAC)	20	20	13-Jan-23	09-Feb-23										1st Floor MPOE 1/2 - Install OH Mechanical (Plumbing and HVAC)		
2258	MEP.D3.18	1st Floor MPOE 1/2 - Install OH Electrical	20	20	13-Jan-23	09-Feb-23										1st Floor MPOE 1/2 - Install OH Electrical		
2259	FRME.D3.2	1st Floor MPOE 1/2 - Install Door Frames	3	3	18-Jan-23	20-Jan-23										1st Floor MPOE 1/2 - Install Door Frames		
2260	FRME.D3.2	1st Floor MPOE 1/2 - Install Drywall Upper	4	4	17-Feb-23	23-Feb-23										1st Floor MPOE 1/2 - Install Drywall Upper		
2261	MEP.D3.18	1st Floor MPOE 1/2 - In-wall Rough-in Electrical	4	4	24-Feb-23	01-Mar-23										1st Floor MPOE 1/2 - In-wall Rough-in Electrical		
2262	FRME.D3.2	1st Floor MPOE 1/2 - Install Structural Grid	10	10	24-Feb-23	09-Mar-23										1st Floor MPOE 1/2 - Install Structural Grid		
2263	FRME.D3.2	1st Floor MPOE 1/2 - Insulate and Inspect	5	5	02-Mar-23	08-Mar-23										1st Floor MPOE 1/2 - Insulate and Inspect		
2264	FRME.D3.2	1st Floor MPOE 1/2 - Hang and Tape Drywall	6	6	09-Mar-23	16-Mar-23										1st Floor MPOE 1/2 - Hang and Tape Drywall		
2265	MEP.D3.18	1st Floor MPOE 1/2 - Install Lighting	5	5	10-Mar-23	16-Mar-23										1st Floor MPOE 1/2 - Install Lighting		
2266	MEP.D3.18	1st Floor MPOE 1/2 - Install Sprinkler Drops	5	5	10-Mar-23	16-Mar-23										1st Floor MPOE 1/2 - Install Sprinkler Drops		
2267	FNSH.D3.1	1st Floor MPOE 1/2 - Paint MPOE	2	2	17-Mar-23	20-Mar-23										1st Floor MPOE 1/2 - Paint MPOE		
2268	FRME.D3.2	1st Floor MPOE 1/2 - Install Overhead Doors	5	5	17-Mar-23	23-Mar-23										1st Floor MPOE 1/2 - Install Overhead Doors		
2269	FNSH.D3.1	1st Floor MPOE 1/2 - Install Finishes	5	5	21-Mar-23	27-Mar-23										1st Floor MPOE 1/2 - Install Finishes		
2270	FNSH.D3.1	1st Floor MPOE 1/2 - Trim Out Electrical Devices	5	5	21-Mar-23	27-Mar-23										1st Floor MPOE 1/2 - Trim Out Electrical Devices		
2271	Equipment		25	25	21-Mar-23	24-Apr-23										24-Apr-23, Equipment		
2272	EQPT.D3.2	1st Floor MPOE 1/2 - Set CRAC Units	5	5	21-Mar-23	27-Mar-23										1st Floor MPOE 1/2 - Set CRAC Units		
2273	EQPT.D3.2	1st Floor MPOE 1/2 - Install HDP Panels	10	10	21-Mar-23	03-Apr-23										1st Floor MPOE 1/2 - Install HDP Panels		
2274	EQPT.D3.3	1st Floor MPOE 1/2 - Install Network COD 2000AMP	10	10	21-Mar-23	03-Apr-23										1st Floor MPOE 1/2 - Install Network COD 2000AMP		
2275	EQPT.D3.2	1st Floor MPOE 1/2 - Set HUM	5	5	28-Mar-23	03-Apr-23										1st Floor MPOE 1/2 - Set HUM		
2276	EQPT.D3.2	1st Floor MPOE 1/2 - Install COD Boards	5	5	30-Mar-23	05-Apr-23										1st Floor MPOE 1/2 - Install COD Boards		
2277	EQPT.D3.2	1st Floor MPOE 1/2 - Final Connections CRAC Units	15	15	04-Apr-23	24-Apr-23										1st Floor MPOE 1/2 - Final Connections CRAC Units		
2278	EQPT.D3.2	1st Floor MPOE 1/2 - Install PDU	5	5	04-Apr-23	10-Apr-23										1st Floor MPOE 1/2 - Install PDU		
2279	Systems Gallery 1001 and 1010 DHA		101	101	02-Dec-22	26-Apr-23										26-Apr-23, Systems Gallery 1001 and 1010 DHA		
2280	Rough-In		68	68	02-Dec-22	10-Mar-23										10-Mar-23, Rough-In		
2281	MEP.D3.20	1st Floor DHA SG1001/1010 - Install Fire Protection	15	15	02-Dec-22	22-Dec-22										1st Floor DHA SG1001/1010 - Install Fire Protection		
2282	MEP.D3.20	1st Floor DHA SG1001/1010 - Install OH Mechanical (Plumbing and HVAC)	15	15	23-Dec-22	16-Jan-23										1st Floor DHA SG1001/1010 - Install OH Mechanical (Plumbing and HVAC)		
2283	MEP.D3.20	1st Floor DHA SG1001/1010 - Install OH Electrical	20	20	23-Dec-22	23-Jan-23										1st Floor DHA SG1001/1010 - Install OH Electrical		
2284	FRME.D3.2	1st Floor DHA SG1001/1010 - Layout and Frame Walls	6	6	07-Feb-23	14-Feb-23										1st Floor DHA SG1001/1010 - Layout and Frame Walls		
2285	FRME.D3.2	1st Floor DHA SG1001/1010 - Install Drywall Upper	6	6	09-Feb-23	16-Feb-23										1st Floor DHA SG1001/1010 - Install Drywall Upper		
2286	MEP.D3.20	1st Floor DHA SG1001/1010 - In-wall Rough-in Electrical	5	5	09-Feb-23	15-Feb-23										1st Floor DHA SG1001/1010 - In-wall Rough-in Electrical		
2287	FRME.D3.2	1st Floor DHA SG1001/1010 - Insulate and Inspect	5	5	16-Feb-23	23-Feb-23										1st Floor DHA SG1001/1010 - Insulate and Inspect		
2288	FRME.D3.2	1st Floor DHA SG1001/1010 - Hang and Tape Drywall	6	6	24-Feb-23	03-Mar-23										1st Floor DHA SG1001/1010 - Hang and Tape Drywall		
2289	FNSH.D3.1	1st Floor DHA SG1001/1010 - Paint - DHA SG	2	2	06-Mar-23	07-Mar-23										1st Floor DHA SG1001/1010 - Paint - DHA SG		
2290	FNSH.D3.1	1st Floor DHA SG1001/1010 - Install Finishes	3	3	08-Mar-23	10-Mar-23										1st Floor DHA SG1001/1010 - Install Finishes		
2291	Equipment		38	38	06-Mar-23	26-Apr-23										26-Apr-23, Equipment		
2292	EQPT.D3.2	1st Floor DHA SG1001/1010 - Install Switch Gear	5	5	06-Mar-23	10-Mar-23										1st Floor DHA SG1001/1010 - Install Switch Gear		
2293	EQPT.D3.2	1st Floor DHA SG1001/1010 - Install ATS	5	5	06-Mar-23	10-Mar-23										1st Floor DHA SG1001/1010 - Install ATS		
2294	EQPT.D3.2	1st Floor DHA SG1001/1010 - Install PDU	5	5	06-Mar-23	10-Mar-23										1st Floor DHA SG1001/1010 - Install PDU		
2295	EQPT.D3.2	1st Floor DHA SG1001/1010 - Install Reserve Busway	5	5	06-Mar-23	10-Mar-												


QTS HIL2 DC2, DC3, DC5 Construction Schedule				Classic Schedule Layout					Timeline View									
#	Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	2022					2023				2024		
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	
2297	EQPT.D3.2	1st Floor DHA SG1001/1010 - Install COD Boards	5	5	30-Mar-23	05-Apr-23										1st Floor DHA SG1001/1010 - Install COD Boards		
2298	EQPT.D3.2	1st Floor DHA SG1001/1010 - Install CRAC Units	5	5	30-Mar-23	05-Apr-23										1st Floor DHA SG1001/1010 - Install CRAC Units		
2299	EQPT.D3.2	1st Floor DHA SG1001/1010 - Final Connections CRAC Units	15	15	06-Apr-23	26-Apr-23										1st Floor DHA SG1001/1010 - Final Connections CRAC Units		
2300	EQPT.D3.2	1st Floor DHA SG1001/1010 - Pull and Terminate Feeders	15	15	06-Apr-23	26-Apr-23										1st Floor DHA SG1001/1010 - Pull and Terminate Feeders		
2301	Mechanical Gallery 1002 DHA			98	98	07-Dec-22	26-Apr-23										26-Apr-23, Mechanical Gallery 1002 DH A	
2302	Rough-In						23	23	07-Dec-22	10-Jan-23							10-Jan-23, Rough-In	
2303	FRME.D3.2	1st Floor DHA MG1002 - Layout and Frame Walls	6	6	07-Dec-22	14-Dec-22											1st Floor DHA MG1002 - Layout and Frame Walls	
2304	MEP.D3.19	1st Floor DHA MG1002 - Install Fire Protection	1	1	07-Dec-22	07-Dec-22											1st Floor DHA MG1002 - Install Fire Protection	
2305	MEP.D3.19	1st Floor DHA MG1002 - Install OH Mechanical (Plumbing and HVAC)	3	3	07-Dec-22	09-Dec-22											1st Floor DHA MG1002 - Install OH Mechanical (Plumbing and HVAC)	
2306	MEP.D3.20	1st Floor DHA MG1002 - Install OH Electrical	5	5	07-Dec-22	13-Dec-22											1st Floor DHA MG1002 - Install OH Electrical	
2307	MEP.D3.19	1st Floor DHA MG1002 - In-wall Rough-in Electrical	3	3	08-Dec-22	12-Dec-22											1st Floor DHA MG1002 - In-wall Rough-in Electrical	
2308	FRME.D3.2	1st Floor DHA MG1002 - Insulate and Inspect	5	5	13-Dec-22	19-Dec-22											1st Floor DHA MG1002 - Insulate and Inspect	
2309	FRME.D3.2	1st Floor DHA MG1002 - Install Drywall Upper	6	6	15-Dec-22	22-Dec-22											1st Floor DHA MG1002 - Install Drywall Upper	
2310	FRME.D3.2	1st Floor DHA MG1002 - Hang and Tape Drywall	6	6	23-Dec-22	03-Jan-23											1st Floor DHA MG1002 - Hang and Tape Drywall	
2311	FNSH.D3.1	1st Floor DHA MG1002 - Paint	2	2	04-Jan-23	05-Jan-23											1st Floor DHA MG1002 - Paint	
2312	FNSH.D3.1	1st Floor DHA MG1002 - Install Finishes	3	3	06-Jan-23	10-Jan-23											1st Floor DHA MG1002 - Install Finishes	
2313	Equipment						56	56	07-Feb-23	26-Apr-23							26-Apr-23, Equipment	
2314	EQPT.D3.2	1st Floor DHA MG1002 - Install HDP Boards	5	5	07-Feb-23	13-Feb-23											1st Floor DHA MG1002 - Install HDP Boards	
2315	EQPT.D3.2	1st Floor DHA MG1002 - Pull and Terminate Feeders	15	15	14-Feb-23	07-Mar-23											1st Floor DHA MG1002 - Pull and Terminate Feeders	
2316	EQPT.D3.2	1st Floor DHA MG1002 - Install CRAC Units	5	5	30-Mar-23	05-Apr-23											1st Floor DHA MG1002 - Install CRAC Units	
2317	EQPT.D3.2	1st Floor DHA MG1002 - Final Connections CRAC Units	15	15	06-Apr-23	26-Apr-23											1st Floor DHA MG1002 - Final Connections CRAC Units	
2318	DH A ROOM 1100						41	41	15-Dec-22	13-Feb-23							13-Feb-23, DH A ROOM 1100	
2319	Rough-In						41	41	15-Dec-22	13-Feb-23							13-Feb-23, Rough-In	
2320	FRME.D3.2	1st Floor DHAR1100 - Layout and Frame Walls	10	10	15-Dec-22	29-Dec-22											1st Floor DHAR1100 - Layout and Frame Walls	
2321	FRME.D3.2	1st Floor DHAR1100 - Install Drywall Upper	4	4	30-Dec-22	05-Jan-23											1st Floor DHAR1100 - Install Drywall Upper	
2322	MEP.D3.18	1st Floor DHAR1100 - Rough-In Fire Protection	3	3	06-Jan-23	10-Jan-23											1st Floor DHAR1100 - Rough-In Fire Protection	
2323	MEP.D3.19	1st Floor DHAR1100 - In-wall Rough-in Electrical	4	4	06-Jan-23	11-Jan-23											1st Floor DHAR1100 - In-wall Rough-in Electrical	
2324	MEP.D3.19	1st Floor DHAR1100 - Install OH Mechanical (Plumbing and HVAC)	5	5	12-Jan-23	18-Jan-23											1st Floor DHAR1100 - Install OH Mechanical (Plumbing and HVAC)	
2325	FRME.D3.2	1st Floor DHAR1100 - Insulate and Inspect	5	5	12-Jan-23	18-Jan-23											1st Floor DHAR1100 - Insulate and Inspect	
2326	MEP.D3.19	1st Floor DHAR1100 - Install OH Electrical	7	7	19-Jan-23	27-Jan-23											1st Floor DHAR1100 - Install OH Electrical	
2327	FRME.D3.2	1st Floor DHAR1100 - Hang and Tape Drywall	6	6	30-Jan-23	06-Feb-23											1st Floor DHAR1100 - Hang and Tape Drywall	
2328	FRME.D3.2	1st Floor DHAR1100 - Install Structural Grid	10	10	30-Jan-23	10-Feb-23											1st Floor DHAR1100 - Install Structural Grid	
2329	FNSH.D3.1	1st Floor DHAR1100 - Paint DHAR	2	2	07-Feb-23	08-Feb-23											1st Floor DHAR1100 - Paint DHAR	
2330	FNSH.D3.1	1st Floor DHAR1100 - Install Finishes	3	3	09-Feb-23	13-Feb-23											1st Floor DHAR1100 - Install Finishes	
2331	Systems Gallery 1001 and 1020 DH D						76	76	17-Jan-23	03-May-23							03-May-23, Systems Gallery 1001 and 1020 DH D	
2332	Rough-In						49	49	17-Jan-23	27-Mar-23							27-Mar-23, Rough-In	
2333	MEP.D3.20	1st Floor DHD SG1003/1020 - Install Fire Protection	5	5	17-Jan-23	23-Jan-23											1st Floor DHD SG1003/1020 - Install Fire Protection	
2334	MEP.D3.21	1st Floor DHD SG1003/1020 - Install OH Mechanical (Plumbing and HVAC)	15	15	24-Jan-23	13-Feb-23											1st Floor DHD SG1003/1020 - Install OH Mechanical (Plumbing and HVAC)	
2335	MEP.D3.21	1st Floor DHD SG1003/1020 - Install OH Electrical	20	20	24-Jan-23	21-Feb-23											1st Floor DHD SG1003/1020 - Install OH Electrical	
2336	FRME.D3.2	1st Floor DHD SG1003/1020 - Layout and Frame Walls	6	6	27-Feb-23	06-Mar-23											1st Floor DHD SG1003/1020 - Layout and Frame Walls	
2337	FRME.D3.2	1st Floor DHD SG1003/1020 - Install Drywall Upper	6	6	01-Mar-23	08-Mar-23											1st Floor DHD SG1003/1020 - Install Drywall Upper	
2338	MEP.D3.21	1st Floor DHD SG1003/1020 - In-wall Rough-in Electrical	3	3	01-Mar-23	03-Mar-23											1st Floor DHD SG1003/1020 - In-wall Rough-in Electrical	
2339	FRME.D3.2	1st Floor DHD SG1003/1020 - Insulate and Inspect	5	5	06-Mar-23	10-Mar-23											1st Floor DHD SG1003/1020 - Insulate and Inspect	
2340	FRME.D3.2	1st Floor DHD SG1003/1020 - Hang and Tape Drywall	6	6	13-Mar-23	20-Mar-23											1st Floor DHD SG1003/1020 - Hang and Tape Drywall	
2341	FNSH.D3.1	1st Floor DHD SG1003/1020 - Paint	2	2	21-Mar-23	22-Mar-23											1st Floor DHD SG1003/1020 - Paint	
2342	FNSH.D3.1	1st Floor DHD SG1003/1020 - Install Finishes	3	3	23-Mar-23	27-Mar-23											1st Floor DHD SG1003/1020 - Install Finishes	
2343	Equipment						32	32	21-Mar-23	03-May-23							03-May-23, Equipment	
2344	EQPT.D3.2	1st Floor DHD SG1003/1020 - Install Switch Gear	5	5	21-Mar-23	27-Mar-23											1st Floor DHD SG1003/1020 - Install Switch Gear	
Remaining Level of Effort				Remaining Work		◆◆	◆◆	Milestone									TASK filter: All Activities	

QTS HIL2 DC2, DC3, DC5 Construction Schedule				Classic Schedule Layout						12-Jul-22 15:37								
#	Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	2022					2023				2024		
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	
2345	EQPT.D3.2	1st Floor DHD SG1003/1020 - Install Reserve Busway	5	5	21-Mar-23	27-Mar-23										1st Floor DHD SG1003/1020 - Install Reserve Busway		
2346		1st Floor DHD SG1003/1020 - Install ATS	5	5	28-Mar-23	03-Apr-23										1st Floor DHD SG1003/1020 - Install ATS		
2347		1st Floor DHD SG1003/1020 - Install COD Boards	5	5	30-Mar-23	05-Apr-23										1st Floor DHD SG1003/1020 - Install COD Boards		
2348		1st Floor DHD SG1003/1020 - Install CRAC Units	5	5	31-Mar-23	06-Apr-23										1st Floor DHD SG1003/1020 - Install CRAC Units		
2349		1st Floor DHD SG1003/1020 - Install HDP	5	5	06-Apr-23	12-Apr-23										1st Floor DHD SG1003/1020 - Install HDP		
2350		1st Floor DHD SG1003/1020 - Install PDU	5	5	06-Apr-23	12-Apr-23										1st Floor DHD SG1003/1020 - Install PDU		
2351		1st Floor DHD SG1003/1020 - Final Connections CRAC Units	15	15	07-Apr-23	27-Apr-23										1st Floor DHD SG1003/1020 - Final Connections CRAC Units		
2352		1st Floor DHD SG1003/1020 - Pull and Terminate Feeders	15	15	13-Apr-23	03-May-23										1st Floor DHD SG1003/1020 - Pull and Terminate Feeders		
2353	Mechanical Gallery 1004 DH D			72	72	17-Jan-23	27-Apr-23										27-Apr-23, Mechanical Gallery 1004 DH D	
2354	Rough-In			57	57	17-Jan-23	06-Apr-23										06-Apr-23, Rough-In	
2355	MEP.D3.2C	1st Floor DHD MG1004 - Install Fire Protection	5	5	17-Jan-23	23-Jan-23											1st Floor DHD MG1004 - Install Fire Protection	
2356	MEP.D3.2C	1st Floor DHD MG1004 - In-wall Rough-in Electrical	3	3	24-Jan-23	26-Jan-23											1st Floor DHD MG1004 - In-wall Rough-in Electrical	
2357	MEP.D3.2C	1st Floor DHD MG1004 - Install OH Mechanical (Plumbing and HVAC)	5	5	24-Jan-23	30-Jan-23											1st Floor DHD MG1004 - Install OH Mechanical (Plumbing and HVAC)	
2358	FRME.D3.2	1st Floor DHD MG1004 - Insulate and Inspect	5	5	27-Jan-23	02-Feb-23											1st Floor DHD MG1004 - Insulate and Inspect	
2359	MEP.D3.2C	1st Floor DHD MG1004 - Install OH Electrical	5	5	31-Jan-23	06-Feb-23											1st Floor DHD MG1004 - Install OH Electrical	
2360	FRME.D3.2	1st Floor DHD MG1004 - Layout and Frame Walls	6	6	07-Mar-23	14-Mar-23											1st Floor DHD MG1004 - Layout and Frame Walls	
2361	FRME.D3.2	1st Floor DHD MG1004 - Install Drywall Upper	6	6	15-Mar-23	22-Mar-23											1st Floor DHD MG1004 - Install Drywall Upper	
2362	FRME.D3.2	1st Floor DHD MG1004 - Hang and Tape Drywall	6	6	23-Mar-23	30-Mar-23											1st Floor DHD MG1004 - Hang and Tape Drywall	
2363	FNSH.D3.1	1st Floor DHD MG1004 - Paint	2	2	31-Mar-23	03-Apr-23											1st Floor DHD MG1004 - Paint	
2364	FNSH.D3.1	1st Floor DHD MG1004 - Install Finishes	3	3	04-Apr-23	06-Apr-23											1st Floor DHD MG1004 - Install Finishes	
2365	Equipment			20	20	31-Mar-23	27-Apr-23										27-Apr-23, Equipment	
2366	EQPT.D3.2	1st Floor DHD MG1004 - Install CRAC Units	5	5	31-Mar-23	06-Apr-23											1st Floor DHD MG1004 - Install CRAC Units	
2367	EQPT.D3.2	1st Floor DHD MG1004 - Install HDP Boards	5	5	31-Mar-23	06-Apr-23											1st Floor DHD MG1004 - Install HDP Boards	
2368	EQPT.D3.2	1st Floor DHD MG1004 - Final Connections CRAC Units	15	15	07-Apr-23	27-Apr-23											1st Floor DHD MG1004 - Final Connections CRAC Units	
2369	EQPT.D3.2	1st Floor DHD MG1004 - Pull and Terminate Feeders	15	15	07-Apr-23	27-Apr-23											1st Floor DHD MG1004 - Pull and Terminate Feeders	
2370	DH D ROOM 1200			41	41	15-Mar-23	10-May-23										10-May-23, DH D ROOM 1200	
2371	Rough-In			41	41	15-Mar-23	10-May-23										10-May-23, Rough-In	
2372	FRME.D3.2	1st Floor DHD R1200 - Layout and Frame Walls	10	10	15-Mar-23	28-Mar-23											1st Floor DHD R1200 - Layout and Frame Walls	
2373	FRME.D3.2	1st Floor DHD R1200 - Install Drywall Upper	4	4	29-Mar-23	03-Apr-23											1st Floor DHD R1200 - Install Drywall Upper	
2374	MEP.D3.19	1st Floor DHD R1200 - Install Fire Protection	3	3	04-Apr-23	06-Apr-23											1st Floor DHD R1200 - Install Fire Protection	
2375	MEP.D3.19	1st Floor DHD R1200 - In-wall Rough-in Electrical	4	4	04-Apr-23	07-Apr-23											1st Floor DHD R1200 - In-wall Rough-in Electrical	
2376	MEP.D3.19	1st Floor DHD R1200 - Install OH Mechanical (Plumbing and HVAC)	5	5	10-Apr-23	14-Apr-23											1st Floor DHD R1200 - Install OH Mechanical (Plumbing and HVAC)	
2377	FRME.D3.2	1st Floor DHD R1200 - Insulate and Inspect	5	5	10-Apr-23	14-Apr-23											1st Floor DHD R1200 - Insulate and Inspect	
2378	MEP.D3.19	1st Floor DHD R1200 - Install OH Electrical	7	7	17-Apr-23	25-Apr-23											1st Floor DHD R1200 - Install OH Electrical	
2379	FRME.D3.2	1st Floor DHD R1200 - Hang and Tape Drywall	6	6	26-Apr-23	03-May-23											1st Floor DHD R1200 - Hang and Tape Drywall	
2380	FRME.D3.2	1st Floor DHD R1200 - Install Structural Grid	10	10	26-Apr-23	09-May-23											1st Floor DHD R1200 - Install Structural Grid	
2381	FNSH.D3.1	1st Floor DHD R1200 - Paint	2	2	04-May-23	05-May-23											1st Floor DHD R1200 - Paint	
2382	FNSH.D3.1	1st Floor DHD R1200 - Install Finishes	3	3	08-May-23	10-May-23											1st Floor DHD R1200 - Install Finishes	
2383	2nd Floor Data Hall			99	99	16-Dec-22	08-May-23										08-May-23, 2nd Floor Data Hall	
2384	BDF 1 and 2			88	88	29-Dec-22	03-May-23										03-May-23, BDF 1 and 2	
2385	Rough-In			40	40	29-Dec-22	24-Feb-23										24-Feb-23, Rough-In	
2386	MEP.D3.21	2nd Floor BDF1/2 - Install Fire Protection	3	3	29-Dec-22	03-Jan-23											2nd Floor BDF1/2 - Install Fire Protection	
2387	MEP.D3.21	2nd Floor BDF1/2 - Install OH Mechanical (Plumbing and HVAC)	5	5	04-Jan-23	10-Jan-23											2nd Floor BDF1/2 - Install OH Mechanical (Plumbing and HVAC)	
2388	MEP.D3.21	2nd Floor BDF1/2 - Install OH Electrical	7	7	04-Jan-23	12-Jan-23											2nd Floor BDF1/2 - Install OH Electrical	
2389	FRME.D3.2	2nd Floor BDF1/2 - Layout and Frame Walls	10	10	13-Jan-23	26-Jan-23											2nd Floor BDF1/2 - Layout and Frame Walls	
2390	FRME.D3.2	2nd Floor BDF1/2 - Install Drywall Upper	4	4	27-Jan-23	01-Feb-23											2nd Floor BDF1/2 - Install Drywall Upper	
2391	MEP.D3.21	2nd Floor BDF1/2 - In-wall Rough-in Electrical	4	4	27-Jan-23	01-Feb-23												

QTS HIL2 DC2, DC3, DC5 Construction Schedule				Classic Schedule Layout						12-Jul-22 15:37							
#	Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	2022					2023				2024	
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2
2393		FRME.D3.2 2nd Floor BDF1/2 - Insulate and Inspect	5	5	02-Feb-23	08-Feb-23											
2394		FRME.D3.2 2nd Floor BDF1/2 - Hang and Tape Drywall	6	6	09-Feb-23	16-Feb-23											
2395		FNSH.D3.1 2nd Floor BDF1/2 - Paint	2	2	17-Feb-23	21-Feb-23											
2396		FNSH.D3.1 2nd Floor BDF1/2 - Install Finishes	3	3	22-Feb-23	24-Feb-23											
2397		Equipment			51	51	22-Feb-23	03-May-23									
2398		EQPT.D3.2 2nd Floor BDF1/2 - Install HDP Panels	10	10	22-Feb-23	07-Mar-23											
2399		EQPT.D3.2 2nd Floor BDF1/2 - Set CRAC's	5	5	30-Mar-23	05-Apr-23											
2400		EQPT.D3.2 2nd Floor BDF1/2 - Set HUM	5	5	06-Apr-23	12-Apr-23											
2401		EQPT.D3.2 2nd Floor BDF1/2 - Final Connections CRAC Units	15	15	06-Apr-23	26-Apr-23											
2402		EQPT.D3.2 2nd Floor BDF1/2 - Pull and Terminate Feeders	15	15	13-Apr-23	03-May-23											
2403		Systems Gallery 2001 and 2010 DH B			91	91	16-Dec-22	26-Apr-23									
2404		Rough-In			58	58	16-Dec-22	10-Mar-23									
2405		MEP.D3.23 2nd Floor DHB SG 2001/2010 - Install Fire Protection	5	5	16-Dec-22	22-Dec-22											
2406		MEP.D3.23 2nd Floor DHB SG 2001/2010 - Install OH Mechanical (Plumbing and HVAC)	15	15	23-Dec-22	16-Jan-23											
2407		MEP.D3.23 2nd Floor DHB SG 2001/2010 - Install OH Electrical	20	20	23-Dec-22	23-Jan-23											
2408		FRME.D3.2 2nd Floor DHB SG 2001/2010 - Layout and Frame Walls	6	6	07-Feb-23	14-Feb-23											
2409		MEP.D3.23 2nd Floor DHB SG 2001/2010 - In-wall Rough-in Electrical	3	3	09-Feb-23	13-Feb-23											
2410		FRME.D3.2 2nd Floor DHB SG 2001/2010 - Insulate and Inspect	5	5	14-Feb-23	21-Feb-23											
2411		FRME.D3.2 2nd Floor DHB SG 2001/2010 - Install Drywall Upper	6	6	15-Feb-23	23-Feb-23											
2412		FRME.D3.2 2nd Floor DHB SG 2001/2010 - Hang and Tape Drywall	6	6	24-Feb-23	03-Mar-23											
2413		FNSH.D3.2 2nd Floor DHB SG 2001/2010 - Paint	2	2	06-Mar-23	07-Mar-23											
2414		FNSH.D3.2 2nd Floor DHB SG 2001/2010 - Install Finishes	3	3	08-Mar-23	10-Mar-23											
2415		Equipment			53	53	10-Feb-23	26-Apr-23									
2416		EQPT.D3.2 2nd Floor DHB SG 2001/2010 - Install Switch Gear	5	5	10-Feb-23	16-Feb-23											
2417		EQPT.D3.2 2nd Floor DHB SG 2001/2010 - Install ATS	5	5	10-Feb-23	16-Feb-23											
2418		EQPT.D3.2 2nd Floor DHB SG 2001/2010 - Install HDP	5	5	10-Feb-23	16-Feb-23											
2419		EQPT.D3.2 2nd Floor DHB SG 2001/2010 - Install PDU	5	5	10-Feb-23	16-Feb-23											
2420		EQPT.D3.2 2nd Floor DHB SG 2001/2010 - Install Reserve Busway	5	5	10-Feb-23	16-Feb-23											
2421		EQPT.D3.2 2nd Floor DHB SG 2001/2010 - Install COD Boards	5	5	30-Mar-23	05-Apr-23											
2422		EQPT.D3.2 2nd Floor DHB SG 2001/2010 - Install CRAC Units	5	5	30-Mar-23	05-Apr-23											
2423		EQPT.D3.2 2nd Floor DHB SG 2001/2010 - Final Connections CRAC Units	15	15	06-Apr-23	26-Apr-23											
2424		EQPT.D3.2 2nd Floor DHB SG 2001/2010 - Pull and Terminate Feeders	15	15	06-Apr-23	26-Apr-23											
2425		Mechanical Gallery 2002 DH B			91	91	16-Dec-22	26-Apr-23									
2426		Rough-In			64	64	16-Dec-22	20-Mar-23									
2427		FRME.D3.2 2nd Floor DHB MG 2002 - Layout and Frame Walls	6	6	16-Dec-22	23-Dec-22											
2428		MEP.D3.22 2nd Floor DHB MG 2002 - Install Fire Protection	1	1	16-Dec-22	16-Dec-22											
2429		MEP.D3.22 2nd Floor DHB MG 2002 - Install OH Mechanical (Plumbing and HVAC)	3	3	16-Dec-22	20-Dec-22											
2430		MEP.D3.22 2nd Floor DHB MG 2002 - Install OH Electrical	5	5	16-Dec-22	22-Dec-22											
2431		MEP.D3.22 2nd Floor DHB MG 2002 - In-wall Rough-in Electrical	3	3	19-Dec-22	21-Dec-22											
2432		FRME.D3.2 2nd Floor DHB MG 2002 - Insulate and Inspect	5	5	22-Dec-22	29-Dec-22											
2433		FRME.D3.2 2nd Floor DHB MG 2002 - Install Drywall Upper	6	6	27-Dec-22	04-Jan-23											
2434		FRME.D3.2 2nd Floor DHB MG 2002 - Hang and Tape Drywall	6	6	06-Mar-23	13-Mar-23											
2435		FNSH.D3.2 2nd Floor DHB MG 2002 - Paint	2	2	14-Mar-23	15-Mar-23											
2436		FNSH.D3.2 2nd Floor DHB MG 2002 - Install Finishes	3	3	16-Mar-23	20-Mar-23											
2437		Equipment			32	32	14-Mar-23	26-Apr-23									
2438		EQPT.D3.2 2nd Floor DHB MG 2002 - Install HDP Boards	5	5	14-Mar-23	20-Mar-23											
2439		EQPT.D3.2 2nd Floor DHB MG 2002 - Pull and Terminate Feeders	15	15	21-Mar-23	10-Apr-23											
2440		EQPT.D3.2 2nd Floor DHB MG 2002 - Install CRAC Units	5	5	30-Mar-23	05-Apr-23											



QTS HIL2 DC2, DC3, DC5 Construction Schedule				Classic Schedule Layout						12-Jul-22 15:37							
#	Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	2022					2023				2024	
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2
2441	EQPT.D3.2	2nd Floor DHB MG 2002 - Final Connections CRAC Units	15	15	06-Apr-23	26-Apr-23										2nd Floor DHB MG 2002 -Final Connections CRAC U	
2442	DH B ROOM 2100			64	64	27-Dec-22	28-Mar-23									28-Mar-23; DH B ROOM 2100	
2443	Rough-In			64	64	27-Dec-22	28-Mar-23									28-Mar-23, Rough-In	
2444	FRME.D3.2	2nd Floor DHB R2100 - Layout and Frame Walls	10	10	27-Dec-22	10-Jan-23										2nd Floor DHB R2100 - Layout and Frame Walls	
2445	MEP.D3.21	2nd Floor DHB R2100 - Install Fire Protection	3	3	27-Dec-22	29-Dec-22										2nd Floor DHB R2100 - Install Fire Protection	
2446	MEP.D3.21	2nd Floor DHB R2100 - Install OH Electrical	7	7	27-Dec-22	05-Jan-23										2nd Floor DHB R2100 - Install OH Electrical	
2447	FRME.D3.2	2nd Floor DHB R2100 - Install Structural Grid	10	10	06-Jan-23	19-Jan-23										2nd Floor DHB R2100 - Install Structural Grid	
2448	FRME.D3.2	2nd Floor DHB R2100 - Install Drywall Upper	4	4	11-Jan-23	16-Jan-23										2nd Floor DHB R2100 -Install Drywall Upper	
2449	MEP.D3.21	2nd Floor DHB R2100 - In-wall Rough-in Electrical	4	4	17-Jan-23	20-Jan-23										2nd Floor DHB R2100 - In-wall Rough-in Electrical	
2450	FRME.D3.2	2nd Floor DHB R2100 - Insulate and Inspect	5	5	23-Jan-23	27-Jan-23										2nd Floor DHB R2100 - Insulate and Inspect	
2451	FRME.D3.2	2nd Floor DHB R2100 - Hang and Tape Drywall	6	6	14-Mar-23	21-Mar-23										2nd Floor DHB R2100 - Hang and Tape Drywall	
2452	FNSH.D3.1	2nd Floor DHB R2100 - Paint	2	2	22-Mar-23	23-Mar-23										2nd Floor DHB R2100 - Paint	
2453	FNSH.D3.1	2nd Floor DHB R2100 - Install Finishes	3	3	24-Mar-23	28-Mar-23										2nd Floor DHB R2100- Install Finishes	
2454	Systems Gallery 2020 and 2003 DH C			79	79	17-Jan-23	08-May-23									08-May-23, Systems Gallery 2020 and 2003 DH C	
2455	Rough-In			59	59	17-Jan-23	10-Apr-23									10-Apr-23, Rough-In	
2456	MEP.D3.23	2nd Floor DHC 2020/2003 - Install Fire Protection	5	5	17-Jan-23	23-Jan-23										2nd Floor DHC 2020/2003- Install Fire Protection	
2457	MEP.D3.23	2nd Floor DHC 2020/2003 - Install OH Mechanical (Plumbing and HVAC)	15	15	24-Jan-23	13-Feb-23										2nd Floor DHC 2020/2003 -Install OH Mechanical (Plumbing a	
2458	MEP.D3.23	2nd Floor DHC 2020/2003 - Install OH Electrical	20	20	24-Jan-23	21-Feb-23										2nd Floor DHC 2020/2003 - Install OH Electrical	
2459	FRME.D3.2	2nd Floor DHC 2020/2003 - Layout and Frame Walls	6	6	27-Feb-23	06-Mar-23										2nd Floor DHC 2020/2003 - Layout and Frame Walls	
2460	FRME.D3.2	2nd Floor DHC 2020/2003 - Install Drywall Upper	6	6	07-Mar-23	14-Mar-23										2nd Floor DHC 2020/2003 - Install Drywall Upper	
2461	MEP.D3.23	2nd Floor DHC 2020/2003 - In-wall Rough-in Electrical	3	3	15-Mar-23	17-Mar-23										2nd Floor DHC 2020/2003 -In-wall Rough-in Electrical	
2462	FRME.D3.2	2nd Floor DHC 2020/2003 - Insulate and Inspect	5	5	20-Mar-23	24-Mar-23										2nd Floor DHC 2020/2003 - Insulate and Inspect	
2463	FRME.D3.2	2nd Floor DHC 2020/2003 - Hang and Tape Drywall	6	6	27-Mar-23	03-Apr-23										2nd Floor DHC 2020/2003 - Hang and Tape Drywall	
2464	FNSH.D3.2	2nd Floor DHC 2020/2003 - Paint	2	2	04-Apr-23	05-Apr-23										2nd Floor DHC 2020/2003 - Paint	
2465	FNSH.D3.2	2nd Floor DHC 2020/2003 - Install Finishes	3	3	06-Apr-23	10-Apr-23										2nd Floor DHC 2020/2003 - Install Finishes	
2466	Equipment			51	51	27-Feb-23	08-May-23									08-May-23, Equipment	
2467	EQPT.D3.2	2nd Floor DHC 2020/2003 - Install ATS	5	5	27-Feb-23	03-Mar-23										2nd Floor DHC 2020/2003 - Install ATS	
2468	EQPT.D3.2	2nd Floor DHC 2020/2003 - Install HDP	5	5	27-Feb-23	03-Mar-23										2nd Floor DHC 2020/2003 - Install HDP	
2469	EQPT.D3.2	2nd Floor DHC 2020/2003 - Install PDU	5	5	27-Feb-23	03-Mar-23										2nd Floor DHC 2020/2003 - Install PDU	
2470	EQPT.D3.2	2nd Floor DHC 2020/2003 - Install Reserve Busway	5	5	27-Feb-23	03-Mar-23										2nd Floor DHC 2020/2003 - Install Reserve Busway	
2471	EQPT.D3.2	2nd Floor DHC 2020/2003 - Install COD Boards	5	5	04-Apr-23	10-Apr-23										2nd Floor DHC 2020/2003 - Install COD Boards	
2472	EQPT.D3.2	2nd Floor DHC 2020/2003 - Install CRAC Units	5	5	04-Apr-23	10-Apr-23										2nd Floor DHC 2020/2003 - Install CRAC Units	
2473	EQPT.D3.2	2nd Floor DHC 2020/2003 - Install Switch Gear	5	5	11-Apr-23	17-Apr-23										2nd Floor DHC 2020/2003 - Install Switch Gear	
2474	EQPT.D3.2	2nd Floor DHC 2020/2003 - Final Connections CRAC Units	15	15	11-Apr-23	01-May-23										2nd Floor DHC 2020/2003 - Final Connections CRA	
2475	EQPT.D3.2	2nd Floor DHC 2020/2003 - Pull and Terminate Feeders	15	15	18-Apr-23	08-May-23										2nd Floor DHC 2020/2003 - Pull and Terminate Fee	
2476	Mechanical Gallery 2003 DH C			74	74	17-Jan-23	01-May-23									01-May-23, Mechanical Gallery 2003 DH C	
2477	Rough-In			30	30	17-Jan-23	28-Feb-23									28-Feb-23, Rough-In	
2478	FRME.D3.2	2nd Floor DHC MG 2003 - Layout and Frame Walls	5	5	17-Jan-23	23-Jan-23										2nd Floor DHC MG 2003 - Layout and Frame Walls	
2479	MEP.D3.22	2nd Floor DHC MG 2003 - Install Fire Protection	1	1	17-Jan-23	17-Jan-23										2nd Floor DHC MG 2003 - Install Fire Protection	
2480	MEP.D3.22	2nd Floor DHC MG 2003 - Install OH Mechanical (Plumbing and HVAC)	3	3	17-Jan-23	19-Jan-23										2nd Floor DHC MG 2003 - Install OH Mechanical (Plumbi	
2481	MEP.D3.23	2nd Floor DHC MG 2003 - Install OH Electrical	5	5	17-Jan-23	23-Jan-23										2nd Floor DHC MG 2003 - Install OH Electrical	
2482	MEP.D3.22	2nd Floor DHC MG 2003 - In-wall Rough-in Electrical	3	3	18-Jan-23	20-Jan-23										2nd Floor DHC MG 2003 - In-wall Rough-in Electrical	
2483	FRME.D3.2	2nd Floor DHC MG 2003 - Insulate and Inspect	5	5	23-Jan-23	27-Jan-23										2nd Floor DHC MG 2003 - Insulate and Inspect	
2484	FRME.D3.2	2nd Floor DHC MG 2003 - Install Drywall Upper	6	6	24-Jan-23	31-Jan-23										2nd Floor DHC MG 2003 - Install Drywall Upper	
2485	FRME.D3.2	2nd Floor DHC MG 2003 - Hang and Tape Drywall	6	6	01-Feb-23	08-Feb-23										2nd Floor DHC MG 2003 - Hang and Tape Drywall	
2486	FNSH.D3.2	2nd Floor DHC MG 2003 - Paint	2	2	09-Feb-23	10-Feb-23										2nd Floor DHC MG 2003 - Paint	
2487	FNSH.D3.2	2nd Floor DHC MG 2003 - Install Finishes	3	3	24-Feb-23	28-Feb-23				</							

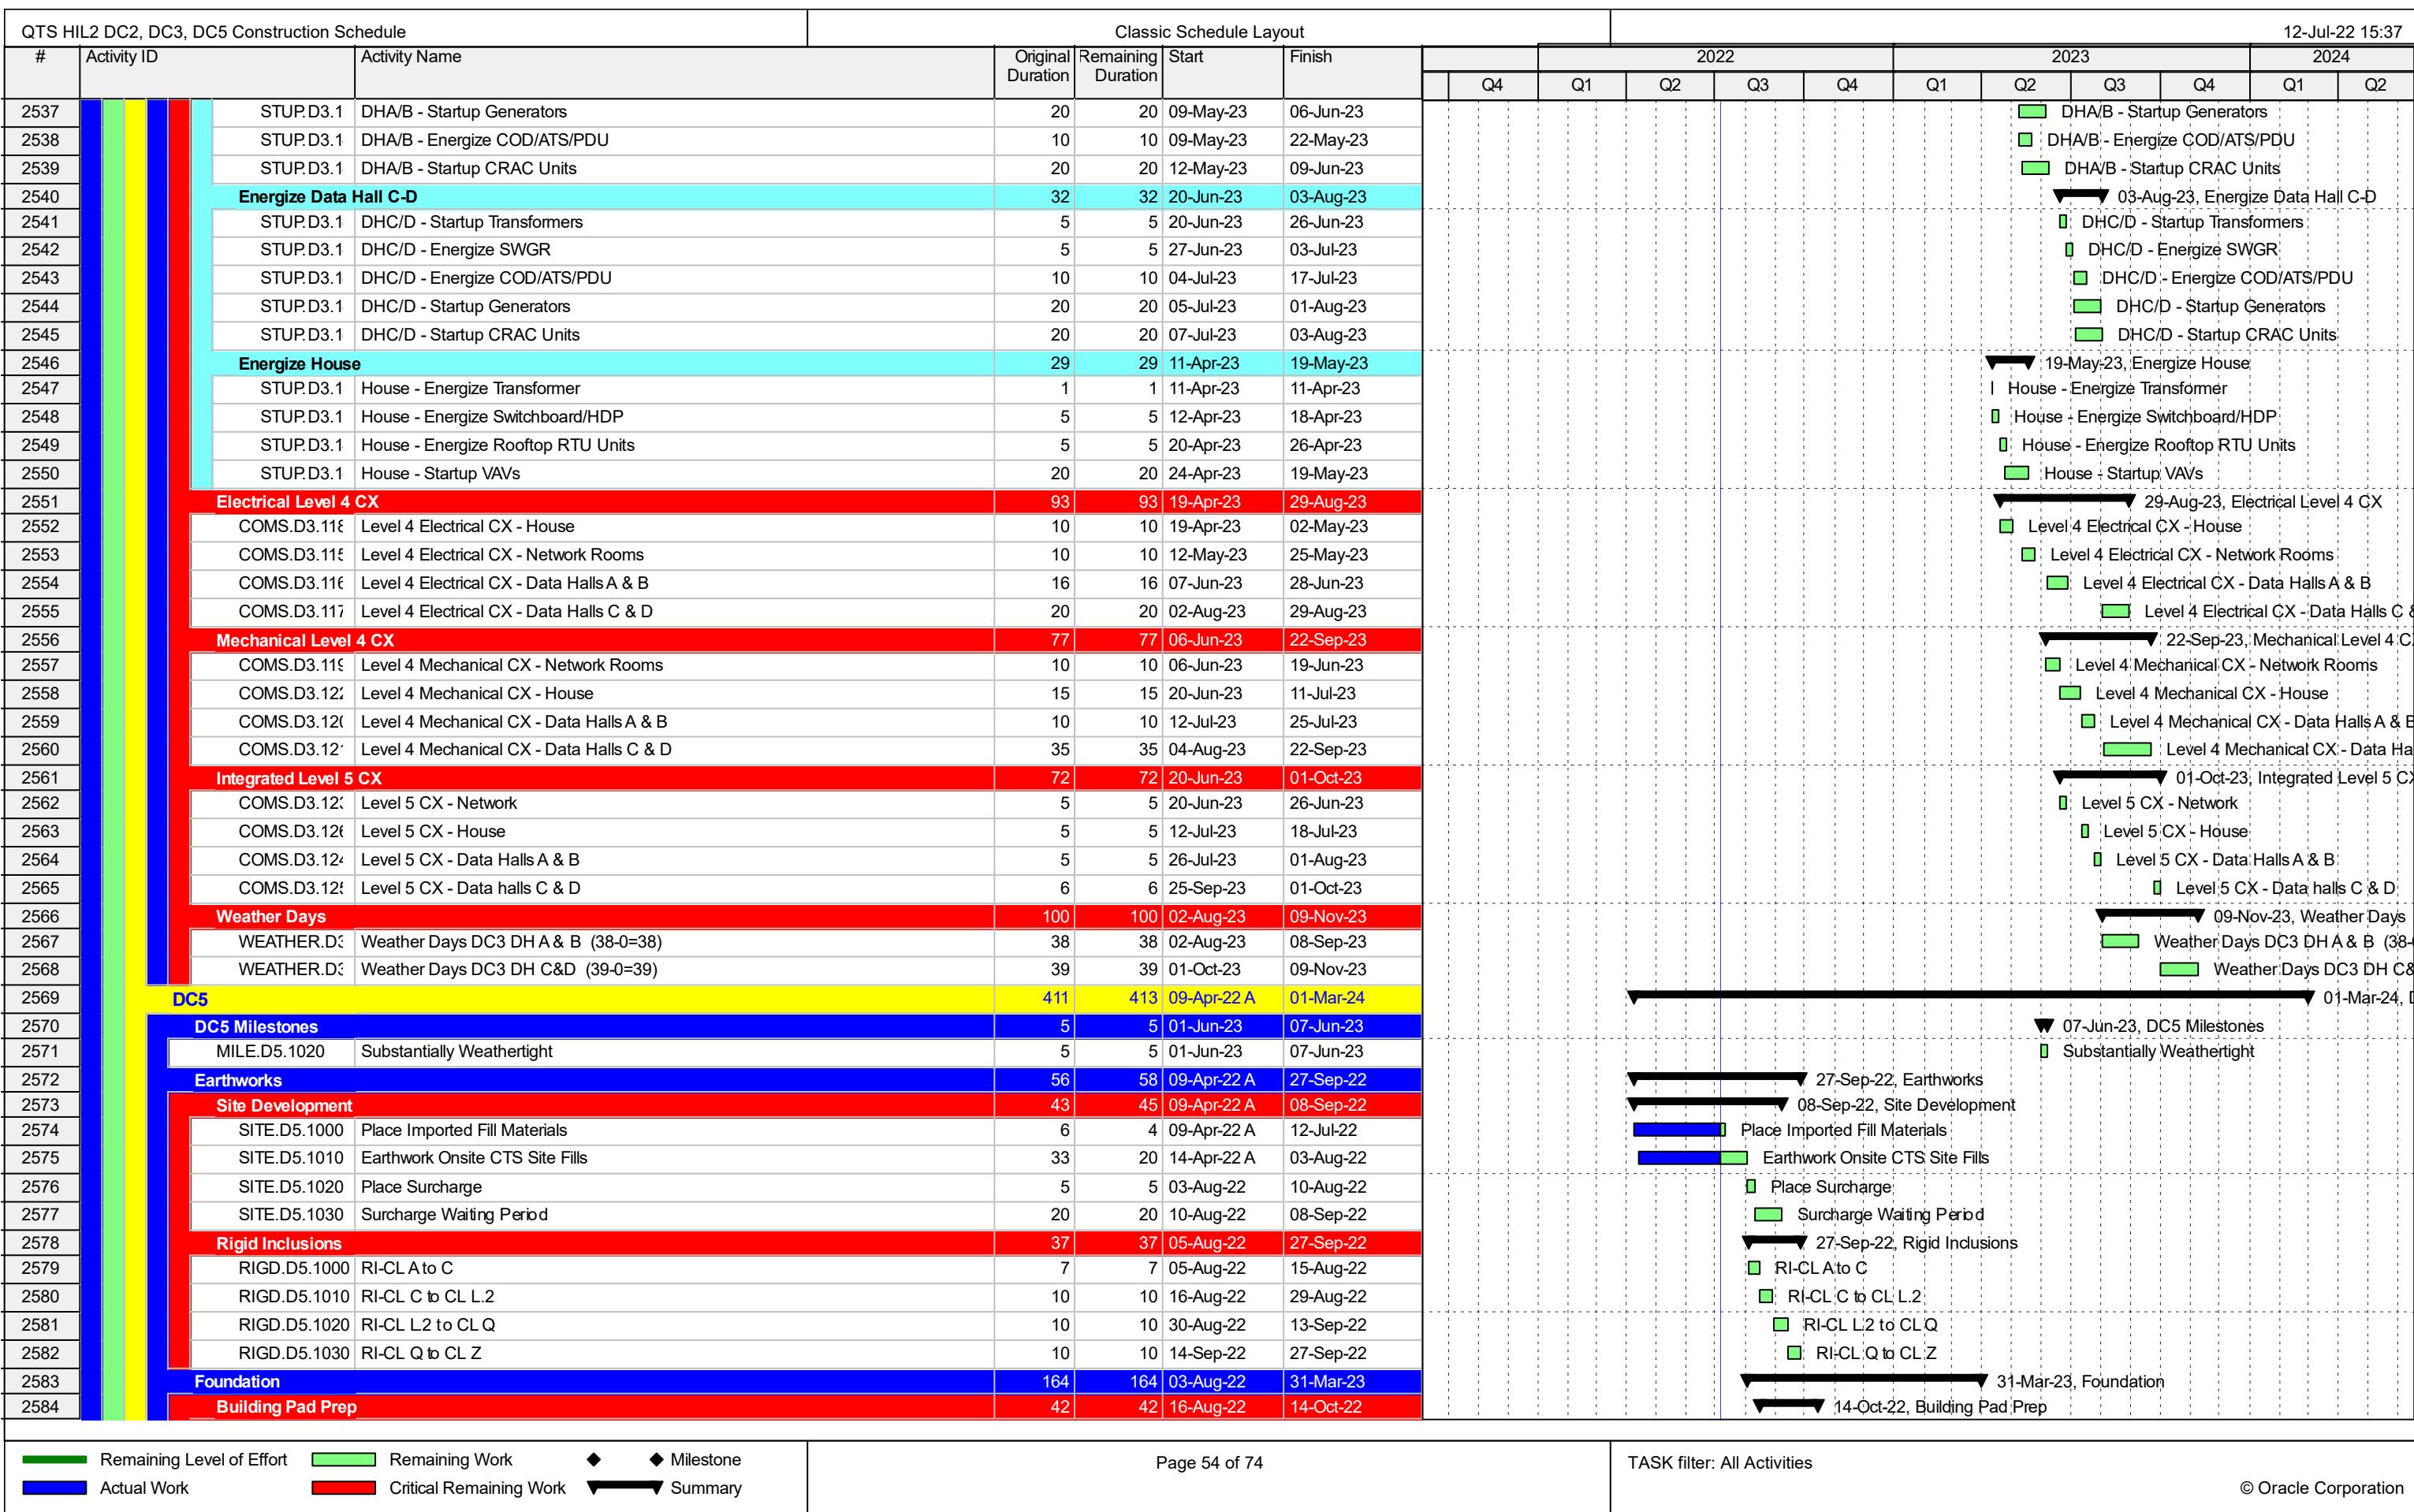

QTS HIL2 DC2, DC3, DC5 Construction Schedule				Classic Schedule Layout					12-Jul-22 15:37											
#	Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish			2022					2023					2024	
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2			
2585	Area Wide	FOND.D5.1 Move Surcharge to DC5	10	10	16-Aug-22	29-Aug-22													▼ 29-Aug-22, Area Wide	
2586		FOND.D5.1 Rock and Compact Slab		5	16-Aug-22	22-Aug-22													Move Surcharge to DC5	
2587		UTIL.D5.11 Under-slab Utilities CL A to C		5	23-Aug-22	29-Aug-22													Rock and Compact Slab	
2588		FOND.D5.1 Backfill/Compact CL A to C		5	16-Sep-22	22-Sep-22													▼ 22-Sep-22, Grid A - C	
2589		UTIL.D5.11 Under-slab Utilities CL C to L2		5	09-Sep-22	15-Sep-22													Under-slab Utilities CL A to C	
2590		FOND.D5.1 Backfill/Compact CL A to C		5	16-Sep-22	22-Sep-22													Backfill/Compact CL A to C	
2591		UTIL.D5.11 Under-slab Utilities CL C to L2		5	16-Sep-22	22-Sep-22													▼ 29-Sep-22, Grid C - L	
2592		FOND.D5.1 Backfill/Compact CL C to L2		5	23-Sep-22	29-Sep-22													Under-slab Utilities CL C to L2	
2593		UTIL.D5.11 Under-slab Utilities CL L.2 to Q		5	23-Sep-22	29-Sep-22													Backfill/Compact CL C to L2	
2594		FOND.D5.1 Backfill/Compact CL L.2 to Q		5	30-Sep-22	06-Oct-22													▼ 06-Oct-22, Grid L - Q.1	
2595		UTIL.D5.11 Under-slab Utilities CL L.2 to Q		5	23-Sep-22	29-Sep-22													Under-slab Utilities CL L.2 to Q	
2596		FOND.D5.1 Backfill/Compact CL L.2 to Q		5	30-Sep-22	06-Oct-22													Backfill/Compact CL L.2 to Q	
2597		UTIL.D5.11 Under-slab Utilities CL Q to Z		5	30-Sep-22	06-Oct-22													▼ 14-Oct-22, Grid Q.1 - Z	
2598		FOND.D5.1 Backfill/Compact CL Q to Z		5	07-Oct-22	14-Oct-22													Under-slab Utilities CL Q to Z	
2599		UTIL.D5.11 Under-slab Utilities CL Q to Z		5	07-Oct-22	14-Oct-22													Backfill/Compact CL Q to Z	
2600		DC5 Foundations			85	85	03-Aug-22	07-Dec-22											▼ 07-Dec-22, DC5 Foundations	
2601		Grid A-C			69	69	03-Aug-22	10-Nov-22											▼ 10-Nov-22, Grid A-C	
2602		FOND.D5.1 Found A-C - Survey Footing Excavation		3	3	03-Aug-22	08-Aug-22												Found A-C - Survey Footing Excavation	
2603		FOND.D5.1 Found A-C - Dig Footings		3	3	13-Oct-22	17-Oct-22												Found A-C - Dig Footings	
2604		FOND.D5.1 Found A-C - Survey Formwork		1	1	18-Oct-22	18-Oct-22												Found A-C - Survey Formwork	
2605		FOND.D5.1 Found A-C - Form Foundations (#1 Formwork Delivery)		5	5	19-Oct-22	25-Oct-22												Found A-C - Form Foundations (#1 Formwork Delivery)	
2606		FOND.D5.1 Found A-C - Install Anchor Bolts		5	5	19-Oct-22	25-Oct-22												Found A-C - Install Anchor Bolts	
2607		FOND.D5.1 Found A-C - Install Reinforcement		5	5	20-Oct-22	26-Oct-22												Found A-C - Install Reinforcement	
2608		FOND.D5.1 Found A-C - Install Elevator Pit		5	5	27-Oct-22	02-Nov-22												Found A-C - Install Elevator Pit	
2609		FOND.D5.1 Found A-C - Place Foundations		1	1	27-Oct-22	27-Oct-22												Found A-C - Place Foundations	
2610		FOND.D5.1 Found A-C - Strip Foundations		3	3	28-Oct-22	01-Nov-22												Found A-C - Strip Foundations	
2611		FOND.D5.1 Found A-C - Plinths and Grade Beams		5	5	28-Oct-22	03-Nov-22												Found A-C - Plinths and Grade Beams	
2612		FOND.D5.1 Found A-C - Waterproof/Insulate		3	3	03-Nov-22	07-Nov-22												Found A-C - Waterproof/Insulate	
2613		FOND.D5.1 Found A-C - Backfill Foundations		3	3	08-Nov-22	10-Nov-22												Found A-C - Backfill Foundations	
2614	Grid C-L			77	77	03-Aug-22	23-Nov-22												▼ 23-Nov-22, Grid C-L	
2615	FOND.D5.1 Found C-L - Survey Footing Excavation		3	3	03-Aug-22	08-Aug-22												Found C-L - Survey Footing Excavation		
2616	FOND.D5.1 Found C-L - Dig Footings		3	3	18-Oct-22	20-Oct-22												Found C-L - Dig Footings		
2617	FOND.D5.1 Found C-L - Survey Formwork		1	1	21-Oct-22	21-Oct-22												Found C-L - Survey Formwork		
2618	FOND.D5.1 Found C-L - Form Foundations (#2 Formwork Delivery)		5	5	26-Oct-22	01-Nov-22												Found C-L - Form Foundations (#2 Formwork Delivery)		
2619	FOND.D5.1 Found C-L - Instal Anchor Bolts		5	5	26-Oct-22	01-Nov-22												Found C-L - Instal Anchor Bolts		
2620	FOND.D5.1 Found C-L - Instal Reinforcement		5	5	02-Nov-22	08-Nov-22												Found C-L - Instal Reinforcement		
2621	FOND.D5.1 Found C-L - Place Foundations		1	1	09-Nov-22	09-Nov-22												Found C-L - Place Foundations		
2622	FOND.D5.1 Found C-L - Strip Foundations		3	3	10-Nov-22	15-Nov-22												Found C-L - Strip Foundations		
2623	FOND.D5.1 Found C-L - Plinths and Grade Beams		5	5	10-Nov-22	17-Nov-22												Found C-L - Plinths and Grade Beams		
2624	FOND.D5.1 Found C-L - Waterproof/Insulate		3	3	16-Nov-22	18-Nov-22												Found C-L - Waterproof/Insulate		
2625	FOND.D5.1 Found C-L - Backfill Foundations		3	3	21-Nov-22	23-Nov-22												Found C-L - Backfill Foundations		
2626	Grid L-Q.1			78	78	03-Aug-22	28-Nov-22												▼ 28-Nov-22, Grid L-Q.1	
2627	FOND.D5.1 Found L-Q.1 - Survey Footing Excavation		3	3	03-Aug-22	08-Aug-22												Found L-Q.1 - Survey Footing Excavation		
2628	FOND.D5.1 Found L-Q.1 - Dig Footings		3	3	14-Sep-22	16-Sep-22												Found L-Q.1 - Dig Footings		
2629	FOND.D5.1 Found L-Q.1 - Survey Formwork		1	1	19-Sep-22	19-Sep-22												Found L-Q.1 - Survey Formwork		
2630	FOND.D5.1 Found L-Q.1 - Form Foundations (Formwork From A-C)		5	5	02-Nov-22	08-Nov-22												Found L-Q.1 - Form Foundations (Formwork From A-C)		
2631	FOND.D5.1 Found L-Q.1 - Install Anchor Bolts		5	5	02-Nov-22	08-Nov-22												Found L-Q.1 - Install Anchor Bolts		
2632																				


QTS HIL2 DC2, DC3, DC5 Construction Schedule				Classic Schedule Layout					Timeline View								
#	Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	2022		2023				2024				
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2
2633	FOND.D5.1	Found L-Q.1 - Place Foundations	1	1	10-Nov-22	10-Nov-22						I	Found L-Q.1 - Place Foundations				
2634	FOND.D5.1	Found L-Q.1 - Strip Foundations		3	3	14-Nov-22	16-Nov-22					I	Found L-Q.1 - Strip Foundations				
2635	FOND.D5.1	Found L-Q.1 - Plinths and Grade Beams		5	5	14-Nov-22	18-Nov-22					■	Found L-Q.1 - Plinths and Grade Beams				
2636	FOND.D5.1	Found L-Q.1 - Waterproof/Insulate		3	3	17-Nov-22	21-Nov-22					I	Found L-Q.1 - Waterproof/Insulate				
2637	FOND.D5.1	Found L-Q.1 - Backfill Foundations		3	3	22-Nov-22	28-Nov-22					■	Found L-Q.1 - Backfill Foundations				
2638	Grid Q.1-Z		60	60	08-Sep-22	07-Dec-22								▼ 07-Dec-22, Grid Q.1-Z			
2639	FOND.D5.1	Grid Q.1-Z - Survey Footing Excavation		3	3	08-Sep-22	13-Sep-22					■	Grid Q.1-Z - Survey Footing Excavation				
2640	FOND.D5.1	Grid Q.1-Z - Dig Footings		3	3	28-Sep-22	30-Sep-22					I	Grid Q.1-Z - Dig Footings				
2641	FOND.D5.1	Grid Q.1-Z - Survey Formwork		1	1	03-Oct-22	03-Oct-22					I	Grid Q.1-Z - Survey Formwork				
2642	FOND.D5.1	Grid Q.1-Z - Form Foundations (Formwork From C-L)		5	5	14-Nov-22	18-Nov-22					■	Grid Q.1-Z - Form Foundations (Formwork From C-L)				
2643	FOND.D5.1	Grid Q.1-Z - Install Anchor Bolts		5	5	14-Nov-22	18-Nov-22					■	Grid Q.1-Z - Install Anchor Bolts				
2644	FOND.D5.1	Grid Q.1-Z - Install Reinforcement		5	5	15-Nov-22	21-Nov-22					■	Grid Q.1-Z - Install Reinforcement				
2645	FOND.D5.1	Grid Q.1-Z - Place Foundations		1	1	22-Nov-22	22-Nov-22					I	Grid Q.1-Z - Place Foundations				
2646	FOND.D5.1	Grid Q.1-Z - Strip Foundations		3	3	23-Nov-22	29-Nov-22					■	Grid Q.1-Z - Strip Foundations				
2647	FOND.D5.1	Grid Q.1-Z - Plinths and Grade Beams		5	5	23-Nov-22	01-Dec-22					■	Grid Q.1-Z - Plinths and Grade Beams				
2648	FOND.D5.1	Grid Q.1-Z - Waterproof/Insulate		3	3	30-Nov-22	02-Dec-22					I	Grid Q.1-Z - Waterproof/Insulate				
2649	FOND.D5.1	Grid Q.1-Z - Backfill Foundations		3	3	05-Dec-22	07-Dec-22					I	Grid Q.1-Z - Backfill Foundations				
2650	DC5 Slab On Grade		95	95	14-Nov-22	31-Mar-23								▼ 31-Mar-23, DC5 Slab On Grade			
2651	Grid A-C		16	16	14-Nov-22	07-Dec-22								▼ 07-Dec-22, Grid A-C			
2652	Pour 1		16	16	14-Nov-22	07-Dec-22								▼ 07-Dec-22, Pour 1			
2653	SOG.D5	SOG A-C P1 - Fine Grade CLA to C		3	3	14-Nov-22	16-Nov-22					I	SOG A-C P1 - Fine Grade CLA to C				
2654	SOG.D5	SOG A-C P1 - Edgeforms/Diamonds		2	2	17-Nov-22	18-Nov-22					I	SOG A-C P1 - Edgeforms/Diamonds				
2655	SOG.D5	SOG A-C P1 - Vapor Barrier		1	1	21-Nov-22	21-Nov-22					I	SOG A-C P1 - Vapor Barrier				
2656	SOG.D5	SOG A-C P1 - Install reinforcement		3	3	22-Nov-22	28-Nov-22					■	SOG A-C P1 - Install reinforcement				
2657	SOG.D5	SOG A-C P1 - MEP Final Set		1	1	29-Nov-22	29-Nov-22					I	SOG A-C P1 - MEP Final Set				
2658	SOG.D5	SOG A-C P1 - Place SOG		1	1	30-Nov-22	30-Nov-22					I	SOG A-C P1 - Place SOG				
2659	SOG.D5	SOG A-C P1 - Cure SOG		5	5	01-Dec-22	07-Dec-22					■	SOG A-C P1 - Cure SOG				
2660	Grid C-L		16	16	28-Nov-22	19-Dec-22								▼ 19-Dec-22, Grid C-L			
2661	Pour 2		16	16	28-Nov-22	19-Dec-22								▼ 19-Dec-22, Pour 2			
2662	SOG.D5	SOG C-L P2 - Fine Grade		3	3	28-Nov-22	30-Nov-22					I	SOG C-L P2 - Fine Grade				
2663	SOG.D5	SOG C-L P2 - Edgeforms/Diamonds		2	2	01-Dec-22	02-Dec-22					I	SOG C-L P2 - Edgeforms/Diamonds				
2664	SOG.D5	SOG C-L P2 - Vapor Barrier		1	1	05-Dec-22	05-Dec-22					I	SOG C-L P2 - Vapor Barrier				
2665	SOG.D5	SOG C-L P2 - Install reinforcement		3	3	06-Dec-22	08-Dec-22					■	SOG C-L P2 - Install reinforcement				
2666	SOG.D5	SOG C-L P2 - MEP Final Set		1	1	09-Dec-22	09-Dec-22					I	SOG C-L P2 - MEP Final Set				
2667	SOG.D5	SOG C-L P2 - Place SOG		1	1	12-Dec-22	12-Dec-22					I	SOG C-L P2 - Place SOG				
2668	SOG.D5	SOG C-L P2 - Cure SOG		5	5	13-Dec-22	19-Dec-22					■	SOG C-L P2 - Cure SOG				
2669	Pour 3		16	16	28-Nov-22	19-Dec-22								▼ 19-Dec-22, Pour 3			
2670	SOG.D5	SOG C-L P3 - Fine Grade		3	3	28-Nov-22	30-Nov-22					I	SOG C-L P3 - Fine Grade				
2671	SOG.D5	SOG C-L P3 - Edgeforms/Diamonds		2	2	01-Dec-22	02-Dec-22					I	SOG C-L P3 - Edgeforms/Diamonds				
2672	SOG.D5	SOG C-L P3 - Vapor Barrier		1	1	05-Dec-22	05-Dec-22					I	SOG C-L P3 - Vapor Barrier				
2673	SOG.D5	SOG C-L P3 - Install reinforcement		3	3	06-Dec-22	08-Dec-22					■	SOG C-L P3 - Install reinforcement				
2674	SOG.D5	SOG C-L P3 - MEP Final Set		1	1	09-Dec-22	09-Dec-22					I	SOG C-L P3 - MEP Final Set				
2675	SOG.D5	SOG C-L P3 - Place SOG		1	1	12-Dec-22	12-Dec-22					I	SOG C-L P3 - Place SOG				
2676	SOG.D5	SOG C-L P3 - Cure SOG		5	5	13-Dec-22	19-Dec-22					■	SOG C-L P3 - Cure SOG				
2677	Grid L-Q.1		16	16	29-Nov-22	20-Dec-22								▼ 20-Dec-22, Grid L-Q.1			
2678	Pour 4		16	16	29-Nov-22	20-Dec-22								▼ 20-Dec-22, Pour 4			
2679	SOG.D5	SOG L-Q.1 P4 - Fine Grade		3	3	29-Nov-22	01-Dec-22					I	SOG L-Q.1 P4 - Fine Grade				
2680	SOG.D5	SOG L-Q.1 P4 - Edgeforms/Diamonds		2	2	02-Dec-22	05-Dec-22					■	SOG L-Q.1 P4 - Edgeforms/Diamonds				

QTS HIL2 DC2, DC3, DC5 Construction Schedule				Classic Schedule Layout					Timeline View											
#	Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	2022					2023				2024				
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2			
2681	SOG.D5	SOG L-Q.1 P4 - Vapor Barrier	1	1	06-Dec-22	06-Dec-22						I	SOG L-Q.1 P4 - Vapor Barrier							
2682	SOG.D5	SOG L-Q.1 P4 - Install reinforcement	3	3	07-Dec-22	09-Dec-22						I	SOG L-Q.1 P4 - Install reinforcement							
2683	SOG.D5	SOG L-Q.1 P4 - MEP Final Set	1	1	12-Dec-22	12-Dec-22						I	SOG L-Q.1 P4 - MEP Final Set							
2684	SOG.D5	SOG L-Q.1 P4 - Place SOG	1	1	13-Dec-22	13-Dec-22						I	SOG L-Q.1 P4 - Place SOG							
2685	SOG.D5	SOG L-Q.1 P4 - Cure SOG	5	5	14-Dec-22	20-Dec-22						I	SOG L-Q.1 P4 - Cure SOG							
2686	Grid Q.1-Z			16	16	08-Dec-22	30-Dec-22						▼ 30-Dec-22, Grid Q.1-Z							
2687	Pour 5			16	16	08-Dec-22	30-Dec-22						▼ 30-Dec-22, Pour 5							
2688	SOG.D5	SOG Q.1-Z P5 - Fine Grade	3	3	08-Dec-22	12-Dec-22						I	SOG Q.1-Z P5 - Fine Grade							
2689	SOG.D5	SOG Q.1-Z P5 - Edgeforms/Diamonds	2	2	13-Dec-22	14-Dec-22						I	SOG Q.1-Z P5 - Edgeforms/Diamonds							
2690	SOG.D5	SOG Q.1-Z P5 - Vapor Barrier	1	1	15-Dec-22	15-Dec-22						I	SOG Q.1-Z P5 - Vapor Barrier							
2691	SOG.D5	SOG Q.1-Z P5 - Install reinforcement	3	3	16-Dec-22	20-Dec-22						I	SOG Q.1-Z P5 - Install reinforcement							
2692	SOG.D5	SOG Q.1-Z P5 - MEP Final Set	1	1	21-Dec-22	21-Dec-22						I	SOG Q.1-Z P5 - MEP Final Set							
2693	SOG.D5	SOG Q.1-Z P5 - Place SOG	1	1	22-Dec-22	22-Dec-22						I	SOG Q.1-Z P5 - Place SOG							
2694	SOG.D5	SOG Q.1-Z P5 - Cure SOG	5	5	23-Dec-22	30-Dec-22						I	SOG Q.1-Z P5 - Cure SOG							
2695	Pour 6			16	16	08-Dec-22	30-Dec-22						▼ 30-Dec-22, Pour 6							
2696	SOG.D5	SOG Q.1-Z P6 - Fine Grade	3	3	08-Dec-22	12-Dec-22						I	SOG Q.1-Z P6 - Fine Grade							
2697	SOG.D5	SOG Q.1-Z P6 - Edgeforms/Diamonds	2	2	13-Dec-22	14-Dec-22						I	SOG Q.1-Z P6 - Edgeforms/Diamonds							
2698	SOG.D5	SOG Q.1-Z P6 - Vapor Barrier	1	1	15-Dec-22	15-Dec-22						I	SOG Q.1-Z P6 - Vapor Barrier							
2699	SOG.D5	SOG Q.1-Z P6 - Install reinforcement	3	3	16-Dec-22	20-Dec-22						I	SOG Q.1-Z P6 - Install reinforcement							
2700	SOG.D5	SOG Q.1-Z P6 - MEP Final Set	1	1	21-Dec-22	21-Dec-22						I	SOG Q.1-Z P6 - MEP Final Set							
2701	SOG.D5	SOG Q.1-Z P6 - Place SOG	1	1	22-Dec-22	22-Dec-22						I	SOG Q.1-Z P6 - Place SOG							
2702	SOG.D5	SOG Q.1-Z P6 - Cure SOG	5	5	23-Dec-22	30-Dec-22						I	SOG Q.1-Z P6 - Cure SOG							
2703	Leave Out			44	44	30-Jan-23	31-Mar-23						▼ 31-Mar-23, Leave Out							
2704	Leave Out Pour 1 C-F.4			16	16	30-Jan-23	21-Feb-23						▼ 21-Feb-23, Leave Out Pour 1 C-F.4							
2705	SOG.D5	SOG Leave Out P2 - Fine Grade CLC-F.4	3	3	30-Jan-23	01-Feb-23						I	SOG Leave Out P2 - Fine Grade CLC-F.4							
2706	SOG.D5	SOG Leave Out P2 - Edgeforms/Diamonds	2	2	02-Feb-23	03-Feb-23						I	SOG Leave Out P2 - Edgeforms/Diamonds							
2707	SOG.D5	SOG Leave Out P2 - Vapor Barrier	1	1	06-Feb-23	06-Feb-23						I	SOG Leave Out P2 - Vapor Barrier							
2708	SOG.D5	SOG Leave Out P2 - Install reinforcement	3	3	07-Feb-23	09-Feb-23						I	SOG Leave Out P2 - Install reinforcement							
2709	SOG.D5	SOG Leave Out P2 - MEP Final Set	1	1	10-Feb-23	10-Feb-23						I	SOG Leave Out P2 - MEP Final Set							
2710	SOG.D5	SOG Leave Out P2 - Place SOG	1	1	13-Feb-23	13-Feb-23						I	SOG Leave Out P2 - Place SOG							
2711	SOG.D5	SOG Leave Out P2 - Cure SOG	5	5	14-Feb-23	21-Feb-23						I	SOG Leave Out P2 - Cure SOG							
2712	Leave Out Pour 2 F.4-J.8			16	16	03-Feb-23	27-Feb-23						▼ 27-Feb-23, Leave Out Pour 2 F.4-J.8							
2713	SOG.D5	SOG Leave Out P3 - Fine Grade CL F.4-J.8	3	3	03-Feb-23	07-Feb-23						I	SOG Leave Out P3 - Fine Grade CL F.4-J.8							
2714	SOG.D5	SOG Leave Out P3 - Edgeforms/Diamonds	2	2	08-Feb-23	09-Feb-23						I	SOG Leave Out P3 - Edgeforms/Diamonds							
2715	SOG.D5	SOG Leave Out P3 - Vapor Barrier	1	1	10-Feb-23	10-Feb-23						I	SOG Leave Out P3 - Vapor Barrier							
2716	SOG.D5	SOG Leave Out P3 - Install reinforcement	3	3	13-Feb-23	15-Feb-23						I	SOG Leave Out P3 - Install reinforcement							
2717	SOG.D5	SOG Leave Out P3 - MEP Final Set	1	1	16-Feb-23	16-Feb-23						I	SOG Leave Out P3 - MEP Final Set							
2718	SOG.D5	SOG Leave Out P3 - Place SOG	1	1	17-Feb-23	17-Feb-23						I	SOG Leave Out P3 - Place SOG							
2719	SOG.D5	SOG Leave Out P3 - Cure SOG	5	5	21-Feb-23	27-Feb-23						I	SOG Leave Out P3 - Cure SOG							
2720	Leave Out Pour 3 J.8 - M.5			16	16	13-Feb-23	07-Mar-23						▼ 07-Mar-23, Leave Out Pour 3 J.8 - M.5							
2721	SOG.D5	SOG Leave Out P4 - Fine Grade CL J.8 - M.5	3	3	13-Feb-23	15-Feb-23						I	SOG Leave Out P4 - Fine Grade CL J.8 - M.5							
2722	SOG.D5	SOG Leave Out P4 - Edgeforms/Diamonds	2	2	16-Feb-23	17-Feb-23						I	SOG Leave Out P4 - Edgeforms/Diamonds							
2723	SOG.D5	SOG Leave Out P4 - Vapor Barrier	1	1	21-Feb-23	21-Feb-23						I	SOG Leave Out P4 - Vapor Barrier							
2724	SOG.D5	SOG Leave Out P4 - Install reinforcement	3	3	22-Feb-23	24-Feb-23						I	SOG Leave Out P4 - Install reinforcement							
2725	SOG.D5	SOG Leave Out P4 - MEP Final Set	1	1	27-Feb-23	27-Feb-23						I	SOG Leave Out P4 - MEP Final Set							
2726	SOG.D5	SOG Leave Out P4 - Place SOG	1	1	28-Feb-23	28-Feb-23						I	SOG Leave Out P4 - Place SOG							
2727	SOG.D5	SOG Leave Out P4 - Cure SOG	5	5	01-Mar-23	07-Mar-23						I	SOG Leave Out P4 - Cure SOG							
2728	Leave Out Pour 4 M.5 - Q			16	16	17-Feb-23	13-Mar-23						▼ 13-Mar-23, Leave Out Pour 4 M.5 - Q							
Remaining Level of Effort				Remaining Work				◆	◆	Milestone	Timeline View					Task Filter: All Activities				
Actual Work				Critical Remaining Work				▼	▼	Summary						© Oracle Corporation				


QTS HIL2 DC2, DC3, DC5 Construction Schedule				Classic Schedule Layout					12-Jul-22 15:37									
#	Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	2022					2023					2024	
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	
2777	SOM	SOMD M.5-Q P5 - Install Reinforcement	3	3	17-Feb-23	22-Feb-23						I	SOMD M.5-Q P5 - Install Reinforcement					
2778	SOM	SOMD M.5-Q P5 - MEP Final	1	1	23-Feb-23	23-Feb-23						I	SOMD M.5-Q P5 - MEP Final					
2779	SOM	SOMD M.5-Q P5 - Place Slab	1	1	24-Feb-23	24-Feb-23						I	SOMD M.5-Q P5 - Place Slab					
2780	Grid Q.1 - Z						13	13	02-Mar-23	20-Mar-23								
2781	Pour 6 Q - T.3						8	8	02-Mar-23	13-Mar-23								
2782	SOM	SOMD Q.T.3 P6 - As-Built Structure	1	1	02-Mar-23	02-Mar-23						I	SOMD Q.T.3 P6 - As-Built Structure					
2783	SOM	SOMD Q.T.3 P6 - MEP	2	2	03-Mar-23	06-Mar-23						I	SOMD Q.T.3 P6 - MEP					
2784	SOM	SOMD Q.T.3 P6 - Edgeforms/Embeds	2	2	03-Mar-23	06-Mar-23						I	SOMD Q.T.3 P6 - Edgeforms/Embeds					
2785	SOM	SOMD Q.T.3 P6 - Install Reinforcement	3	3	07-Mar-23	09-Mar-23						I	SOMD Q.T.3 P6 - Install Reinforcement					
2786	SOM	SOMD Q.T.3 P6 - MEP Final	1	1	10-Mar-23	10-Mar-23						I	SOMD Q.T.3 P6 - MEP Final					
2787	SOM	SOMD Q.T.3 P6 - Place Slab	1	1	13-Mar-23	13-Mar-23						I	SOMD Q.T.3 P6 - Place Slab					
2788	Pour 7 T.3 - W.3						7	7	08-Mar-23	16-Mar-23								
2789	SOM	SOMD T.3-W.3 P7 - MEP	2	2	08-Mar-23	09-Mar-23						I	SOMD T.3-W.3 P7 - MEP					
2790	SOM	SOMD T.3-W.3 P7 - Edgeforms/Embeds	2	2	08-Mar-23	09-Mar-23						I	SOMD T.3-W.3 P7 - Edgeforms/Embeds					
2791	SOM	SOMD T.3-W.3 P7 - Install Reinforcement	3	3	10-Mar-23	14-Mar-23						I	SOMD T.3-W.3 P7 - Install Reinforcement					
2792	SOM	SOMD T.3-W.3 P7 - MEP Final	1	1	15-Mar-23	15-Mar-23						I	SOMD T.3-W.3 P7 - MEP Final					
2793	SOM	SOMD T.3-W.3 P7 - Place Slab	1	1	16-Mar-23	16-Mar-23						I	SOMD T.3-W.3 P7 - Place Slab					
2794	Pour 8 W.3 - Z						7	7	10-Mar-23	20-Mar-23								
2795	SOM	SOMD W.3-Z P8 - MEP	2	2	10-Mar-23	13-Mar-23						I	SOMD W.3-Z P8 - MEP					
2796	SOM	SOMD W.3-Z P8 - Edgeforms/Embeds	2	2	10-Mar-23	13-Mar-23						I	SOMD W.3-Z P8 - Edgeforms/Embeds					
2797	SOM	SOMD W.3-Z P8 - Install Reinforcement	3	3	14-Mar-23	16-Mar-23						I	SOMD W.3-Z P8 - Install Reinforcement					
2798	SOM	SOMD W.3-Z P8 - MEP Final	1	1	17-Mar-23	17-Mar-23						I	SOMD W.3-Z P8 - MEP Final					
2799	SOM	SOMD W.3-Z P8 - Place Slab	1	1	20-Mar-23	20-Mar-23						I	SOMD W.3-Z P8 - Place Slab					
2800	Steel						78	78	06-Jan-23	26-Apr-23								
2801	Steel Erection						44	44	06-Jan-23	09-Mar-23								
2802	ERCT.D5.1530	Erect Steel - Sequence 11	3	3	06-Jan-23	10-Jan-23						I	Erect Steel - Sequence 11					
2803	ERCT.D5.1550	Erect Steel - Sequence 12	3	3	11-Jan-23	13-Jan-23						I	Erect Steel - Sequence 12					
2804	ERCT.D5.1540	Erect Steel - Sequence 21	2	2	16-Jan-23	17-Jan-23						I	Erect Steel - Sequence 21					
2805	ERCT.D5.1590	Erect Steel - Sequence 31	2	2	18-Jan-23	19-Jan-23						I	Erect Steel - Sequence 31					
2806	ERCT.D5.1560	Erect Steel - Sequence 22	2	2	20-Jan-23	23-Jan-23						I	Erect Steel - Sequence 22					
2807	ERCT.D5.1600	Erect Steel - Sequence 32	2	2	24-Jan-23	25-Jan-23						I	Erect Steel - Sequence 32					
2808	ERCT.D5.1570	Erect Steel - Sequence 23	2	2	26-Jan-23	27-Jan-23						I	Erect Steel - Sequence 23					
2809	ERCT.D5.1610	Erect Steel - Sequence 33	2	2	30-Jan-23	31-Jan-23						I	Erect Steel - Sequence 33					
2810	ERCT.D5.1580	Erect Steel - Sequence 24	3	3	01-Feb-23	03-Feb-23						I	Erect Steel - Sequence 24					
2811	ERCT.D5.1620	Erect Steel - Sequence 34	3	3	06-Feb-23	08-Feb-23						I	Erect Steel - Sequence 34					
2812	ERCT.D5.1630	Erect Steel - Sequence 25	2	2	09-Feb-23	10-Feb-23						I	Erect Steel - Sequence 25					
2813	ERCT.D5.1670	Erect Steel - Sequence 35	2	2	13-Feb-23	14-Feb-23						I	Erect Steel - Sequence 35					
2814	ERCT.D5.1640	Erect Steel - Sequence 26	3	3	15-Feb-23	17-Feb-23						I	Erect Steel - Sequence 26					
2815	ERCT.D5.1680	Erect Steel - Sequence 36	3	3	21-Feb-23	23-Feb-23						I	Erect Steel - Sequence 36					
2816	ERCT.D5.1650	Erect Steel - Sequence 27	2	2	24-Feb-23	27-Feb-23						I	Erect Steel - Sequence 27					
2817	ERCT.D5.1690	Erect Steel - Sequence 37	2	2	28-Feb-23	01-Mar-23						I	Erect Steel - Sequence 37					
2818	ERCT.D5.1660	Erect Steel - Sequence 28	2	2	02-Mar-23	03-Mar-23						I	Erect Steel - Sequence 28					
2819	ERCT.D5.1700	Erect Steel - Sequence 38	2	2	06-Mar-23	07-Mar-23						I	Erect Steel - Sequence 38					
2820	ERCT.D5.1710	Erect Steel - Sequence 40	2	2	08-Mar-23	09-Mar-23						I	Erect Steel - Sequence 40					
2821	Stairs						75	75	11-Jan-23	26-Apr-23								
2822	ERCT.D5.1480	Stair 1 (S Loading Dock)	2	2	11-Jan-23	12-Jan-23						I	Stair 1 (S Loading Dock)					
2823	ERCT.D5.1490	Stair 2 (Admin)	2	2	16-Jan-23	17-Jan-23						I	Stair 2 (Admin)					
2824	ERCT.D5.1520	Stair 3 (Back of House)	2	2	10-Mar-23	13-Mar-23						I	Stair 3 (Back of House)					

█ Remaining Level of Effort █ Remaining Work ◆ Milestone
█ Actual Work █ Critical Remaining Work ▼ Summary

QTS HIL2 DC2, DC3, DC5 Construction Schedule				Classic Schedule Layout						12-Jul-22 15:37							
#	Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	2022					2023				2024	
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2
2825		ERCT.D5.1500	10	10	21-Mar-23	03-Apr-23										Exterior Equipment Yard (2 Sets)	
2826		ERCT.D5.1510	10	10	13-Apr-23	26-Apr-23										Exterior Exit Stair (2 Sets)	
2827		Precast	30	30	16-Mar-23	26-Apr-23										26-Apr-23, Precast	
2828		PCST.D5.1200	3	3	16-Mar-23	20-Mar-23										Precast - CL Q to L.2 - East Elevation	
2829		PCST.D5.1210	3	3	21-Mar-23	23-Mar-23										Precast - CL L.2 to C.1 - East Elevation	
2830		PCST.D5.1220	2	2	24-Mar-23	27-Mar-23										Precast - CL C.1 to A - East Elevation	
2831		PCST.D5.1230	4	4	28-Mar-23	31-Mar-23										Precast - CL 8 to 1 - South Elevation	
2832		PCST.D5.1240	2	2	03-Apr-23	04-Apr-23										Precast - CL A to C.1 - West Elevation	
2833		PCST.D5.1250	3	3	05-Apr-23	07-Apr-23										Precast - CL C.1 to L.2 - West Elevation	
2834		PCST.D5.1260	3	3	10-Apr-23	12-Apr-23										Precast - CL L.2 to Q - West Elevation	
2835		PCST.D5.1270	3	3	13-Apr-23	17-Apr-23										Precast - CL Q to Z - West Elevation	
2836		PCST.D5.1280	4	4	18-Apr-23	21-Apr-23										Precast - CL 1 to 8 - True North	
2837		PCST.D5.1290	3	3	24-Apr-23	26-Apr-23										Precast - CL Z to Q - East Elevation	
2838		Glazing and Metal Paneling	42	42	03-Apr-23	31-May-23										31-May-23, Glazing and Metal Paneling	
2839		GZMP.D5.1070	15	15	03-Apr-23	21-Apr-23										Metal Paneling - S Elevation	
2840		GZMP.D5.1050	2	2	03-Apr-23	04-Apr-23										Precast Field Verification for Glazing	
2841		GZMP.D5.1060	15	15	03-May-23	23-May-23										Install Glazing - S Elevation CL-8 to CL-1	
2842		GZMP.D5.1080	5	5	24-May-23	31-May-23										Install Glazing - W Elevation CL-C to CL-A	
2843		Roof	78	78	16-Jan-23	04-May-23										04-May-23, Roof	
2844		CL A to CL C	62	62	16-Jan-23	12-Apr-23										12-Apr-23, CL A to CL C	
2845		ROOF.D5.164	3	3	16-Jan-23	18-Jan-23										Roof A-C - Install Curbs	
2846		ROOF.D5.165	3	3	19-Jan-23	23-Jan-23										Roof A-C - Roof Penetrations	
2847		ROOF.D5.167	2	2	20-Jan-23	23-Jan-23										Roof A-C - Temp Roof	
2848		ROOF.D5.166	1	1	23-Jan-23	23-Jan-23										Roof A-C - Inspect/Punch/QAAC	
2849		ROOF.D5.168	5	5	24-Jan-23	30-Jan-23										Roof A-C - Foam Insulation	
2850		ROOF.D5.169	5	5	31-Jan-23	06-Feb-23										Roof A-C - Install Roofing Material	
2851		ROOF.D5.170	5	5	30-Mar-23	05-Apr-23										Roof A-C - Interior Wall Covering	
2852		ROOF.D5.171	5	5	06-Apr-23	12-Apr-23										Roof A-C - Wall Cap	
2853		CL C to CLL	57	57	26-Jan-23	17-Apr-23										17-Apr-23, CL C to CLL	
2854		ROOF.D5.172	3	3	26-Jan-23	30-Jan-23										Roof C-L - Install Curbs	
2855		ROOF.D5.173	3	3	31-Jan-23	02-Feb-23										Roof C-L - Roof Penetrations	
2856		ROOF.D5.175	5	5	01-Feb-23	07-Feb-23										Roof C-L - Temp Roof	
2857		ROOF.D5.174	1	1	02-Feb-23	02-Feb-23										Roof C-L - Inspect/Punch/QAAC	
2858		ROOF.D5.176	5	5	08-Feb-23	14-Feb-23										Roof C-L - Foam Insulation	
2859		ROOF.D5.177	5	5	15-Feb-23	22-Feb-23										Roof C-L - Roofing Material	
2860		ROOF.D5.178	5	5	04-Apr-23	10-Apr-23										Roof C-L - Interior Wall Covering	
2861		ROOF.D5.179	5	5	11-Apr-23	17-Apr-23										Roof C-L - Wall Cap	
2862		CL L to CL Q	46	46	15-Feb-23	20-Apr-23										20-Apr-23, CL L to CL Q	
2863		ROOF.D5.180	3	3	15-Feb-23	17-Feb-23										Roof L-Q - Install Curbs	
2864		ROOF.D5.181	3	3	21-Feb-23	23-Feb-23										Roof L-Q - Roof Penetrations	
2865		ROOF.D5.182	1	1	23-Feb-23	23-Feb-23										Roof L-Q - Inspect/Punch/QAAC	
2866		ROOF.D5.183	5	5	24-Feb-23	02-Mar-23										Roof L-Q - Temp Roof	
2867		ROOF.D5.184	5	5	03-Mar-23	09-Mar-23										Roof L-Q - Foam Insulation	
2868		ROOF.D5.185	5	5	10-Mar-23	16-Mar-23										Roof L-Q - Roofing Material	
2869		ROOF.D5.186	5	5	07-Apr-23	13-Apr-23										Roof L-Q - Interior Wall Covering	
2870		ROOF.D5.187	5	5	14-Apr-23	20-Apr-23										Roof L-Q - Wall Cap	
2871		CL Q to CL Z	42	42	08-Mar-23	04-May-23										04-May-23, CL Q to CL Z	
2872		ROOF.D5.188	3	3	08-Mar-23	10-Mar-23										Roof Q-Z - Install Curbs	




QTS HIL2 DC2, DC3, DC5 Construction Schedule				Classic Schedule Layout					12-Jul-22 15:37									
#	Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	2022					2023					2024	
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	
2873		ROOF.D5.191	5	5	10-Mar-23	16-Mar-23												
2874		ROOF.D5.189	3	3	13-Mar-23	15-Mar-23												
2875		ROOF.D5.190	1	1	15-Mar-23	15-Mar-23												
2876		ROOF.D5.192	5	5	17-Mar-23	23-Mar-23												
2877		ROOF.D5.193	5	5	24-Mar-23	30-Mar-23												
2878		ROOF.D5.194	5	5	21-Apr-23	27-Apr-23												
2879		ROOF.D5.195	5	5	28-Apr-23	04-May-23												
2880	Rooftop Equipment			102	102	07-Feb-23	28-Jun-23											
2881		House		102	102	07-Feb-23	28-Jun-23											
2882	MEP84	House - Rough In Roof MEP	5	5	07-Feb-23	13-Feb-23												
2883	EQPT.D5.3960	House - Set Rooftop RTU Equipment	5	5	08-Jun-23	14-Jun-23												
2884	EQPT.D5.3970	House - Pull and Terminate RTU Feeders	5	5	15-Jun-23	21-Jun-23												
2885	EQPT.D5.3980	House - Mechanical RTU Final Connections	5	5	22-Jun-23	28-Jun-23												
2886	MPOE/BDF			74	74	17-Mar-23	28-Jun-23											
2887	MEP74	MPOE/BDF - Rough In Roof MEP	5	5	17-Mar-23	23-Mar-23												
2888	EQPT.D5.3930	MPOE/BDF - Set Rooftop ACCU Equipment	5	5	08-Jun-23	14-Jun-23												
2889	EQPT.D5.3940	MPOE/BDF - Pull and Terminate ACCU Feeders	5	5	15-Jun-23	21-Jun-23												
2890	EQPT.D5.3950	MPOE/BDF - Mechanical ACCU Final Connections	5	5	22-Jun-23	28-Jun-23												
2891	DH A - B			90	90	23-Feb-23	28-Jun-23											
2892	MEP54	DH A/B - Rough In Roof MEP	5	5	23-Feb-23	01-Mar-23												
2893	EQPT.D5.3880	DH A/B - Set Rooftop ACCU Equipment	5	5	08-Jun-23	14-Jun-23												
2894	EQPT.D5.3890	DH A/B - Pull and Terminate ACCU Feeders	5	5	15-Jun-23	21-Jun-23												
2895	EQPT.D5.3050	Mechanical ACCU Final Connections DH AB	5	5	22-Jun-23	28-Jun-23												
2896	DH C - D			64	64	31-Mar-23	28-Jun-23											
2897	MEP64	DH C/D - Rough In Roof MEP	5	5	31-Mar-23	06-Apr-23												
2898	EQPT.D5.3900	DH C/D - Set Rooftop ACCU Equipment	5	5	08-Jun-23	14-Jun-23												
2899	EQPT.D5.3910	DH C/D - Pull and Terminate ACCU Feeders	5	5	15-Jun-23	21-Jun-23												
2900	EQPT.D5.3920	DH C/D - Mechanical ACCU Final Connections	5	5	22-Jun-23	28-Jun-23												
2901	Equipment Yard			101	101	01-Feb-23	23-Jun-23											
2902	Medium Voltage Ductbank			77	77	01-Feb-23	19-May-23											
2903	EXCV.D5.1410	Excavate Medium Voltage Underground - Sequence 1	6	6	01-Feb-23	08-Feb-23												
2904	EXCV.D5.1420	Excavate Medium Voltage Underground - Sequence 2	14	14	09-Feb-23	01-Mar-23												
2905	MVDP.D5.114	Install Medium Voltage Underground - Sequence 1	2	2	09-Feb-23	10-Feb-23												
2906	EXCV.D5.1430	Excavate Medium Voltage Underground - Sequence 3	13	13	02-Mar-23	20-Mar-23												
2907	MVDP.D5.115	Install Medium Voltage Underground - Sequence 2	8	8	02-Mar-23	13-Mar-23												
2908	EXCV.D5.1440	Excavate Medium Voltage Underground - Sequence 4	13	13	21-Mar-23	06-Apr-23												
2909	MVDP.D5.116	Install Medium Voltage Underground - Sequence 3	7	7	21-Mar-23	29-Mar-23												
2910	EXCV.D5.1450	Excavate Medium Voltage Underground - Sequence 5	17	17	07-Apr-23	01-May-23												
2911	MVDP.D5.117	Install Medium Voltage Underground - Sequence 4	8	8	07-Apr-23	18-Apr-23												
2912	EXCV.D5.1460	Excavate Medium Voltage Underground - North Vault Group 1	5	5	02-May-23	08-May-23												
2913	MVDP.D5.118	Install Medium Voltage Underground - Sequence 5	14	14	02-May-23	19-May-23												
2914	EXCV.D5.1470	Excavate Medium Voltage Underground - North Vault Group 2	5	5	09-May-23	15-May-23												
2915	MVDP.D5.119	Install Medium Voltage Underground - North Vault Group 1	4	4	09-May-23	12-May-23												
2916	MVDP.D5.120	Install Medium Voltage Underground - North Vault Group 2	4	4	16-May-23	19-May-23												
2917	Equipment Yard Pads and Set Equipment			68	68	21-Mar-23	23-Jun-23											
2918	House			20	20	07-Apr-23	04-May-23											
2919	EXCV.D5.1	Yard House - Excavation Transformer Foundations	2	2	07-Apr-23	10-Apr-23												
2920	CONC.D5.	Yard House - Form Transformer Foundations DH AB	2	2	10-Apr-23	11-Apr-23												



QTS HIL2 DC2, DC3, DC5 Construction Schedule				Classic Schedule Layout					12-Jul-22 15:37								
#	Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	2022					2023				2024	
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2
2921		CONC.D5. Yard House - Rebar Transformer Foundations	2	2	11-Apr-23	12-Apr-23										I	Yard House - Rebar Transformer Foundations
2922		CONC.D5. Yard House - Pour Transformer Foundations	1	1	13-Apr-23	13-Apr-23										I	Yard House - Pour Transformer Foundations
2923		CONC.D5. Yard House - Cure Transformer Foundations	5	5	14-Apr-23	20-Apr-23										■	Yard House - Cure Transformer Foundations
2924		EQPT.D5.2 Yard House - Set Transformers	5	5	21-Apr-23	27-Apr-23										■	Yard House - Set Transformers
2925		EQPT.D5.2 Yard House - Pull and Terminate Transformers	5	5	28-Apr-23	04-May-23										■	Yard House - Pull and Terminate Transformers
2926	MPOE/BDF Pads and Set Equipment			28	28	21-Mar-23	27-Apr-23									▼	27-Apr-23, MPOE/BDF Pads and Set Equipment
2927	SURV.D5.1	Survey MPOE/BDF Equipment Foundations	1	1	21-Mar-23	21-Mar-23										I	Survey MPOE/BDF Equipment Foundations
2928	Pod Pads and Set Equipment			25	25	22-Mar-23	25-Apr-23									▼	25-Apr-23, Pod Pads and Set Equipment
2929	EXCV.D	Yard MPOE/BDF - Excavate UPS Pod Foundations	2	2	22-Mar-23	23-Mar-23										I	Yard MPOE/BDF - Excavate UPS Pod Foundations
2930	CONC.I	Yard MPOE/BDF - Form UPS Pod Foundations MPOE BDF	2	2	23-Mar-23	24-Mar-23										I	Yard MPOE/BDF - Form UPS Pod Foundations MPOE BDF
2931	CONC.I	Yard MPOE/BDF - Rebar UPS Pod Foundations	2	2	24-Mar-23	27-Mar-23										I	Yard MPOE/BDF - Rebar UPS Pod Foundations
2932	CONC.I	Yard MPOE/BDF - Pour UPS Pod Foundations	3	3	28-Mar-23	30-Mar-23										I	Yard MPOE/BDF - Pour UPS Pod Foundations
2933	CONC.I	Yard MPOE/BDF - Cure UPS Pod Foundations	5	5	31-Mar-23	06-Apr-23										■	Yard MPOE/BDF - Cure UPS Pod Foundations
2934	CONC.I	Yard MPOE/BDF - Install Steel Rails UPS Pod Foundations	3	3	07-Apr-23	11-Apr-23										■	Yard MPOE/BDF - Install Steel Rails UPS Pod Foundations
2935	EQPT.D	Yard MPOE/BDF - Set UPS Pods	5	5	12-Apr-23	18-Apr-23										■	Yard MPOE/BDF - Set UPS Pods
2936	EQPT.D	Yard MPOE/BDF - Pull and Terminate UPS Pods	5	5	19-Apr-23	25-Apr-23										■	Yard MPOE/BDF - Pull and Terminate UPS Pods
2937	Transformer Pads and Set Equipment			23	23	22-Mar-23	21-Apr-23									▼	21-Apr-23, Transformer Pads and Set Equipment
2938	EXCV.D	Yard MPOE/BDF - Excavation Transformer Foundations	2	2	22-Mar-23	23-Mar-23										I	Yard MPOE/BDF - Excavation Transformer Foundations
2939	CONC.I	Yard MPOE/BDF - Form Transformer Foundations	2	2	23-Mar-23	24-Mar-23										I	Yard MPOE/BDF - Form Transformer Foundations
2940	CONC.I	Yard MPOE/BDF - Rebar Transformer Foundations	2	2	24-Mar-23	27-Mar-23										■	Yard MPOE/BDF - Rebar Transformer Foundations
2941	CONC.I	Yard MPOE/BDF - Pour Transformer Foundations	1	1	31-Mar-23	31-Mar-23										I	Yard MPOE/BDF - Pour Transformer Foundations
2942	CONC.I	Yard MPOE/BDF - Cure Transformer Foundations	5	5	03-Apr-23	07-Apr-23										■	Yard MPOE/BDF - Cure Transformer Foundations
2943	EQPT.D	Yard MPOE/BDF - Set Transformers	5	5	10-Apr-23	14-Apr-23										■	Yard MPOE/BDF - Set Transformers
2944	EQPT.D	Yard MPOE/BDF - Pull and Terminate Transformers	5	5	17-Apr-23	21-Apr-23										▼	21-Apr-23, Generator Pads and Set Equipment
2945	Generator Pads and Set Equipment			25	25	24-Mar-23	27-Apr-23									I	Yard MPOE/BDF - Excavation Generator Foundations
2946	EXCV.D	Yard MPOE/BDF - Excavation Generator Foundations	2	2	24-Mar-23	27-Mar-23										I	Yard MPOE/BDF - Form Generator Foundations
2947	CONC.I	Yard MPOE/BDF - Rebar Generator Foundations	2	2	27-Mar-23	28-Mar-23										■	Yard MPOE/BDF - Rebar Generator Foundations
2948	CONC.I	Yard MPOE/BDF - Pour Generator Foundations	3	3	28-Mar-23	30-Mar-23										■	Yard MPOE/BDF - Pour Generator Foundations
2949	CONC.I	Yard MPOE/BDF - Cure Generator Foundations	4	4	03-Apr-23	06-Apr-23										■	Yard MPOE/BDF - Cure Generator Foundations
2950	CONC.I	Yard MPOE/BDF - Set Generators	5	5	07-Apr-23	13-Apr-23										■	Yard MPOE/BDF - Set Generators
2951	EQPT.D	Yard MPOE/BDF - Pull and Terminate Generators	5	5	14-Apr-23	20-Apr-23										▼	19-Jun-23, Data Hall A and B Pads and Set Equipment
2952	EQPT.D	Yard MPOE/BDF - Pull and Terminate Generators	5	5	21-Apr-23	27-Apr-23										I	Survey DH A/B - Equipment Foundations
2953	Data Hall A and B Pads and Set Equipment			61	61	24-Mar-23	19-Jun-23									▼	04-May-23, Transformer Pads and Set Equipment
2954	SURV.D5.1	Survey DH A/B - Equipment Foundations	1	1	24-Mar-23	24-Mar-23										I	Yard DH A/B - Excavation Transformer Foundations
2955	Transformer Pads and Set Equipment			20	20	07-Apr-23	04-May-23									I	Yard DH A/B - Form Transformer Foundations DH AB
2956	EXCV.D	Yard DH A/B - Excavation Transformer Foundations	2	2	07-Apr-23	10-Apr-23										I	Yard DH A/B - Rebar Transformer Foundations
2957	CONC.I	Yard DH A/B - Pour Transformer Foundations DH AB	2	2	10-Apr-23	11-Apr-23										I	Yard DH A/B - Cure Transformer Foundations
2958	CONC.I	Yard DH A/B - Set Transformers	5	5	14-Apr-23	20-Apr-23										■	Yard DH A/B - Pull and Terminate Transformers
2959	EQPT.D	Yard DH A/B - Pull and Terminate Transformers	5	5	21-Apr-23	27-Apr-23										▼	12-May-23, Generator Pads and Set Equipment
2960	EQPT.D	Yard DH A/B - Set Transformers	5	5	28-Apr-23	04-May-23										I	Yard DH A/B - Excavation Generator Foundations
2961	CONC.I	Yard DH A/B - Form Generator Foundations	3	3	13-Apr-23	17-Apr-23										I	Yard DH A/B - Rebar Generator Foundations
2962	CONC.I	Yard DH A/B - Pour Generator Foundations	4	4	18-Apr-23	21-Apr-23										I	Yard DH A/B - Cure Generator Foundations
2963	Generator Pads and Set Equipment			24	24	11-Apr-23	12-May-23									I	Yard DH A/B - Pull and Terminate Generators
2964	EXCV.D	Yard DH A/B - Excavation Generator Foundations	2	2	11-Apr-23	12-Apr-23										I	Yard DH A/B - Form Generator Foundations
2965	CONC.I	Yard DH A/B - Rebar Generator Foundations	2	2	12-Apr-23	13-Apr-23										I	Yard DH A/B - Pour Generator Foundations
2966	CONC.I	Yard DH A/B - Cure Generator Foundations	5	5	24-Apr-23	28-Apr-23										I	Yard DH A/B - Set Generators
2967	CONC.I	Yard DH A/B - Set Transformers	5	5	28-Apr-23	04-May-23										■	Yard DH A/B - Excavation Transformers
2968	CONC.I	Yard DH A/B - Pull and Terminate Transformers	5	5	24-Apr-23	28-Apr-23										I	Yard DH A/B - Form Transformers

QTS HIL2 DC2, DC3, DC5 Construction Schedule				Classic Schedule Layout						12-Jul-22 15:37							
#	Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	2022					2023				2024	
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2
2969	EQPT.D	Yard DH A/B - Set Generators	5	5	01-May-23	05-May-23										Yard DH A/B - Set Generators	
2970		Yard DH A/B - Pull and Terminate Generators	5	5	08-May-23	12-May-23										Yard DH A/B - Pull and Terminate Generators	
2971		Medium Voltage Pads and Set Equipment	47	47	13-Apr-23	19-Jun-23										19-Jun-23, Medium Voltage Pads and Set Equipment	
2972		EXCV.D Yard DH A/B - Excavation MV Pads	2	2	13-Apr-23	14-Apr-23										Yard DH A/B - Excavation MV Pads	
2973		CONC.I Yard DH A/B - Form MV Pads	2	2	17-Apr-23	18-Apr-23										Yard DH A/B - Form MV Pads	
2974		CONC.I Yard DH A/B - Rebar MV Foundations	3	3	19-Apr-23	21-Apr-23										Yard DH A/B - Rebar MV Foundations	
2975		CONC.I Yard DH A/B - Pour MV Pads	4	4	22-May-23	25-May-23										Yard DH A/B - Pour MV Pads	
2976		CONC.I Yard DH A/B - Cure MV Pads	5	5	26-May-23	02-Jun-23										Yard DH A/B - Cure MV Pads	
2977		EQPT.D Yard DH A/B - Set MV Equipment	5	5	05-Jun-23	09-Jun-23										Yard DH A/B - Set MV Equipment	
2978		EQPT.D Yard DH A/B - Pull and Terminate MV Feeders	10	10	06-Jun-23	19-Jun-23										Yard DH A/B - Pull and Terminate MV Feeders	
2979	Data Hall C and D Pads and Set Equipment			41	41	27-Apr-23	23-Jun-23									23-Jun-23, Data Hall C and D Pads and Set Equipment	
2980	SURV.D5.1	Survey DH C/D Equipment Foundations	1	1	27-Apr-23	27-Apr-23										Survey DH C/D Equipment Foundations	
2981	Transformer Pads and Set Equipment			20	20	28-Apr-23	25-May-23									25-May-23, Transformer Pads and Set Equipment	
2982	EXCV.D	Yard DH C/D - Excavation Transformer Foundations	2	2	28-Apr-23	01-May-23										Yard DH C/D - Excavation Transformer Foundations	
2983	CONC.I	Yard DH C/D - Form Transformer Foundations	2	2	01-May-23	02-May-23										Yard DH C/D - Form Transformer Foundations	
2984	CONC.I	Yard DH C/D - Rebar Transformer Foundations	2	2	02-May-23	03-May-23										Yard DH C/D - Rebar Transformer Foundations	
2985	CONC.I	Yard DH C/D - Pour Transformer Foundations	1	1	04-May-23	04-May-23										Yard DH C/D - Pour Transformer Foundations	
2986	CONC.I	Yard DH C/D - Cure Transformer Foundations	5	5	05-May-23	11-May-23										Yard DH C/D - Cure Transformer Foundations	
2987	EQPT.D	Yard DH C/D - Set Transformers	5	5	12-May-23	18-May-23										Yard DH C/D - Set Transformers	
2988	EQPT.D	Yard DH C/D - Pull and Terminate Transformers	5	5	19-May-23	25-May-23										Yard DH C/D - Pull and Terminate Transformers	
2989	Generator Pads and Set Equipment			24	24	02-May-23	05-Jun-23									05-Jun-23, Generator Pads and Set Equipment	
2990	EXCV.D	Yard DH C/D - Excavation Generator Foundations	2	2	02-May-23	03-May-23										Yard DH C/D - Excavation Generator Foundations	
2991	CONC.I	Yard DH C/D - Form Generator Foundations	2	2	03-May-23	04-May-23										Yard DH C/D - Form Generator Foundations	
2992	CONC.I	Yard DH C/D - Rebar Generator Foundations	3	3	04-May-23	08-May-23										Yard DH C/D - Rebar Generator Foundations	
2993	CONC.I	Yard DH C/D - Pour Generator Foundations	4	4	09-May-23	12-May-23										Yard DH C/D - Pour Generator Foundations	
2994	CONC.I	Yard DH C/D - Cure Generator Foundations	5	5	15-May-23	19-May-23										Yard DH C/D - Cure Generator Foundations	
2995	EQPT.D	Yard DH C/D - Set Generators	5	5	22-May-23	26-May-23										Yard DH C/D - Set Generators	
2996	EQPT.D	Yard DH C/D - Pull and Terminate Generators	5	5	30-May-23	05-Jun-23										Yard DH C/D - Pull and Terminate Generators	
2997	Medium Voltage Pads and Set Equipment			36	36	04-May-23	23-Jun-23									23-Jun-23, Medium Voltage Pads and Set Equipment	
2998	EXCV.D	Yard DH C/D - Excavation MV Pads	2	2	04-May-23	05-May-23										Yard DH C/D - Excavation MV Pads	
2999	CONC.I	Yard DH C/D - Form MV Pads	2	2	22-May-23	23-May-23										Yard DH C/D - Form MV Pads	
3000	CONC.I	Yard DH C/D - Rebar MV Foundations	2	2	24-May-23	25-May-23										Yard DH C/D - Rebar MV Foundations	
3001	CONC.I	Yard DH C/D - Pour MV Pads	4	4	26-May-23	01-Jun-23										Yard DH C/D - Pour MV Pads	
3002	CONC.I	Yard DH C/D - Cure MV Pads	5	5	02-Jun-23	08-Jun-23										Yard DH C/D - Cure MV Pads	
3003	EQPT.D	Yard DH C/D - Set MV Equipment	5	5	09-Jun-23	15-Jun-23										Yard DH C/D - Set MV Equipment	
3004	EQPT.D	Yard DH C/D - Pull and Terminate MV Feeders	10	10	12-Jun-23	23-Jun-23										Yard DH C/D - Pull and Terminate MV Feeders	
3005	Elevators			86	86	09-Mar-23	10-Jul-23									10-Jul-23, Elevators	
3006	Freight Elevator E03			61	61	13-Apr-23	10-Jul-23									10-Jul-23, Freight Elevator E03	
3007	ELVT.D5.1660	Freight Elev. 3 - Hoisting Equipment	7	7	13-Apr-23	21-Apr-23										Freight Elev. 3 - Hoisting Equipment	
3008	ELVT.D5.1670	Freight Elev. 3 - Pit Rails/Frame/Cab	5	5	24-Apr-23	28-Apr-23										Freight Elev. 3 - Pit Rails/Frame/Cab	
3009	ELVT.D5.1680	Freight Elev. 3 - Tirak & Governor Rope	5	5	01-May-23	05-May-23										Freight Elev. 3 - Tirak & Governor Rope	
3010	ELVT.D5.1690	Freight Elev. 3 - Rails	8	8	08-May-23	17-May-23										Freight Elev. 3 - Rails	
3011	ELVT.D5.1700	Freight Elev. 3 - Door entrances	4	4	18-May-23	23-May-23										Freight Elev. 3 - Door entrances	
3012	ELVT.D5.1710	Freight Elev. 3 - Duct/Wire Machine/Startup	7	7	24-May-23	02-Jun-23										Freight Elev. 3 - Duct/Wire Machine/Startup	
3013	ELVT.D5.1720	Freight Elev. 3 - Rope Elevator/Remove Tirak	4	4	05-Jun-23	08-Jun-23										Freight Elev. 3 - Rope Elevator/Remove Tirak	
3014	ELVT.D5.1730	Freight Elev. 3 - Pipe and Wire Hatch Devices	6	6	09-Jun-23	16-Jun-23										Freight Elev. 3 - Pipe and Wire Hatch Devices	
3015	ELVT.D5.1740	Freight Elev. 3 - Terminate Devices	8	8	19-Jun-23	28-Jun-23										Freight Elev. 3 - Terminate Devices	
3016	ELVT.D5.1750	Freight Elev. 3 - Clean Rails	2	2	29-Jun-23	30-Jun-23										Freight Elev. 3 - Clean Rails	



QTS HIL2 DC2, DC3, DC5 Construction Schedule				Classic Schedule Layout						12-Jul-22 15:37							
#	Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	2022					2023				2024	
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2
3017	ELVT.D5.1760	Freight Elev. 3 - Inspect	5	5	03-Jul-23	10-Jul-23										Freight Elev. 3 - Inspect	
3018	Freight Elevator E02A and E02B			85	85	09-Mar-23	07-Jul-23									07-Jul-23, Freight Elevator E02A and E02B	
3019	ELVT.D5.1770	Freight Elev. E02A/E02B - Hoisting Equipment	10	10	09-Mar-23	22-Mar-23										Freight Elev. E02A/E02B - Hoisting Equipment	
3020	ELVT.D5.1780	Freight Elev. E02A/E02B - Pit Rails/Frame/Cab	7	7	23-Mar-23	31-Mar-23										Freight Elev. E02A/E02B - Pit Rails/Frame/Cab	
3021	ELVT.D5.1790	Freight Elev. E02A/E02B - Trak & Governor Rope	7	7	03-Apr-23	11-Apr-23										Freight Elev. E02A/E02B - Trak & Governor Rope	
3022	ELVT.D5.1800	Freight Elev. E02A/E02B - Rails	10	10	12-Apr-23	25-Apr-23										Freight Elev. E02A/E02B - Rails	
3023	ELVT.D5.1810	Freight Elev. E02A/E02B - Door entrances	6	6	26-Apr-23	03-May-23										Freight Elev. E02A/E02B - Door entrances	
3024	ELVT.D5.1820	Freight Elev. E02A/E02B - Duct/Wire Machine/Startup	9	9	04-May-23	16-May-23										Freight Elev. E02A/E02B - Duct/Wire Machine/Startup	
3025	ELVT.D5.1830	Freight Elev. E02A/E02B - Rope Elevator/Remove Tirak	6	6	17-May-23	24-May-23										Freight Elev. E02A/E02B - Rope Elevator/Remove Tirak	
3026	ELVT.D5.1840	Freight Elev. E02A/E02B - Pipe and Wire Hatch Devices	8	8	25-May-23	06-Jun-23										Freight Elev. E02A/E02B - Pipe and Wire Hatch Devices	
3027	ELVT.D5.1850	Freight Elev. E02A/E02B - Terminate Devices	10	10	07-Jun-23	20-Jun-23										Freight Elev. E02A/E02B - Terminate Devices	
3028	ELVT.D5.1860	Freight Elev. E02A/E02B - Clean Rails	4	4	21-Jun-23	26-Jun-23										Freight Elev. E02A/E02B - Clean Rails	
3029	ELVT.D5.1870	Freight Elev. E02A/E02B - Inspect	8	8	27-Jun-23	07-Jul-23										Freight Elev. E02A/E02B - Inspect	
3030	Passenger Elevator			61	61	09-Mar-23	02-Jun-23									02-Jun-23, Passenger Elevator	
3031	ELVT.D5.1880	Pass. Elev. - Hoisting Equipment - Pass Elev.	7	7	09-Mar-23	17-Mar-23										Pass. Elev. - Hoisting Equipment - Pass Elev.	
3032	ELVT.D5.1890	Pass. Elev. - Pit Rails/Frame/Cab	5	5	20-Mar-23	24-Mar-23										Pass. Elev. - Pit Rails/Frame/Cab	
3033	ELVT.D5.1900	Pass. Elev. - Tirak & Governor Rope	5	5	27-Mar-23	31-Mar-23										Pass. Elev. - Tirak & Governor Rope	
3034	ELVT.D5.1910	Pass. Elev. - Rails	8	8	03-Apr-23	12-Apr-23										Pass. Elev. - Rails	
3035	ELVT.D5.1920	Pass. Elev. - Door entrances	4	4	13-Apr-23	18-Apr-23										Pass. Elev. - Door entrances	
3036	ELVT.D5.1930	Pass. Elev. - Duct/Wire Machine/Startup	7	7	19-Apr-23	27-Apr-23										Pass. Elev. - Duct/Wire Machine/Startup	
3037	ELVT.D5.1940	Pass. Elev. - Rope Elevator/Remove Tirak	4	4	28-Apr-23	03-May-23										Pass. Elev. - Rope Elevator/Remove Tirak	
3038	ELVT.D5.1950	Pass. Elev. - Pipe and Wire Hatch Devices	6	6	04-May-23	11-May-23										Pass. Elev. - Pipe and Wire Hatch Devices	
3039	ELVT.D5.1960	Pass. Elev. - Terminate Devices	8	8	12-May-23	23-May-23										Pass. Elev. - Terminate Devices	
3040	ELVT.D5.1970	Pass. Elev. - Clean Rails	2	2	24-May-23	25-May-23										Pass. Elev. - Clean Rails	
3041	ELVT.D5.1980	Pass. Elev. - Inspect	5	5	26-May-23	02-Jun-23										Pass. Elev. - Inspect	
3042	Interior Buildout			85	85	27-Jan-23	26-May-23									26-May-23, Interior Buildout	
3043	1st Floor Sector 2F1&F2 Lobby/Admin			54	54	27-Jan-23	13-Apr-23									13-Apr-23, 1st Floor Sector 2F1&F2 Lobby/Admin	
3044	FRME.D5.352	1st Floor 2F1/F2 - Layout and Frame Walls	13	13	27-Jan-23	14-Feb-23										1st Floor 2F1/F2 - Layout and Frame Walls	
3045	MEP.D5.3200	1st Floor 2F1/F2 - Rough-in Plumbing	8	8	27-Jan-23	07-Feb-23										1st Floor 2F1/F2 - Rough-in Plumbing	
3046	MEP.D5.3210	1st Floor 2F1/F2 - Rough-in HVAC	7	7	27-Jan-23	06-Feb-23										1st Floor 2F1/F2 - Rough-in HVAC	
3047	MEP.D5.3220	1st Floor 2F1/F2 - Rough-in Fire	7	7	27-Jan-23	06-Feb-23										1st Floor 2F1/F2 - Rough-in Fire	
3048	MEP.D5.3230	1st Floor 2F1/F2 - Rough-in Electric	8	8	27-Jan-23	07-Feb-23										1st Floor 2F1/F2 - Rough-in Electric	
3049	MEP.D5.3240	1st Floor 2F1/F2 - Rough-in Low Volt	8	8	27-Jan-23	07-Feb-23										1st Floor 2F1/F2 - Rough-in Low Volt	
3050	FRME.D5.353	1st Floor 2F1/F2 - Insulate	4	4	10-Feb-23	15-Feb-23										1st Floor 2F1/F2 - Insulate	
3051	FRME.D5.358	1st Floor 2F1/F2 - Install HM Door Frames	5	5	15-Feb-23	21-Feb-23										1st Floor 2F1/F2 - Install HM Door Frames	
3052	FRME.D5.354	1st Floor 2F1/F2 - Install Drywall Upper	5	5	16-Feb-23	23-Feb-23										1st Floor 2F1/F2 - Install Drywall Upper	
3053	FRME.D5.355	1st Floor 2F1/F2 - Hang and Tape Drywall	8	8	24-Feb-23	07-Mar-23										1st Floor 2F1/F2 - Hang and Tape Drywall	
3054	FNSH.D5.2820	1st Floor 2F1/F2 - Paint - 2F1F2	3	3	08-Mar-23	10-Mar-23										1st Floor 2F1/F2 - Paint - 2F1F2	
3055	MEP.D5.3250	1st Floor 2F1/F2 - Fire caulk	2	2	13-Mar-23	14-Mar-23										1st Floor 2F1/F2 - Fire caulk	
3056	FRME.D5.356	1st Floor 2F1/F2 - Grid Ceiling	5	5	13-Mar-23	17-Mar-23										1st Floor 2F1/F2 - Grid Ceiling	
3057	FRME.D5.357	1st Floor 2F1/F2 - Wood Ceiling	3	3	20-Mar-23	22-Mar-23										1st Floor 2F1/F2 - Wood Ceiling	
3058	FNSH.D5.2830	1st Floor 2F1/F2 - Doors / Hardware	5	5	20-Mar-23	24-Mar-23										1st Floor 2F1/F2 - Doors / Hardware	
3059	FNSH.D5.2840	1st Floor 2F1/F2 - Install Millwork	3	3	20-Mar-23	22-Mar-23										1st Floor 2F1/F2 - Install Millwork	
3060	FNSH.D5.2870	1st Floor 2F1/F2 - Finish Electric	5	5	20-Mar-23	24-Mar-23										1st Floor 2F1/F2 - Finish Electric	
3061	FNSH.D5.2850	1st Floor 2F1/F2 - Backsplash Tile	3	3	23-Mar-23	27-Mar-23										1st Floor 2F1/F2 - Backsplash Tile	
3062	FNSH.D5.2880	1st Floor 2F1/F2 - Drop Remaining Ceiling Tile	1	1	27-Mar-23	27-Mar-23										1st Floor 2F1/F2 - Drop Remaining Ceiling Tile	
3063	FNSH.D5.2860	1st Floor 2F1/F2 - Tile in Restroom	5	5	28-Mar-23	03-Apr-23										1st Floor 2F1/F2 - Tile in Restroom	

Remaining Level of Effort
Actual Work


Remaining Work
Critical Remaining Work

Milestone
Summary

QTS HIL2 DC2, DC3, DC5 Construction Schedule				Classic Schedule Layout						12-Jul-22 15:37									
#	Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	2022					2023					2024		
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2		
3064	FNSH.D5.2890	1st Floor 2F1/F2 - Finish Plumbing	4	4	28-Mar-23	31-Mar-23													
3065	FNSH.D5.2900	1st Floor 2F1/F2 - Finish HVAC		3	3	03-Apr-23	05-Apr-23												
3066	FNSH.D5.2910	1st Floor 2F1/F2 - Floor Coverings		6	6	06-Apr-23	13-Apr-23												
3067	1st Floor Sector 2G1&G2 Back of House			49	49	21-Mar-23	26-May-23												
3068	FRME.D5.359	1st Floor 2G1/G2 - Layout and Frame Walls		9	9	21-Mar-23	31-Mar-23												
3069	MEP.D5.3260	1st Floor 2G1/G2 - Rough-in Plumbing		8	8	21-Mar-23	30-Mar-23												
3070	MEP.D5.3270	1st Floor 2G1/G2 - Rough-in HVAC		7	7	21-Mar-23	29-Mar-23												
3071	MEP.D5.3280	1st Floor 2G1/G2 - Rough-in Fire		7	7	21-Mar-23	29-Mar-23												
3072	MEP.D5.3290	1st Floor 2G1/G2 - Rough-in Electric		8	8	21-Mar-23	30-Mar-23												
3073	MEP.D5.3300	1st Floor 2G1/G2 - Rough-in Low Volt		8	8	21-Mar-23	30-Mar-23												
3074	MEP.D5.3310	1st Floor 2G1/G2 - Fire caulk		2	2	31-Mar-23	03-Apr-23												
3075	FRME.D5.360	1st Floor 2G1/G2 - Insulate		2	2	31-Mar-23	03-Apr-23												
3076	FRME.D5.361	1st Floor 2G1/G2 - Install Drywall Upper		5	5	04-Apr-23	10-Apr-23												
3077	FRME.D5.362	1st Floor 2G1/G2 - Hang and Tape Drywall		7	7	11-Apr-23	19-Apr-23												
3078	FNSH.D5.2940	1st Floor 2G1/G2 - Tile in Restroom		3	3	11-Apr-23	13-Apr-23												
3079	FNSH.D5.2950	1st Floor 2G1/G2 - Backsplash Tile		5	5	14-Apr-23	20-Apr-23												
3080	FNSH.D5.2920	1st Floor 2G1/G2 - Paint		3	3	20-Apr-23	24-Apr-23												
3081	FRME.D5.363	1st Floor 2G1/G2 - Grid Ceiling		5	5	25-Apr-23	01-May-23												
3082	FRME.D5.364	1st Floor 2G1/G2 - Wood Ceiling		3	3	02-May-23	04-May-23												
3083	FNSH.D5.2930	1st Floor 2G1/G2 - Doors & Hardware		5	5	02-May-23	08-May-23												
3084	FRME.D5.365	1st Floor 2G1/G2 - Install Millwork		3	3	02-May-23	04-May-23												
3085	FNSH.D5.2960	1st Floor 2G1/G2 - Finish Electric		5	5	02-May-23	08-May-23												
3086	FNSH.D5.2970	1st Floor 2G1/G2 - Drop Remaining Ceiling Tile		1	1	09-May-23	09-May-23												
3087	FNSH.D5.2980	1st Floor 2G1/G2 - Finish Plumbing		4	4	10-May-23	15-May-23												
3088	FNSH.D5.2990	1st Floor 2G1/G2 - Finish HVAC		3	3	16-May-23	18-May-23												
3089	FNSH.D5.3000	1st Floor 2G1/G2 - Floor Coverings		6	6	19-May-23	26-May-23												
3090	2nd Floor Sector 2F1&F2 Admin			54	54	09-Feb-23	26-Apr-23												
3091	FRME.D5.366	2nd Floor 2F1/F2 - Layout and Frame Walls		13	13	09-Feb-23	28-Feb-23												
3092	MEP.D5.3320	2nd Floor 2F1/F2 - Rough-in Plumbing		8	8	09-Feb-23	21-Feb-23												
3093	MEP.D5.3330	2nd Floor 2F1/F2 - Rough-in HVAC		7	7	09-Feb-23	17-Feb-23												
3094	MEP.D5.3340	2nd Floor 2F1/F2 - Rough-in Fire		7	7	09-Feb-23	17-Feb-23												
3095	MEP.D5.3350	2nd Floor 2F1/F2 - Rough-in Electric		8	8	09-Feb-23	21-Feb-23												
3096	MEP.D5.3360	2nd Floor 2F1/F2 - Rough-in Low Volt		8	8	09-Feb-23	21-Feb-23												
3097	FRME.D5.371	2nd Floor 2F1/F2 - Install HM Door Frames		5	5	09-Feb-23	15-Feb-23												
3098	MEP.D5.3370	2nd Floor 2F1/F2 - Fire caulk		2	2	22-Feb-23	23-Feb-23												
3099	FRME.D5.367	2nd Floor 2F1/F2 - Insulate		4	4	24-Feb-23	01-Mar-23												
3100	FRME.D5.368	2nd Floor 2F1/F2 - Install Drywall Upper		5	5	02-Mar-23	08-Mar-23												
3101	FRME.D5.369	2nd Floor 2F1/F2 - Hang and Tape Drywall		8	8	09-Mar-23	20-Mar-23												
3102	FNSH.D5.3010	2nd Floor 2F1/F2 - Paint		3	3	21-Mar-23	23-Mar-23												
3103	FRME.D5.370	2nd Floor 2F1/F2 - Grid Ceiling		5	5	24-Mar-23	30-Mar-23												
3104	FNSH.D5.3020	2nd Floor 2F1/F2 - Doors & Hardware		5	5	31-Mar-23	06-Apr-23												
3105	FNSH.D5.3030	2nd Floor 2F1/F2 - Tile in Restroom		5	5	31-Mar-23	06-Apr-23												
3106	FNSH.D5.3040	2nd Floor 2F1/F2 - Finish Electric		5	5	31-Mar-23	06-Apr-23												
3107	FNSH.D5.3050	2nd Floor 2F1/F2 - Drop Remaining Ceiling Tile		1	1	07-Apr-23	07-Apr-23												
3108	FNSH.D5.3060	2nd Floor 2F1/F2 - Finish Plumbing		4	4	10-Apr-23	13-Apr-23												
3109	FNSH.D5.3070	2nd Floor 2F1/F2 - Finish HVAC		3	3	14-Apr-23	18-Apr-23												
3110	FNSH.D5.3080	2nd Floor 2F1/F2 - Floor Coverings		6	6	19-Apr-23	26-Apr-23												
Remaining Level of Effort			Remaining Work			Milestone			Page 65 of 74										
Actual Work			Critical Remaining Work			TASK filter: All Activities										© Oracle Corporation			

QTS HIL2 DC2, DC3, DC5 Construction Schedule				Classic Schedule Layout					12-Jul-22 15:37										
#	Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	2022					2023				2024			
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2		
3111	2nd Floor Sector 2G1&G2 Back of House	FRME.D5.372	2nd Floor 2G1/G2 - Layout and Frame Walls	9	9	21-Mar-23	31-Mar-23									12-May-23, 2nd Floor Sector 2G1&G2 Back of Hou			
3112		MEP.D5.3380	2nd Floor 2G1/G2 - Rough-in Plumbing	8	8	21-Mar-23	30-Mar-23									2nd Floor 2G1/G2- Layout and Frame Walls			
3113		MEP.D5.3390	2nd Floor 2G1/G2 - Rough-in HVAC	7	7	21-Mar-23	29-Mar-23									2nd Floor 2G1/G2- Rough-in Plumbing			
3114		MEP.D5.3400	2nd Floor 2G1/G2 - Rough-in Fire	7	7	21-Mar-23	29-Mar-23									2nd Floor 2G1/G2- Rough-in HVAC			
3115		MEP.D5.3410	2nd Floor 2G1/G2 - Rough-in Electric	8	8	21-Mar-23	30-Mar-23									2nd Floor 2G1/G2- Rough-in Fire			
3116		MEP.D5.3420	2nd Floor 2G1/G2 - Rough-in Low Volt	8	8	21-Mar-23	30-Mar-23									2nd Floor 2G1/G2- Rough-in Electric			
3117		FRME.D5.377	2nd Floor 2G1/G2 - Install HM Door Frame	5	5	21-Mar-23	27-Mar-23									2nd Floor 2G1/G2- Rough-in Low Volt			
3118		MEP.D5.3430	2nd Floor 2G1/G2 - Fire caulk	2	2	31-Mar-23	03-Apr-23									2nd Floor 2G1/G2 - Install HM Door Frame			
3119		FRME.D5.373	2nd Floor 2G1/G2 - Insulate	2	2	04-Apr-23	05-Apr-23									2nd Floor 2G1/G2 - Fire caulk			
3120		FRME.D5.374	2nd Floor 2G1/G2 - Install Drywall Upper	5	5	06-Apr-23	12-Apr-23									2nd Floor 2G1/G2 - Insulate			
3121		FRME.D5.375	2nd Floor 2G1/G2 - Hang and Tape Drywall	7	7	13-Apr-23	21-Apr-23									2nd Floor 2G1/G2 - Install Drywall Upper			
3122		FNSH.D5.3110	2nd Floor 2G1/G2 - Tile in Restroom	3	3	13-Apr-23	17-Apr-23									2nd Floor 2G1/G2 - Hang and Tape Drywall			
3123		FNSH.D5.3090	2nd Floor 2G1/G2 - Paint	3	3	24-Apr-23	26-Apr-23									2nd Floor 2G1/G2 - Tile in Restroom			
3124		FRME.D5.376	2nd Floor 2G1/G2 - Wood Ceiling	3	3	27-Apr-23	01-May-23									2nd Floor 2G1/G2 - Paint			
3125		FNSH.D5.3100	2nd Floor 2G1/G2 - Doors & Hardware	5	5	27-Apr-23	03-May-23									2nd Floor 2G1/G2 - Wood Ceiling			
3126		FNSH.D5.3120	2nd Floor 2G1/G2 - Finish Electric	5	5	27-Apr-23	03-May-23									2nd Floor 2G1/G2 - Doors & Hardware			
3127		FNSH.D5.3130	2nd Floor 2G1/G2 - Finish Plumbing	4	4	04-May-23	09-May-23									2nd Floor 2G1/G2 - Finish Electric			
3128		FNSH.D5.3140	2nd Floor 2G1/G2 - Finish HVAC	3	3	10-May-23	12-May-23									2nd Floor 2G1/G2 - Finish Plumbing			
3129		Site Finishes		67	67	07-Apr-23	12-Jul-23									2nd Floor 2G1/G2 - Finish HVAC			
3130		Trash Enclosure		9	9	07-Apr-23	19-Apr-23									12-Jul-23, Site Finishes			
3131		FOND.D5.257	Trash Encl - Dig Footings	1	1	07-Apr-23	07-Apr-23									19-Apr-23, Trash Enclosure			
3132		FOND.D5.258	Trash Encl - Form Footings	1	1	07-Apr-23	07-Apr-23									Trash Encl - Dig Footings			
3133		FOND.D5.259	Trash Encl - Install Rebar & Bollards	1	1	10-Apr-23	10-Apr-23									Trash Encl - Form Footings			
3134		FOND.D5.260	Trash Encl - Inspect & Pour	1	1	10-Apr-23	10-Apr-23									Trash Encl - Install Rebar & Bollards			
3135		CONC.D5.232	Trash Encl - Embeds for Gate	3	3	10-Apr-23	12-Apr-23									Trash Encl - Inspect & Pour			
3136		SOG.D5.2280	Trash Encl - SOG	2	2	11-Apr-23	12-Apr-23									Trash Encl - Embeds for Gate			
3137		CONC.D5.233	Trash Encl - CMU - Trash Enc.	3	3	13-Apr-23	17-Apr-23									Trash Encl - SOG			
3138		CONC.D5.234	Trash Encl - Grout CMU	1	1	18-Apr-23	18-Apr-23									Trash Encl - CMU - Trash Enc.			
3139		FNSH.D5.3150	Trash Encl - Install Gate	1	1	19-Apr-23	19-Apr-23									Trash Encl - Grout CMU			
3140		FNSH.D5.3160	Trash Encl - Install Steel Coping	1	1	19-Apr-23	19-Apr-23									Trash Encl - Install Gate			
3141		FNSH.D5.3170	Trash Encl - Paint	1	1	19-Apr-23	19-Apr-23									Trash Encl - Install Steel Coping			
3142		Parking Lot		24	24	25-May-23	28-Jun-23									28-Jun-23, Parking Lot			
3143		UTIL.D5.1160	Park. Lot - Install/Adjust Manhole Covers	3	3	25-May-23	30-May-23									Park. Lot - Install/Adjust Manhole Covers			
3144		FOND.D5.261	Park. Lot - Rough Grade Parking Lot	2	2	25-May-23	26-May-23									Park. Lot - Rough Grade Parking Lot			
3145		FNSH.D5.3190	Park. Lot - Landscape Sleeves	3	3	25-May-23	30-May-23									Park. Lot - Landscape Sleeves			
3146		CONC.D5.234	Park. Lot - Cut Curbs	2	2	30-May-23	31-May-23									Park. Lot - Cut Curbs			
3147		UTIL.D5.1170	Park. Lot - Install Catch Basins	3	3	01-Jun-23	05-Jun-23									Park. Lot - Install Catch Basins			
3148		MEP.D5.3440	Park. Lot - Street Light Conduits	2	2	06-Jun-23	07-Jun-23									Park. Lot - Street Light Conduits			
3149		CONC.D5.235	Park. Lot - Install Curbs & Inlets	3	3	06-Jun-23	08-Jun-23									Park. Lot - Install Curbs & Inlets			
3150		CONC.D5.236	Park. Lot - Street Light Bases	5	5	09-Jun-23	15-Jun-23									Park. Lot - Street Light Bases			
3151		FOND.D5.262	Park. Lot - Fine Grade Parking Lot	2	2	16-Jun-23	19-Jun-23									Park. Lot - Fine Grade Parking Lot			
3152		ASPV.D5.1040	Park. Lot - 1st Lift Asphalt - DC2	2	2	20-Jun-23	21-Jun-23									Park. Lot - 1st Lift Asphalt - DC2			
3153		CONC.D5.237	Park. Lot - Sidewalks	3	3	22-Jun-23	26-Jun-23									Park. Lot - Sidewalks			
3154		ASPV.D5.1050	Park. Lot - 2nd Lift Asphalt	1	1	27-Jun-23	27-Jun-23									Park. Lot - 2nd Lift Asphalt			
3155		CONC.D5.238	Park. Lot - Wheel Stops	1	1	28-Jun-23	28-Jun-23									Park. Lot - Wheel Stops			
3156		CONC.D5.239	Park. Lot - Strip	1	1	28-Jun-23	28-Jun-23									Park. Lot - Strip			
3157																			
 Remaining Level of Effort				 Remaining Work	 Milestone		 Summary					Page 66 of 74				TASK filter: All Activities			
																© Oracle Corporation			

QTS HIL2 DC2, DC3, DC5 Construction Schedule				Classic Schedule Layout						12-Jul-22 15:37							
#	Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	2022					2023				2024	
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2
3158	FNSH.D5.3180	Park. Lot - Signage	1	1	28-Jun-23	28-Jun-23									I	Park. Lot - Signage	
3159	Landscape and Fencing			14	14	22-Jun-23	12-Jul-23								▼	12-Jul-23, Landscape and Fencing	
3160	CONC.D5.240	Land Scp. - Site Concrete for Fence - DC2	3	3	22-Jun-23	26-Jun-23									■	Land Scp. - Site Concrete for Fence - DC2	
3161	FNSH.D5.3200	Land Scp. - Landscape Power and Irrigation	10	10	27-Jun-23	11-Jul-23									■	Land Scp. - Landscape Power and Irrigation	
3162	FNSH.D5.3210	Land Scp. - Fill Planters	2	2	27-Jun-23	28-Jun-23									I	Land Scp. - Fill Planters	
3163	FNSH.D5.3230	Land Scp. - Ground Cover	5	5	27-Jun-23	03-Jul-23									■	Land Scp. - Ground Cover	
3164	FNSH.D5.3240	Land Scp. - Install Fence	7	7	27-Jun-23	05-Jul-23									■	Land Scp. - Install Fence	
3165	FNSH.D5.3220	Land Scp. - Plantings	5	5	29-Jun-23	06-Jul-23									■	Land Scp. - Plantings	
3166	FNSH.D5.3250	Land Scp. - Gates and Access Control	5	5	06-Jul-23	12-Jul-23									■	Land Scp. - Gates and Access Control	
3167	1st Floor Data Hall			117	117	27-Jan-23	13-Jul-23								▼	13-Jul-23, 1st Floor Data Hall	
3168	House			109	109	27-Jan-23	30-Jun-23								▼	30-Jun-23, House	
3169	Rough-In			85	85	27-Jan-23	26-May-23								▼	26-May-23, Rough-In	
3170	FRME.D5.1	1st Floor House - Layout and Frame Walls	10	10	27-Jan-23	09-Feb-23									■	1st Floor House - Layout and Frame Walls	
3171	FRME.D5.1	1st Floor House - Install Door Frames	3	3	10-Feb-23	14-Feb-23									■	1st Floor House - Install Door Frames	
3172	MEP.D5.50	1st Floor House - Install Fire Protection	10	10	17-Mar-23	30-Mar-23									■	1st Floor House - Install Fire Protection	
3173	MEP.D5.50	1st Floor House - Install OH Mechanical (Plumbing and HVAC)	20	20	17-Mar-23	13-Apr-23									■	1st Floor House - Install OH Mechanical (Plumbing and HVAC)	
3174	MEP.D5.50	1st Floor House - Install OH Electrical	20	20	17-Mar-23	13-Apr-23									■	1st Floor House - Install OH Electrical	
3175	FRME.D5.1	1st Floor House - Install Drywall Upper	4	4	21-Apr-23	26-Apr-23									■	1st Floor House - Install Drywall Upper	
3176	MEP.D5.50	1st Floor House - In-wall Rough-in Electrical	4	4	27-Apr-23	02-May-23									■	1st Floor House - In-wall Rough-in Electrical	
3177	FRME.D5.1	1st Floor House - Install Structural Grid	10	10	27-Apr-23	10-May-23									■	1st Floor House - Install Structural Grid	
3178	FRME.D5.1	1st Floor House - Insulate and Inspect	5	5	03-May-23	09-May-23									■	1st Floor House - Insulate and Inspect	
3179	FRME.D5.1	1st Floor House - Hang and Tape Drywall	6	6	10-May-23	17-May-23									■	1st Floor House - Hang and Tape Drywall	
3180	MEP.D5.50	1st Floor House - Install Lighting	5	5	11-May-23	17-May-23									■	1st Floor House - Install Lighting	
3181	MEP.D5.50	1st Floor House - Install Sprinkler Drops	5	5	11-May-23	17-May-23									■	1st Floor House - Install Sprinkler Drops	
3182	FNSH.D5.5	1st Floor House - Paint House	2	2	18-May-23	19-May-23									I	1st Floor House - Paint House	
3183	FRME.D5.1	1st Floor House - Install Overhead Doors	5	5	18-May-23	24-May-23									■	1st Floor House - Install Overhead Doors	
3184	FNSH.D5.5	1st Floor House - Install Finishes	5	5	22-May-23	26-May-23									■	1st Floor House - Install Finishes	
3185	FNSH.D5.5	1st Floor House - Trim Out Electrical Devices	5	5	22-May-23	26-May-23									■	1st Floor House - Trim Out Electrical Devices	
3186	Equipment			29	29	22-May-23	30-Jun-23								▼	30-Jun-23, Equipment	
3187	EQPT.D5.5	1st Floor House - Install HDP Panels	10	10	22-May-23	05-Jun-23									■	1st Floor House - Install HDP Panels	
3188	EQPT.D5.5	1st Floor House - Install PDU	5	5	22-May-23	26-May-23									■	1st Floor House - Install PDU	
3189	EQPT.D5.5	1st Floor House - Set CRAC Units	5	5	08-Jun-23	14-Jun-23									■	1st Floor House - Set CRAC Units	
3190	EQPT.D5.5	1st Floor House - Install COD Boards	5	5	08-Jun-23	14-Jun-23									■	1st Floor House - Install COD Boards	
3191	EQPT.D5.5	1st Floor House - Final Connections CRAC Units	15	15	12-Jun-23	30-Jun-23									■	1st Floor House - Final Connections CRAC Units	
3192	EQPT.D5.5	1st Floor House - Set HUM	5	5	15-Jun-23	21-Jun-23									■	1st Floor House - Set HUM	
3193	MPOE 1 and 2			82	82	08-Mar-23	30-Jun-23								▼	30-Jun-23, MPOE 1 and 2	
3194	Rough-In			58	58	08-Mar-23	26-May-23								▼	26-May-23, Rough-In	
3195	FRME.D5.1	1st Floor MPOE 1/2 - Layout and Frame Walls	10	10	08-Mar-23	21-Mar-23									■	1st Floor MPOE 1/2 - Layout and Frame Walls	
3196	MEP.D5.26	1st Floor MPOE 1/2 - Install Fire Protection	10	10	17-Mar-23	30-Mar-23									■	1st Floor MPOE 1/2 - Install Fire Protection	
3197	MEP.D5.26	1st Floor MPOE 1/2 - Install OH Mechanical (Plumbing and HVAC)	20	20	17-Mar-23	13-Apr-23									■	1st Floor MPOE 1/2 - Install OH Mechanical (Plumbing and HVAC)	
3198	MEP.D5.26	1st Floor MPOE 1/2 - Install OH Electrical	20	20	17-Mar-23	13-Apr-23									■	1st Floor MPOE 1/2 - Install OH Electrical	
3199	FRME.D5.1	1st Floor MPOE 1/2 - Install Door Frames	3	3	22-Mar-23	24-Mar-23									■	1st Floor MPOE 1/2 - Install Door Frames	
3200	FRME.D5.1	1st Floor MPOE 1/2 - Install Drywall Upper	4	4	21-Apr-23	26-Apr-23									■	1st Floor MPOE 1/2 - Install Drywall Upper	
3201	MEP.D5.26	1st Floor MPOE 1/2 - In-wall Rough-in Electrical	4	4	27-Apr-23	02-May-23									■	1st Floor MPOE 1/2 - In-wall Rough-in Electrical	
3202	FRME.D5.1	1st Floor MPOE 1/2 - Install Structural Grid	10	10	27-Apr-23	10-May-23									■	1st Floor MPOE 1/2 - Install Structural Grid	
3203	FRME.D5.1	1st Floor MPOE 1/2 - Insulate and Inspect	5	5	03-May-23	09-May-23									■	1st Floor MPOE 1/2 - Insulate and Inspect	
3204	FRME.D5.1	1st Floor MPOE 1/2 - Hang and Tape Drywall	6	6	10-May-23	17-May-23									■	1st Floor MPOE 1/2 - Hang and Tape Drywall	
3205	MEP.D5.26	1st Floor MPOE 1/2 - Install Lighting	5	5	11-May-23	17-May-23									■	1st Floor MPOE 1/2 - Install Lighting	




QTS HIL2 DC2, DC3, DC5 Construction Schedule				Classic Schedule Layout					Timeline View									
#	Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	2022					2023				2024		
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	
3206	Equipment	MEP.D5.26 1st Floor MPOE 1/2 - Install Sprinkler Drops	5	5	11-May-23	17-May-23										1st Floor MPOE 1/2 - Install Sprinkler Drops		
3207		FNSH.D5.2 1st Floor MPOE 1/2 - Paint MPOE	2	2	18-May-23	19-May-23										1st Floor MPOE 1/2 - Paint MPOE		
3208		FRME.D5.2 1st Floor MPOE 1/2 - Install Overhead Doors	5	5	18-May-23	24-May-23										1st Floor MPOE 1/2 - Install Overhead Doors		
3209		FNSH.D5.2 1st Floor MPOE 1/2 - Install Finishes	5	5	22-May-23	26-May-23										1st Floor MPOE 1/2 - Install Finishes		
3210		FNSH.D5.2 1st Floor MPOE 1/2 - Trim Out Electrical Devices	5	5	22-May-23	26-May-23										1st Floor MPOE 1/2 - Trim Out Electrical Devices		
3211		Equipment		29	29	22-May-23	30-Jun-23									30-Jun-23; Equipment:		
3212		EQPT.D5.3 1st Floor MPOE 1/2 - Install HDP Panels	10	10	22-May-23	05-Jun-23										1st Floor MPOE 1/2 - Install HDP Panels		
3213		EQPT.D5.3 1st Floor MPOE 1/2 - Install Network COD 2000AMP	10	10	22-May-23	05-Jun-23										1st Floor MPOE 1/2 - Install Network COD 2000AMP		
3214		EQPT.D5.3 1st Floor MPOE 1/2 - Install PDU	5	5	06-Jun-23	12-Jun-23										1st Floor MPOE 1/2 - Install PDU		
3215		EQPT.D5.3 1st Floor MPOE 1/2 - Set CRAC Units	5	5	08-Jun-23	14-Jun-23										1st Floor MPOE 1/2 - Set CRAC Units		
3216	Systems Gallery 1001 and 1010 DH A	EQPT.D5.3 1st Floor MPOE 1/2 - Install COD Boards	5	5	08-Jun-23	14-Jun-23										1st Floor MPOE 1/2 - Install COD Boards		
3217		EQPT.D5.3 1st Floor MPOE 1/2 - Final Connections CRAC Units	15	15	12-Jun-23	30-Jun-23										1st Floor MPOE 1/2 - Final Connections CRAC Units		
3218		EQPT.D5.3 1st Floor MPOE 1/2 - Set HUM	5	5	15-Jun-23	21-Jun-23										1st Floor MPOE 1/2 - Set HUM		
3219		Systems Gallery 1001 and 1010 DH A		106	106	06-Feb-23	06-Jul-23									06-Jul-23; Systems Gallery 1001 and 1010 DH A		
3220		Rough-In		68	68	06-Feb-23	11-May-23									11-May-23; Rough-In		
3221		MEP.D5.28 1st Floor DHA SG1001/1010 - Install Fire Protection	15	15	06-Feb-23	27-Feb-23										1st Floor DHA SG1001/1010 - Install Fire Protection		
3222		MEP.D5.28 1st Floor DHA SG1001/1010 - Install OH Mechanical (Plumbing and HVAC)	15	15	28-Feb-23	20-Mar-23										1st Floor DHA SG1001/1010 - Install OH Mechanical (Plumbing and HVAC)		
3223		MEP.D5.28 1st Floor DHA SG1001/1010 - Install OH Electrical	20	20	28-Feb-23	27-Mar-23										1st Floor DHA SG1001/1010 - Install OH Electrical		
3224		FRME.D5.2 1st Floor DHA SG1001/1010 - Layout and Frame Walls	6	6	11-Apr-23	18-Apr-23										1st Floor DHA SG1001/1010 - Layout and Frame Walls		
3225		FRME.D5.2 1st Floor DHA SG1001/1010 - Install Drywall Upper	6	6	13-Apr-23	20-Apr-23										1st Floor DHA SG1001/1010 - Install Drywall Upper		
3226		MEP.D5.28 1st Floor DHA SG1001/1010 - In-wall Rough-in Electrical	5	5	13-Apr-23	19-Apr-23										1st Floor DHA SG1001/1010 - In-wall Rough-in Electrical		
3227		FRME.D5.2 1st Floor DHA SG1001/1010 - Insulate and Inspect	5	5	20-Apr-23	26-Apr-23										1st Floor DHA SG1001/1010 - Insulate and Inspect		
3228		FRME.D5.2 1st Floor DHA SG1001/1010 - Hang and Tape Drywall	6	6	27-Apr-23	04-May-23										1st Floor DHA SG1001/1010 - Hang and Tape Drywall		
3229	Equipment	FNSH.D5.2 1st Floor DHA SG1001/1010 - Paint - DHA SG	2	2	05-May-23	08-May-23										1st Floor DHA SG1001/1010 - Paint - DHA SG		
3230		FNSH.D5.2 1st Floor DHA SG1001/1010 - Install Finishes	3	3	09-May-23	11-May-23										1st Floor DHA SG1001/1010 - Install Finishes		
3231		Equipment		43	43	05-May-23	06-Jul-23									06-Jul-23; Equipment		
3232		EQPT.D5.3 1st Floor DHA SG1001/1010 - Install Switch Gear	5	5	05-May-23	11-May-23										1st Floor DHA SG1001/1010 - Install Switch Gear		
3233		EQPT.D5.3 1st Floor DHA SG1001/1010 - Install ATS	5	5	05-May-23	11-May-23										1st Floor DHA SG1001/1010 - Install ATS		
3234		EQPT.D5.3 1st Floor DHA SG1001/1010 - Install PDU	5	5	05-May-23	11-May-23										1st Floor DHA SG1001/1010 - Install PDU		
3235		EQPT.D5.3 1st Floor DHA SG1001/1010 - Install Reserve Busway	5	5	05-May-23	11-May-23										1st Floor DHA SG1001/1010 - Install Reserve Busway		
3236		EQPT.D5.3 1st Floor DHA SG1001/1010 - Install HDP	5	5	09-May-23	15-May-23										1st Floor DHA SG1001/1010 - Install HDP		
3237		EQPT.D5.3 1st Floor DHA SG1001/1010 - Install COD Boards	5	5	08-Jun-23	14-Jun-23										1st Floor DHA SG1001/1010 - Install COD Boards		
3238		EQPT.D5.3 1st Floor DHA SG1001/1010 - Install CRAC Units	5	5	08-Jun-23	14-Jun-23										1st Floor DHA SG1001/1010 - Install CRAC Units		
3239		EQPT.D5.3 1st Floor DHA SG1001/1010 - Final Connections CRAC Units	15	15	15-Jun-23	06-Jul-23										1st Floor DHA SG1001/1010 - Final Connections CRAC Units		
3240		EQPT.D5.3 1st Floor DHA SG1001/1010 - Pull and Terminate Feeders	15	15	15-Jun-23	06-Jul-23										1st Floor DHA SG1001/1010 - Pull and Terminate Feeders		
3241	Mechanical Gallery 1002 DHA		103	103	09-Feb-23	06-Jul-23										06-Jul-23; Mechanical Gallery 1002 DHA		
3242	Rough-In	Rough-In		23	23	09-Feb-23	14-Mar-23									14-Mar-23; Rough-In		
3243		FRME.D5.2 1st Floor DHA MG1002 - Layout and Frame Walls	6	6	09-Feb-23	16-Feb-23										1st Floor DHA MG1002 - Layout and Frame Walls		
3244		MEP.D5.27 1st Floor DHA MG1002 - Install Fire Protection	1	1	09-Feb-23	09-Feb-23										1st Floor DHA MG1002 - Install Fire Protection		
3245		MEP.D5.28 1st Floor DHA MG1002 - Install OH Mechanical (Plumbing and HVAC)	3	3	09-Feb-23	13-Feb-23										1st Floor DHA MG1002 - Install OH Mechanical (Plumbing and HVAC)		
3246		MEP.D5.28 1st Floor DHA MG1002 - Install OH Electrical	5	5	09-Feb-23	15-Feb-23										1st Floor DHA MG1002 - Install OH Electrical		
3247		MEP.D5.27 1st Floor DHA MG1002 - In-wall Rough-in Electrical	3	3	10-Feb-23	14-Feb-23										1st Floor DHA MG1002 - In-wall Rough-in Electrical		
3248		FRME.D5.2 1st Floor DHA MG1002 - Insulate and Inspect	5	5	15-Feb-23	22-Feb-23										1st Floor DHA MG1002 - Insulate and Inspect		
3249		FRME.D5.2 1st Floor DHA MG1002 - Install Drywall Upper	6	6	17-Feb-23	27-Feb-23										1st Floor DHA MG1002 - Install Drywall Upper		
3250		FRME.D5.2 1st Floor DHA MG1002 - Hang and Tape Drywall	6	6	28-Feb-23	07-Mar-23										1st Floor DHA MG1002 - Hang and Tape Drywall		
3251		FNSH.D5.2 1st Floor DHA MG1002 - Paint	2	2	08-Mar-23	09-Mar-23										1st Floor DHA MG1002 - Paint		
3252		FNSH.D5.2 1st Floor DHA MG1002 - Install Finishes	3	3	10-Mar-23	14-Mar-23										1st Floor DHA MG1002 - Install Finishes		
3253	Equipment		61	61	11-Apr-23	06-Jul-23										06-Jul-23; Equipment		
Remaining Level of Effort				Remaining Work		◆	◆	Milestone								TASK filter: All Activities		

QTS HIL2 DC2, DC3, DC5 Construction Schedule				Classic Schedule Layout						12-Jul-22 15:37							
#	Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	2022					2023				2024	
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2
3254	EQPT.D5.3	1st Floor DHA MG1002 - Install HDP Boards	5	5	11-Apr-23	17-Apr-23										1st Floor DHA MG1002 - Install HDP Boards	
3255	EQPT.D5.3	1st Floor DHA MG1002 - Pull and Terminate Feeders	15	15	18-Apr-23	08-May-23										1st Floor DHA MG1002 - Pull and Terminate Feeders	
3256	EQPT.D5.3	1st Floor DHA MG1002 - Install CRAC Units	5	5	08-Jun-23	14-Jun-23										1st Floor DHA MG1002 - Install CRAC Units	
3257	EQPT.D5.3	1st Floor DHA MG1002 - Final Connections CRAC Units	15	15	15-Jun-23	06-Jul-23										1st Floor DHA MG1002 - Final Connections	
3258	DHA ROOM 1100			41	41	17-Feb-23	17-Apr-23									17-Apr-23, DH A ROOM 1100	
3259	Rough-In			41	41	17-Feb-23	17-Apr-23									17-Apr-23, Rough-In	
3260	FRME.D5.1	1st Floor DHA R1100 - Layout and Frame Walls	10	10	17-Feb-23	03-Mar-23										1st Floor DHA R1100 - Layout and Frame Walls	
3261	FRME.D5.1	1st Floor DHA R1100 - Install Drywall Upper	4	4	06-Mar-23	09-Mar-23										1st Floor DHA R1100 - Install Drywall Upper	
3262	MEP.D5.27	1st Floor DHA R1100 - Rough-In Fire Protection	3	3	10-Mar-23	14-Mar-23										1st Floor DHA R1100 - Rough-In Fire Protection	
3263	MEP.D5.27	1st Floor DHA R1100 - In-wall Rough-in Electrical	4	4	10-Mar-23	15-Mar-23										1st Floor DHA R1100 - In-wall Rough-in Electrical	
3264	MEP.D5.27	1st Floor DHA R1100 - Install OH Mechanical (Plumbing and HVAC)	5	5	16-Mar-23	22-Mar-23										1st Floor DHA R1100 - Install OH Mechanical (Plumbing and HVAC)	
3265	FRME.D5.1	1st Floor DHA R1100 - Insulate and Inspect	5	5	16-Mar-23	22-Mar-23										1st Floor DHA R1100 - Insulate and Inspect	
3266	MEP.D5.27	1st Floor DHA R1100 - Install OH Electrical	7	7	23-Mar-23	31-Mar-23										1st Floor DHA R1100 - Install OH Electrical	
3267	FRME.D5.1	1st Floor DHA R1100 - Hang and Tape Drywall	6	6	03-Apr-23	10-Apr-23										1st Floor DHA R1100 - Hang and Tape Drywall	
3268	FRME.D5.1	1st Floor DHA R1100 - Install Structural Grid	10	10	03-Apr-23	14-Apr-23										1st Floor DHA R1100 - Install Structural Grid	
3269	FNSH.D5.2	1st Floor DHA R1100 - Paint DHA R	2	2	11-Apr-23	12-Apr-23										1st Floor DHA R1100 - Paint DHA R	
3270	FNSH.D5.2	1st Floor DHA R1100 - Install Finishes	3	3	13-Apr-23	17-Apr-23										1st Floor DHA R1100 - Install Finishes	
3271	Systems Gallery 1003 and 1020 DH D			81	81	21-Mar-23	13-Jul-23									13-Jul-23, Systems Gallery 1003 and 1020	
3272	Rough-In			49	49	21-Mar-23	26-May-23									26-May-23, Rough-In	
3273	MEP.D5.29	1st Floor DHD SG1003/1020 - Install Fire Protection	5	5	21-Mar-23	27-Mar-23										1st Floor DHD SG1003/1020 - Install Fire Protection	
3274	MEP.D5.29	1st Floor DHD SG1003/1020 - Install OH Mechanical (Plumbing and HVAC)	15	15	28-Mar-23	17-Apr-23										1st Floor DHD SG1003/1020 - Install OH Mechanical (Plumbing and HVAC)	
3275	MEP.D5.29	1st Floor DHD SG1003/1020 - Install OH Electrical	20	20	28-Mar-23	24-Apr-23										1st Floor DHD SG1003/1020 - Install OH Electrical	
3276	FRME.D5.1	1st Floor DHD SG1003/1020 - Layout and Frame Walls	6	6	28-Apr-23	05-May-23										1st Floor DHD SG1003/1020 - Layout and Frame Walls	
3277	FRME.D5.1	1st Floor DHD SG1003/1020 - Install Drywall Upper	6	6	02-May-23	09-May-23										1st Floor DHD SG1003/1020 - Install Drywall Upper	
3278	MEP.D5.29	1st Floor DHD SG1003/1020 - In-wall Rough-in Electrical	3	3	02-May-23	04-May-23										1st Floor DHD SG1003/1020 - In-wall Rough-in Electrical	
3279	FRME.D5.1	1st Floor DHD SG1003/1020 - Insulate and Inspect	5	5	05-May-23	11-May-23										1st Floor DHD SG1003/1020 - Insulate and Inspect	
3280	FRME.D5.1	1st Floor DHD SG1003/1020 - Hang and Tape Drywall	6	6	12-May-23	19-May-23										1st Floor DHD SG1003/1020 - Hang and Tape Drywall	
3281	FNSH.D5.2	1st Floor DHD SG1003/1020 - Paint	2	2	22-May-23	23-May-23										1st Floor DHD SG1003/1020 - Paint	
3282	FNSH.D5.2	1st Floor DHD SG1003/1020 - Install Finishes	3	3	24-May-23	26-May-23										1st Floor DHD SG1003/1020 - Install Finishes	
3283	Equipment			37	37	22-May-23	13-Jul-23									13-Jul-23, Equipment	
3284	EQPT.D5.3	1st Floor DHD SG1003/1020 - Install Switch Gear	5	5	22-May-23	26-May-23										1st Floor DHD SG1003/1020 - Install Switch Gear	
3285	EQPT.D5.3	1st Floor DHD SG1003/1020 - Install Reserve Busway	5	5	22-May-23	26-May-23										1st Floor DHD SG1003/1020 - Install Reserve Busway	
3286	EQPT.D5.3	1st Floor DHD SG1003/1020 - Install ATS	5	5	30-May-23	05-Jun-23										1st Floor DHD SG1003/1020 - Install ATS	
3287	EQPT.D5.3	1st Floor DHD SG1003/1020 - Install COD Boards	5	5	08-Jun-23	14-Jun-23										1st Floor DHD SG1003/1020 - Install COD Boards	
3288	EQPT.D5.3	1st Floor DHD SG1003/1020 - Install CRAC Units	5	5	08-Jun-23	14-Jun-23										1st Floor DHD SG1003/1020 - Install CRAC Units	
3289	EQPT.D5.3	1st Floor DHD SG1003/1020 - Install HDP	5	5	15-Jun-23	21-Jun-23										1st Floor DHD SG1003/1020 - Install HDP	
3290	EQPT.D5.3	1st Floor DHD SG1003/1020 - Install PDU	5	5	15-Jun-23	21-Jun-23										1st Floor DHD SG1003/1020 - Install PDU	
3291	EQPT.D5.3	1st Floor DHD SG1003/1020 - Final Connections CRAC Units	15	15	15-Jun-23	06-Jul-23										1st Floor DHD SG1003/1020 - Final Connections CRAC Units	
3292	EQPT.D5.3	1st Floor DHD SG1003/1020 - Pull and Terminate Feeders	15	15	22-Jun-23	13-Jul-23										1st Floor DHD SG1003/1020 - Pull and Terminate Feeders	
3293	Mechanical Gallery 1004 DH D			76	76	21-Mar-23	06-Jul-23									06-Jul-23, Mechanical Gallery 1004 DH D	
3294	Rough-In			57	57	21-Mar-23	08-Jun-23									08-Jun-23, Rough-In	
3295	MEP.D5.28	1st Floor DHD MG1004 - Install Fire Protection	5	5	21-Mar-23	27-Mar-23										1st Floor DHD MG1004 - Install Fire Protection	
3296	MEP.D5.28	1st Floor DHD MG1004 - In-wall Rough-in Electrical	3	3	28-Mar-23	30-Mar-23										1st Floor DHD MG1004 - In-wall Rough-in Electrical	
3297	MEP.D5.28	1st Floor DHD MG1004 - Install OH Mechanical (Plumbing and HVAC)	5	5	28-Mar-23	03-Apr-23										1st Floor DHD MG1004 - Install OH Mechanical (Plumbing and HVAC)	
3298	FRME.D5.1	1st Floor DHD MG1004 - Insulate and Inspect	5	5	31-Mar-23	06-Apr-23										1st Floor DHD MG1004 - Insulate and Inspect	
3299	MEP.D5.28	1st Floor DHD MG1004 - Install OH Electrical	5	5	04-Apr-23	10-Apr-23										1st Floor DHD MG1004 - Install OH Electrical	
3300	FRME.D5.1	1st Floor DHD MG1004 - Layout and Frame Walls	6	6	08-May-23	15-May-23											

QTS HIL2 DC2, DC3, DC5 Construction Schedule				Classic Schedule Layout						12-Jul-22 15:37							
#	Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	2022					2023				2024	
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2
3302	FRME.D5.1	1st Floor DHD MG1004 - Hang and Tape Drywall	6	6	24-May-23	01-Jun-23										1st Floor DHD MG1004 - Hang and Tape Drywall	
3303	FNSH.D5.2	1st Floor DHD MG1004 - Paint		2	2	02-Jun-23	05-Jun-23									1st Floor DHD MG1004 - Paint	
3304	FNSH.D5.2	1st Floor DHD MG1004 - Install Finishes		3	3	06-Jun-23	08-Jun-23									1st Floor DHD MG1004 - Install Finishes	
3305	Equipment			24	24	02-Jun-23	06-Jul-23									06-Jul-23; Equipment	
3306	EQPT.D5.3	1st Floor DHD MG1004 - Install HDP Boards		5	5	02-Jun-23	08-Jun-23									1st Floor DHD MG1004 - Install HDP Boards	
3307	EQPT.D5.3	1st Floor DHD MG1004 - Install CRAC Units		5	5	08-Jun-23	14-Jun-23									1st Floor DHD MG1004 - Install CRAC Units	
3308	EQPT.D5.3	1st Floor DHD MG1004 - Pull and Terminate Feeders		15	15	09-Jun-23	29-Jun-23									1st Floor DHD MG1004 - Pull and Terminate	
3309	EQPT.D5.3	1st Floor DHD MG1004 - Final Connections CRAC Units		15	15	15-Jun-23	06-Jul-23									1st Floor DHD MG1004 - Final Connections	
3310	DH D ROOM 1200			41	41	16-May-23	13-Jul-23									13-Jul-23; DH D ROOM 1200	
3311	Rough-In			41	41	16-May-23	13-Jul-23									13-Jul-23; Rough-In	
3312	FRME.D5.1	1st Floor DHD R1200 - Layout and Frame Walls		10	10	16-May-23	30-May-23									1st Floor DHD R1200 - Layout and Frame Walls	
3313	FRME.D5.1	1st Floor DHD R1200 - Install Drywall Upper		4	4	31-May-23	05-Jun-23									1st Floor DHD R1200 - Install Drywall Upper	
3314	MEP.D5.27	1st Floor DHD R1200 - Install Fire Protection		3	3	06-Jun-23	08-Jun-23									1st Floor DHD R1200 - Install Fire Protection	
3315	MEP.D5.27	1st Floor DHD R1200 - In-wall Rough-in Electrical		4	4	06-Jun-23	09-Jun-23									1st Floor DHD R1200 - In-wall Rough-in Electric	
3316	MEP.D5.27	1st Floor DHD R1200 - Install OH Mechanical (Plumbing and HVAC)		5	5	12-Jun-23	16-Jun-23									1st Floor DHD R1200 - Install OH Mechanical	
3317	FRME.D5.1	1st Floor DHD R1200 - Insulate and Inspect		5	5	12-Jun-23	16-Jun-23									1st Floor DHD R1200 - Insulate and Inspect	
3318	MEP.D5.27	1st Floor DHD R1200 - Install OH Electrical		7	7	19-Jun-23	27-Jun-23									1st Floor DHD R1200 - Install OH Electrical	
3319	FRME.D5.1	1st Floor DHD R1200 - Hang and Tape Drywall		6	6	28-Jun-23	06-Jul-23									1st Floor DHD R1200 - Hang and Tape Dry	
3320	FRME.D5.1	1st Floor DHD R1200 - Install Structural Grid		10	10	28-Jun-23	12-Jul-23									1st Floor DHD R1200 - Install Structural Gr	
3321	FNSH.D5.2	1st Floor DHD R1200 - Paint		2	2	07-Jul-23	10-Jul-23									1st Floor DHD R1200 - Paint	
3322	FNSH.D5.2	1st Floor DHD R1200 - Install Finishes		3	3	11-Jul-23	13-Jul-23									1st Floor DHD R1200 - Install Finishes	
3323	2nd Floor Data Hall			101	101	21-Feb-23	13-Jul-23									13-Jul-23; 2nd Floor Data Hall	
3324	BDF 1 and 2			93	93	03-Mar-23	13-Jul-23									13-Jul-23; BDF 1 and 2	
3325	Rough-In			40	40	03-Mar-23	27-Apr-23									27-Apr-23; Rough-In	
3326	MEP.D5.29	2nd Floor BDF1/2 - Install Fire Protection		3	3	03-Mar-23	07-Mar-23									2nd Floor BDF1/2 - Install Fire Protection	
3327	MEP.D5.29	2nd Floor BDF1/2 - Install OH Mechanical (Plumbing and HVAC)		5	5	08-Mar-23	14-Mar-23									2nd Floor BDF1/2 - Install OH Mechanical	
3328	MEP.D5.29	2nd Floor BDF1/2 - Install OH Electrical		7	7	08-Mar-23	16-Mar-23									2nd Floor BDF1/2 - Install OH Electrical	
3329	FRME.D5.1	2nd Floor BDF1/2 - Layout and Frame Walls		10	10	17-Mar-23	30-Mar-23									2nd Floor BDF1/2 - Layout and Frame Walls	
3330	FRME.D5.1	2nd Floor BDF1/2 - Install Drywall Upper		4	4	31-Mar-23	05-Apr-23									2nd Floor BDF1/2 - Install Drywall Upper	
3331	MEP.D5.29	2nd Floor BDF1/2 - In-wall Rough-in Electrical		4	4	31-Mar-23	05-Apr-23									2nd Floor BDF1/2 - In-wall Rough-in Electrical	
3332	FRME.D5.1	2nd Floor BDF1/2 - Install Structural Grid		10	10	06-Apr-23	19-Apr-23									2nd Floor BDF1/2 - Install Structural Grid	
3333	FRME.D5.1	2nd Floor BDF1/2 - Insulate and Inspect		5	5	06-Apr-23	12-Apr-23									2nd Floor BDF1/2 - Insulate and Inspect	
3334	FRME.D5.1	2nd Floor BDF1/2 - Hang and Tape Drywall		6	6	13-Apr-23	20-Apr-23									2nd Floor BDF1/2 - Hang and Tape Drywall	
3335	FNSH.D5.2	2nd Floor BDF1/2 - Paint		2	2	21-Apr-23	24-Apr-23									2nd Floor BDF1/2 - Paint	
3336	FNSH.D5.2	2nd Floor BDF1/2 - Install Finishes		3	3	25-Apr-23	27-Apr-23									2nd Floor BDF1/2 - Install Finishes	
3337	Equipment			56	56	25-Apr-23	13-Jul-23									13-Jul-23; Equipment	
3338	EQPT.D5.3	2nd Floor BDF1/2 - Install HDP Panels		10	10	25-Apr-23	08-May-23									2nd Floor BDF1/2 - Install HDP Panels	
3339	EQPT.D5.3	2nd Floor BDF1/2 - Set CRAC's		5	5	08-Jun-23	14-Jun-23									2nd Floor BDF1/2 - Set CRAC's	
3340	EQPT.D5.3	2nd Floor BDF1/2 - Set HUM		5	5	15-Jun-23	21-Jun-23									2nd Floor BDF1/2 - Set HUM	
3341	EQPT.D5.3	2nd Floor BDF1/2 - Final Connections CRAC Units		15	15	15-Jun-23	06-Jul-23									2nd Floor BDF1/2 - Final Connections CRA	
3342	EQPT.D5.3	2nd Floor BDF1/2 - Pull and Terminate Feeders		15	15	22-Jun-23	13-Jul-23									2nd Floor BDF1/2 - Pull and Terminate Feed	
3343	Systems Gallery 2001 and 2010 DH B			96	96	21-Feb-23	06-Jul-23									06-Jul-23; Systems Gallery 2001 and 2010 D	
3344	Rough-In			58	58	21-Feb-23	11-May-23									11-May-23; Rough-In	
3345	MEP.D5.31	2nd Floor DHB SG 2001/2010 - Install Fire Protection		5	5	21-Feb-23	27-Feb-23									2nd Floor DHB SG 2001/2010 - Install Fire Protection	
3346	MEP.D5.31	2nd Floor DHB SG 2001/2010 - Install OH Mechanical (Plumbing and HVAC)		15	15	28-Feb-23	20-Mar-23									2nd Floor DHB SG 2001/2010 - Install OH Mechanical	
3347	MEP.D5.31	2nd Floor DHB SG 2001/2010 - Install OH Electrical		20	20	28-Feb-23	27-Mar-23									2nd Floor DHB SG 2001/2010 - Install OH Electrical	
3348	FRME.D5.1	2nd Floor DHB SG 2001/2010 - Layout and Frame Walls		6	6	11-Apr-23	18-Apr-23									2nd Floor DHB SG 2001/2010 - Layout and Frame Wa	
3349	MEP.D5.31	2nd Floor DHB SG 2001/2010 - In-wall Rough-in Electrical		3	3	13-Apr-23	17-Apr-23									2nd Floor DHB SG 2001/2010 - In-wall Rough-in Elect	

QTS HIL2 DC2, DC3, DC5 Construction Schedule				Classic Schedule Layout					Timeline View									
#	Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	2022					2023				2024		
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	
3350		FRME.D5.1 2nd Floor DHB SG 2001/2010 - Insulate and Inspect	5	5	18-Apr-23	24-Apr-23												2nd Floor DHB SG 2001/2010 - Insulate and Inspect
3351		FRME.D5.1 2nd Floor DHB SG 2001/2010 - Install Drywall Upper	6	6	19-Apr-23	26-Apr-23												2nd Floor DHB SG 2001/2010 - Install Drywall Upper
3352		FRME.D5.1 2nd Floor DHB SG 2001/2010 - Hang and Tape Drywall	6	6	27-Apr-23	04-May-23												2nd Floor DHB SG 2001/2010 - Hang and Tape Drywall
3353		FNSH.D5.2 2nd Floor DHB SG 2001/2010 - Paint	2	2	05-May-23	08-May-23												2nd Floor DHB SG 2001/2010 - Paint
3354		FNSH.D5.2 2nd Floor DHB SG 2001/2010 - Install Finishes	3	3	09-May-23	11-May-23												2nd Floor DHB SG 2001/2010 - Install Finishes
3355	Equipment			58	58	14-Apr-23	06-Jul-23											06-Jul-23; Equipment
3356		EQPT.D5.3 2nd Floor DHB SG 2001/2010 - Install Switch Gear	5	5	14-Apr-23	20-Apr-23												2nd Floor DHB SG 2001/2010 - Install Switch Gear
3357		EQPT.D5.3 2nd Floor DHB SG 2001/2010 - Install ATS	5	5	14-Apr-23	20-Apr-23												2nd Floor DHB SG 2001/2010 - Install ATS
3358		EQPT.D5.3 2nd Floor DHB SG 2001/2010 - Install HDP	5	5	14-Apr-23	20-Apr-23												2nd Floor DHB SG 2001/2010 - Install HDP
3359		EQPT.D5.3 2nd Floor DHB SG 2001/2010 - Install PDU	5	5	14-Apr-23	20-Apr-23												2nd Floor DHB SG 2001/2010 - Install PDU
3360		EQPT.D5.3 2nd Floor DHB SG 2001/2010 - Install Reserve Busway	5	5	14-Apr-23	20-Apr-23												2nd Floor DHB SG 2001/2010 - Install Reserve Busway
3361		EQPT.D5.3 2nd Floor DHB SG 2001/2010 - Install COD Boards	5	5	08-Jun-23	14-Jun-23												2nd Floor DHB SG 2001/2010 - Install COD Boards
3362		EQPT.D5.3 2nd Floor DHB SG 2001/2010 - Install CRAC Units	5	5	08-Jun-23	14-Jun-23												2nd Floor DHB SG 2001/2010 - Install CRAC Units
3363		EQPT.D5.3 2nd Floor DHB SG 2001/2010 - Final Connections CRAC Units	15	15	15-Jun-23	06-Jul-23												2nd Floor DHB SG 2001/2010 - Final Connections CRAC Units
3364		EQPT.D5.3 2nd Floor DHB SG 2001/2010 - Pull and Terminate Feeders	15	15	15-Jun-23	06-Jul-23												2nd Floor DHB SG 2001/2010 - Pull and Terminate Feeders
3365	Mechanical Gallery 2002 DH B			96	96	21-Feb-23	06-Jul-23											06-Jul-23; Mechanical Gallery 2002 DH B
3366	Rough-In			64	64	21-Feb-23	19-May-23											19-May-23; Rough-In
3367		FRME.D5.1 2nd Floor DHB MG 2002 - Layout and Frame Walls	6	6	21-Feb-23	28-Feb-23												2nd Floor DHB MG 2002 - Layout and Frame Walls
3368		MEP.D5.3C 2nd Floor DHB MG 2002 - Install Fire Protection	1	1	21-Feb-23	21-Feb-23												2nd Floor DHB MG 2002 - Install Fire Protection
3369		MEP.D5.3C 2nd Floor DHB MG 2002 - Install OH Mechanical (Plumbing and HVAC)	3	3	21-Feb-23	23-Feb-23												2nd Floor DHB MG 2002 - Install OH Mechanical (Plumbing and HVAC)
3370		MEP.D5.3C 2nd Floor DHB MG 2002 - Install OH Electrical	5	5	21-Feb-23	27-Feb-23												2nd Floor DHB MG 2002 - Install OH Electrical
3371		MEP.D5.3C 2nd Floor DHB MG 2002 - In-wall Rough-in Electrical	3	3	22-Feb-23	24-Feb-23												2nd Floor DHB MG 2002 - In-wall Rough-in Electrical
3372		FRME.D5.1 2nd Floor DHB MG 2002 - Insulate and Inspect	5	5	27-Feb-23	03-Mar-23												2nd Floor DHB MG 2002 - Insulate and Inspect
3373		FRME.D5.1 2nd Floor DHB MG 2002 - Install Drywall Upper	6	6	01-Mar-23	08-Mar-23												2nd Floor DHB MG 2002 - Install Drywall Upper
3374		FRME.D5.1 2nd Floor DHB MG 2002 - Hang and Tape Drywall	6	6	05-May-23	12-May-23												2nd Floor DHB MG 2002 - Hang and Tape Drywall
3375		FNSH.D5.2 2nd Floor DHB MG 2002 - Paint	2	2	15-May-23	16-May-23												2nd Floor DHB MG 2002 - Paint
3376		FNSH.D5.2 2nd Floor DHB MG 2002 - Install Finishes	3	3	17-May-23	19-May-23												2nd Floor DHB MG 2002 - Install Finishes
3377	Equipment			37	37	15-May-23	06-Jul-23											06-Jul-23; Equipment
3378		EQPT.D5.3 2nd Floor DHB MG 2002 - Install HDP Boards	5	5	15-May-23	19-May-23												2nd Floor DHB MG 2002 - Install HDP Boards
3379		EQPT.D5.3 2nd Floor DHB MG 2002 - Pull and Terminate Feeders	15	15	22-May-23	12-Jun-23												2nd Floor DHB MG 2002 - Pull and Terminate Feeders
3380		EQPT.D5.3 2nd Floor DHB MG 2002 - Install CRAC Units	5	5	08-Jun-23	14-Jun-23												2nd Floor DHB MG 2002 - Install CRAC Units
3381		EQPT.D5.3 2nd Floor DHB MG 2002 - Final Connections CRAC Units	15	15	15-Jun-23	06-Jul-23												2nd Floor DHB MG 2002 - Final Connections CRAC Units
3382	DH B ROOM 2100			64	64	01-Mar-23	30-May-23											30-May-23; DH B ROOM 2100
3383	Rough-In			64	64	01-Mar-23	30-May-23											30-May-23; Rough-In
3384		FRME.D5.1 2nd Floor DHB R2100 - Layout and Frame Walls	10	10	01-Mar-23	14-Mar-23												2nd Floor DHB R2100 - Layout and Frame Walls
3385		MEP.D5.29 2nd Floor DHB R2100 - Install Fire Protection	3	3	01-Mar-23	03-Mar-23												2nd Floor DHB R2100 - Install Fire Protection
3386		MEP.D5.30 2nd Floor DHB R2100 - Install OH Electrical	7	7	01-Mar-23	09-Mar-23												2nd Floor DHB R2100 - Install OH Electrical
3387		FRME.D5.1 2nd Floor DHB R2100 - Install Structural Grid	10	10	10-Mar-23	23-Mar-23												2nd Floor DHB R2100 - Install Structural Grid
3388		FRME.D5.1 2nd Floor DHB R2100 - Install Drywall Upper	4	4	15-Mar-23	20-Mar-23												2nd Floor DHB R2100 - Install Drywall Upper
3389		MEP.D5.29 2nd Floor DHB R2100 - In-wall Rough-in Electrical	4	4	21-Mar-23	24-Mar-23												2nd Floor DHB R2100 - In-wall Rough-in Electrical
3390		FRME.D5.1 2nd Floor DHB R2100 - Insulate and Inspect	5	5	27-Mar-23	31-Mar-23												2nd Floor DHB R2100 - Insulate and Inspect
3391		FRME.D5.1 2nd Floor DHB R2100 - Hang and Tape Drywall	6	6	15-May-23	22-May-23												2nd Floor DHB R2100 - Hang and Tape Drywall
3392		FNSH.D5.2 2nd Floor DHB R2100 - Paint	2	2	23-May-23	24-May-23												2nd Floor DHB R2100 - Paint
3393		FNSH.D5.2 2nd Floor DHB R2100 - Install Finishes	3	3	25-May-23	30-May-23												2nd Floor DHB R2100 - Install Finishes
3394	Systems Gallery 2020 and 2003 DH C			81	81	21-Mar-23	13-Jul-23											13-Jul-23; Systems Gallery 2020 and 2003 DH C
3395	Rough-In			59	59	21-Mar-23	12-Jun-23											12-Jun-23; Rough-In
3396		MEP.D5.31 2nd Floor DHC 2020/2003 - Install Fire Protection	5	5	21-Mar-23	27-Mar-23												2nd Floor DHC 2020/2003 - Install Fire Protection
3397		MEP.D5.31 2nd Floor DHC 2020/2003 - Install OH Mechanical (Plumbing and HVAC)	15	15	28-Mar-23	17-Apr-23												2nd Floor DHC 2020/2003 - Install OH Mechanical (Plumbing and HVAC)
█ Remaining Level of Effort █ Remaining Work ◆ Milestone ◆ Critical Remaining Work █ Summary			Page 71 of 74															

QTS HIL2 DC2, DC3, DC5 Construction Schedule				Classic Schedule Layout						12-Jul-22 15:37								
#	Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	2022					2023				2024		
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	
3398		MEP.D5.31 2nd Floor DHC 2020/2003 - Install OH Electrical	20	20	28-Mar-23	24-Apr-23												2nd Floor DHC 2020/2003 - Install OH Electrical
3399		FRME.D5.1 2nd Floor DHC 2020/2003 - Layout and Frame Walls	6	6	28-Apr-23	05-May-23												2nd Floor DHC 2020/2003 - Layout and Frame Wall
3400		FRME.D5.1 2nd Floor DHC 2020/2003 - Install Drywall Upper	6	6	08-May-23	15-May-23												2nd Floor DHC 2020/2003 - Install Drywall Upper
3401		MEP.D5.31 2nd Floor DHC 2020/2003 - In-wall Rough-in Electrical	3	3	16-May-23	18-May-23												2nd Floor DHC 2020/2003 - In-wall Rough-in Elect
3402		FRME.D5.1 2nd Floor DHC 2020/2003 - Insulate and Inspect	5	5	19-May-23	25-May-23												2nd Floor DHC 2020/2003 - Insulate and Inspect
3403		FRME.D5.1 2nd Floor DHC 2020/2003 - Hang and Tape Drywall	6	6	26-May-23	05-Jun-23												2nd Floor DHC 2020/2003 - Hang and Tape Dry
3404		FNSH.D5.2 2nd Floor DHC 2020/2003 - Paint	2	2	06-Jun-23	07-Jun-23												2nd Floor DHC 2020/2003 - Paint
3405		FNSH.D5.2 2nd Floor DHC 2020/2003 - Install Finishes	3	3	08-Jun-23	12-Jun-23												2nd Floor DHC 2020/2003 - Install Finishes
3406	Equipment			53	53	28-Apr-23	13-Jul-23											13-Jul-23, Equipment
3407		EQPT.D5.3 2nd Floor DHC 2020/2003 - Install ATS	5	5	28-Apr-23	04-May-23												2nd Floor DHC 2020/2003 - Install ATS
3408		EQPT.D5.3 2nd Floor DHC 2020/2003 - Install HDP	5	5	28-Apr-23	04-May-23												2nd Floor DHC 2020/2003 - Install HDP
3409		EQPT.D5.3 2nd Floor DHC 2020/2003 - Install PDU	5	5	28-Apr-23	04-May-23												2nd Floor DHC 2020/2003 - Install PDU
3410		EQPT.D5.3 2nd Floor DHC 2020/2003 - Install Reserve Busway	5	5	28-Apr-23	04-May-23												2nd Floor DHC 2020/2003 - Install Reserve Busway
3411		EQPT.D5.3 2nd Floor DHC 2020/2003 - Install COD Boards	5	5	08-Jun-23	14-Jun-23												2nd Floor DHC 2020/2003 - Install COD Board
3412		EQPT.D5.3 2nd Floor DHC 2020/2003 - Install CRAC Units	5	5	08-Jun-23	14-Jun-23												2nd Floor DHC 2020/2003 - Install CRAC Units
3413		EQPT.D5.3 2nd Floor DHC 2020/2003 - Install Switch Gear	5	5	15-Jun-23	21-Jun-23												2nd Floor DHC 2020/2003 - Install Switch Gear
3414		EQPT.D5.3 2nd Floor DHC 2020/2003 - Final Connections CRAC Units	15	15	15-Jun-23	06-Jul-23												2nd Floor DHC 2020/2003 - Final Connectio
3415		EQPT.D5.3 2nd Floor DHC 2020/2003 - Pull and Terminate Feeders	15	15	22-Jun-23	13-Jul-23												2nd Floor DHC 2020/2003 - Pull and Terminate Feeders
3416	Mechanical Gallery 2003 DH C			76	76	21-Mar-23	06-Jul-23											06-Jul-23, Mechanical Gallery 2003 DH C
3417	Rough-In			30	30	21-Mar-23	01-May-23											01-May-23, Rough-In
3418		FRME.D5.1 2nd Floor DHC MG 2003 - Layout and Frame Walls	5	5	21-Mar-23	27-Mar-23												2nd Floor DHC MG 2003 - Layout and Frame Walls
3419		MEP.D5.30 2nd Floor DHC MG 2003 - Install Fire Protection	1	1	21-Mar-23	21-Mar-23												2nd Floor DHC MG 2003 - Install Fire Protection
3420		MEP.D5.31 2nd Floor DHC MG 2003 - Install OH Mechanical (Plumbing and HVAC)	3	3	21-Mar-23	23-Mar-23												2nd Floor DHC MG 2003 - Install OH Mechanical (Plumbin
3421		MEP.D5.31 2nd Floor DHC MG 2003 - Install OH Electrical	5	5	21-Mar-23	27-Mar-23												2nd Floor DHC MG 2003 - Install OH Electrical
3422		MEP.D5.30 2nd Floor DHC MG 2003 - In-wall Rough-in Electrical	3	3	22-Mar-23	24-Mar-23												2nd Floor DHC MG 2003 - In-wall Rough-in Electrical
3423		FRME.D5.1 2nd Floor DHC MG 2003 - Insulate and Inspect	5	5	27-Mar-23	31-Mar-23												2nd Floor DHC MG 2003 - Insulate and Inspect
3424		FRME.D5.1 2nd Floor DHC MG 2003 - Install Drywall Upper	6	6	28-Mar-23	04-Apr-23												2nd Floor DHC MG 2003 - Install Drywall Upper
3425		FRME.D5.1 2nd Floor DHC MG 2003 - Hang and Tape Drywall	6	6	05-Apr-23	12-Apr-23												2nd Floor DHC MG 2003 - Hang and Tape Drywall
3426		FNSH.D5.2 2nd Floor DHC MG 2003 - Paint	2	2	13-Apr-23	14-Apr-23												2nd Floor DHC MG 2003 - Paint
3427		FNSH.D5.2 2nd Floor DHC MG 2003 - Install Finishes	3	3	27-Apr-23	01-May-23												2nd Floor DHC MG 2003 - Install Finishes
3428	Equipment			57	57	17-Apr-23	06-Jul-23											06-Jul-23, Equipment
3429		EQPT.D5.3 2nd Floor DHC MG 2003 - Ducting	4	4	17-Apr-23	20-Apr-23												2nd Floor DHC MG 2003 - Ducting
3430		EQPT.D5.3 2nd Floor DHC MG 2003 - Install HDP Boards	5	5	28-Apr-23	04-May-23												2nd Floor DHC MG 2003 - Install HDP Boards
3431		EQPT.D5.3 2nd Floor DHC MG 2003 - Pull and Terminate Feeders	15	15	05-May-23	25-May-23												2nd Floor DHC MG 2003 - Pull and Terminate Feeders
3432		EQPT.D5.3 2nd Floor DHC MG 2003 - Install CRAC Units	5	5	08-Jun-23	14-Jun-23												2nd Floor DHC MG 2003 - Install CRAC Units
3433		EQPT.D5.3 2nd Floor DHC MG 2003 - Final Connections CRAC Units	15	15	15-Jun-23	06-Jul-23												2nd Floor DHC MG 2003 - Final Connection
3434	DH C ROOM 2200			34	34	28-Mar-23	12-May-23											12-May-23, DH C ROOM 2200
3435	Rough-In			34	34	28-Mar-23	12-May-23											12-May-23, Rough-In
3436		FRME.D5.1 2nd Floor DHC R2200 - Layout and Frame Walls	10	10	28-Mar-23	10-Apr-23												2nd Floor DHC R2200 - Layout and Frame Walls
3437		MEP.D5.30 2nd Floor DHC R2200 - Install Fire Protection	3	3	28-Mar-23	30-Mar-23												2nd Floor DHC R2200 - Install Fire Protection
3438		MEP.D5.30 2nd Floor DHC R2200 - Install OH Electrical	7	7	28-Mar-23	05-Apr-23												2nd Floor DHC R2200 - Install OH Electrical
3439		FRME.D5.1 2nd Floor DHC R2200 - Install Structural Grid	10	10	06-Apr-23	19-Apr-23												2nd Floor DHC R2200 - Install Structural Grid
3440		FRME.D5.1 2nd Floor DHC R2200 - Install Drywall Upper	4	4	11-Apr-23	14-Apr-23												2nd Floor DHC R2200 - Install Drywall Upper
3441		MEP.D5.30 2nd Floor DHC R2200 - In-wall Rough-in Electrical	4	4	17-Apr-23	20-Apr-23												2nd Floor DHC R2200 - In-wall Rough-in Electrical
3442		FRME.D5.1 2nd Floor DHC R2200 - Insulate and Inspect	5	5	21-Apr-23	27-Apr-23												2nd Floor DHC R2200 - Insulate and Inspect
3443		FRME.D5.1 2nd Floor DHC R2200 - Hang and Tape Drywall	6	6	28-Apr-23	05-May-23			</td									

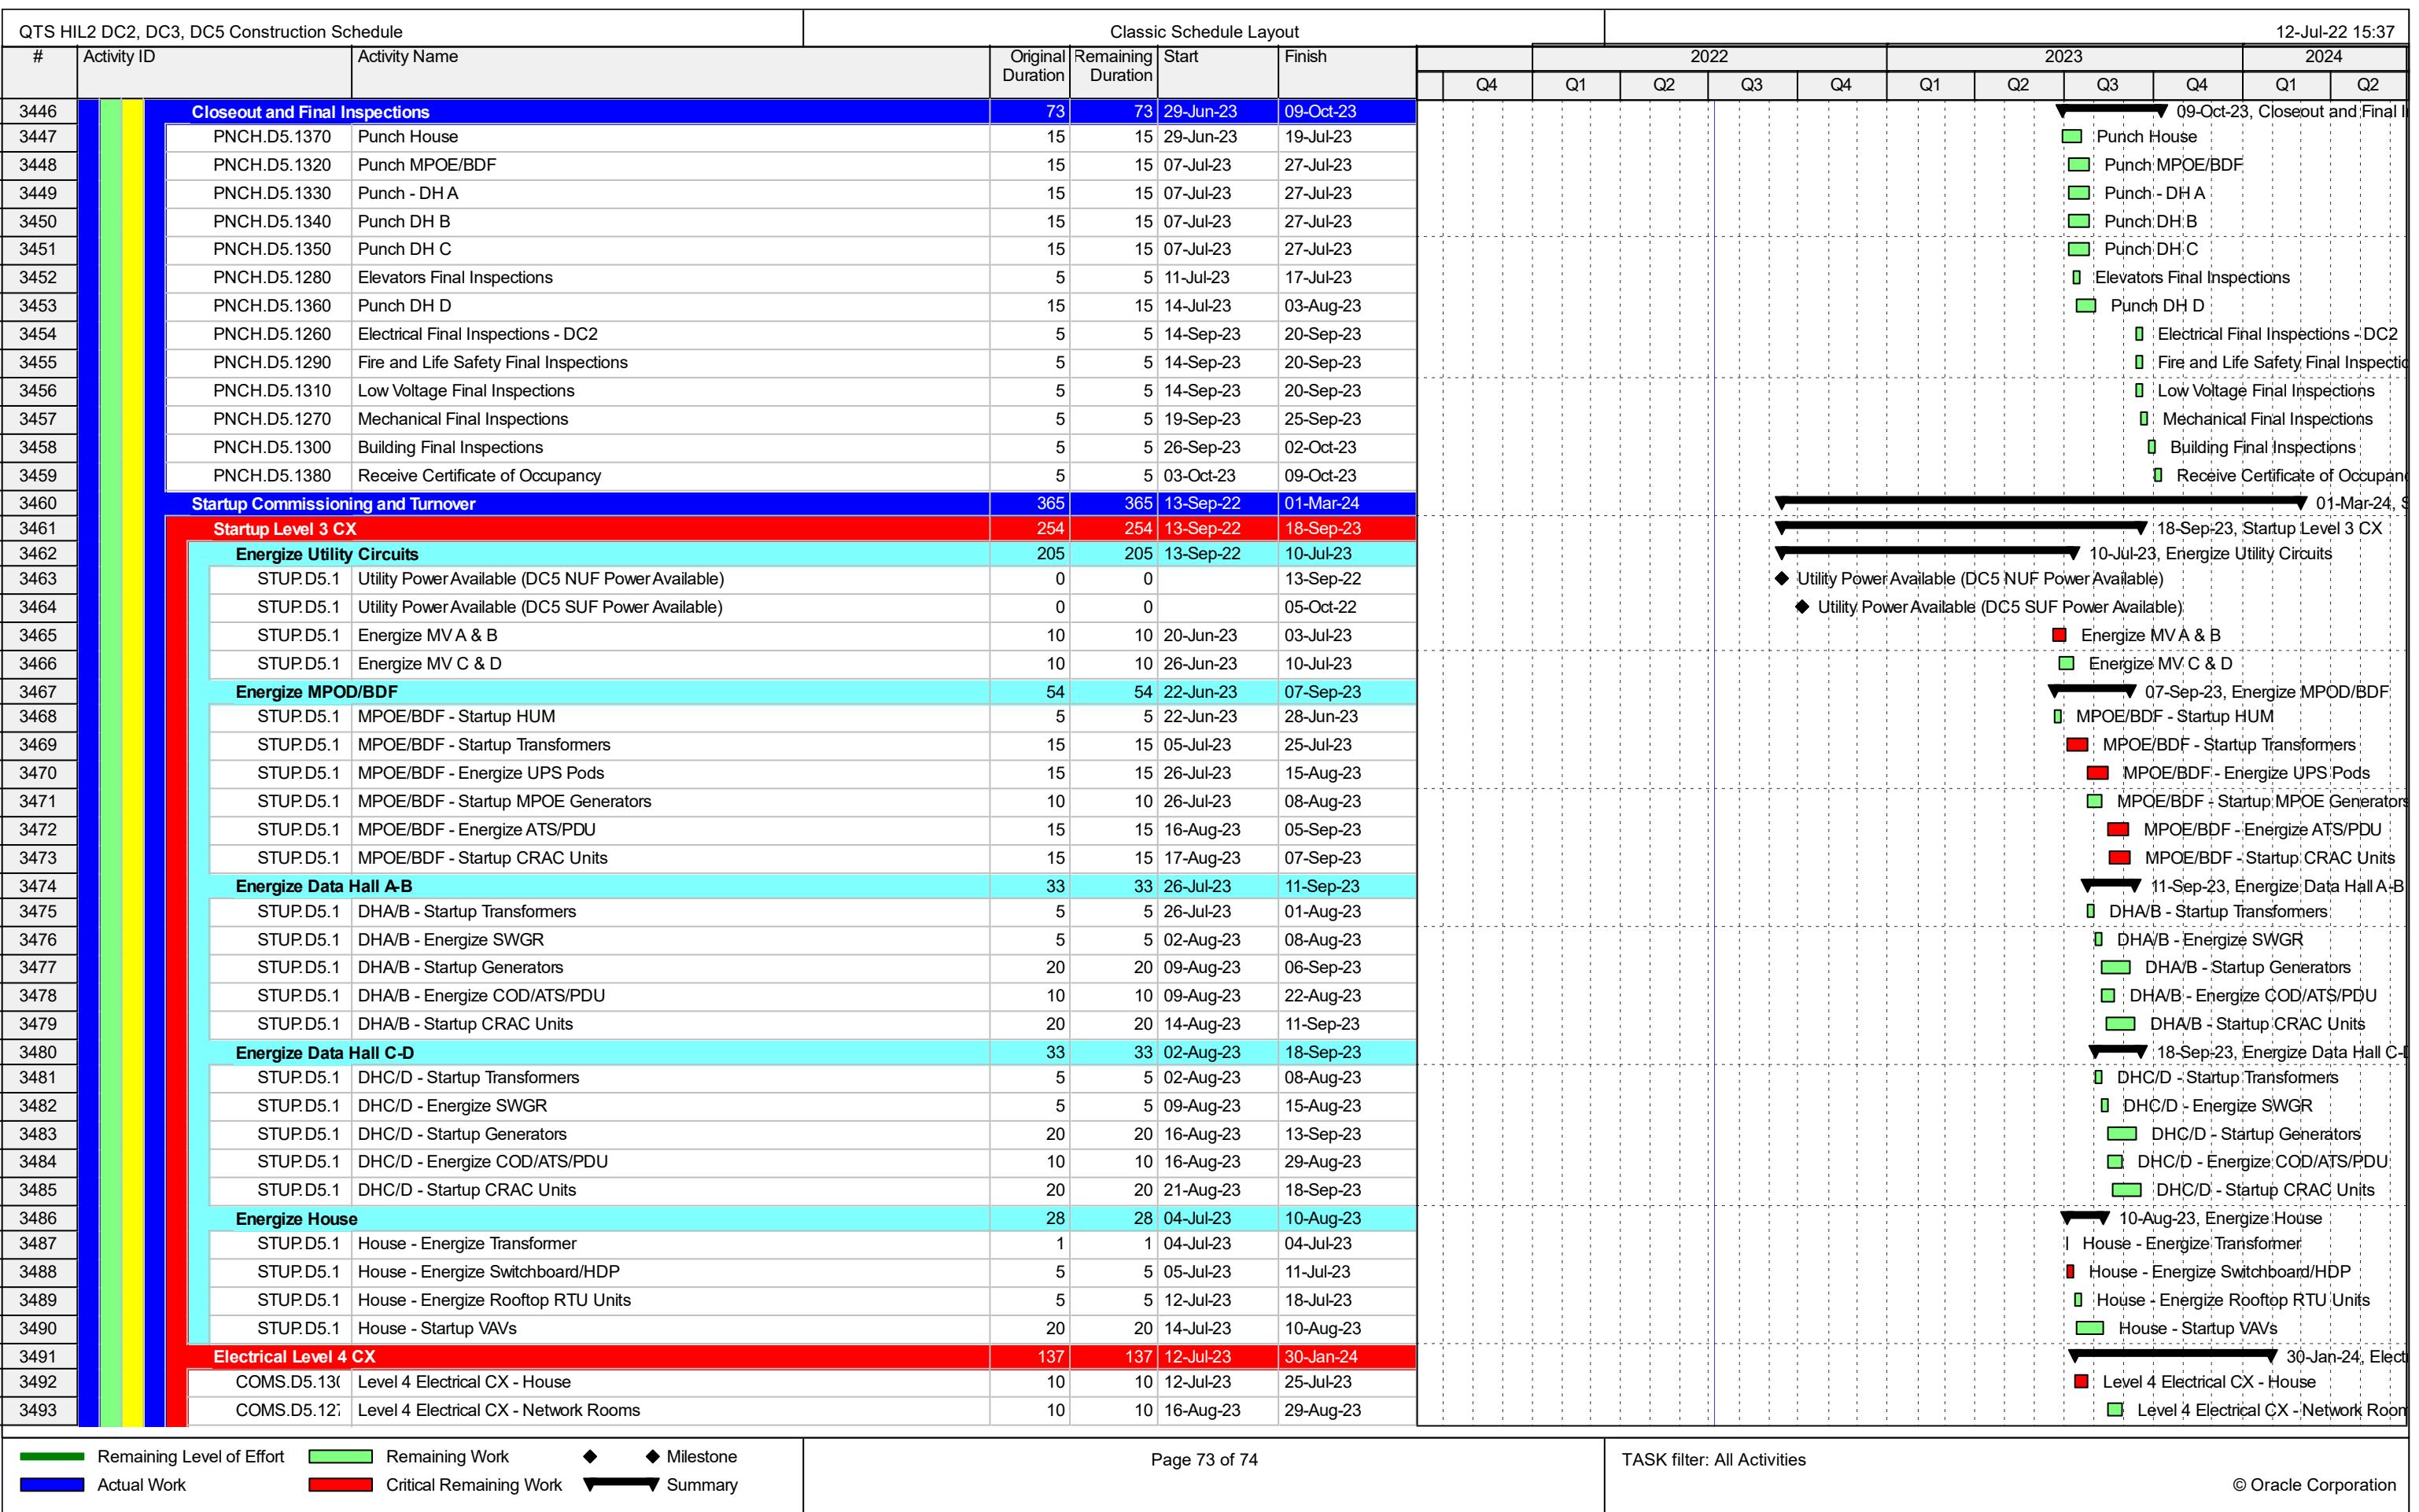

QTS HIL2 DC2, DC3, DC5 Construction Schedule				Classic Schedule Layout					12-Jul-22 15:37									
#	Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	2022				2023				2024			
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	
3494	COMS.D5.12t	Level 4 Electrical CX - Data Halls A & B	20	20	07-Sep-23	04-Oct-23												
3495	COMS.D5.12t	Level 4 Electrical CX - Data Halls C & D	20	20	02-Jan-24	30-Jan-24												
3496	Mechanical Level 4 CX						110	110	08-Sep-23	20-Feb-24								
3497	COMS.D5.13t	Level 4 Mechanical CX - Network Rooms	17	17	08-Sep-23	02-Oct-23												
3498	COMS.D5.13t	Level 4 Mechanical CX - House	20	20	03-Oct-23	31-Oct-23												
3499	COMS.D5.13t	Level 4 Mechanical CX - Data Halls A & B	16	16	01-Nov-23	27-Nov-23												
3500	COMS.D5.13t	Level 4 Mechanical CX - Data Halls C & D	34	34	02-Jan-24	20-Feb-24												
3501	Integrated Level 5 CX						101	101	03-Oct-23	01-Mar-24								
3502	COMS.D5.13t	Level 5 CX - Network	5	5	03-Oct-23	10-Oct-23												
3503	COMS.D5.13t	Level 5 CX - House	5	5	01-Nov-23	07-Nov-23												
3504	COMS.D5.13t	Level 5 CX - Data Halls A & B	5	5	26-Dec-23	01-Jan-24												
3505	COMS.D5.13t	Level 5 CX - Data halls C & D	5	5	26-Feb-24	01-Mar-24												
3506	Weather Days						64	64	28-Nov-23	23-Feb-24								
3507	WEATHER.D5t	Weather Days DC5 DH A & B (40-0=40)	19	19	28-Nov-23	22-Dec-23												
3508	WEATHER.D5t	Weather Days DC5 DH C&D (41-0=41)	3	3	21-Feb-24	23-Feb-24												
3509	Deleted activities						48	48	07-Jul-22	13-Sep-22								
